Alpha
Consulting Engineers Pte Ltd

PROJECT QUALITY PLAN

POLYCLINIC & NURSING HOME AT 200 JURONG EAST AVE 1

For

MOH HOLDINGS PTE LTD

Copy No.	1

Prepared By : Lim Chai Hoon / Chuan Kian Heng / Bervyn Tan / Ching Mun Chung

Authorised By : Loh Fook Yuen

Date : 10 December 2025

TABLE OF CONTENTS

SECTION	DESCRIPTION
-	**TITLE PAGE**
-	**TABLE OF CONTENTS**
1	**QUALITY PLAN CONTROL AND DISTRIBUTION**
1.1	List of Copy Holders
1.2	Revision Record
2	**PROJECT INFORMATION**
2.1	Project Description
2.2	Project Cost
2.3	Scope of Works
3	**ORGANISATION**
3.1	Organisation Chart
3.2	ACEPL's Project Team Member
3.3	Client/Client's Representative
3.4	Other Consultants - Local - Overseas – NOT APPLICABLE
3.5	Contractor/Sub-Contractors
3.6	Authorities
4	**PROGRAMME**
4.1	Overall Programme
4.2	Authority Submission Status for M&E Services – 1st Submission
4.3	Authority Submission Status for M&E Services (Amendment) – 2nd Submission - NOT APPLICABLE
5	**PROJECT RECORDS**
5.1	List of Internal Files
5.2	Filing of Drawings

TABLE OF CONTENTS

SECTION	DESCRIPTION
6	**INTERFACING**
6.1	Method of Interface
6.2	Internal Design Interface
6.3	Circulation of Documents to External Parties
7	**WORK AUTHORISATION**
8	**DESIGN INPUT AND METHODOLOGY**
8.1	List of Client's Standards, Reference Documents or Brief
8.2	List of Applicable Code of Practice and Regulations
8.3	List of Design Guide or Handbook Used
8.4	List of Pre-Consultation and Waiver
8.5	List of Applicable Quality System Procedures
8.6	List of Software Used for Design/Analysis
9	**ENVIRONMENTAL CONSIDERATIONS**
9.1	Sustainable Design Features / Criteria
9.2	Site PPE Requirement – NOT APPLICABLE
9.3	Site Emergency Preparedness
9.4	Reporting of Environmental Non-conformances
9.5	List of Applicable Environmental Management System Procedures – NOT APPLICABLE
10	**CLIENT'S REQUIREMENTS**
10.1	List of Output Required by Client
10.2	Specific Procedures Required by Client
11	**LIST OF SUB-JOB**
11.1	List of Sub-Job Numbers

SECTION 1

QUALITY PLAN CONTROL AND DISTRIBUTION

1.1 List of Copy Holders

Copy No.	Copy Holder	Date of Issue
1	6286-PQP	10 December 2025

1.2 Revision Record

Revision	Date of Issue	Section Reference	Page(s)	Remarks
0	6 January 2021	1 to 11	30	+ 1 pg (Section 4.1 – Overall Programme)
1	7 February 2022	1 to 11	30	+ 1 pg (Section 4.1 – Overall Programme)
2	9 January 2024	1 to 11	30	+ 3 pgs (Section 4.1 – Overall Programme)
3	13 January 2025	1 to 11	30	+ 44 pgs (Section 4.1 – Overall Programme) + 2 pgs (Section 9.3 – Site Emergency Preparedness)
4	10 December 2025	1 to 11	30	+ 42 pgs (Section 4.1 – Overall Programme) + 4 pgs (Section 9.3 – Site Emergency Preparedness)

SECTION 2

PROJECT INFORMATION

2.1 Project Description

Type of Development	Polyclinic & Nursing Home

Statistics of Development	
Site Area, m²	12,180.2
Nett Floor Area, m²	-
Gross Floor Area, m²	36,261
Covered Carpark, m²	-
No. of Covered Carpark Lots	114
No. of Apartments/Houses	NA
No. of Beds (for Hospitals)	732
No. of Guestroom (for Hotels)	NA
No. of Blocks / No. of Storeys	9
Green Mark Category	Platinum SLEB
No. of Phases	1

2.2 Project Cost

M&E Services Cost Plan (S$ x 1M)										
Services	EI	ACVI	LEI	FFAI	PSI	SPFI	Total			
Estimate	12.6	11.6	2.7	3.7	7.4	-	38			
Awarded	12.9	12.9	1.6	3.2	5.3	-	35.9			

Total Project Construction Cost (S$ x1M)			
	Site Clearance	Piling Works	Main Contract
Estimate	-	-	161.7
Awarded	-	5	201

Site Clearance shall include earth work, soil improvement, service diversion and termination.

2.3 Scope of Works

2.3.1 Scope of Consultancy Services

Conceptual/Schematic Design	✓
Detailed Design	✓
Tender Documentation	✓
Tender Evaluation	✓
Contract Supervision	✓
M&E Costing	✓
Submissions to Authority	✓

(✓*where applicable*)

2.3.2 Scope of M&E Services

ELECTRICAL	✓	AIR CONDITIONING	✓	SPRINKLER	✓	SANITARY	✓	SWIMMING POOL	
LIFT	✓	MECHANICAL VENTILATION	✓	FIRE ALARM	✓	COLD WATER	✓	STEAM BOILER	
ESCALATOR		MECHANICAL SMOKE EXTRACT	✓	HOSEREEL	✓	HOT WATER	✓	FUEL STORAGE	
PABX		COMPUTER A/C		WET RISER		TOWN GAS	✓		
SECURITY	✓	BST CARPARK EXH		DRY RISER	✓	LPG GAS			
TELELIFT		HEATING				MEDICAL GAS			
DATA COMM.	✓								
FLUSHFLOOR TRUNKING									

(✓*where applicable*)

2.3.3 Submission to Relevant Authorities by Others


EJECTOR & DIVERTER		SUMP PUMP		FUEL OIL TANK		LIFT & ESCALATOR	✓	PRESSURE VESSEL		HOISTS		FOAM	

(✓*where applicable*)

SECTION 3

ORGANISATION

3.1 Organisational Chart

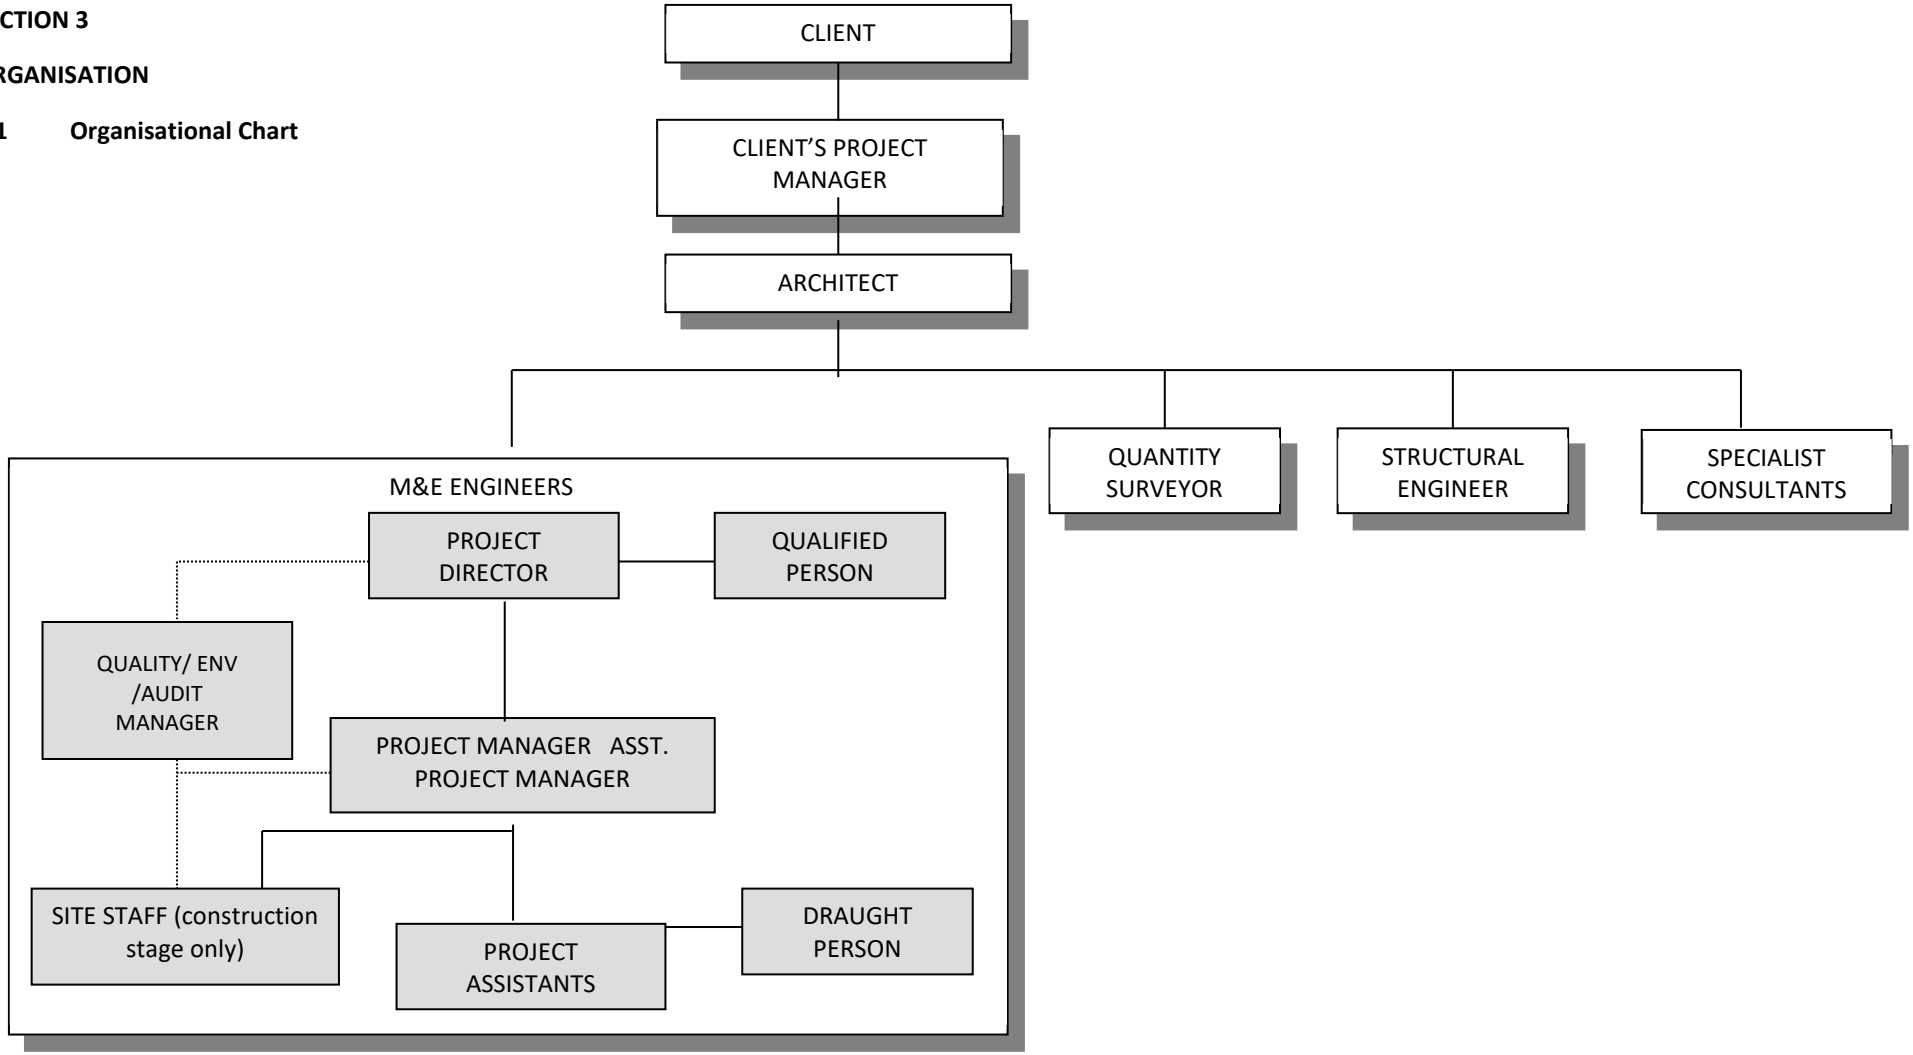

SECTION 3

ORGANISATION

3.2 ACEPL's Project Team Member

TITLE		NAME
Project Director		Loh Fook Yuen (LFY)
Qualified Person	Mechanical	Choong Choon Guan (CCG)
	Electrical	Loh Fook Yuen (LFY)
Project Manager		Lim Chai Hoon (LCY)
Assistant Project Manager		Chuan Kian Heng (CKH)
Project Assistant (Mech)		Ching Mun Chung (CMC)
Project Assistant (Elect)		Bervyn Tan Woo Seng (TWS)
Draughtsperson		Common Pool
Resident Engineer (M&E)		-
Assistant Resident Engineer (M&E)		-
Clerk-of-Work (M&E)		-
Resident Technical Officer (M&E)		Ho Tuck Seng (HTS)

3.3 Client/Client's Representatives

Client: MOH Holdings Pte Ltd

Address: 1 Maritime Square (Lobby C) #11-25 HarbourFront Centre
Singapore 099253

Tel: 6622 0980

Fax: 6720 0980

Client's Representatives:-

Name of Company	Contact Person	Contact
MOH Holdings Pte Ltd	Name: Mr Kenneth Wong Position: Senior Manager	Tel: - Fax: 67200980 Handphone: 97521311 Email: kenneth.wong2@mohh.com.sg
	Name: Mr Shaun Phua Position: Assistant Director	Tel: - Fax: 67200980 Handphone: 96733851 Email: shaun.phua@mohh.com.sg
	Name: Ms Alexis Chan Position: Senior Manager	Tel: 68881241 Fax: 67200980 Handphone: 90687738 Email: alexis.chan@mohh.com.sg
	Name: Position:	Tel: Fax: Handphone: Email:
	Name: Position:	Tel: Fax: Handphone: Email:

3.4 **Other Consultants** (Local)

Function / Name of Company	Contact Person	Contact
Architect W Architects Pte Ltd	Name: Mr Ng Weng Pan Position: Director	Tel: 6672 6200 Fax:- Handphone:- Email: ngwengpan@w-architects.com.sg
Quantity Surveyor CPG Consultants Pte Ltd	Name: Ms Wang Hui Zhen Position: Principal Quantity Surveyor	Tel: - Fax:- Handphone: 90235149 Email: wang.hui.zhen@cpgcorp.com.sg
Structural Engineer KTP Consultants Pte Ltd	Name: Mr Kevin Christian Nair Position: Principal Engineer	Tel: - Fax:- Handphone: 82420620 Email: kevin.nair@ktpworld.com
Planning & Construction Manager SIPM Consultants Pte Ltd	Name: Mr Luqman Hakim Bin Ismail Position: Senior Executive Project Manager	Tel:- Fax:- Handphone: 9176 0699 Email: luqman.ismail@sipmconsultants.com
Interior Designer W Architects Pte Ltd	Name: Mr Ng Weng Pan Position: Director	Tel: 6672 6200 Fax:- Handphone:- Email: ngwengpan@w-architects.com.sg
Acoustic Consultant CCW Associates Pte Ltd	Name: Ms Febi Rhiana Position:	Tel: 6278 4918 Fax: 6275 7206 Handphone: 9738 1795 Email: febi@ccw.com.sg
Security Consultant SSTech Security Consultancy Pte Ltd	Name: Mr Simon Sng Yong Lim Position: Principal Security Consultant	Tel: 6659 1086 Fax: 6659 1071 Handphone: 9682 8555 Email: simonsng@sstech.com.sg
Environmentally Sustainable Design Consultant Building System & Diagnostics Pte Ltd	Name: Tan Phay Ping Position: Managing Director	Tel: 6560 0702 Fax: 6795 0020 Handphone: 9878 6876 Email: tanpp@bsd.com.sg

3.4 Other Consultants (Overseas) – **NOT APPLICABLE**

Function / Name of Company	Contact Person	Contact
Architect	Name: Position:	Tel: Fax: Handphone: Email:
M&E Consultant	Name: Position:	Tel: Fax: Handphone: Email:
Quantity Surveyor	Name: Position:	Tel: Fax: Handphone: Email:
Structural Engineer	Name: Position:	Tel: Fax: Handphone: Email:
Interior Designer	Name: Position:	Tel: Fax: Handphone: Email:
Lighting Consultant	Name: Position:	Tel: Fax: Handphone: Email:
Acoustic Consultant	Name: Position:	Tel: Fax: Handphone: Email:
_____	Name: Position:	Tel: Fax: Handphone: Email:

3.5 Contractors/Sub-Contractors

Function / Name of Company	Contract *	Contact Person	Contact
Main Contractor Kwan Yong Construction Pte Ltd	NSC	Name: Tang Siew Tuck Position: Project Director	Tel: - Fax: - Handphone: 9382 2292 Email: st.tang@kwanyong.com.sg
Air Conditioning & Ventilation Installation Sub-Contractor Poh Meng Engineering Pte Ltd	NSC	Name: K Vinoth Kumar Position: Senior Project Manager	Tel: - Fax: - Handphone: 8368 5378 Email: vino@pohmeng.com.sg
Plumbing & Sanitary Installation Sub-Contractor YCP Pte Ltd	NSC	Name: Ho Kee Kwan Position: Project Manager	Tel: - Fax: - Handphone: 9759 5392 Email: hokeekwan@ycp.sg
Electrical Installation Sub-Contractor HEC Electrical & Construction Pte Ltd	NSC	Name: Chong Position: Project Manager	Tel: - Fax: - Handphone: 9062 3982 Email: chong@hec.com.sg
Lift & Escalator Installation Sub-Contractor Otis Elevator Company (S) Pte Ltd	NSC	Name: Vincent Leow Position: Senior Project Manager	Tel: - Fax: - Handphone: 9852 5960 Email: Vincent.leow@otis.com
Fire Fighting & Alarm Installation Sub-Contractor Rico Engineering Works Pte Ltd	NSC	Name: William Kow Position: Project Manager	Tel: Fax: Handphone: 8292 6689 Email: William.Kow@ricoeng.com.sg
Swimming Pool Filtration Plant Installation Sub-Contractor		Name: Position:	Tel: Fax: Handphone: Email:
Carpark System Installation Sub-Contractor		Name: Position:	Tel: Fax: Handphone: Email:
_____		Name: Position:	Tel: Fax: Handphone: Email:

** Type of Contract*
- *NSC (Nominated Sub-Contract)*
- *DSC (Domesticated Sub-Contract)*
- *DC (Direct Contract)*
- *NS (Nominated Supplier)*

3.6 Authorities

Authorities/Department	Contact Person	Tel/Fax Nos./E-mail
SP PowerGrid:		
(a) Sub-Station	Mr Goh Li Qing	6916 8679
(b) Diversion		
SP Services:		
(a) Customer Supply		
(b) Installation		
(c) Meter Section		
(d) Road Lighting		
TFCC:		
(a) SCV		
(b) SingTel	Mr Lee Chong Beng	96497 719
(c) IDA	Mr Seah Koon Chye	6211 1751
BCA:		
(a) Building Plan		
(b) Green Mark		
FSSD:		
(a) Building Plan		
(b) M&E Plan		
PUB (Water Supply) Network Dept:		
(a) Water Conservation		
(b) Plumbing Plan		
(c) Diversion		
(d) NEWater		
PUB Water Reclamation (Network) Dept:		
(a) Building Plan/CBPU		
(b) M&E Plan		
(c) Diversion		
City Gas Pte Ltd:		
(a) Planning/Submission	Mr Liew Khee Boon	6578 7603
(b) Installation/Inspection		
PowerGas Pte Ltd		
(a) Diversion		
NEA (Pollution Control)		
(a) Planning/Submission		
(b) Inspection		

SECTION 4


PROGRAMME

4.1 Overall Programme – Refer to the attachment

ID	TASK NAME	MONTHS	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
1.	Preliminary Planning																									
2.	Planning Submission																									
3.	Detail Design																									
4.	BP Submission																									
5.	BP Submission (Amendments)																									
6.	Tender Period for Piling																									
7.	Tender Period for Sub-Structure																									
8.	Tender Period for Super-Structure																									
9.	Piling Period																									
10.	Sub-Structure Construction Period																									
11.	Super-Structure Construction Period																									
12.	TOP																									
13.	CSC																									

Kwan Yong Construction Pte Ltd — **Master Programme For Co-Located Polyclinic & Nursing Home At 200 Jurong East Ave 1**

ID	Task Name	Duration	Start	Finish	Predecessors
1	**Preliminary Works Schedule**	**400 days**	**Thu 4/7/24**	**Mon 27/10/25**	
2	**Pre-commencement activities**	**16 days**	**Thu 4/7/24**	**Mon 22/7/24**	
3	Letter of award	0 days	Thu 4/7/24	Thu 4/7/24	
4	Site Procession	0 days	Mon 8/7/24	Mon 8/7/24	
5	Factory permit (MOM)	7 days	Mon 15/7/24	Mon 22/7/24	
6	**Insurance**	**9 days**	**Mon 8/7/24**	**Wed 17/7/24**	
7	Cover Note	5 days	Mon 8/7/24	Fri 12/7/24	
8	Full policy	4 days	Sat 13/7/24	Wed 17/7/24	7
9	**Site facitlities setup**	**84 days**	**Tue 9/7/24**	**Tue 15/10/24**	
10	Oversite excavation	15 days	Mon 22/7/24	Wed 7/8/24	
11	**Site access**	**47 days**	**Mon 29/7/24**	**Sat 21/9/24**	
12	Gate 1	14 days	Mon 29/7/24	Wed 14/8/24	
13	Gate 2	14 days	Fri 6/9/24	Sat 21/9/24	
14	ECM/vehicle washing bay	7 days	Mon 15/7/24	Mon 22/7/24	
15	**Site office/mtg rm/toilets**	**84 days**	**Tue 9/7/24**	**Tue 15/10/24**	
16	Temporary Container Offices	5 days	Tue 9/7/24	Sat 13/7/24	
17	3-storey prefab office	32 days	Mon 9/9/24	Tue 15/10/24	
18	**Precondition survey**	**17 days**	**Thu 11/7/24**	**Tue 30/7/24**	
19	Site survey	3 days	Thu 11/7/24	Sat 13/7/24	
20	Submit report	14 days	Mon 15/7/24	Tue 30/7/24	19
21	Precomputation survey submission/approval/setting out	14 days	Tue 16/7/24	Wed 31/7/24	
22	**Underground services detection & submission**	**72 days**	**Tue 9/7/24**	**Tue 1/10/24**	
23	Purchase drawings from agencies	12 days	Tue 9/7/24	Mon 22/7/24	
24	Site survey	2 days	Tue 23/7/24	Wed 24/7/24	23
25	**Trial Hole Report Submission & Approval**	**43 days**	**Tue 13/8/24**	**Tue 1/10/24**	
26	SPPG	1 day	Tue 13/8/24	Tue 13/8/24	
27	NetLink	14 days	Mon 16/9/24	Tue 1/10/24	
28	**Instrumentation monitoring works**	**20 days**	**Wed 17/7/24**	**Thu 8/8/24**	
29	Submission & approval	6 days	Wed 17/7/24	Tue 23/7/24	
30	Site installation	14 days	Wed 24/7/24	Thu 8/8/24	29
31	**Authorities submissions and approvals**	**388 days**	**Thu 18/7/24**	**Mon 27/10/25**	
32	Site entrance/exit road opening submission/approval	21 days	Fri 19/7/24	Tue 13/8/24	
33	Crane clearance (RSAF/CAAS) - Piling works	14 days	Thu 18/7/24	Fri 2/8/24	
34	ECM (PUB)	21 days	Thu 18/7/24	Mon 12/8/24	
35	Temporary electrical supply (Powergrid/EMA)	60 days	Mon 22/7/24	Mon 30/9/24	
36	Temporary toilet & water (PUB/CBPU)	30 days	Mon 22/7/24	Mon 26/8/24	
37	PUB POWS For Piling	14 days	Thu 12/9/24	Fri 27/9/24	
38	PUB POWS For Tangent Pile	14 days	Fri 10/10/25	Mon 27/10/25	
39	**ERSS (BCA)**	**91 days**	**Fri 30/8/24**	**Fri 13/12/24**	
40	Tangent Pile Submission to BCA (ST102)	30 days	Fri 30/8/24	Thu 3/10/24	
41	Sheet Piling Submisison to BCA (ST103)	30 days	Sat 5/10/24	Sat 9/11/24	
42	Raking Strut Submission to BCA (ST 104)	30 days	Mon 11/11/24	Fri 13/12/24	
43	Pre -commencement CCTV(PUB/NEA)	21 days	Mon 22/7/24	Thu 15/8/24	
44	**Tower Cranes**	**42 days**	**Sat 14/9/24**	**Sat 2/11/24**	
45	PE Design	14 days	Sat 14/9/24	Mon 30/9/24	
46	Crane clearance (RSAF/CAAS)	21 days	Tue 1/10/24	Thu 24/10/24	45
47	MOS/Presentation to MOHH	7 days	Fri 25/10/24	Sat 2/11/24	46
48	**Erection**	**52 days**	**Tue 24/12/24**	**Wed 26/2/25**	
49	TC 1	7 days	Tue 24/12/24	Thu 2/1/25	
50	TC 2	7 days	Fri 31/1/25	Fri 7/2/25	
51	TC 3	7 days	Wed 19/2/25	Wed 26/2/25	
52	**RDS**	**298 days**	**Tue 1/10/24**	**Wed 24/9/25**	
53	**Mock Up (NH & PC)**	**151 days**	**Tue 1/10/24**	**Sat 29/3/25**	
54	shopdrawing - 1st submission	35 days	Tue 1/10/24	Mon 11/11/24	

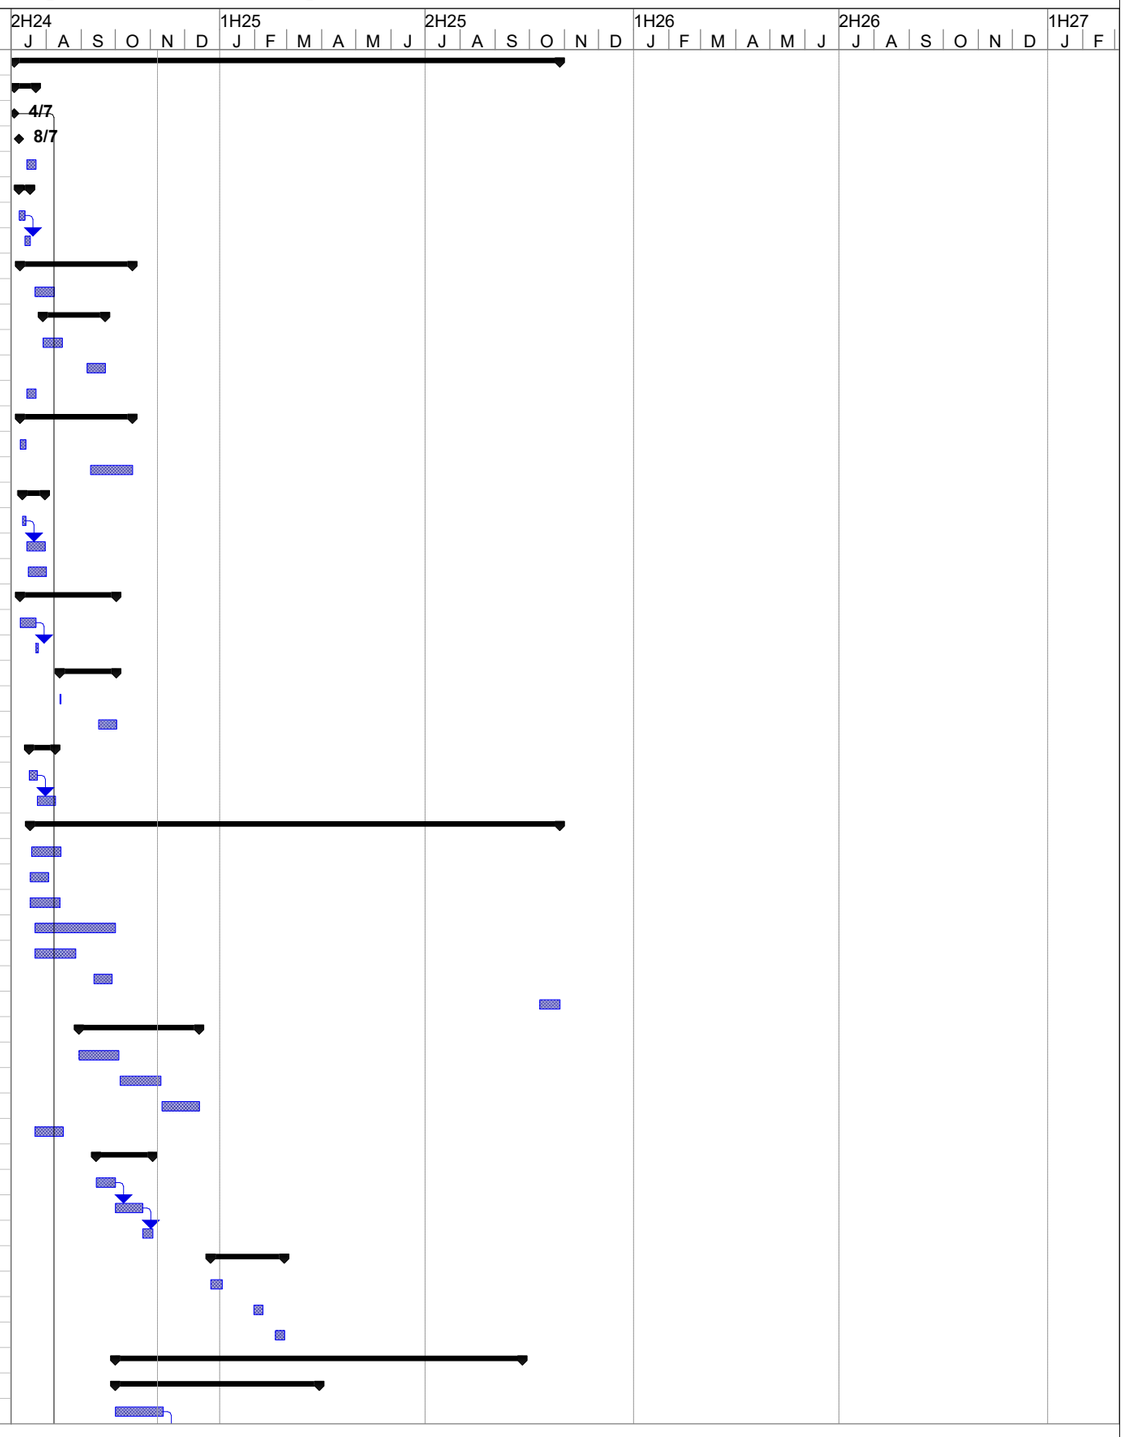


Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task — Split — Milestone — Summary
Project Summary — External Tasks — External Milestone — Inactive Milestone
Inactive Summary — Manual Task — Duration-only — Manual Summary Rollup
Manual Summary — Start-only — Finish-only — External Tasks
External Milestone — Progress — Deadline

Kwan Yong Construction Pte Ltd — **Master Programme For Co-Located Polyclinic & Nursing Home At 200 Jurong East Ave 1**

ID	Task Name	Duration	Start	Finish	Predecessors
55	Consultants reply	35 days	Tue 12/11/24	Fri 20/12/24	54
56	shopdrawing - 2nd submission	33 days	Sat 21/12/24	Sat 1/2/25	55
57	Consultants approval & RDS Update	33 days	Mon 3/2/25	Wed 12/3/25	56
58	Briefing to Operator (NUP & Sunnyville) - by consultants	14 days	Thu 13/3/25	Fri 28/3/25	57
59	Sign-off by Operator	1 day	Sat 29/3/25	Sat 29/3/25	58
60	**Remaining - PC**	**255 days**	**Thu 21/11/24**	**Wed 24/9/25**	
61	shopdrawing - 1st submission	60 days	Thu 21/11/24	Sat 1/2/25	
62	Consultants reply	60 days	Mon 3/2/25	Mon 14/4/25	
63	shopdrawing - 2nd submission	60 days	Tue 15/4/25	Fri 27/6/25	
64	Consultants approval & RDS Update	60 days	Sat 28/6/25	Sat 6/9/25	
65	Briefing to Operator (NUP) - by consultants	14 days	Mon 8/9/25	Tue 23/9/25	
66	Sign-off by Operator	1 day	Wed 24/9/25	Wed 24/9/25	
67	**Remaining - NH**	**218 days**	**Tue 1/10/24**	**Sat 21/6/25**	
68	shopdrawing - 1st submission	60 days	Tue 1/10/24	Mon 9/12/24	
69	Consultants reply	60 days	Tue 10/12/24	Fri 21/2/25	68
70	shopdrawing - 2nd submission	40 days	Sat 22/2/25	Thu 10/4/25	69
71	Consultants approval & RDS Update	44 days	Fri 11/4/25	Wed 4/6/25	70
72	Briefing to Operator (Sunnyville) - by consultants	14 days	Thu 5/6/25	Sat 21/6/25	71
73	Sign-off by Operator	1 day	Fri 20/6/25	Fri 20/6/25	
74	**Appointment of Equipment Vendor**	**314 days**	**Mon 11/11/24**	**Sat 22/11/25**	
75	**Polyclinic**	**264 days**	**Mon 11/11/24**	**Wed 24/9/25**	
76	Conveyor System (Pharmacy L1 to L3)	1 day	Mon 11/11/24	Mon 11/11/24	205SS-95 days
77	Last Mile Automation (Pharmacy L1 to L3)	1 day	Mon 11/11/24	Mon 11/11/24	205SS-95 days
78	ROWA (Pharmacy L3)	1 day	Wed 11/12/24	Wed 11/12/24	205SS-68 days
79	RFID Shelves (Pharmacy L1 & L3)	1 day	Mon 11/11/24	Mon 11/11/24	205SS-95 days
80	Compactus System (Pharmacy L3)	1 day	Wed 19/2/25	Wed 19/2/25	205SS-12 days
81	Blister - Pharmacy L3	1 day	Mon 21/4/25	Mon 21/4/25	207SS-60 days
82	X-Ray (X-Ray Room L1)	1 day	Fri 20/12/24	Fri 20/12/24	205SS-60 days
83	AV - MPH/ Seminar Room (Ceiling Mounting L3)	1 day	Mon 21/4/25	Mon 21/4/25	207SS-60 days
84	Surgical Ceiling Light (Minor Surgical Procudure Room L1)	1 day	Tue 1/4/25	Tue 1/4/25	205SS-60 days
85	Dental Chair (Dental L2)	1 day	Wed 24/9/25	Wed 24/9/25	357SS-60 days
86	Dental Tilter (Dental L2)	1 day	Wed 24/9/25	Wed 24/9/25	357SS-60 days
87	Dental X-Ray (Dental L2)	1 day	Wed 24/9/25	Wed 24/9/25	357SS-60 days
88	Anti-theft panel Sensormatic Gate (Retail Pharmacy L1)	1 day	Fri 20/12/24	Fri 20/12/24	205SS-60 days
89	E-Gate (Retail Pharmacy L1, Entrance L1)	1 day	Fri 20/12/24	Fri 20/12/24	205SS-60 days
90	Wall Mounted Self-Reg Kiosk (Entrance L1)	1 day	Tue 21/1/25	Tue 21/1/25	234SS-30 days
91	Wall Mounted Medicine Self Collection Kiosk (Social Void Deck L1)	1 day	Tue 21/1/25	Tue 21/1/25	234SS-30 days
92	Compressor (Compressor Room L2)	1 day	Wed 24/9/25	Wed 24/9/25	357SS-60 days
93	Double Ended Washer Disinfector (Sterilisation & Decon L2)	1 day	Wed 24/9/25	Wed 24/9/25	357SS-60 days
94	**Nursing Home**	**279 days**	**Fri 20/12/24**	**Sat 22/11/25**	
95	Laundry - L1	1 day	Fri 20/12/24	Fri 20/12/24	205SS-60 days
96	AMR	1 day	Tue 10/6/25	Tue 10/6/25	319SS-60 days
97	Projectors - Ops/IT (Ceiling Mounting) L2	1 day	Wed 20/8/25	Wed 20/8/25	343SS-60 days
98	Bed Hoist - L2	1 day	Wed 20/8/25	Wed 20/8/25	343SS-60 days
99	Kitchen - L9	1 day	Sat 22/11/25	Sat 22/11/25	213SS-60 days
100	**External**	**1 day**	**Tue 21/1/25**	**Tue 21/1/25**	
101	Electronic Parking System (EPS)	1 day	Tue 21/1/25	Tue 21/1/25	261SS-60 days
102	**Blackout Dates - Subject To JVSS Management Request**	**135 days**	**Fri 26/7/24**	**Thu 2/1/25**	
103	**JVSS Exam Timetable (Year 2024)**	**91 days**	**Fri 26/7/24**	**Mon 11/11/24**	
104	N & O Level Prelim Examination	15 days	Fri 26/7/24	Tue 13/8/24	
105	O Level Written	21 days	Thu 17/10/24	Mon 11/11/24	
106	N Level Written	26 days	Mon 9/9/24	Tue 8/10/24	
107	EOY Exam	13 days	Thu 26/9/24	Thu 10/10/24	
108	**Blackout Dates (Year 2025)**	**1 day**	**Thu 2/1/25**	**Thu 2/1/25**	

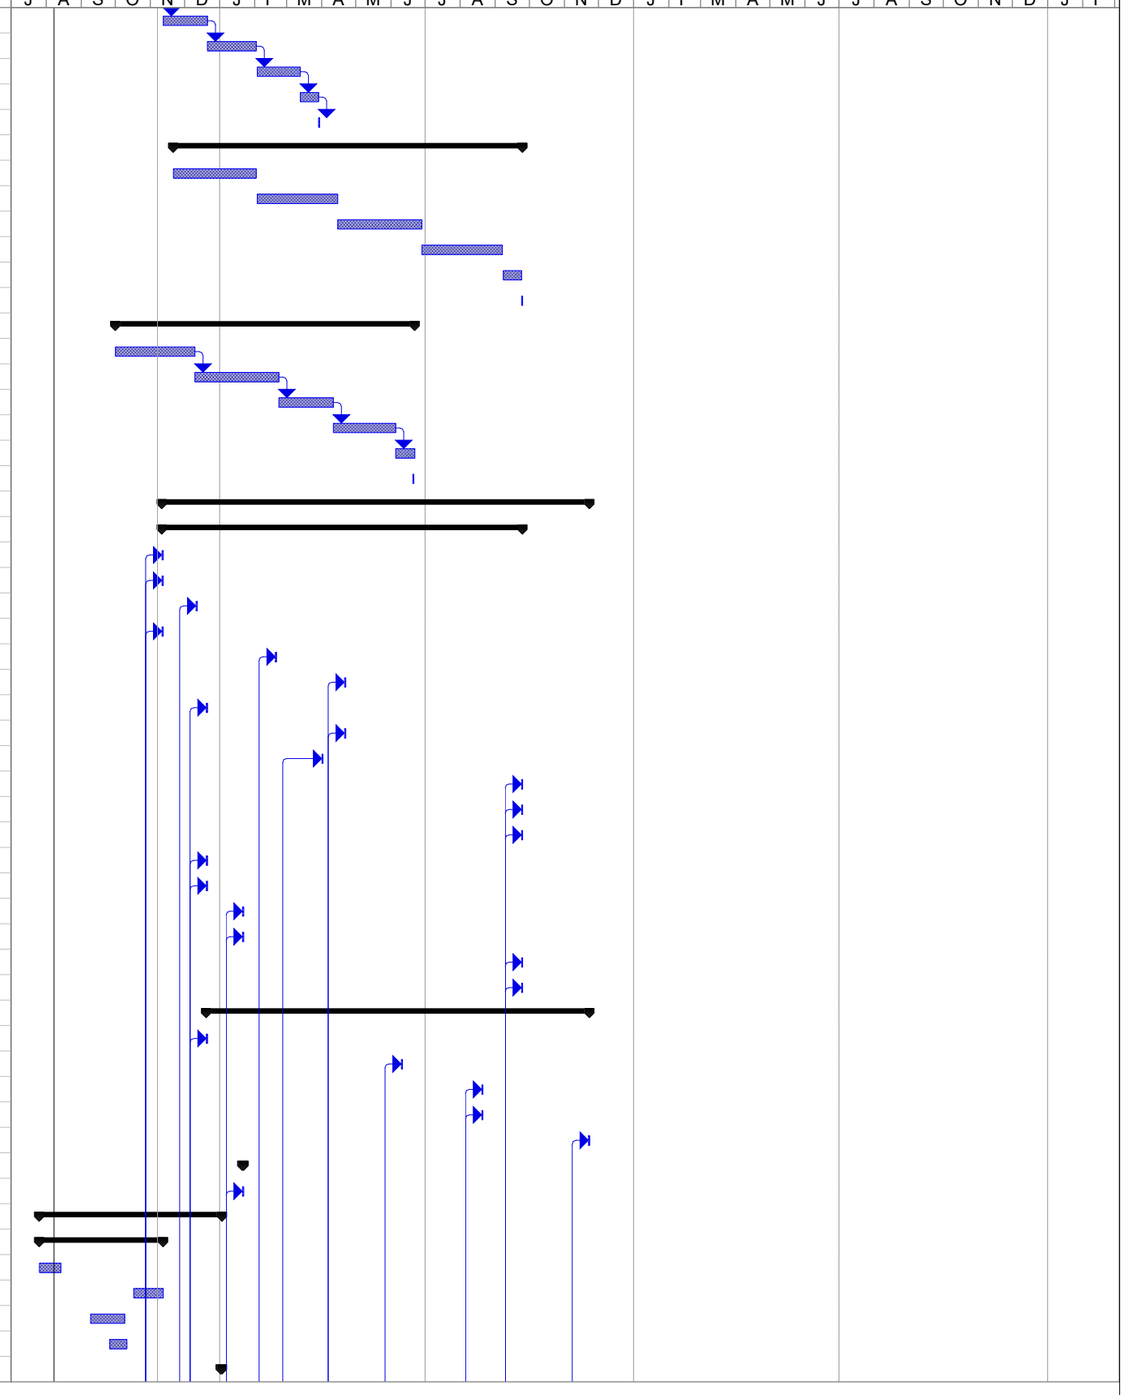


Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task — Split — Milestone — Summary
Project Summary — External Tasks — External Milestone — Inactive Milestone
Inactive Summary — Manual Task — Duration-only — Manual Summary Rollup
Manual Summary — Start-only — Finish-only — External Tasks
External Milestone — Progress — Deadline

Kwan Yong Construction Pte Ltd **Master Programme For Co-Located Polyclinic & Nursing Home At 200 Jurong East Ave 1**

ID	Task Name	Duration	Start	Finish	Predecessors
109	School Kick off (1st day of School)	1 day	Thu 2/1/25	Thu 2/1/25	
110	**M&E Combined Services Drawing (CSD) Submission & Approval**	**508 days**	**Mon 2/9/24**	**Thu 7/5/26**	
111	**Underground Level (PC & NH)**	**44 days**	**Mon 2/9/24**	**Tue 22/10/24**	
112	M&E shopdrawing submission & approval	14 days	Mon 2/9/24	Tue 17/9/24	
113	CSD submisison & approval	30 days	Wed 18/9/24	Tue 22/10/24	112
114	**Basement Level (PC & NH)**	**89 days**	**Fri 11/10/24**	**Fri 24/1/25**	
115	M&E shopdrawing submission & approval	50 days	Fri 11/10/24	Sat 7/12/24	
116	CSD submisison & approval	30 days	Thu 19/12/24	Fri 24/1/25	198SS-14 days
117	**Level 1 (PC & NH)**	**91 days**	**Tue 3/12/24**	**Sat 22/3/25**	
118	M&E shopdrawing submission & approval	60 days	Tue 3/12/24	Fri 14/2/25	
119	CSD submisison & approval	30 days	Mon 17/2/25	Sat 22/3/25	205SS-14 days
120	**Level 2 (PC & NH)**	**91 days**	**Fri 7/2/25**	**Wed 28/5/25**	
121	M&E shopdrawing submission & approval	60 days	Fri 7/2/25	Sat 19/4/25	
122	CSD submisison & approval	30 days	Tue 22/4/25	Wed 28/5/25	206SS-14 days
123	**Level 3 (PC & NH)**	**103 days**	**Tue 18/3/25**	**Mon 21/7/25**	
124	M&E shopdrawing submission & approval	60 days	Tue 18/3/25	Fri 30/5/25	
125	CSD submisison & approval	30 days	Tue 17/6/25	Mon 21/7/25	207SS-14 days
126	**Level 4 (PC Roof & NH)**	**103 days**	**Thu 24/4/25**	**Tue 26/8/25**	
127	M&E shopdrawing submission & approval	60 days	Thu 24/4/25	Sat 5/7/25	
128	CSD submisison & approval	30 days	Tue 22/7/25	Tue 26/8/25	208SS-14 days
129	**Level 5 (NH)**	**102 days**	**Mon 2/6/25**	**Tue 30/9/25**	
130	M&E shopdrawing submission & approval	60 days	Mon 2/6/25	Tue 12/8/25	
131	CSD submisison & approval	30 days	Wed 27/8/25	Tue 30/9/25	209SS-14 days
132	**Level 6 (NH)**	**103 days**	**Mon 7/7/25**	**Wed 5/11/25**	
133	M&E shopdrawing submission & approval	60 days	Mon 7/7/25	Mon 15/9/25	
134	CSD submisison & approval	30 days	Wed 1/10/25	Wed 5/11/25	210SS-14 days
135	**Lvel 7 (NH)**	**101 days**	**Thu 14/8/25**	**Wed 10/12/25**	
136	M&E shopdrawing submission & approval	60 days	Thu 14/8/25	Thu 23/10/25	
137	CSD submisison & approval	30 days	Thu 6/11/25	Wed 10/12/25	211SS-14 days
138	**Level 8 (NH)**	**102 days**	**Wed 17/9/25**	**Fri 16/1/26**	
139	M&E shopdrawing submission & approval	60 days	Wed 17/9/25	Wed 26/11/25	
140	CSD submisison & approval	30 days	Thu 11/12/25	Fri 16/1/26	212SS-14 days
141	**Level 9 (NH)**	**98 days**	**Tue 28/10/25**	**Mon 23/2/26**	
142	M&E shopdrawing submission & approval	60 days	Tue 28/10/25	Wed 7/1/26	
143	CSD submisison & approval	30 days	Sat 17/1/26	Mon 23/2/26	213SS-14 days
144	**Lower Roof (NH)**	**101 days**	**Fri 28/11/25**	**Tue 31/3/26**	
145	M&E shopdrawing submission & approval	60 days	Fri 28/11/25	Sat 7/2/26	
146	CSD submisison & approval	30 days	Tue 24/2/26	Tue 31/3/26	214SS-14 days
147	**External Works**	**131 days**	**Fri 28/11/25**	**Thu 7/5/26**	
148	M&E shopdrawing submission & approval	60 days	Fri 28/11/25	Sat 7/2/26	
149	CSD submisison & approval	30 days	Wed 1/4/26	Thu 7/5/26	215SS-14 days
150					
151	**Project Duration (30 Months)**	**757 days**	**Thu 8/8/24**	**Sun 7/2/27**	
152	Project commencement date	1 day	Thu 8/8/24	Thu 8/8/24	3FS+30 days
153	Permit to commence works (BCA) - Piling	8 days	Wed 14/8/24	Thu 22/8/24	152FS+3 days
154	**Overall piling schedule**	**160 days**	**Thu 8/8/24**	**Sat 15/2/25**	
155	**Ultimate load tests**	**36 days**	**Thu 8/8/24**	**Thu 19/9/24**	
156	ULT 1 (Dia 1000mm)	12 days	Thu 8/8/24	Thu 22/8/24	
157	**ULT 2 (Dia 1000mm)**	**26 days**	**Tue 13/8/24**	**Wed 11/9/24**	
158	Boring and casting test pile	1 day	Tue 13/8/24	Tue 13/8/24	
159	Boring and casting of additional 6 support piles to Kentledge base system	3 days	Thu 29/8/24	Sat 31/8/24	
160	Test block stacking	5 days	Mon 2/9/24	Fri 6/9/24	159
161	Loading Cycle	4 days	Sat 7/9/24	Wed 11/9/24	
162	**ULT 3 (Dia 1000mm)**	**16 days**	**Mon 2/9/24**	**Thu 19/9/24**	

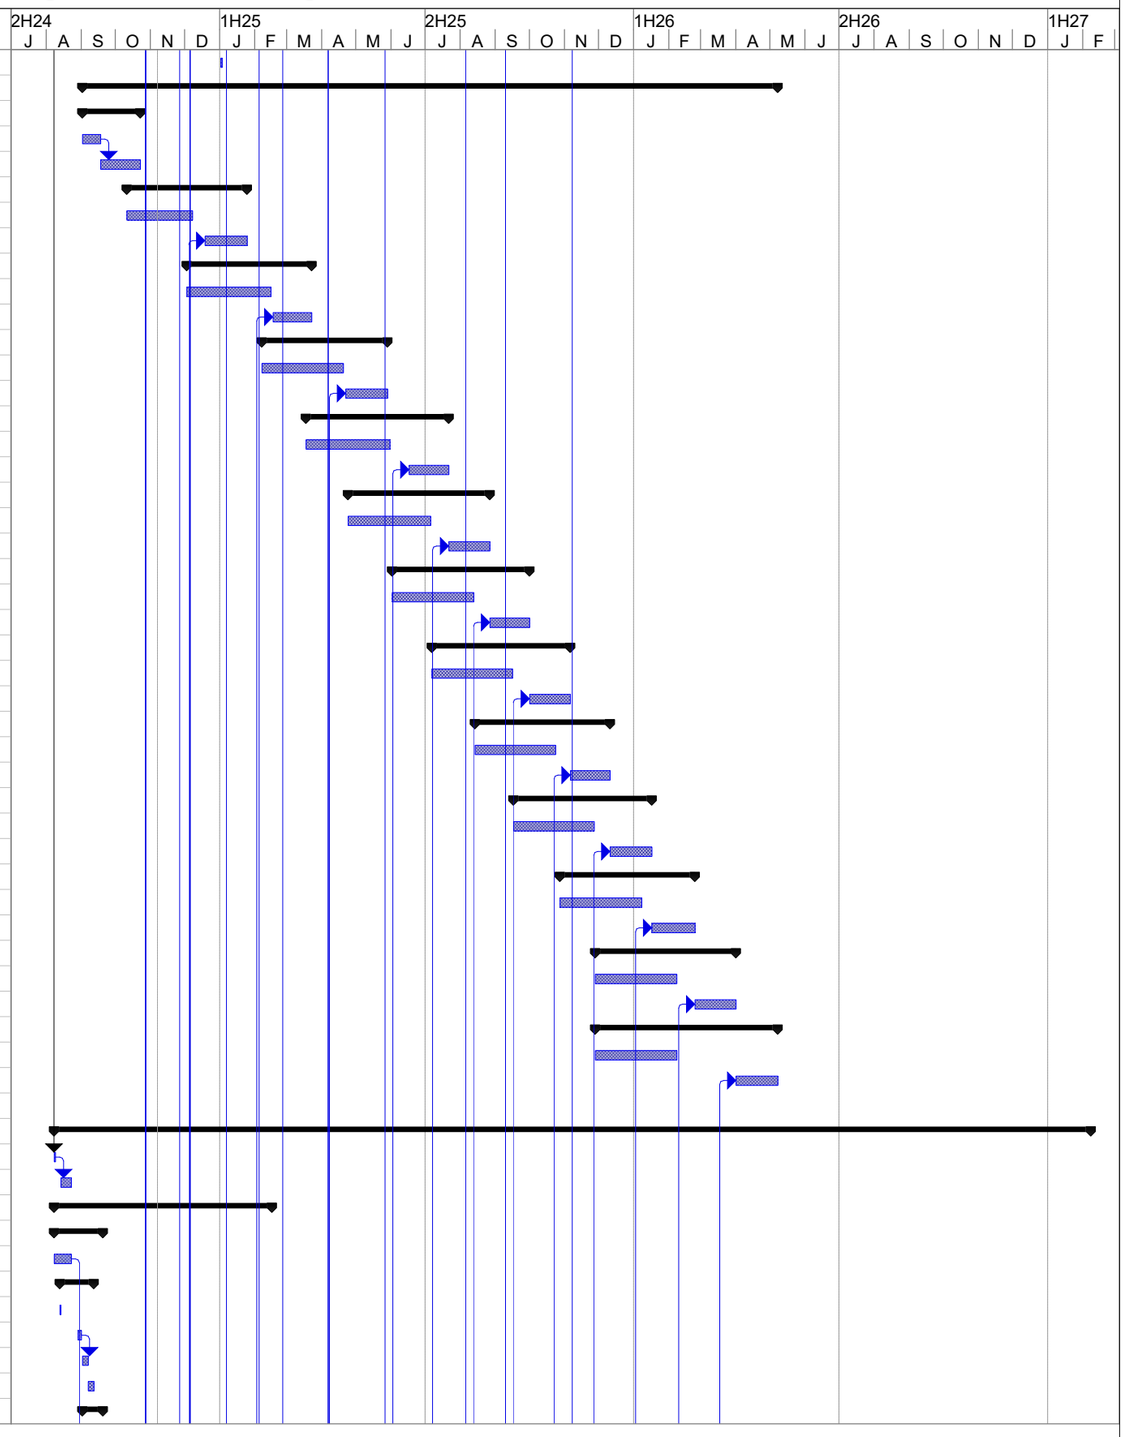


Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	

Kwan Yong Construction Pte Ltd **Master Programme For Co-Located Polyclinic & Nursing Home At 200 Jurong East Ave 1**

ID	Task Name	Duration	Start	Finish	Predecessors
163	Boring and casting test pile	1 day	Mon 2/9/24	Mon 2/9/24	
164	Boring and casting of additional 6 support piles to Kentledge base system	3 days	Wed 4/9/24	Fri 6/9/24	
165	Test block stacking	4 days	Wed 11/9/24	Sat 14/9/24	
166	Loading Cycle	4 days	Mon 16/9/24	Thu 19/9/24	165
167	**Working piles (3 rigs@3piles/2 days/rig)**	**108 days**	**Mon 26/8/24**	**Mon 30/12/24**	
168	**Bored piles - 484(Nos)**	**108 days**	**Mon 26/8/24**	**Mon 30/12/24**	
169	Part 1 - GL I-RW/RW to 8 (Zone 2, 3, 5 & 6) - 137 Nos)	50 days	Mon 26/8/24	Tue 22/10/24	156FS+2 days
170	Part 2 - GL PE-RW/RW-8 (Zone 6, 8, 9 & 10 - 110 Nos)	45 days	Wed 4/9/24	Fri 25/10/24	220SS
171	Part 3 - GL RW-PD/RW-9 (Zone 7, 8 & 9 - 97 Nos)	35 days	Wed 23/10/24	Mon 2/12/24	169
172	Part 4 - GL RW-H/RW-20 (Zone 1, 2, 4 & 5 - 140 Nos.)	55 days	Sat 26/10/24	Mon 30/12/24	170
173	**Working load tests**	**70 days**	**Wed 23/10/24**	**Tue 14/1/25**	
174	WLT 1 (Dia.1000mm)	12 days	Wed 23/10/24	Wed 6/11/24	169
175	WLT 2 (Dia 1000mm)	12 days	Sat 26/10/24	Sat 9/11/24	170
176	WLT 3 (Dia 1000mm)	12 days	Tue 3/12/24	Mon 16/12/24	171
177	WLT 4 (Dia 800mm)	12 days	Tue 17/12/24	Tue 31/12/24	176
178	WLT 5 (Dia 1000mm)	12 days	Tue 31/12/24	Tue 14/1/25	172
179	PDA Tests (10 Nos)	87 days	Sat 26/10/24	Sat 8/2/25	
180	Submission of test reports	157 days	Tue 13/8/24	Sat 15/2/25	
181					
182	**Main Building**	**757 days**	**Thu 8/8/24**	**Sun 7/2/27**	
183	**Structure Works**	**661 days**	**Mon 26/8/24**	**Thu 29/10/26**	
184	**Part 1 - GL I-RW/RW to 8 (Zone 2, 3, 5 & 6)**	**601 days**	**Mon 26/8/24**	**Thu 20/8/26**	
185	**Piling**	**81 days**	**Mon 26/8/24**	**Thu 28/11/24**	
186	Working piles (137 Nos)	50 days	Mon 26/8/24	Tue 22/10/24	169SS
187	**Working load tests**	**31 days**	**Wed 23/10/24**	**Thu 28/11/24**	
188	WLT 1 (Dia.1000mm)	12 days	Wed 23/10/24	Wed 6/11/24	186
189	PDA Tests (3 Nos)	10 days	Fri 1/11/24	Tue 12/11/24	
190	Submission of test reports	19 days	Thu 7/11/24	Thu 28/11/24	188
191	**Substructure**	**98 days**	**Thu 7/11/24**	**Tue 4/3/25**	
192	**ERSS pilecaps & basement**	**98 days**	**Thu 7/11/24**	**Tue 4/3/25**	**188**
193	Installation of Tangent pile & capping beam	21 days	Thu 7/11/24	Sat 30/11/24	
194	Sheet pile installation + excavation (incl. waterstorm water tank)	10 days	Sat 23/11/24	Tue 3/12/24	193SS+14 days
195	Excavation to pilecap level	10 days	Mon 16/12/24	Fri 27/12/24	196
196	Construct stormwork tank	10 days	Wed 4/12/24	Sat 14/12/24	194
197	Pilecap construction	10 days	Tue 24/12/24	Mon 6/1/25	195SS+7 days
198	Slab construction	10 days	Tue 7/1/25	Fri 17/1/25	197
199	Installation of raking strut	14 days	Sat 18/1/25	Wed 5/2/25	198
200	Excavation to the soil berm	14 days	Sat 1/2/25	Mon 17/2/25	199SS+10 days
201	Pilecap construction (Soil Berm Location)	14 days	Mon 10/2/25	Tue 25/2/25	200SS+7 days
202	Slab Construction (Soil Berm Location)	10 days	Fri 21/2/25	Tue 4/3/25	201SS+10 days
203	Installation of Sanitary ICs, Sanitary Piping, & Waste Sumps	90 days	Thu 7/11/24	Sat 22/2/25	
204	**Superstructure**	**441 days**	**Wed 5/3/25**	**Thu 20/8/26**	
205	1st storey	53 days	Wed 5/3/25	Thu 8/5/25	192
206	2nd storey	45 days	Fri 9/5/25	Wed 2/7/25	205
207	3rd storey	30 days	Thu 3/7/25	Wed 6/8/25	206
208	4th storey	30 days	Thu 7/8/25	Thu 11/9/25	207
209	5th storey	30 days	Fri 12/9/25	Thu 16/10/25	208
210	6th storey	30 days	Fri 17/10/25	Fri 21/11/25	209
211	7th storey	30 days	Sat 22/11/25	Sat 27/12/25	210
212	8th storey	30 days	Mon 29/12/25	Mon 2/2/26	211
213	9th storey	30 days	Tue 3/2/26	Wed 11/3/26	212
214	Lower Roof	30 days	Thu 12/3/26	Fri 17/4/26	213
215	Upper Roof	15 days	Sat 18/4/26	Wed 6/5/26	214
216	Parapet walls/Metal trellis	45 days	Mon 27/4/26	Sat 20/6/26	214FS+7 days

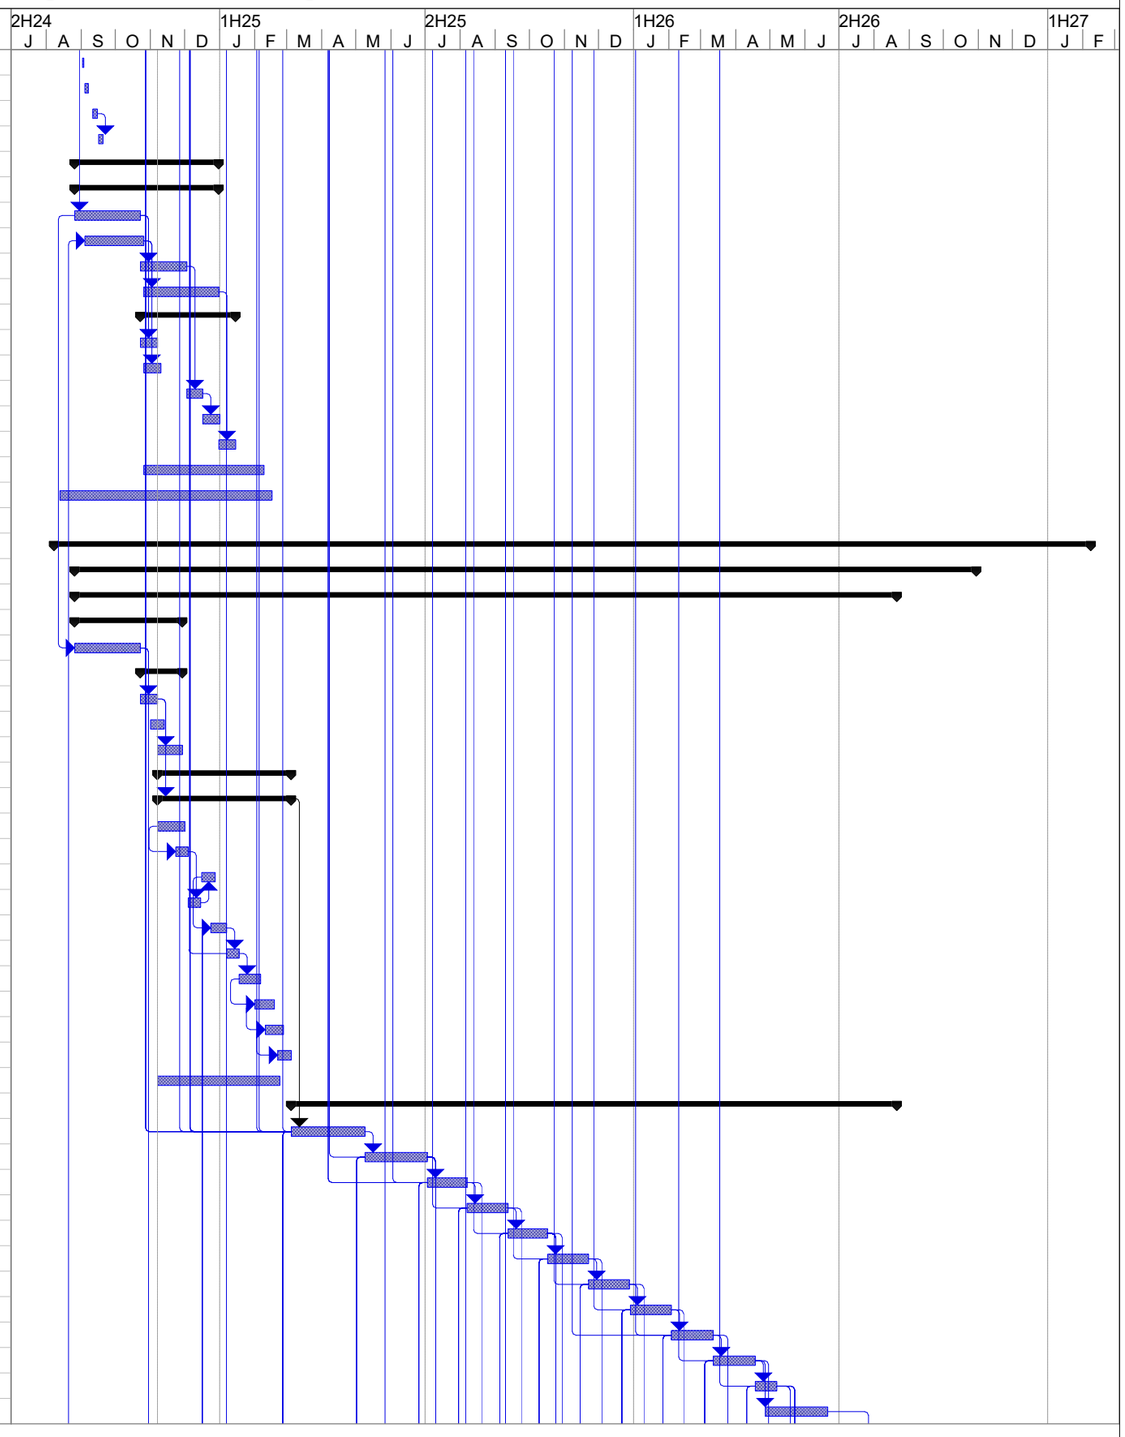


Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Progress | Deadline

Kwan Yong Construction Pte Ltd — **Master Programme For Co-Located Polyclinic & Nursing Home At 200 Jurong East Ave 1**


ID	Task Name	Duration	Start	Finish	Predecessors
217	Construction of TC 1 basement slab	14 days	Tue 4/8/26	Thu 20/8/26	304
218	**Part 2 - GL PE-RW/RW-8 (Zone 6, 8, 9 & 10)**	**477 days**	**Wed 4/9/24**	**Wed 1/4/26**	
219	**Piling**	**94 days**	**Wed 4/9/24**	**Sat 21/12/24**	
220	Working piles (110 Nos)	45 days	Wed 4/9/24	Fri 25/10/24	
221	**Working load tests**	**49 days**	**Sat 26/10/24**	**Sat 21/12/24**	
222	WLT 2 (Dia.1000mm)	12 days	Sat 26/10/24	Sat 9/11/24	220
223	PDA Tests (2 Nos)	7 days	Mon 9/12/24	Mon 16/12/24	
224	Submission of test reports	40 days	Thu 7/11/24	Sat 21/12/24	
225	**Substructure**	**90 days**	**Mon 11/11/24**	**Wed 26/2/25**	
226	**ERSS plecaps & basement**	**90 days**	**Mon 11/11/24**	**Wed 26/2/25**	**222**
227	Installation of Tangent pile & capping beam	25 days	Mon 11/11/24	Sat 7/12/24	
228	Excavation to pilecap level	16 days	Mon 9/12/24	Fri 27/12/24	227
229	Sheet pile installation	14 days	Sat 28/12/24	Tue 14/1/25	228
230	Pilecap construction	21 days	Wed 15/1/25	Mon 10/2/25	229
231	Slab construction	14 days	Tue 11/2/25	Wed 26/2/25	230
232	Installation of Sanitary ICs, Sanitary Piping, & Waste Sumps	90 days	Mon 11/11/24	Wed 26/2/25	226SS
233	**Superstructure**	**330 days**	**Thu 27/2/25**	**Wed 1/4/26**	
234	1st storey	60 days	Thu 27/2/25	Sat 10/5/25	232
235	2nd storey	60 days	Tue 13/5/25	Tue 22/7/25	234
236	3rd storey	60 days	Wed 23/7/25	Wed 1/10/25	235
237	Lower Roof	60 days	Thu 2/10/25	Thu 11/12/25	236
238	Upper roof	30 days	Fri 12/12/25	Sat 17/1/26	237
239	Parapet walls/Metal trellis	60 days	Mon 19/1/26	Wed 1/4/26	238
240	**Part 3 - GL RW-PD/RW-9 (Zone 7, 8 & 9)**	**592 days**	**Wed 23/10/24**	**Wed 7/10/26**	
241	**Piling**	**81 days**	**Wed 23/10/24**	**Mon 27/1/25**	
242	Working piles (97 Nos)	35 days	Wed 23/10/24	Mon 2/12/24	186
243	**Working load tests**	**46 days**	**Tue 3/12/24**	**Mon 27/1/25**	
244	WLT 3 (Dia 1000mm)	12 days	Tue 3/12/24	Mon 16/12/24	242
245	WLT 4 (Dia 800mm)	12 days	Tue 17/12/24	Tue 31/12/24	244
246	PDA Tests (2 Nos)	7 days	Mon 13/1/25	Mon 20/1/25	
247	Submission of test reports	43 days	Fri 6/12/24	Mon 27/1/25	
248	**Substructure**	**90 days**	**Sat 14/12/24**	**Thu 3/4/25**	
249	**ERSS plecaps & basement**	**90 days**	**Sat 14/12/24**	**Thu 3/4/25**	
250	Installation of Tangent pile & capping beam	21 days	Sat 14/12/24	Thu 9/1/25	
251	Excavation to pilecap level	14 days	Thu 2/1/25	Fri 17/1/25	250SS+14 days
252	Sheet pile installation	14 days	Sat 18/1/25	Wed 5/2/25	251
253	Pilecap construction	18 days	Fri 10/1/25	Sat 1/2/25	251SS+7 days
254	Slab construction	12 days	Mon 3/2/25	Sat 15/2/25	253
255	Installation of raking strut	14 days	Mon 17/2/25	Tue 4/3/25	254
256	Excavation to the soil berm	14 days	Fri 28/2/25	Sat 15/3/25	255SS+10 days
257	Pilecap construction (Soil Berm Location)	14 days	Sat 8/3/25	Mon 24/3/25	256SS+7 days
258	Slab Construction (Soil Berm Location)	12 days	Thu 20/3/25	Thu 3/4/25	257SS+10 days
259	Installation of Sanitary ICs, Sanitary Piping, & Waste Sumps	60 days	Fri 10/1/25	Sat 22/3/25	253SS
260	**Superstructure**	**457 days**	**Fri 4/4/25**	**Wed 7/10/26**	
261	1st storey	60 days	Fri 4/4/25	Tue 17/6/25	258
262	2nd storey	60 days	Wed 18/6/25	Wed 27/8/25	261
263	3rd storey	60 days	Thu 28/8/25	Thu 6/11/25	262
264	Lower Roof	60 days	Fri 7/11/25	Sat 17/1/26	263
265	Upper roof	30 days	Mon 19/1/26	Tue 24/2/26	264
266	Parapet walls/Metal trellis	60 days	Wed 25/2/26	Fri 8/5/26	265
267	Casting of TC2 slab opening casting	30 days	Wed 24/6/26	Tue 28/7/26	306
268	CIS staircase (L1 to L2)	30 days	Wed 29/7/26	Wed 2/9/26	267
269	CIS staircase (L2 to L3)	30 days	Thu 3/9/26	Wed 7/10/26	268
270	**Part 4 - GL RW-H/RW-20 (Zone 1, 2, 4 & 5)**	**608 days**	**Sat 26/10/24**	**Thu 29/10/26**	

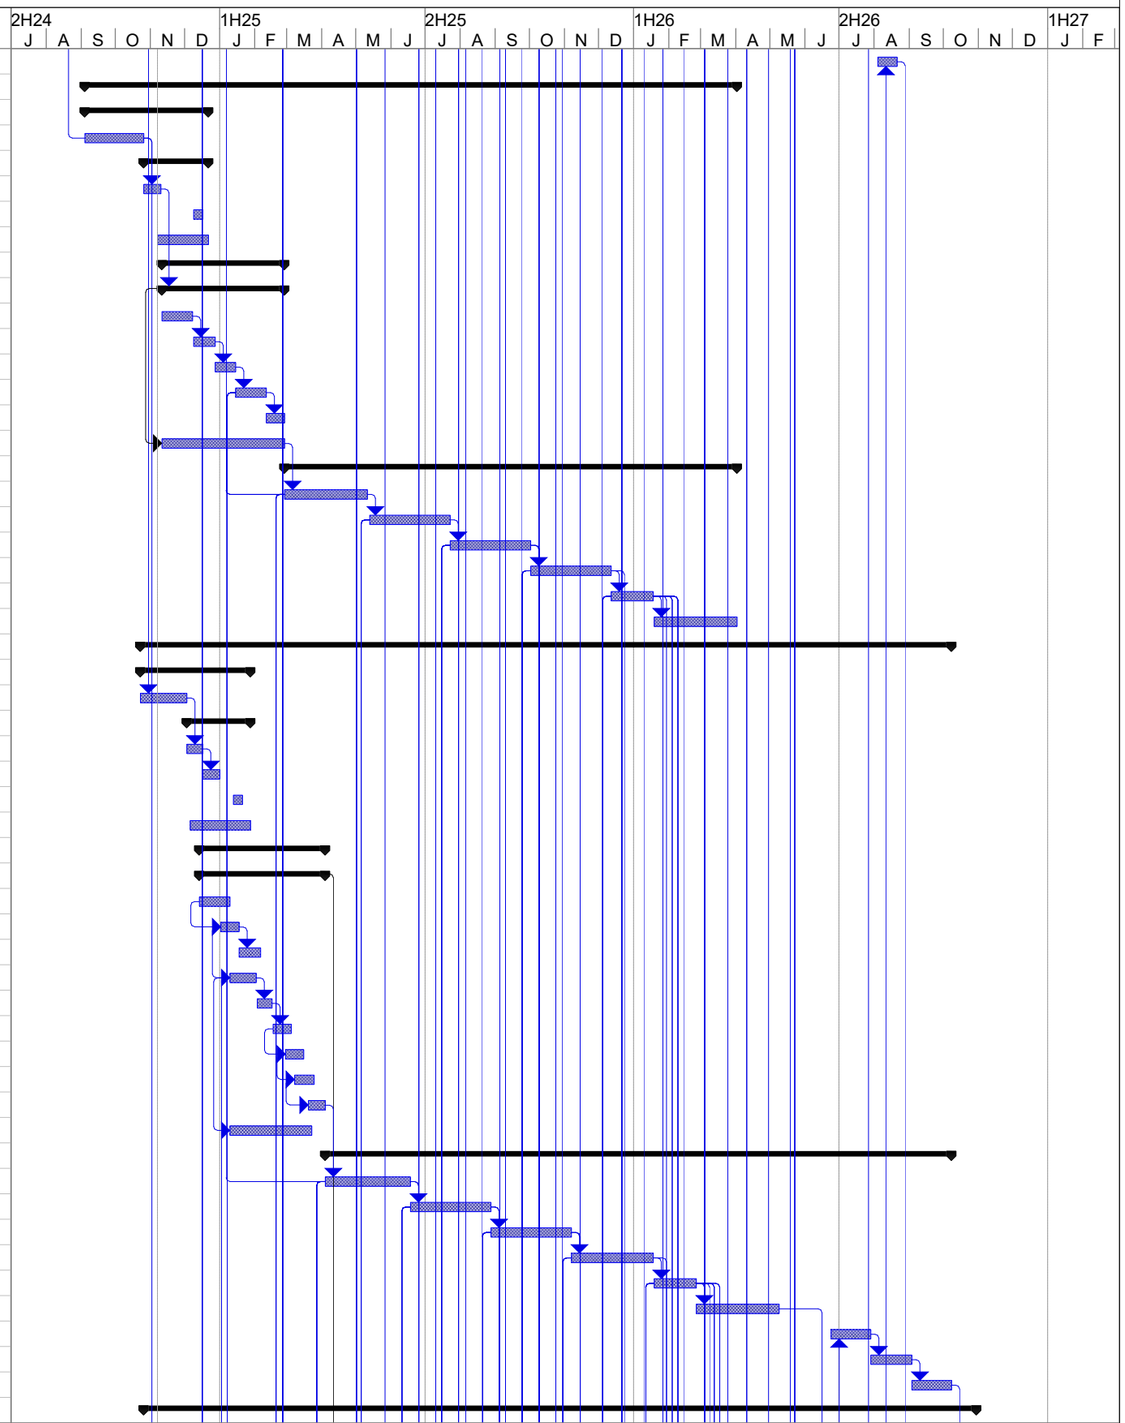

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	


ID	Task Name	Duration	Start	Finish	Predecessors
271	**Piling**	**103 days**	**Sat 26/10/24**	**Thu 27/2/25**	
272	Working piles (140 Nos)	55 days	Sat 26/10/24	Mon 30/12/24	220
273	**Working load tests**	**48 days**	**Tue 31/12/24**	**Thu 27/2/25**	
274	WLT 5 (Dia.1000mm)	12 days	Tue 31/12/24	Tue 14/1/25	272
275	PDA Tests (3 Nos)	10 days	Mon 10/2/25	Thu 20/2/25	
276	Submission of test reports	43 days	Tue 7/1/25	Thu 27/2/25	
277	**Substructure**	**90 days**	**Wed 15/1/25**	**Mon 5/5/25**	
278	**ERSS plecaps & basement**	**90 days**	**Wed 15/1/25**	**Mon 5/5/25**	**274**
279	Installation of Tangent pile & capping beam	21 days	Wed 15/1/25	Mon 10/2/25	
280	Excavation to pilecap level	21 days	Mon 3/2/25	Wed 26/2/25	279SS+14 days
281	Sheet pile installation	14 days	Thu 27/2/25	Fri 14/3/25	280
282	Pilecap construction	18 days	Tue 11/2/25	Mon 3/3/25	280SS+7 days
283	Slab construction	12 days	Tue 4/3/25	Mon 17/3/25	282
284	Installation of raking strut	14 days	Tue 18/3/25	Thu 3/4/25	283
285	Excavation to the soil berm	14 days	Sat 29/3/25	Tue 15/4/25	284SS+10 days
286	Pilecap construction (Soil Berm Location)	14 days	Tue 8/4/25	Thu 24/4/25	285SS+7 days
287	Slab Construction (Soil Berm Location)	12 days	Mon 21/4/25	Mon 5/5/25	286SS+10 days
288	Installation of Sanitary ICs, Sanitary Piping, & Waste Sumps	90 days	Wed 15/1/25	Mon 5/5/25	
289	**Superstructure**	**451 days**	**Tue 6/5/25**	**Thu 29/10/26**	
290	1st storey	60 days	Tue 6/5/25	Wed 16/7/25	288
291	2nd storey	46 days	Thu 17/7/25	Tue 9/9/25	290
292	3rd storey	30 days	Wed 10/9/25	Tue 14/10/25	291
293	4th storey	30 days	Wed 15/10/25	Wed 19/11/25	292
294	5th storey	30 days	Thu 20/11/25	Wed 24/12/25	293
295	6th storey	30 days	Fri 26/12/25	Fri 30/1/26	294
296	7th storey	30 days	Sat 31/1/26	Mon 9/3/26	295
297	8th storey	30 days	Tue 10/3/26	Wed 15/4/26	296
298	9th storey	30 days	Thu 16/4/26	Thu 21/5/26	297
299	Lower Roof	25 days	Fri 22/5/26	Mon 22/6/26	298
300	Upper roof	15 days	Tue 23/6/26	Thu 9/7/26	299
301	Parapet walls/Metal trellis	45 days	Thu 9/7/26	Mon 31/8/26	299FS+14 days
302	Construction of TC 3 basement slab	14 days	Wed 14/10/26	Thu 29/10/26	305
303	**Tower Crane Dismantling**	**102 days**	**Tue 16/6/26**	**Tue 13/10/26**	
304	TC 1	7 days	Mon 27/7/26	Mon 3/8/26	216FS+30 days
305	TC 3	7 days	Tue 6/10/26	Tue 13/10/26	301FS+30 days
306	TC 2	7 days	Tue 16/6/26	Tue 23/6/26	266FS+30 days
307					
308	**Precast Submission/Fabrication/Delivery**	**463 days**	**Tue 1/10/24**	**Mon 13/4/26**	
309	**Shopdrwgs submission & approval (Progressively submission)**	**160 days**	**Tue 1/10/24**	**Thu 10/4/25**	
310	APCS - Column Shoes Shopdrawing Submission & Approval	120 days	Tue 1/10/24	Fri 21/2/25	
311	APCS - Beam Connection Shopdrawing Submission & Approvcal	120 days	Wed 6/11/24	Fri 28/3/25	310SS+30 days
312	Precast HCS, Large Panel, Wall, Façade and etc	100 days	Tue 10/12/24	Thu 10/4/25	311SS+30 days
313	Mould fabrications (Progressively)	120 days	Tue 10/12/24	Tue 6/5/25	310SS+60 days
314	Offsite castings (Progressively)	365 days	Thu 16/1/25	Thu 2/4/26	313SS+30 days
315	Deliveries to site	293 days	Thu 24/4/25	Mon 13/4/26	
316	**Architecture/ID Works**	**386 days**	**Wed 20/8/25**	**Thu 26/11/26**	
317	**Part 1 - GL I-RW/RW to 8**	**375 days**	**Wed 20/8/25**	**Fri 13/11/26**	
318	**Basement**	**197 days**	**Wed 20/8/25**	**Tue 14/4/26**	
319	PC/PF/Drywalls, etc.	21 days	Wed 20/8/25	Fri 12/9/25	207FS+10 days
320	Doors	14 days	Sat 13/9/25	Mon 29/9/25	319
321	Wall plastering & skimming	30 days	Thu 16/10/25	Thu 20/11/25	322
322	Waterproofing works	14 days	Tue 30/9/25	Wed 15/10/25	320
323	Wall & floor finishes	30 days	Thu 16/10/25	Thu 20/11/25	322
324	Ceiling	30 days	Mon 2/2/26	Tue 10/3/26	321FS+60 days

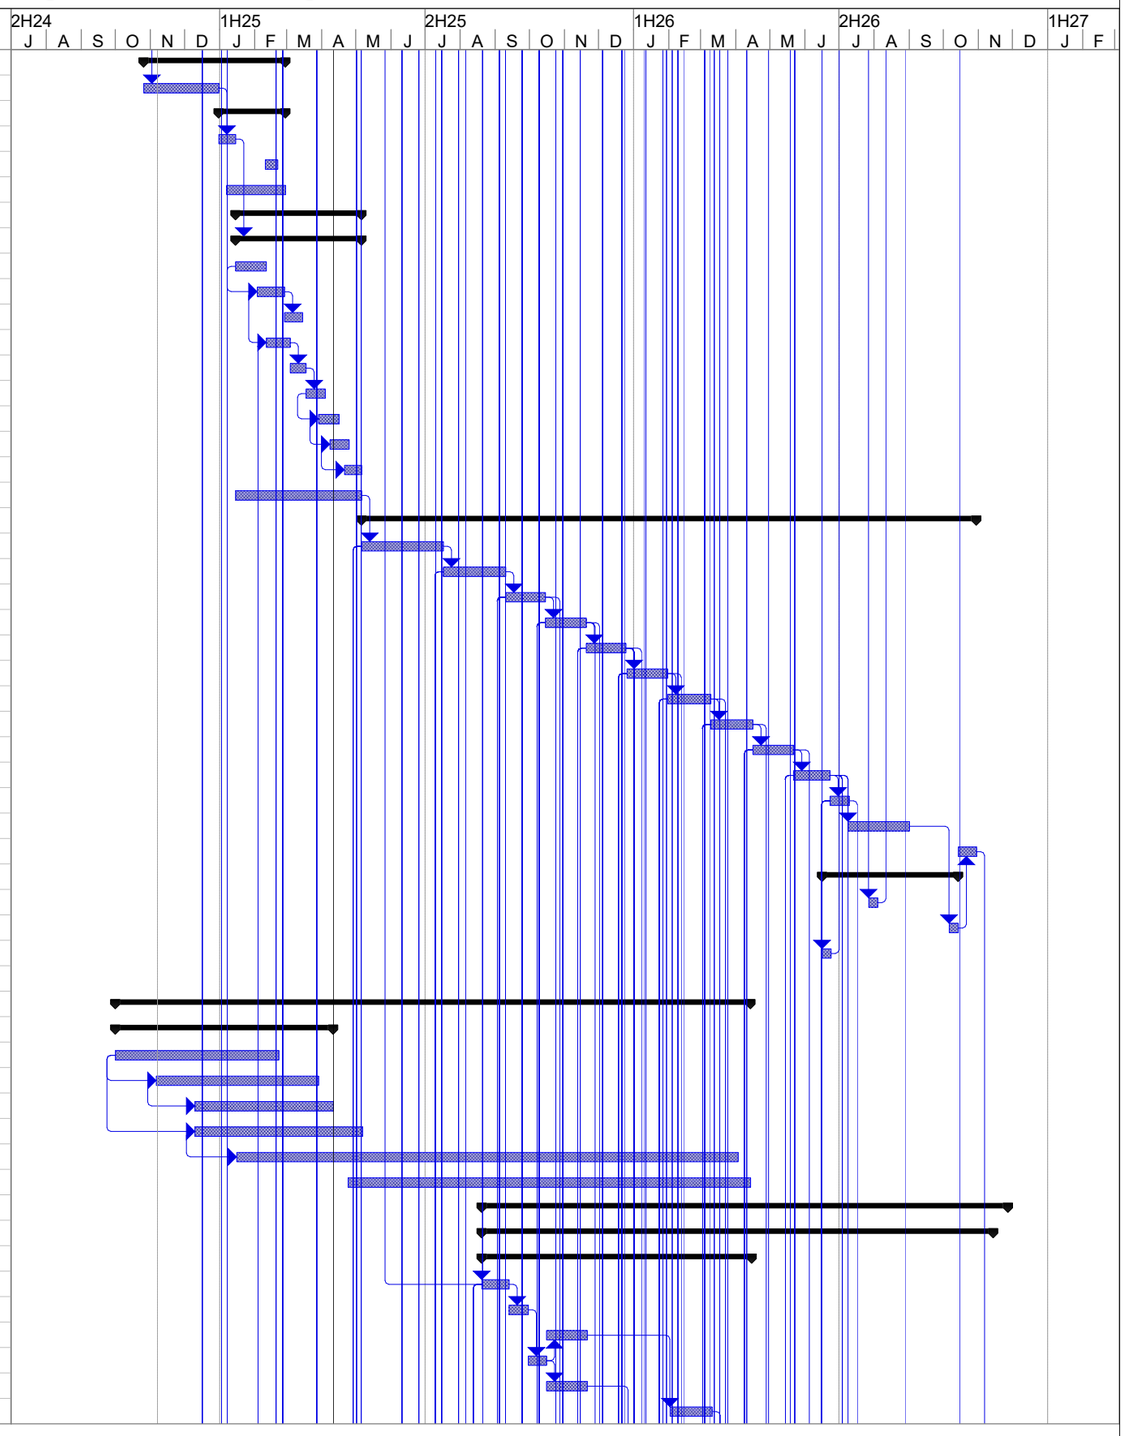

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	


ID	Task Name	Duration	Start	Finish	Predecessors
325	Internal Painting	14 days	Wed 11/3/26	Fri 27/3/26	324
326	Plants & landscape	14 days	Sat 27/12/25	Tue 13/1/26	323FS+30 days
327	Signage	14 days	Sat 28/3/26	Tue 14/4/26	325
328	**Level 1**	**139 days**	**Wed 24/9/25**	**Tue 10/3/26**	
329	PC/PF/Drywalls, etc.	21 days	Wed 24/9/25	Fri 17/10/25	208FS+10 days
330	Doors & windows	14 days	Thu 2/10/25	Fri 17/10/25	329SS+7 days
331	Internal plastering & skimming	30 days	Wed 5/11/25	Tue 9/12/25	333
332	Railings, metalworks etc.	21 days	Wed 10/12/25	Mon 5/1/26	334
333	Waterproofing works	14 days	Sat 18/10/25	Tue 4/11/25	330
334	Wall & floor finishes including lead line to X-Ray Room	30 days	Wed 5/11/25	Tue 9/12/25	333
335	Ceiling	30 days	Wed 10/12/25	Thu 15/1/26	331
336	Internal painting	14 days	Fri 16/1/26	Sat 31/1/26	335
337	Furniture & fitments	30 days	Wed 10/12/25	Thu 15/1/26	334
338	External plastering & Skimming	30 days	Wed 10/12/25	Thu 15/1/26	331
339	External painting	30 days	Fri 16/1/26	Sat 21/2/26	338
340	Plants & landscape	14 days	Mon 23/2/26	Tue 10/3/26	339
341	Signage	14 days	Mon 2/2/26	Thu 19/2/26	337FS+14 days
342	**Level 2**	**125 days**	**Thu 30/10/25**	**Mon 30/3/26**	
343	PC/PF/Drywalls, etc.	21 days	Thu 30/10/25	Sat 22/11/25	209FS+10 days
344	Doors & windows	14 days	Fri 7/11/25	Sat 22/11/25	343SS+7 days
345	Internal plastering & skimming	30 days	Mon 24/11/25	Mon 29/12/25	347SS+7 days
346	Railings, metalworks etc.	21 days	Thu 8/1/26	Sat 31/1/26	348
347	Waterproofing works	14 days	Sat 15/11/25	Mon 1/12/25	344SS+7 days
348	Wall & floor finishes	30 days	Tue 2/12/25	Wed 7/1/26	347
349	Ceiling	30 days	Tue 30/12/25	Tue 3/2/26	345
350	Internal painting	14 days	Wed 4/2/26	Sat 21/2/26	349
351	Furniture & fitments	30 days	Thu 8/1/26	Wed 11/2/26	348
352	External plastering & skimming	30 days	Tue 30/12/25	Tue 3/2/26	345
353	External painting	30 days	Wed 4/2/26	Thu 12/3/26	352
354	Plants & landscape	14 days	Fri 13/3/26	Mon 30/3/26	353
355	Signage	14 days	Tue 3/3/26	Wed 18/3/26	351FS+14 days
356	**Level 3**	**125 days**	**Thu 4/12/25**	**Wed 6/5/26**	
357	PC/PF/Drywalls, etc.	21 days	Thu 4/12/25	Mon 29/12/25	210FS+10 days
358	Doors & windows	14 days	Fri 12/12/25	Mon 29/12/25	357SS+7 days
359	Internal plastering & skimming	30 days	Tue 30/12/25	Tue 3/2/26	361SS+7 days
360	Railings, metalworks, screen etc.	30 days	Thu 12/2/26	Sat 21/3/26	362
361	Waterproofing works	14 days	Sat 20/12/25	Wed 7/1/26	358SS+7 days
362	Wall & floor finishes	30 days	Thu 8/1/26	Wed 11/2/26	361
363	Ceiling	30 days	Wed 4/2/26	Thu 12/3/26	359
364	Curtain Track	14 days	Tue 31/3/26	Thu 16/4/26	365
365	Internal painting	14 days	Fri 13/3/26	Mon 30/3/26	363
366	Furniture & fitments	30 days	Thu 12/2/26	Sat 21/3/26	362
367	External plastering & skimming	30 days	Wed 4/2/26	Thu 12/3/26	359
368	External painting	30 days	Fri 13/3/26	Sat 18/4/26	367
369	Plants & landscape	14 days	Mon 20/4/26	Wed 6/5/26	368
370	Signage	14 days	Thu 9/4/26	Fri 24/4/26	366FS+14 days
371	**Level 4**	**125 days**	**Sat 10/1/26**	**Fri 12/6/26**	
372	PC/PF/Drywalls, etc.	21 days	Sat 10/1/26	Tue 3/2/26	211FS+10 days
373	Doors & windows	14 days	Mon 19/1/26	Tue 3/2/26	372SS+7 days
374	Internal plastering & skimming	30 days	Wed 4/2/26	Thu 12/3/26	376SS+7 days
375	Railings, metalworks, screen etc.	30 days	Mon 23/3/26	Mon 27/4/26	377
376	Waterproofing works	14 days	Tue 27/1/26	Wed 11/2/26	373SS+7 days
377	Wall & floor finishes	30 days	Thu 12/2/26	Sat 21/3/26	376
378	Ceiling	30 days	Fri 13/3/26	Sat 18/4/26	374

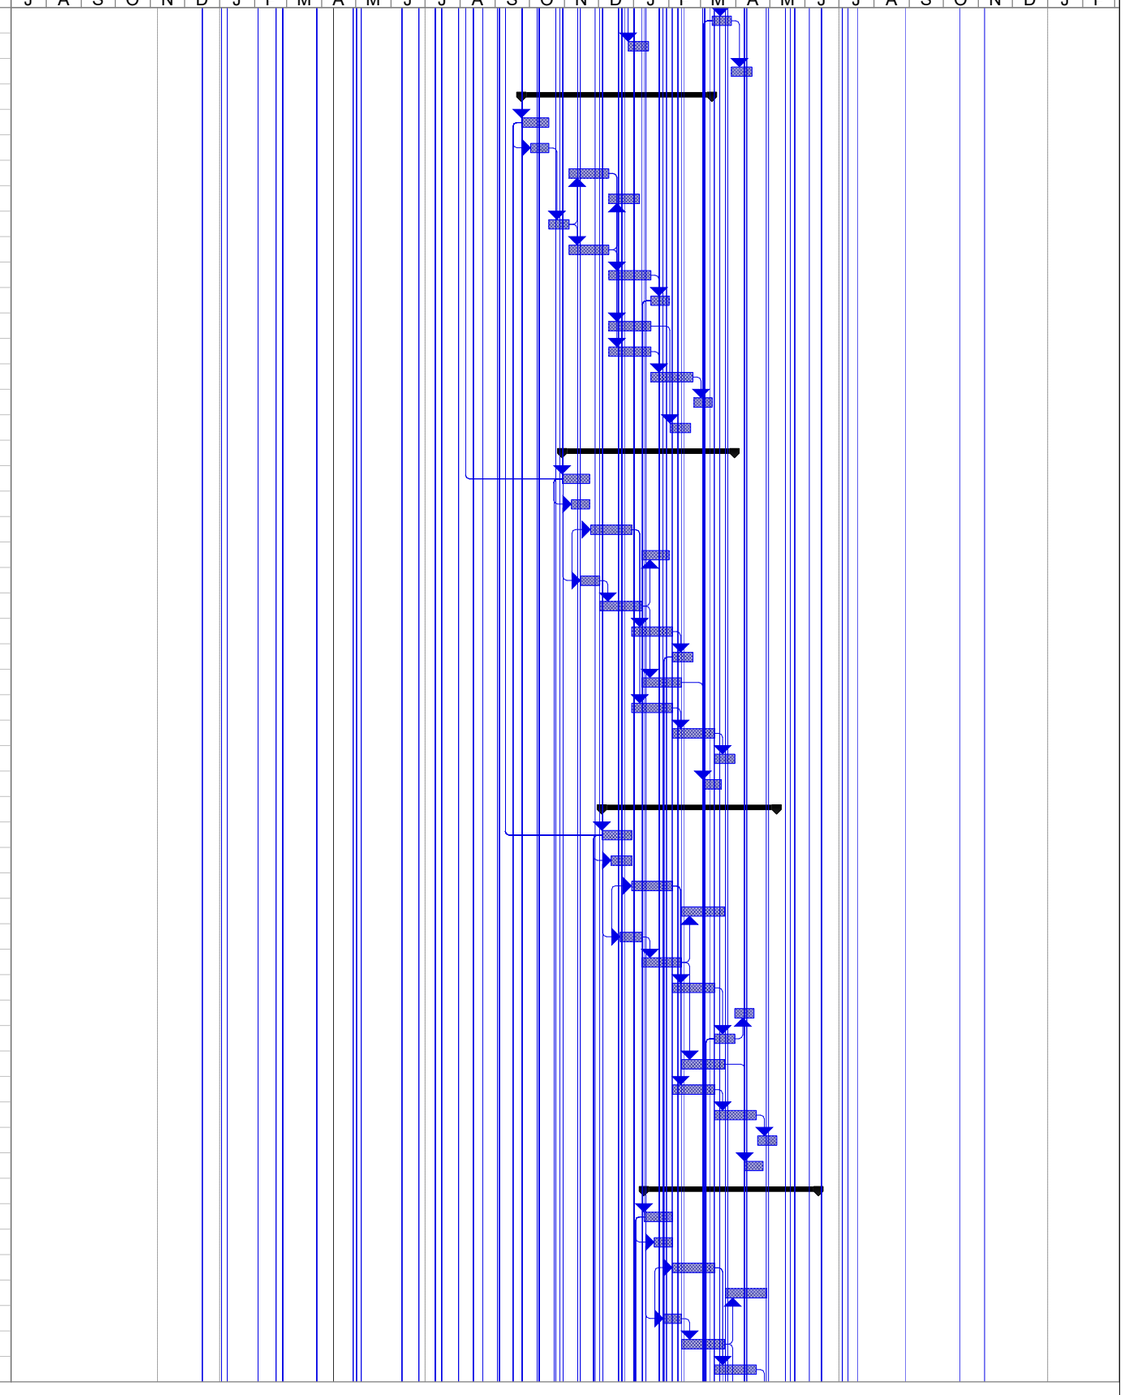

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	


ID	Task Name	Duration	Start	Finish	Predecessors
379	Curtain Track	30 days	Thu 7/5/26	Fri 12/6/26	380
380	Internal painting	14 days	Mon 20/4/26	Wed 6/5/26	378
381	Furniture & fitments	30 days	Mon 23/3/26	Mon 27/4/26	377
382	External plastering & skimming	30 days	Fri 13/3/26	Sat 18/4/26	374
383	External painting	30 days	Mon 20/4/26	Mon 25/5/26	382
384	Plants & landscape	14 days	Tue 26/5/26	Fri 12/6/26	383
385	Signage	14 days	Fri 15/5/26	Tue 2/6/26	381FS+14 days
386	**Level 5**	**125 days**	**Sat 14/2/26**	**Fri 17/7/26**	
387	PC/PF/Drywalls, etc.	21 days	Sat 14/2/26	Thu 12/3/26	212FS+10 days
388	Doors & windows	14 days	Wed 25/2/26	Thu 12/3/26	387SS+7 days
389	Internal plastering & skimming	30 days	Fri 13/3/26	Sat 18/4/26	391SS+7 days
390	Railings, metalworks, screen etc.	30 days	Tue 28/4/26	Thu 4/6/26	392
391	Waterproofing works	14 days	Thu 5/3/26	Sat 21/3/26	388SS+7 days
392	Wall & floor finishes	30 days	Mon 23/3/26	Mon 27/4/26	391
393	Ceiling	30 days	Mon 20/4/26	Mon 25/5/26	389
394	Curtain Track	14 days	Sat 13/6/26	Mon 29/6/26	395
395	Internal painting	14 days	Tue 26/5/26	Fri 12/6/26	393
396	Furniture & fitments	30 days	Tue 28/4/26	Thu 4/6/26	392
397	External plastering & skimming	30 days	Mon 20/4/26	Mon 25/5/26	389
398	External painting	30 days	Tue 26/5/26	Wed 1/7/26	397
399	Plants & landscape	14 days	Thu 2/7/26	Fri 17/7/26	398
400	Signage	14 days	Mon 22/6/26	Tue 7/7/26	396FS+14 days
401	**Level 6**	**125 days**	**Wed 25/3/26**	**Sat 22/8/26**	
402	PC/PF/Drywalls, etc.	21 days	Wed 25/3/26	Sat 18/4/26	213FS+10 days
403	Doors & windows	14 days	Thu 2/4/26	Sat 18/4/26	402SS+7 days
404	Internal plastering & skimming	30 days	Mon 20/4/26	Mon 25/5/26	406SS+7 days
405	Railings, metalworks, screen etc.	30 days	Fri 5/6/26	Thu 9/7/26	407
406	Waterproofing works	14 days	Sat 11/4/26	Mon 27/4/26	403SS+7 days
407	Wall & floor finishes	30 days	Tue 28/4/26	Thu 4/6/26	406
408	Ceiling	30 days	Tue 26/5/26	Wed 1/7/26	404
409	Curtain Track	14 days	Sat 18/7/26	Mon 3/8/26	410
410	Internal painting	14 days	Thu 2/7/26	Fri 17/7/26	408
411	Furniture & fitments	30 days	Fri 5/6/26	Thu 9/7/26	407
412	External plastering & skimming	30 days	Tue 26/5/26	Wed 1/7/26	404
413	External painting	30 days	Thu 2/7/26	Wed 5/8/26	412
414	Plants & landscape	14 days	Thu 6/8/26	Sat 22/8/26	413
415	Signage	14 days	Mon 27/7/26	Wed 12/8/26	411FS+14 days
416	**Level 7**	**125 days**	**Thu 30/4/26**	**Sat 26/9/26**	
417	PC/PF/Drywalls, etc.	21 days	Thu 30/4/26	Mon 25/5/26	214FS+10 days
418	Doors & windows	14 days	Sat 9/5/26	Mon 25/5/26	417SS+7 days
419	Internal plastering & skimming	30 days	Tue 26/5/26	Wed 1/7/26	421SS+7 days
420	Railings, metalworks etc.	30 days	Fri 10/7/26	Fri 14/8/26	422
421	Waterproofing works	14 days	Mon 18/5/26	Thu 4/6/26	418SS+7 days
422	Wall & floor finishes	30 days	Fri 5/6/26	Thu 9/7/26	421
423	Ceiling	30 days	Thu 2/7/26	Wed 5/8/26	419
424	Curtain Track	14 days	Mon 24/8/26	Tue 8/9/26	425
425	Internal painting	14 days	Thu 6/8/26	Sat 22/8/26	423
426	Furniture & fitments	30 days	Fri 10/7/26	Fri 14/8/26	422
427	External plastering & skimming	30 days	Thu 2/7/26	Wed 5/8/26	419
428	External painting	30 days	Thu 6/8/26	Thu 10/9/26	427
429	Plants & landscape	14 days	Fri 11/9/26	Sat 26/9/26	428
430	Signage	14 days	Tue 1/9/26	Wed 16/9/26	426FS+14 days
431	**Level 8**	**125 days**	**Tue 19/5/26**	**Wed 14/10/26**	
432	PC/PF/Drywalls, etc.	21 days	Tue 19/5/26	Sat 13/6/26	215FS+10 days

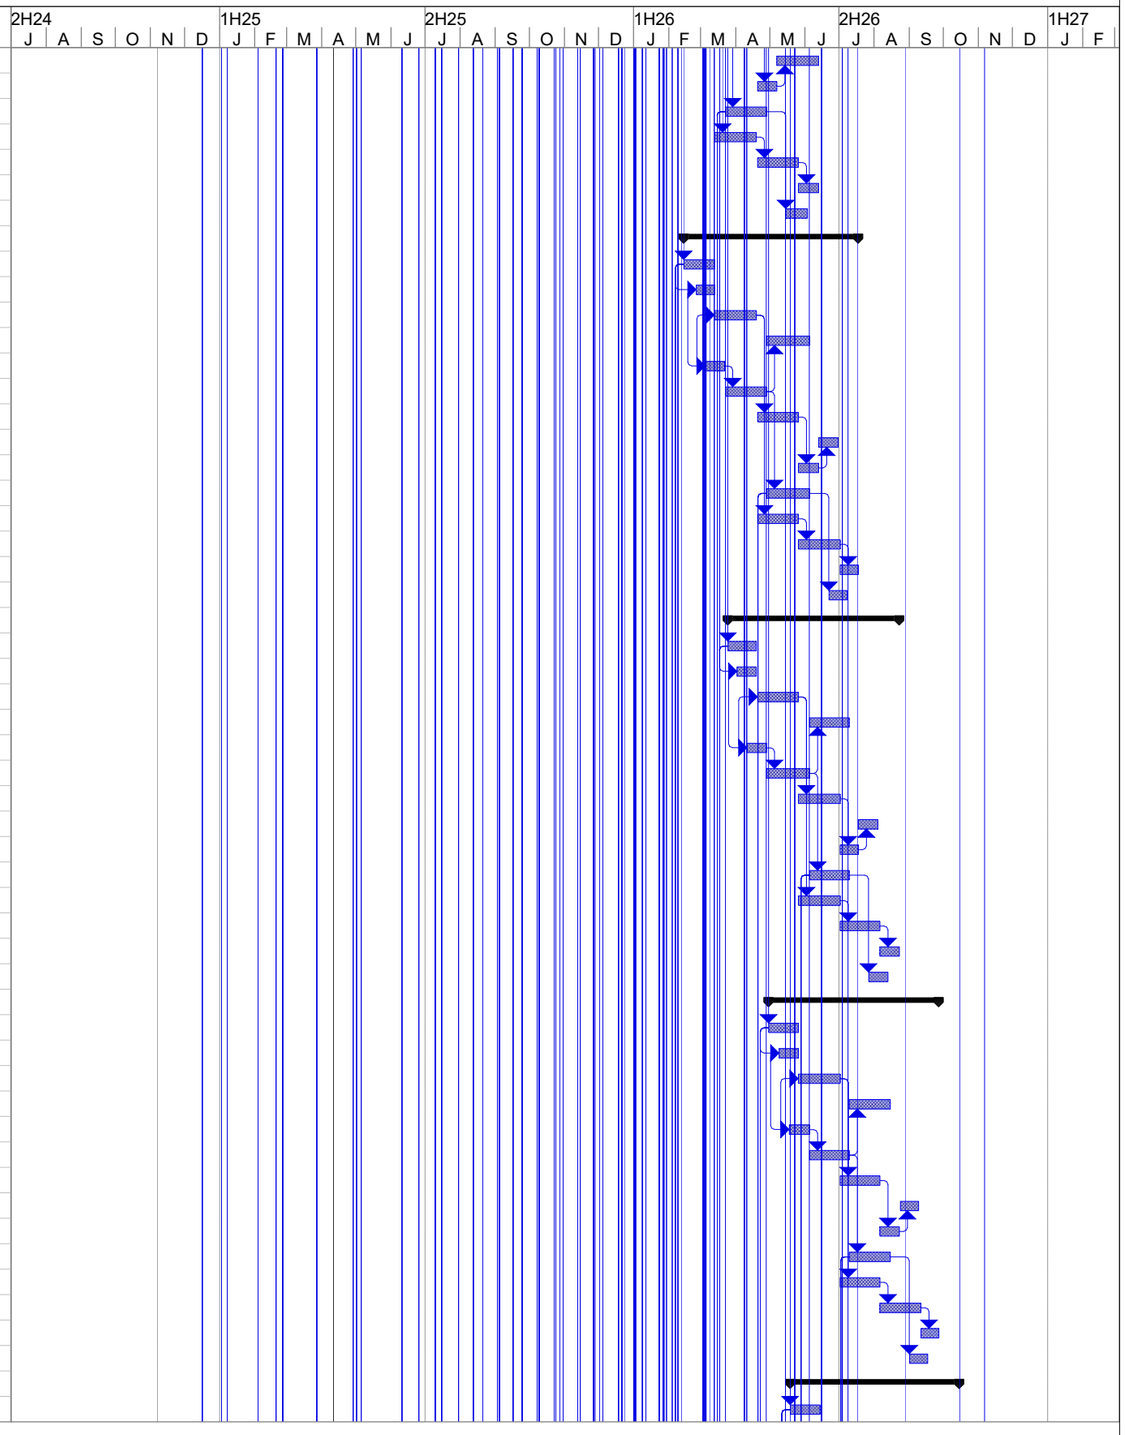

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone	
Split	External Tasks	Manual Task	Start-only	Progress	
Milestone	External Milestone	Duration-only	Finish-only	Deadline	
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks		


ID	Task Name	Duration	Start	Finish	Predecessors
433	Doors & windows	14 days	Thu 28/5/26	Sat 13/6/26	432SS+7 days
434	Internal plastering & skimming	30 days	Mon 15/6/26	Sat 18/7/26	436SS+7 days
435	Railings, metalworks etc.	30 days	Tue 28/7/26	Tue 1/9/26	437
436	Waterproofing works	14 days	Sat 6/6/26	Mon 22/6/26	433SS+7 days
437	Wall & floor finishes	30 days	Tue 23/6/26	Mon 27/7/26	436
438	Ceiling	30 days	Mon 20/7/26	Mon 24/8/26	434
439	Curtain Track	14 days	Thu 10/9/26	Fri 25/9/26	440
440	Internal painting	14 days	Tue 25/8/26	Wed 9/9/26	438
441	Furniture & fitments	30 days	Tue 28/7/26	Tue 1/9/26	437
442	External plastering & skimming	30 days	Mon 20/7/26	Mon 24/8/26	434
443	External painting	30 days	Tue 25/8/26	Mon 28/9/26	442
444	Plants & landscape	14 days	Tue 29/9/26	Wed 14/10/26	443
445	Signage	14 days	Fri 18/9/26	Sat 3/10/26	441FS+14 days
446	**Level 9**	**125 days**	**Tue 19/5/26**	**Wed 14/10/26**	
447	PC/PF/Drywalls, etc.	21 days	Tue 19/5/26	Sat 13/6/26	215FS+10 days
448	Doors & windows	14 days	Thu 28/5/26	Sat 13/6/26	447SS+7 days
449	Internal plastering & skimming	30 days	Mon 15/6/26	Sat 18/7/26	451SS+7 days
450	Railings, metalworks etc.	30 days	Tue 28/7/26	Tue 1/9/26	452
451	Waterproofing works	14 days	Sat 6/6/26	Mon 22/6/26	448SS+7 days
452	Wall & floor finishes	30 days	Tue 23/6/26	Mon 27/7/26	451
453	Ceiling	30 days	Mon 20/7/26	Mon 24/8/26	449
454	Internal painting	14 days	Tue 25/8/26	Wed 9/9/26	453
455	Furniture & fitments	30 days	Tue 28/7/26	Tue 1/9/26	452
456	External plastering & skimming	30 days	Mon 20/7/26	Mon 24/8/26	449
457	External painting	30 days	Tue 25/8/26	Mon 28/9/26	456
458	Plants & landscape	14 days	Tue 29/9/26	Wed 14/10/26	457
459	Signage	14 days	Fri 18/9/26	Sat 3/10/26	455FS+14 days
460	**Lower Roof**	**146 days**	**Sat 23/5/26**	**Fri 13/11/26**	
461	PC/PF/Drywalls, etc.	14 days	Sat 23/5/26	Wed 10/6/26	215FS+14 days
462	Doors	14 days	Thu 11/6/26	Fri 26/6/26	461
463	Internal plastering & skimming	30 days	Tue 14/7/26	Tue 18/8/26	465
464	Metalworks	60 days	Wed 19/8/26	Tue 27/10/26	466
465	Waterproofing works	14 days	Sat 27/6/26	Mon 13/7/26	462
466	Wall & floor finishes	30 days	Tue 14/7/26	Tue 18/8/26	465
467	Ceiling	21 days	Wed 23/9/26	Fri 16/10/26	463FS+30 days
468	Internal painting	30 days	Fri 9/10/26	Fri 13/11/26	467SS+14 days
469	External plastering & skimming	30 days	Wed 19/8/26	Tue 22/9/26	463
470	External painting	30 days	Wed 23/9/26	Tue 27/10/26	469
471	Signage	14 days	Sat 17/10/26	Mon 2/11/26	468SS+7 days
472	**Upper Roof**	**134 days**	**Sat 23/5/26**	**Thu 29/10/26**	
473	Railings, metalworks etc.	90 days	Sat 23/5/26	Tue 8/9/26	215FS+14 days
474	Internal painting	30 days	Wed 9/9/26	Tue 13/10/26	473
475	External painting	30 days	Wed 23/9/26	Tue 27/10/26	469
476	Signage	14 days	Wed 14/10/26	Thu 29/10/26	474
477	**Upon TC1 Dismantling**	**21 days**	**Fri 21/8/26**	**Mon 14/9/26**	
478	Waterproofing to planter box	7 days	Fri 21/8/26	Fri 28/8/26	217
479	Landscape	14 days	Sat 29/8/26	Mon 14/9/26	478
480	**Part 2 - GL PE-RW/RW-8**	**260 days**	**Fri 10/10/25**	**Fri 21/8/26**	
481	**Basement**	**197 days**	**Fri 10/10/25**	**Mon 8/6/26**	
482	PC/PF/Drywalls, etc.	21 days	Fri 10/10/25	Tue 4/11/25	236FS+7 days
483	Doors	14 days	Wed 5/11/25	Thu 20/11/25	482
484	Wall plastering & skimming	30 days	Mon 8/12/25	Tue 13/1/26	485
485	Waterproofing works	14 days	Fri 21/11/25	Sat 6/12/25	483
486	Wall & floor finishes	30 days	Mon 8/12/25	Tue 13/1/26	485

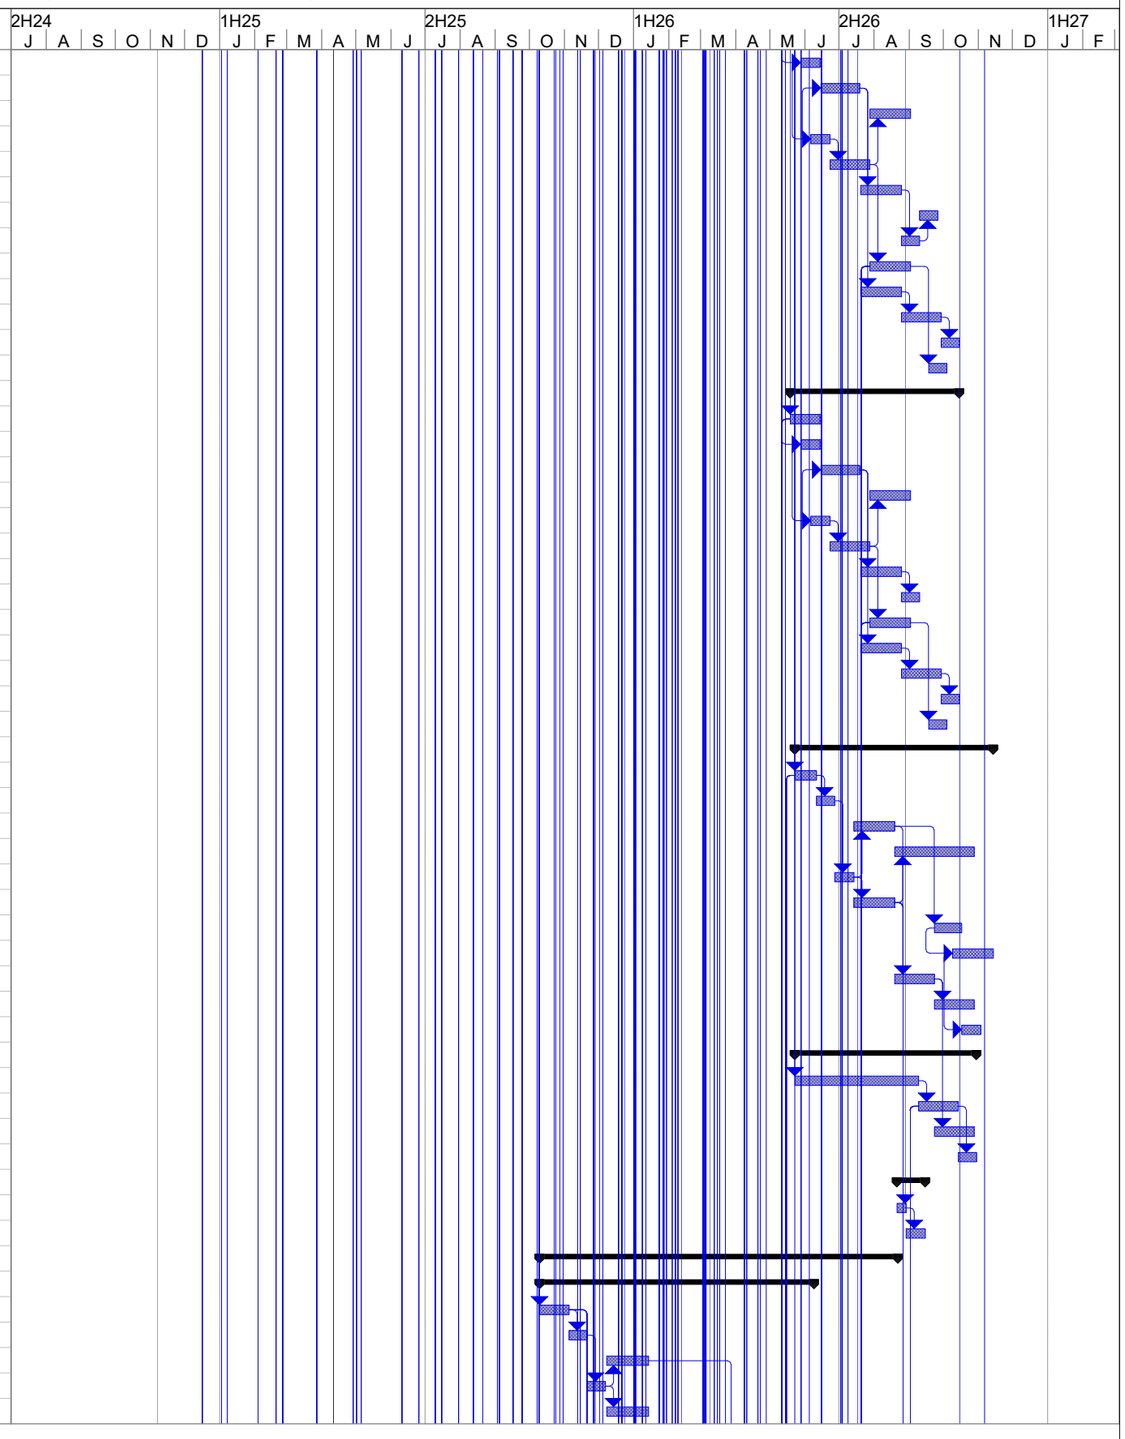

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone	
Split	External Tasks	Manual Task	Start-only	Progress	
Milestone	External Milestone	Duration-only	Finish-only	Deadline	
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks		


ID	Task Name	Duration	Start	Finish	Predecessors
487	Ceiling	30 days	Sat 28/3/26	Mon 4/5/26	484FS+60 days
488	Internal painting	14 days	Tue 5/5/26	Wed 20/5/26	487
489	Signage	14 days	Thu 21/5/26	Mon 8/6/26	488
490	**Level 1**	**167 days**	**Wed 24/12/25**	**Thu 16/7/26**	
491	PC/PF/Drywalls, etc.	14 days	Wed 24/12/25	Sat 10/1/26	237FS+10 days
492	Doors & windows	21 days	Mon 12/1/26	Wed 4/2/26	491
493	Internal plastering & skimming	30 days	Tue 24/2/26	Tue 31/3/26	495
494	Railings, metalworks etc.	21 days	Wed 1/4/26	Sat 25/4/26	496
495	Waterproofing works	14 days	Thu 5/2/26	Mon 23/2/26	492
496	Wall & floor finishes	30 days	Tue 24/2/26	Tue 31/3/26	495
497	Ceiling	30 days	Fri 8/5/26	Sat 13/6/26	493FS+30 days
498	Curtain Track	14 days	Wed 1/7/26	Thu 16/7/26	499
499	Internal painting	14 days	Mon 15/6/26	Tue 30/6/26	497
500	Furniture & fitments	30 days	Wed 1/4/26	Thu 7/5/26	496
501	External plastering & Skimming	30 days	Wed 1/4/26	Thu 7/5/26	493
502	External painting	30 days	Fri 8/5/26	Sat 13/6/26	501
503	Plants & landscape	14 days	Mon 15/6/26	Tue 30/6/26	502
504	Signage	14 days	Mon 25/5/26	Thu 11/6/26	500FS+14 days
505	**Level 2**	**167 days**	**Fri 30/1/26**	**Fri 21/8/26**	
506	PC/PF/Drywalls, etc.	14 days	Fri 30/1/26	Sat 14/2/26	238FS+10 days
507	Doors & windows	21 days	Mon 16/2/26	Fri 13/3/26	506
508	Internal plastering & skimming	30 days	Wed 1/4/26	Thu 7/5/26	510
509	Railings, metalworks etc.	21 days	Fri 8/5/26	Wed 3/6/26	511
510	Waterproofing works	14 days	Sat 14/3/26	Tue 31/3/26	507
511	Wall & floor finishes	30 days	Wed 1/4/26	Thu 7/5/26	510
512	Ceiling	30 days	Mon 15/6/26	Sat 18/7/26	508FS+30 days
513	Curtain Track	14 days	Wed 5/8/26	Fri 21/8/26	514
514	Internal painting	14 days	Mon 20/7/26	Tue 4/8/26	512
515	Furniture & fitments	30 days	Fri 8/5/26	Sat 13/6/26	511
516	External plastering & Skimming	30 days	Fri 8/5/26	Sat 13/6/26	508
517	External painting	30 days	Mon 15/6/26	Sat 18/7/26	516
518	Plants & landscape	14 days	Mon 20/7/26	Tue 4/8/26	517
519	Signage	14 days	Wed 1/7/26	Thu 16/7/26	515FS+14 days
520	**Level 3**	**153 days**	**Wed 4/2/26**	**Sat 8/8/26**	
521	PC/PF/Drywalls, etc.	14 days	Wed 4/2/26	Sat 21/2/26	238FS+14 days
522	Doors & windows	21 days	Mon 23/2/26	Wed 18/3/26	521
523	Internal plastering & skimming	30 days	Tue 7/4/26	Tue 12/5/26	525
524	Railings, metalworks, screen etc.	30 days	Wed 13/5/26	Thu 18/6/26	526
525	Waterproofing works	14 days	Thu 19/3/26	Mon 6/4/26	522
526	Wall & floor finishes	30 days	Tue 7/4/26	Tue 12/5/26	525
527	Ceiling	30 days	Fri 19/6/26	Thu 23/7/26	523FS+30 days
528	Internal painting	14 days	Fri 24/7/26	Sat 8/8/26	527
529	Furniture & fitments	30 days	Wed 13/5/26	Thu 18/6/26	526
530	External plastering & Skimming	30 days	Wed 13/5/26	Thu 18/6/26	523
531	External painting	30 days	Fri 19/6/26	Thu 23/7/26	530
532	Sunshades, alu fins, claddings, etc.	14 days	Fri 24/7/26	Sat 8/8/26	531
533	Plants & landscape	14 days	Fri 24/7/26	Sat 8/8/26	531
534	Signage	14 days	Mon 6/7/26	Tue 21/7/26	529FS+14 days
535	**PC Lower Roof**	**153 days**	**Mon 9/2/26**	**Fri 14/8/26**	
536	PC/PF/Drywalls, etc.	14 days	Mon 9/2/26	Thu 26/2/26	238FS+18 days
537	Doors & windows	21 days	Fri 27/2/26	Tue 24/3/26	536
538	Internal plastering & skimming	30 days	Sat 11/4/26	Sat 16/5/26	539
539	Waterproofing works	14 days	Wed 25/3/26	Fri 10/4/26	537
540	Wall & floor finishes	30 days	Sat 11/4/26	Sat 16/5/26	539

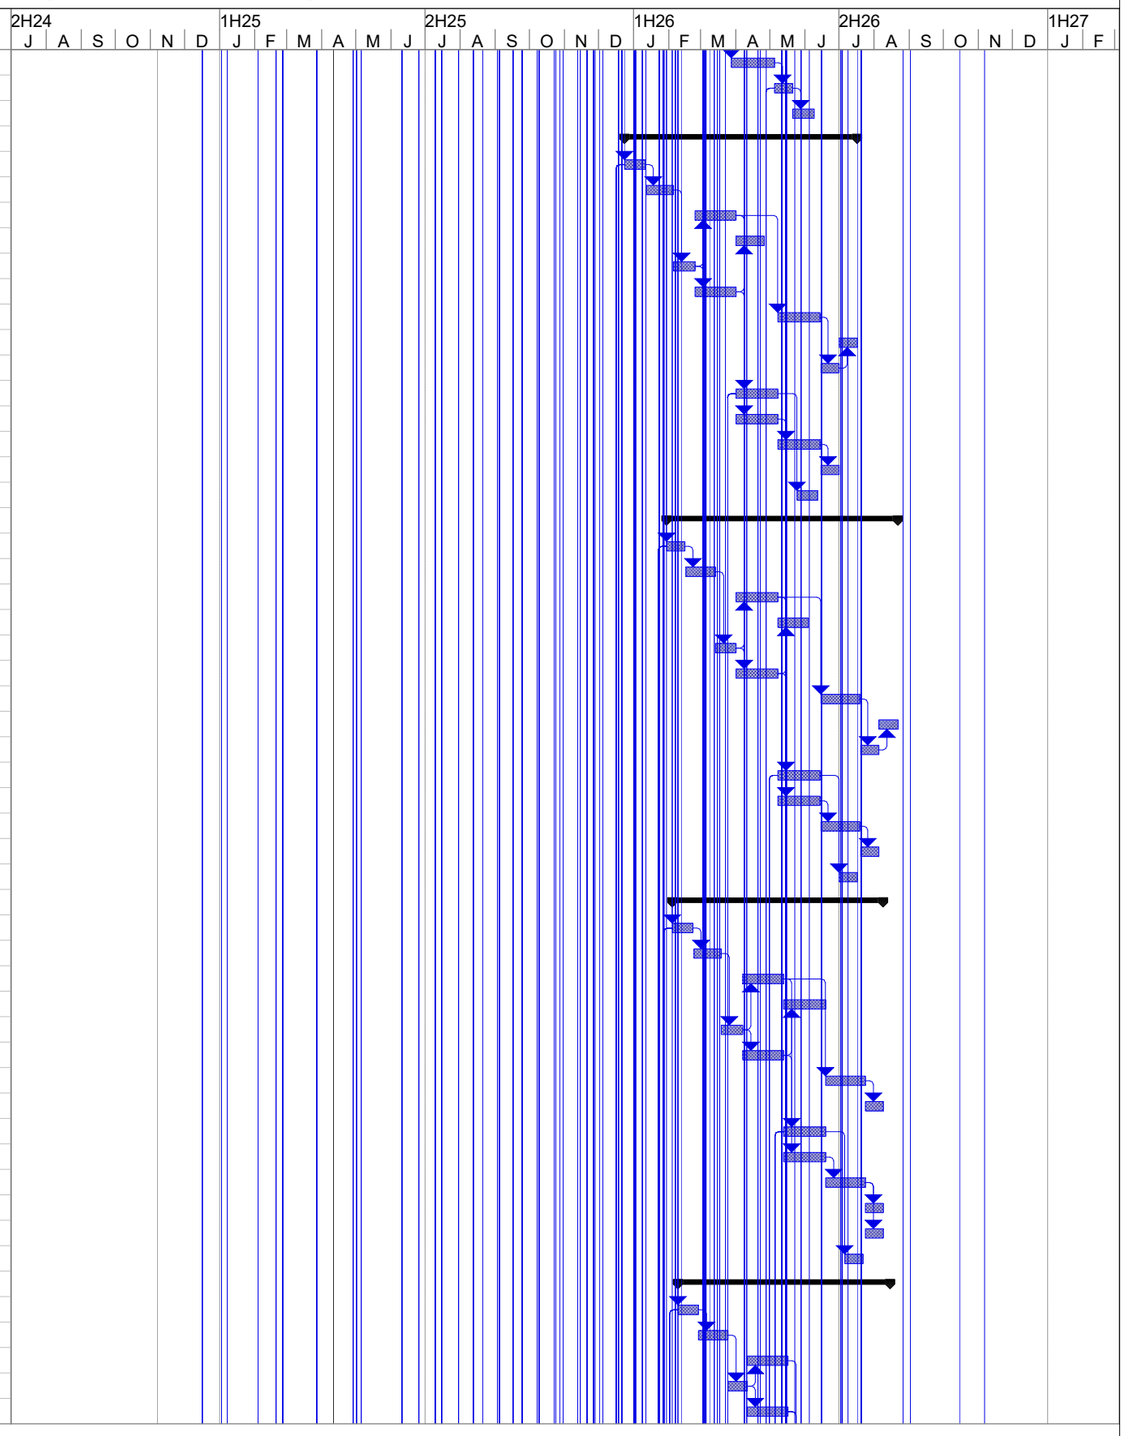

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	


ID	Task Name	Duration	Start	Finish	Predecessors
541	Internal painting	14 days	Mon 18/5/26	Thu 4/6/26	540
542	External plastering & Skimming	30 days	Mon 18/5/26	Tue 23/6/26	538
543	External painting	30 days	Wed 24/6/26	Tue 28/7/26	542
544	Skylight	60 days	Mon 18/5/26	Tue 28/7/26	540
545	BRC Fencing	30 days	Mon 18/5/26	Tue 23/6/26	540
546	Plants & landscape	14 days	Wed 29/7/26	Fri 14/8/26	543
547	Signage	14 days	Fri 5/6/26	Sat 20/6/26	541
548	**PC Upper Roof**	**118 days**	**Mon 9/2/26**	**Fri 3/7/26**	
549	Railings, metalworks etc.	90 days	Mon 9/2/26	Sat 30/5/26	238FS+18 days
550	Aluminium Trellis	90 days	Mon 9/2/26	Sat 30/5/26	238FS+18 days
551	Internal painting	14 days	Tue 2/6/26	Wed 17/6/26	550
552	External painting	14 days	Thu 18/6/26	Fri 3/7/26	551
553	Signage	14 days	Thu 18/6/26	Fri 3/7/26	551
554	**Part 3 - GL RW-PE/RW-8**	**312 days**	**Sat 15/11/25**	**Thu 26/11/26**	
555	**Basement**	**167 days**	**Sat 15/11/25**	**Mon 8/6/26**	
556	PC/PF/Drywalls, etc.	21 days	Sat 15/11/25	Tue 9/12/25	263FS+7 days
557	Doors	14 days	Wed 10/12/25	Fri 26/12/25	556
558	Wall plastering & skimming	30 days	Wed 14/1/26	Thu 19/2/26	559
559	Waterproofing works	14 days	Sat 27/12/25	Tue 13/1/26	557
560	Wall & floor finishes	30 days	Wed 14/1/26	Thu 19/2/26	559
561	Ceiling	30 days	Sat 28/3/26	Mon 4/5/26	559FS+60 days
562	Internal painting	14 days	Tue 5/5/26	Wed 20/5/26	561
563	Signage	14 days	Thu 21/5/26	Mon 8/6/26	562
564	**Level 1**	**153 days**	**Fri 30/1/26**	**Tue 4/8/26**	
565	PC/PF/Drywalls, etc.	14 days	Fri 30/1/26	Sat 14/2/26	264FS+10 days
566	Doors & windows	21 days	Mon 16/2/26	Fri 13/3/26	565
567	Internal plastering & skimming	30 days	Wed 1/4/26	Thu 7/5/26	569
568	Railings, metalworks etc.	21 days	Fri 8/5/26	Wed 3/6/26	570
569	Waterproofing works	14 days	Sat 14/3/26	Tue 31/3/26	566
570	Wall & floor finishes	30 days	Wed 1/4/26	Thu 7/5/26	569
571	Ceiling	30 days	Mon 15/6/26	Sat 18/7/26	567FS+30 days
572	Internal painting	14 days	Mon 20/7/26	Tue 4/8/26	571
573	Furniture & fitments	30 days	Fri 8/5/26	Sat 13/6/26	570
574	External plastering & Skimming	30 days	Fri 8/5/26	Sat 13/6/26	567
575	External painting	30 days	Mon 15/6/26	Sat 18/7/26	574
576	Plants & landscape	14 days	Mon 20/7/26	Tue 4/8/26	575
577	Signage	14 days	Wed 1/7/26	Thu 16/7/26	573FS+14 days
578	**Level 2**	**167 days**	**Mon 9/3/26**	**Fri 25/9/26**	
579	PC/PF/Drywalls, etc.	14 days	Mon 9/3/26	Wed 25/3/26	265FS+10 days
580	Doors & windows	21 days	Thu 26/3/26	Mon 20/4/26	579
581	Internal plastering & skimming	30 days	Fri 8/5/26	Sat 13/6/26	583
582	Railings, metalworks etc.	21 days	Mon 15/6/26	Wed 8/7/26	584
583	Waterproofing works	14 days	Tue 21/4/26	Thu 7/5/26	580
584	Wall & floor finishes including Lead Line to Dental Consult Room	30 days	Fri 8/5/26	Sat 13/6/26	583
585	Ceiling	30 days	Mon 20/7/26	Mon 24/8/26	581FS+30 days
586	Curtain Track	14 days	Thu 10/9/26	Fri 25/9/26	587
587	Internal painting	14 days	Tue 25/8/26	Wed 9/9/26	585
588	Furniture & fitments	30 days	Mon 15/6/26	Sat 18/7/26	584
589	External plastering & Skimming	30 days	Mon 15/6/26	Sat 18/7/26	581
590	External painting	30 days	Mon 20/7/26	Mon 24/8/26	589
591	Plants & landscape	14 days	Tue 25/8/26	Wed 9/9/26	590
592	Signage	14 days	Wed 5/8/26	Fri 21/8/26	588FS+14 days
593	**Level 3**	**153 days**	**Fri 13/3/26**	**Mon 14/9/26**	
594	PC/PF/Drywalls, etc.	14 days	Fri 13/3/26	Mon 30/3/26	265FS+14 days

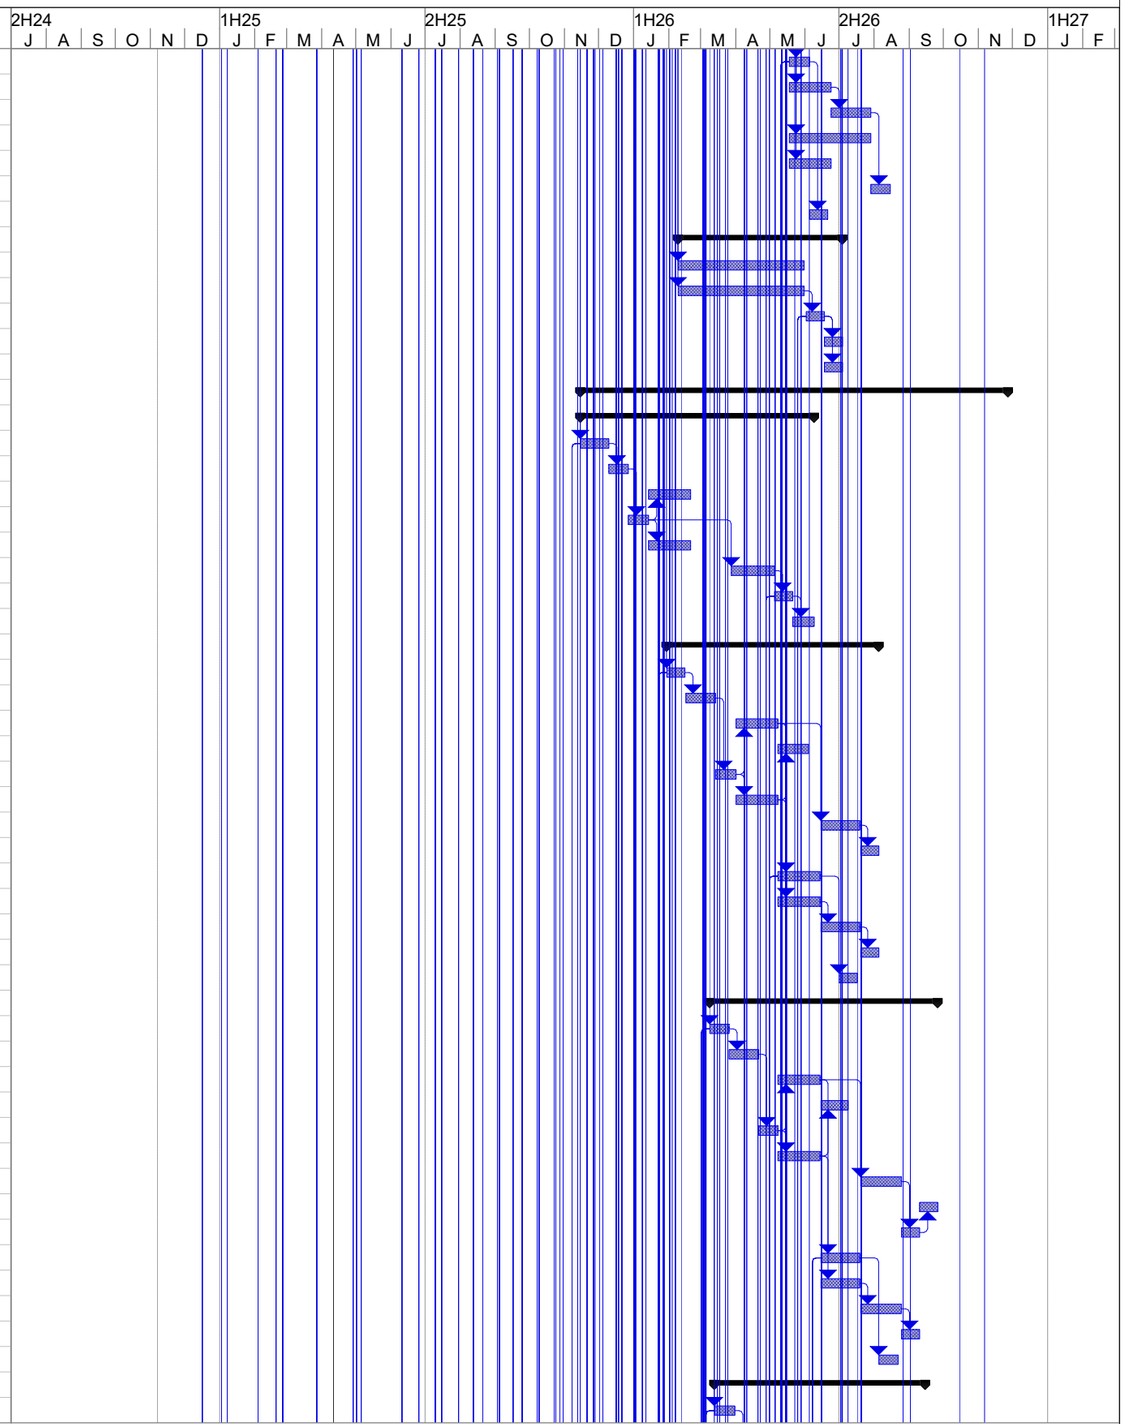

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	


ID	Task Name	Duration	Start	Finish	Predecessors
595	Doors & windows	21 days	Tue 31/3/26	Fri 24/4/26	594
596	Internal plastering & skimming	30 days	Wed 13/5/26	Thu 18/6/26	598
597	Railings, metalworks etc.	21 days	Fri 19/6/26	Mon 13/7/26	599
598	Waterproofing works	14 days	Sat 25/4/26	Tue 12/5/26	595
599	Wall & floor finishes	30 days	Wed 13/5/26	Thu 18/6/26	598
600	Ceiling	30 days	Fri 24/7/26	Fri 28/8/26	596FS+30 days
601	Internal painting	14 days	Sat 29/8/26	Mon 14/9/26	600
602	Furniture & fitments	30 days	Fri 19/6/26	Thu 23/7/26	599
603	External plastering & Skimming	30 days	Fri 19/6/26	Thu 23/7/26	596
604	External painting	30 days	Fri 24/7/26	Fri 28/8/26	603
605	Plants & landscape	14 days	Sat 29/8/26	Mon 14/9/26	604
606	Signage	14 days	Tue 11/8/26	Wed 26/8/26	602FS+14 days
607	**PC Lower Roof**	**153 days**	**Wed 18/3/26**	**Fri 18/9/26**	
608	PC/PF/Drywalls, etc.	14 days	Wed 18/3/26	Sat 4/4/26	265FS+18 days
609	Doors & windows	21 days	Mon 6/4/26	Wed 29/4/26	608
610	Internal plastering & skimming	30 days	Mon 18/5/26	Tue 23/6/26	611
611	Waterproofing works	14 days	Thu 30/4/26	Sat 16/5/26	609
612	Wall & floor finishes	30 days	Mon 18/5/26	Tue 23/6/26	611
613	Internal painting	14 days	Wed 24/6/26	Thu 9/7/26	612
614	External plastering & Skimming	30 days	Wed 24/6/26	Tue 28/7/26	610
615	External painting	30 days	Wed 29/7/26	Wed 2/9/26	614
616	Skylight	60 days	Wed 24/6/26	Wed 2/9/26	612
617	BRC Fencing	30 days	Wed 24/6/26	Tue 28/7/26	612
618	Plants & landscape	14 days	Thu 3/9/26	Fri 18/9/26	615
619	Signage	14 days	Fri 10/7/26	Sat 25/7/26	613
620	**PC Upper Roof**	**178 days**	**Wed 18/3/26**	**Sat 17/10/26**	
621	Railings, metalworks etc.	60 days	Wed 18/3/26	Sat 30/5/26	265FS+18 days
622	Aluminium Trellis	90 days	Tue 2/6/26	Tue 15/9/26	621
623	Internal painting	14 days	Wed 16/9/26	Thu 1/10/26	622
624	External painting	14 days	Fri 2/10/26	Sat 17/10/26	623
625	Signage	14 days	Fri 2/10/26	Sat 17/10/26	623
626	**Upon TC 2 Dismantling**	**42 days**	**Thu 8/10/26**	**Thu 26/11/26**	
627	Wall plastering & skimming	14 days	Thu 8/10/26	Fri 23/10/26	269
628	Wall & floor finishes	14 days	Sat 24/10/26	Tue 10/11/26	627
629	Ceiling installation	14 days	Wed 11/11/26	Thu 26/11/26	628
630	Railing (MS & Vinyl) installation	14 days	Wed 11/11/26	Thu 26/11/26	628
631	Solid surface installation	7 days	Wed 11/11/26	Wed 18/11/26	628
632	Waterproofing to planter box	7 days	Wed 11/11/26	Wed 18/11/26	628
633	Landscape	7 days	Thu 19/11/26	Thu 26/11/26	632
634	MS Screen	14 days	Wed 11/11/26	Thu 26/11/26	628
635	**Part 4 - GL RW-I/RW-20**	**326 days**	**Tue 28/10/25**	**Tue 24/11/26**	
636	**Basement**	**197 days**	**Tue 28/10/25**	**Wed 24/6/26**	
637	PC/PF/Drywalls, etc.	21 days	Tue 28/10/25	Thu 20/11/25	292FS+10 days
638	Doors	14 days	Fri 21/11/25	Sat 6/12/25	637
639	Wall plastering & skimming	30 days	Wed 24/12/25	Thu 29/1/26	640
640	Waterproofing works	14 days	Mon 8/12/25	Tue 23/12/25	638
641	Wall & floor finishes	30 days	Wed 24/12/25	Thu 29/1/26	640
642	Ceiling	30 days	Wed 15/4/26	Wed 20/5/26	639FS+60 days
643	Internal painting	14 days	Thu 21/5/26	Mon 8/6/26	642
644	Plants & landscape	14 days	Mon 9/3/26	Wed 25/3/26	641FS+30 days
645	Signage	14 days	Tue 9/6/26	Wed 24/6/26	643
646	**Level 1**	**111 days**	**Tue 2/12/25**	**Thu 16/4/26**	
647	PC/PF/Drywalls, etc.	21 days	Tue 2/12/25	Fri 26/12/25	293FS+10 days
648	Doors & windows	14 days	Wed 10/12/25	Fri 26/12/25	647SS+7 days

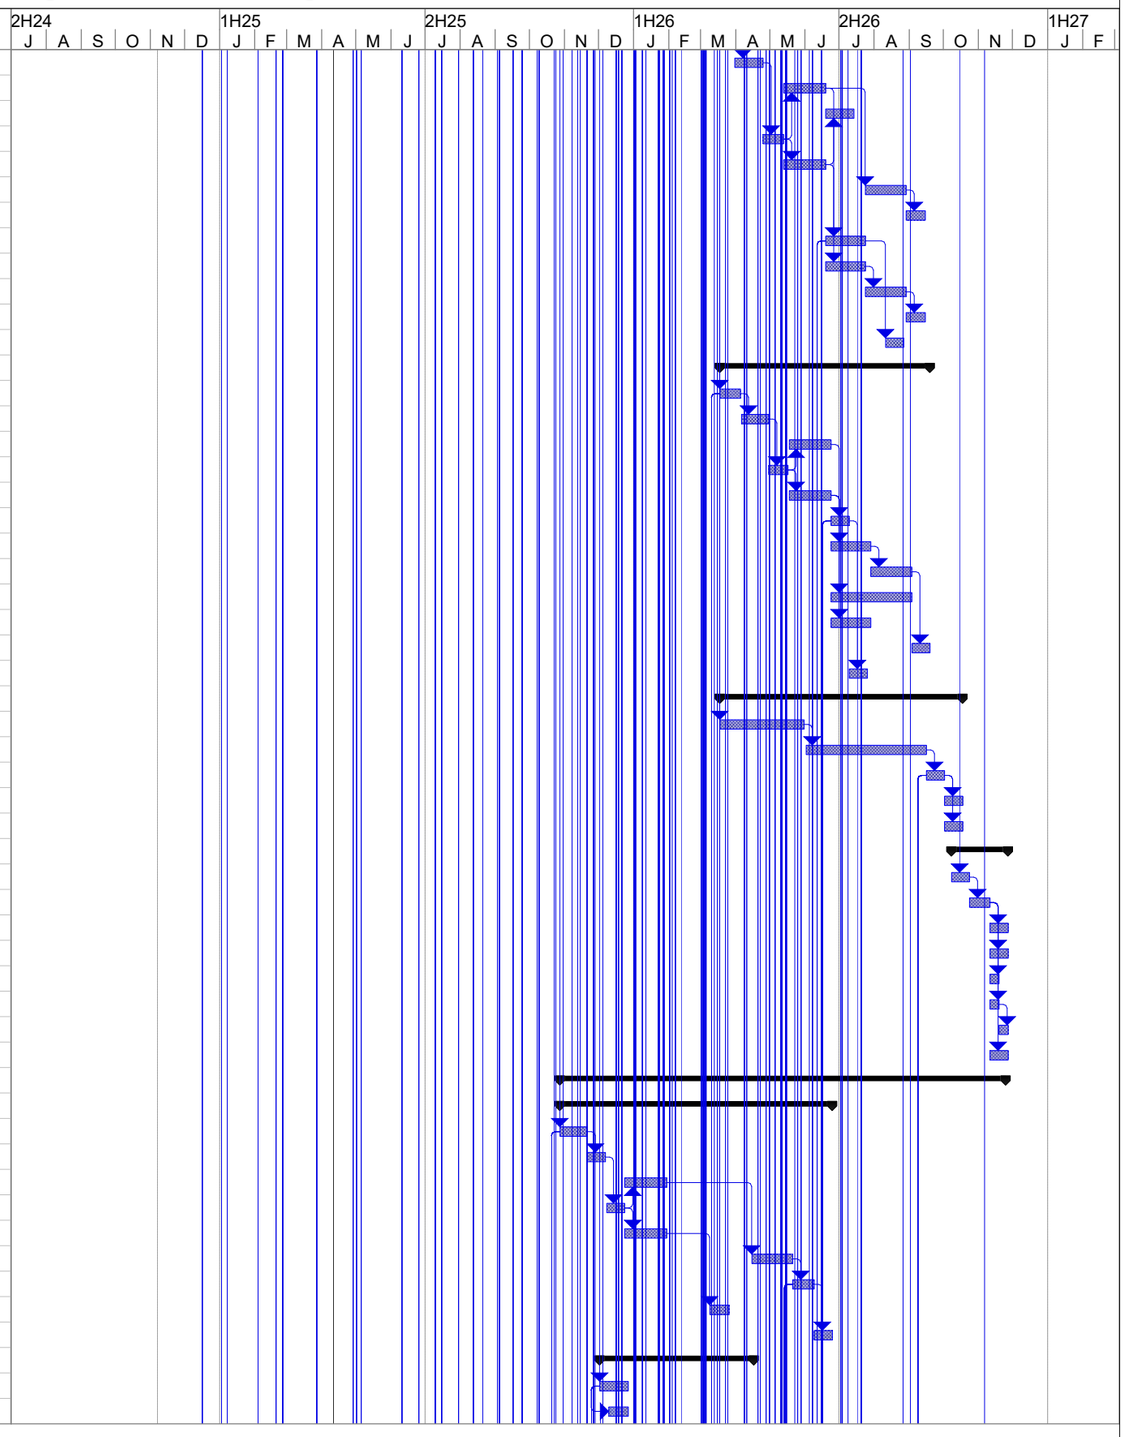

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Progress | Deadline


ID	Task Name	Duration	Start	Finish	Predecessors
649	Internal plastering & skimming	30 days	Sat 27/12/25	Sat 31/1/26	651SS+7 days
650	Railings, metalworks etc.	21 days	Mon 2/2/26	Fri 27/2/26	652
651	Waterproofing works	14 days	Thu 18/12/25	Mon 5/1/26	648SS+7 days
652	Wall & floor finishes including lead line to X-Ray Room, Mammogram Room	30 days	Sat 27/12/25	Sat 31/1/26	651SS+7 days
653	Ceiling	30 days	Mon 2/2/26	Tue 10/3/26	649
654	Internal painting	10 days	Wed 11/3/26	Mon 23/3/26	653
655	Furniture & fitments	30 days	Mon 2/2/26	Tue 10/3/26	652
656	External plastering & Skimming	30 days	Mon 2/2/26	Tue 10/3/26	649
657	External painting	30 days	Wed 11/3/26	Thu 16/4/26	656
658	Plants & landscape	14 days	Mon 2/2/26	Thu 19/2/26	652
659	Signage	14 days	Sat 28/3/26	Tue 14/4/26	655FS+14 days
660	**Level 2**	**111 days**	**Thu 8/1/26**	**Fri 22/5/26**	
661	PC/PF/Drywalls, etc.	21 days	Thu 8/1/26	Sat 31/1/26	294FS+10 days
662	Doors & windows	14 days	Fri 16/1/26	Sat 31/1/26	661SS+7 days
663	Internal plastering & skimming	30 days	Mon 2/2/26	Tue 10/3/26	665SS+7 days
664	Railings, metalworks etc.	21 days	Wed 11/3/26	Mon 6/4/26	666
665	Waterproofing works	14 days	Sat 24/1/26	Mon 9/2/26	662SS+7 days
666	Wall & floor finishes	30 days	Mon 2/2/26	Tue 10/3/26	665SS+7 days
667	Ceiling	30 days	Wed 11/3/26	Thu 16/4/26	663
668	Internal painting	10 days	Fri 17/4/26	Tue 28/4/26	667
669	Furniture & fitments	30 days	Wed 11/3/26	Thu 16/4/26	666
670	External plastering & Skimming	30 days	Wed 11/3/26	Thu 16/4/26	663
671	External painting	30 days	Fri 17/4/26	Fri 22/5/26	670
672	Plants & landscape	14 days	Wed 11/3/26	Fri 27/3/26	666
673	Signage	14 days	Tue 5/5/26	Wed 20/5/26	669FS+14 days
674	**Level 3**	**111 days**	**Thu 12/2/26**	**Mon 29/6/26**	
675	PC/PF/Drywalls, etc.	21 days	Thu 12/2/26	Tue 10/3/26	295FS+10 days
676	Doors & windows	14 days	Mon 23/2/26	Tue 10/3/26	675SS+7 days
677	Internal plastering & skimming	30 days	Wed 11/3/26	Thu 16/4/26	679SS+7 days
678	Railings, metalworks, screen etc.	21 days	Fri 17/4/26	Tue 12/5/26	680
679	Waterproofing works	14 days	Tue 3/3/26	Wed 18/3/26	676SS+7 days
680	Wall & floor finishes	30 days	Wed 11/3/26	Thu 16/4/26	679SS+7 days
681	Ceiling	30 days	Fri 17/4/26	Fri 22/5/26	677
682	Curtain Track	10 days	Sat 6/6/26	Wed 17/6/26	683
683	Internal painting	10 days	Sat 23/5/26	Fri 5/6/26	681
684	Furniture & fitments	30 days	Fri 17/4/26	Fri 22/5/26	680
685	External plastering & Skimming	30 days	Fri 17/4/26	Fri 22/5/26	677
686	External painting	30 days	Sat 23/5/26	Mon 29/6/26	685
687	Plants & landscape	14 days	Fri 17/4/26	Mon 4/5/26	680
688	Signage	14 days	Thu 11/6/26	Fri 26/6/26	684FS+14 days
689	**Level 4**	**111 days**	**Mon 23/3/26**	**Mon 3/8/26**	
690	PC/PF/Drywalls, etc.	21 days	Mon 23/3/26	Thu 16/4/26	296FS+10 days
691	Doors & windows	14 days	Tue 31/3/26	Thu 16/4/26	690SS+7 days
692	Internal plastering & skimming	30 days	Fri 17/4/26	Fri 22/5/26	694SS+7 days
693	Railings, metalworks, screen etc.	30 days	Sat 23/5/26	Mon 29/6/26	695
694	Waterproofing works	14 days	Thu 9/4/26	Fri 24/4/26	691SS+7 days
695	Wall & floor finishes	30 days	Fri 17/4/26	Fri 22/5/26	694SS+7 days
696	Ceiling	30 days	Sat 23/5/26	Mon 29/6/26	692
697	Curtain Track	10 days	Sat 11/7/26	Wed 22/7/26	698
698	Internal painting	10 days	Tue 30/6/26	Fri 10/7/26	696
699	Furniture & fitments	30 days	Sat 23/5/26	Mon 29/6/26	695
700	External plastering & Skimming	30 days	Sat 23/5/26	Mon 29/6/26	692
701	External painting	30 days	Tue 30/6/26	Mon 3/8/26	700
702	Plants & landscape	14 days	Sat 23/5/26	Wed 10/6/26	695

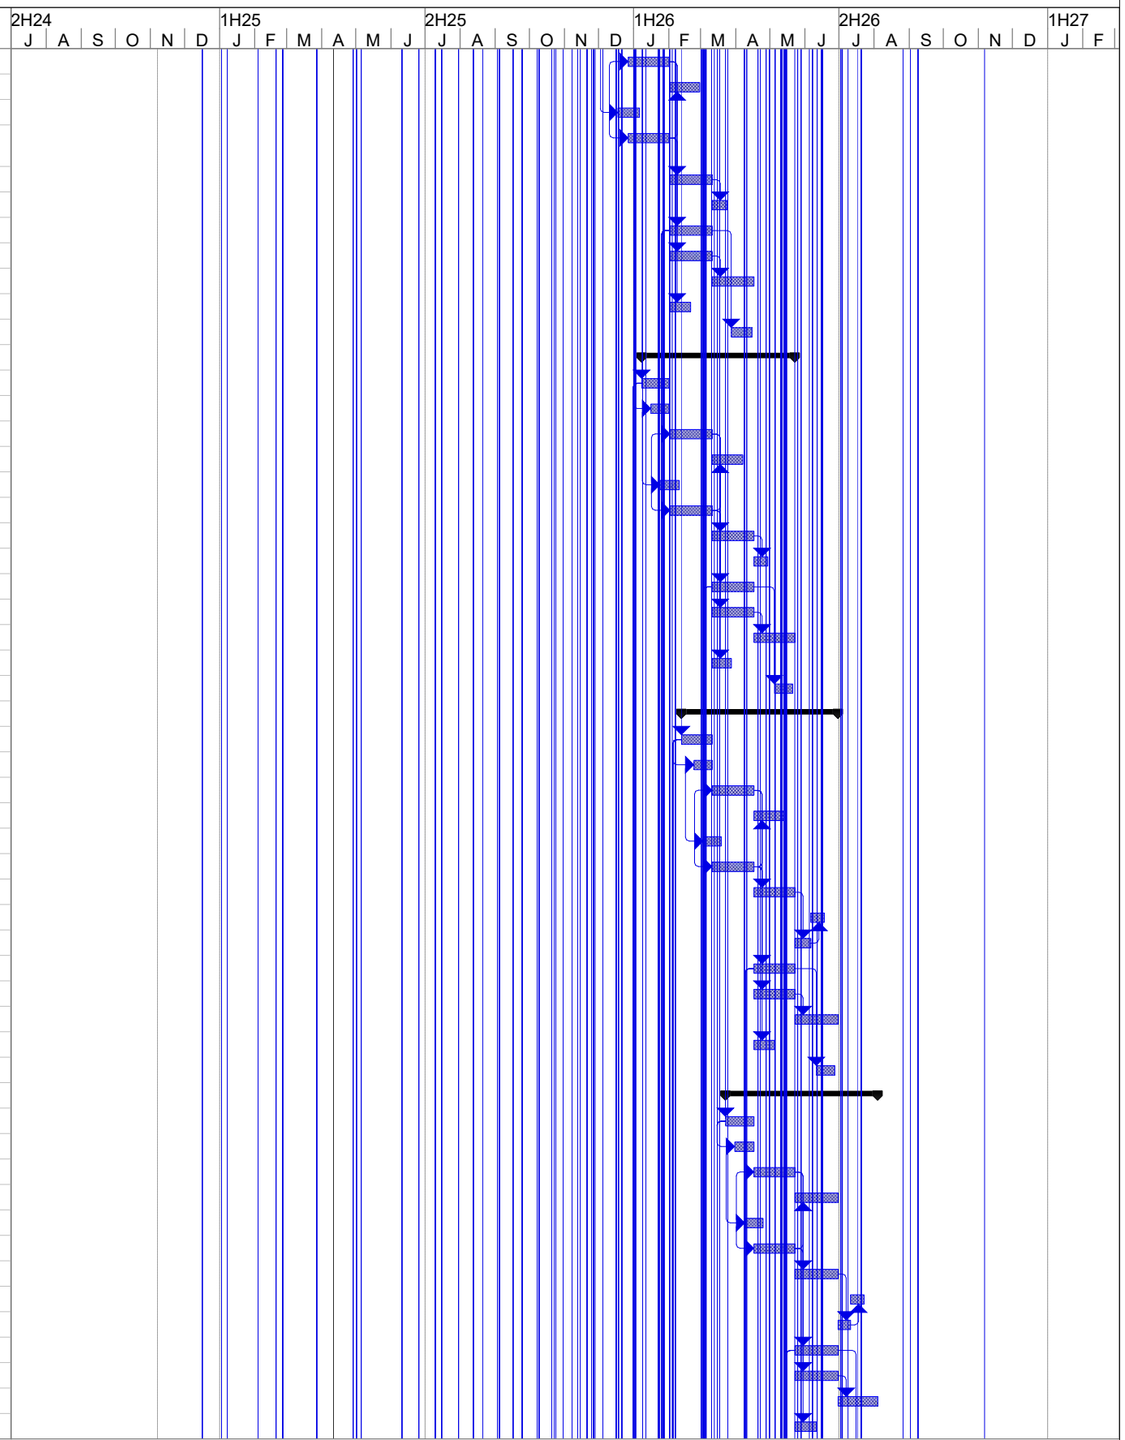

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Progress
Deadline


ID	Task Name	Duration	Start	Finish	Predecessors
703	Signage	14 days	Thu 16/7/26	Fri 31/7/26	699FS+14 days
704	**Level 5**	**111 days**	**Tue 28/4/26**	**Tue 8/9/26**	
705	PC/PF/Drywalls, etc.	21 days	Tue 28/4/26	Fri 22/5/26	297FS+10 days
706	Doors & windows	14 days	Thu 7/5/26	Fri 22/5/26	705SS+7 days
707	Internal plastering & skimming	30 days	Sat 23/5/26	Mon 29/6/26	709SS+7 days
708	Railings, metalworks, screen etc.	30 days	Tue 30/6/26	Mon 3/8/26	710
709	Waterproofing works	14 days	Fri 15/5/26	Tue 2/6/26	706SS+7 days
710	Wall & floor finishes	30 days	Sat 23/5/26	Mon 29/6/26	709SS+7 days
711	Ceiling	30 days	Tue 30/6/26	Mon 3/8/26	707
712	Curtain Track	10 days	Mon 17/8/26	Thu 27/8/26	713
713	Internal painting	10 days	Tue 4/8/26	Sat 15/8/26	711
714	Furniture & fitments	30 days	Tue 30/6/26	Mon 3/8/26	710
715	External plastering & Skimming	30 days	Tue 30/6/26	Mon 3/8/26	707
716	External painting	30 days	Tue 4/8/26	Tue 8/9/26	715
717	Plants & landscape	14 days	Tue 30/6/26	Wed 15/7/26	710
718	Signage	14 days	Fri 21/8/26	Sat 5/9/26	714FS+14 days
719	**Level 6**	**111 days**	**Fri 5/6/26**	**Tue 13/10/26**	
720	PC/PF/Drywalls, etc.	21 days	Fri 5/6/26	Mon 29/6/26	298FS+10 days
721	Doors & windows	14 days	Sat 13/6/26	Mon 29/6/26	720SS+7 days
722	Internal plastering & skimming	30 days	Tue 30/6/26	Mon 3/8/26	724SS+7 days
723	Railings, metalworks, screen etc.	30 days	Tue 4/8/26	Tue 8/9/26	725
724	Waterproofing works	14 days	Mon 22/6/26	Tue 7/7/26	721SS+7 days
725	Wall & floor finishes	30 days	Tue 30/6/26	Mon 3/8/26	724SS+7 days
726	Ceiling	30 days	Tue 4/8/26	Tue 8/9/26	722
727	Curtain Track	10 days	Mon 21/9/26	Thu 1/10/26	728
728	Internal painting	10 days	Wed 9/9/26	Sat 19/9/26	726
729	Furniture & fitments	30 days	Tue 4/8/26	Tue 8/9/26	725
730	External plastering & Skimming	30 days	Tue 4/8/26	Tue 8/9/26	722
731	External painting	30 days	Wed 9/9/26	Tue 13/10/26	730
732	Plants & landscape	14 days	Tue 4/8/26	Thu 20/8/26	725
733	Signage	14 days	Fri 25/9/26	Sat 10/10/26	729FS+14 days
734	**Level 7**	**111 days**	**Sat 4/7/26**	**Thu 12/11/26**	
735	PC/PF/Drywalls, etc.	21 days	Sat 4/7/26	Tue 28/7/26	299FS+10 days
736	Doors & windows	14 days	Mon 13/7/26	Tue 28/7/26	735SS+7 days
737	Internal plastering & skimming	30 days	Wed 29/7/26	Wed 2/9/26	739SS+7 days
738	Railings, metalworks, screen etc.	30 days	Thu 3/9/26	Wed 7/10/26	740
739	Waterproofing works	14 days	Tue 21/7/26	Wed 5/8/26	736SS+7 days
740	Wall & floor finishes	30 days	Wed 29/7/26	Wed 2/9/26	739SS+7 days
741	Ceiling	30 days	Thu 3/9/26	Wed 7/10/26	737
742	Curtain Track	10 days	Tue 20/10/26	Fri 30/10/26	743
743	Internal painting	10 days	Thu 8/10/26	Mon 19/10/26	741
744	Furniture & fitments	30 days	Thu 3/9/26	Wed 7/10/26	740
745	External plastering & Skimming	30 days	Thu 3/9/26	Wed 7/10/26	737
746	External painting	30 days	Thu 8/10/26	Thu 12/11/26	745
747	Plants & landscape	14 days	Thu 3/9/26	Fri 18/9/26	740
748	Signage	14 days	Sat 24/10/26	Tue 10/11/26	744FS+14 days
749	**Level 8**	**112 days**	**Sat 4/7/26**	**Fri 13/11/26**	
750	PC/PF/Drywalls, etc.	21 days	Sat 4/7/26	Tue 28/7/26	299FS+10 days
751	Doors & windows	14 days	Mon 13/7/26	Tue 28/7/26	750SS+7 days
752	Internal plastering & skimming	30 days	Wed 29/7/26	Wed 2/9/26	754SS+7 days
753	Railings, metalworks, screen etc.	30 days	Thu 3/9/26	Wed 7/10/26	755
754	Waterproofing works	14 days	Tue 21/7/26	Wed 5/8/26	751SS+7 days
755	Wall & floor finishes	30 days	Wed 29/7/26	Wed 2/9/26	754SS+7 days
756	Ceiling	30 days	Thu 8/10/26	Thu 12/11/26	752FS+30 days

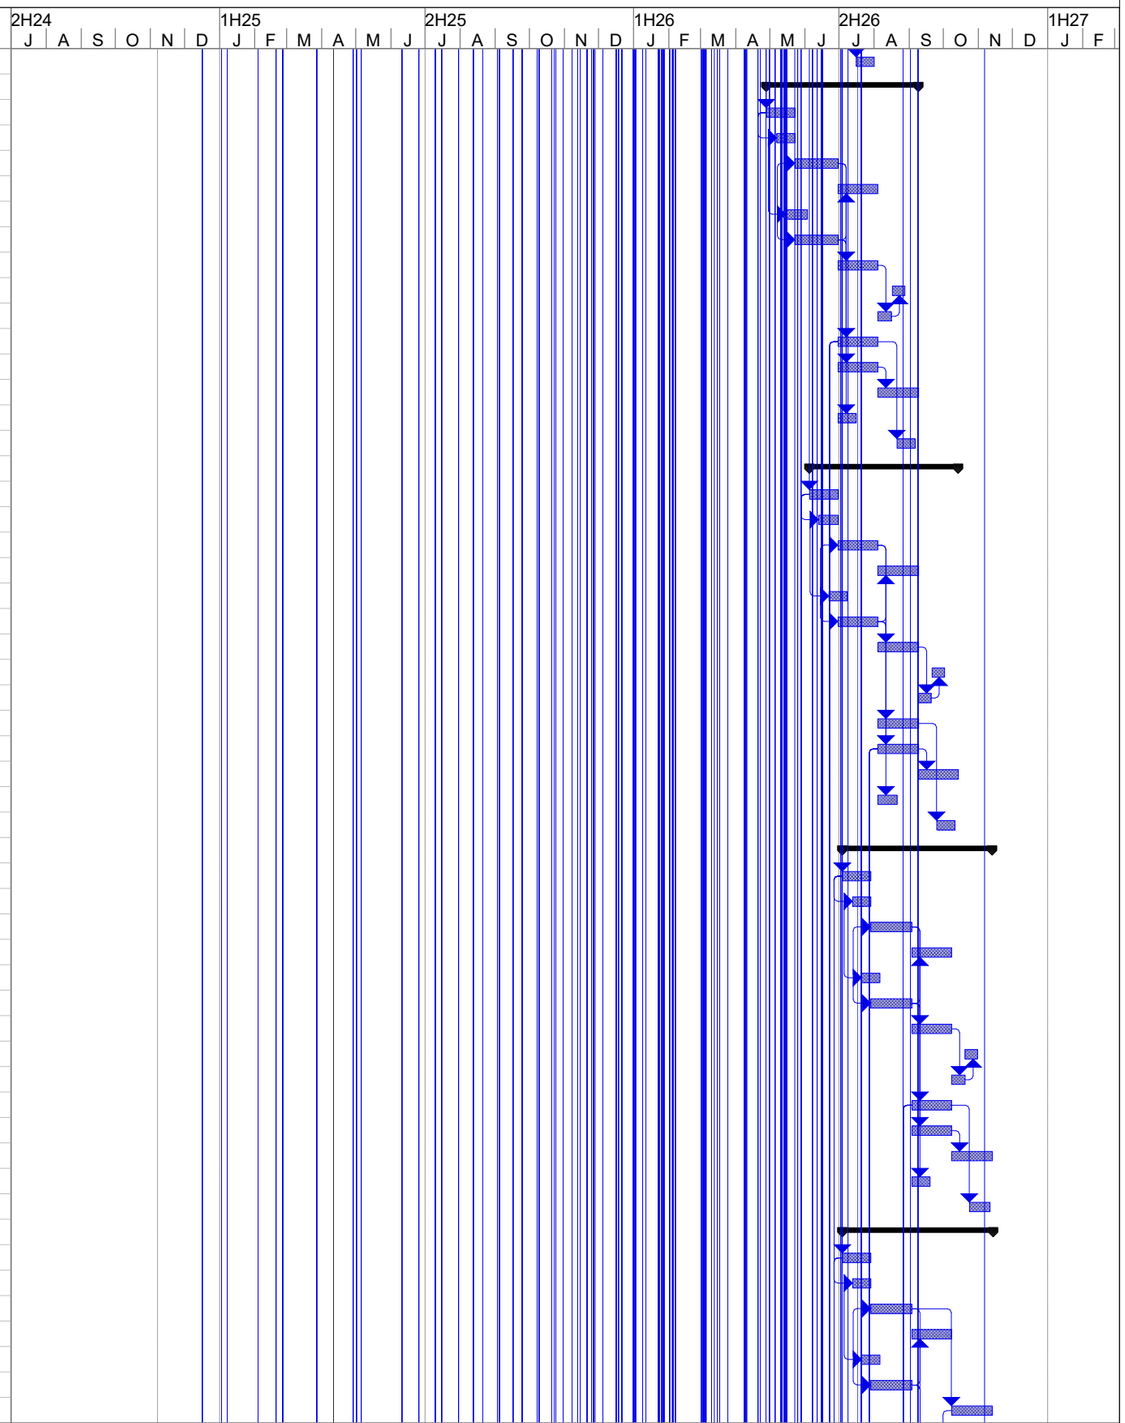

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	


ID	Task Name	Duration	Start	Finish	Predecessors
757	Curtain Track	10 days	Mon 2/11/26	Fri 13/11/26	758SS+7 days
758	Internal painting	14 days	Sat 24/10/26	Tue 10/11/26	756SS+14 days
759	Furniture & fitments	30 days	Thu 3/9/26	Wed 7/10/26	755
760	External plastering & Skimming	30 days	Thu 3/9/26	Wed 7/10/26	752
761	External painting	30 days	Thu 8/10/26	Thu 12/11/26	760
762	Plants & landscape	14 days	Thu 3/9/26	Fri 18/9/26	755
763	Signage	14 days	Sat 24/10/26	Tue 10/11/26	759FS+14 days
764	**Level 9**	**111 days**	**Sat 4/7/26**	**Thu 12/11/26**	
765	PC/PF/Drywalls, etc.	21 days	Sat 4/7/26	Tue 28/7/26	299FS+10 days
766	Doors & windows	14 days	Mon 13/7/26	Tue 28/7/26	765SS+7 days
767	Internal plastering & skimming	30 days	Wed 29/7/26	Wed 2/9/26	769SS+7 days
768	Railings, metalworks, etc.	30 days	Thu 3/9/26	Wed 7/10/26	770
769	Waterproofing works	14 days	Tue 21/7/26	Wed 5/8/26	766SS+7 days
770	Wall & floor finishes	30 days	Wed 29/7/26	Wed 2/9/26	769SS+7 days
771	Ceiling	30 days	Thu 3/9/26	Wed 7/10/26	767
772	Internal painting	14 days	Thu 8/10/26	Fri 23/10/26	771
773	Furniture & fitments	30 days	Thu 3/9/26	Wed 7/10/26	770
774	External plastering & Skimming	30 days	Thu 3/9/26	Wed 7/10/26	767
775	External painting	30 days	Thu 8/10/26	Thu 12/11/26	774
776	Plants & landscape	14 days	Thu 3/9/26	Fri 18/9/26	770
777	Signage	14 days	Sat 24/10/26	Tue 10/11/26	773FS+14 days
778	**Lower Roof**	**114 days**	**Thu 9/7/26**	**Fri 20/11/26**	
779	Doors & windows	7 days	Thu 9/7/26	Thu 16/7/26	299FS+14 days
780	Internal plastering & skimming	21 days	Mon 3/8/26	Thu 27/8/26	782
781	Metalworks	30 days	Tue 8/9/26	Mon 12/10/26	783
782	Waterproofing works	14 days	Fri 17/7/26	Sat 1/8/26	779
783	Wall & floor finishes	30 days	Mon 3/8/26	Mon 7/9/26	782
784	Ceiling	14 days	Fri 2/10/26	Sat 17/10/26	780FS+30 days
785	Internal painting	14 days	Mon 19/10/26	Tue 3/11/26	784
786	External plastering & Skimming	30 days	Fri 28/8/26	Thu 1/10/26	780
787	External painting	30 days	Fri 2/10/26	Thu 5/11/26	786
788	Signage	14 days	Wed 4/11/26	Fri 20/11/26	785
789	**Upper Roof**	**74 days**	**Fri 28/8/26**	**Mon 23/11/26**	
790	Railings, metalworks etc.	30 days	Fri 28/8/26	Thu 1/10/26	780
791	Internal painting	14 days	Fri 2/10/26	Sat 17/10/26	790
792	External painting	30 days	Mon 19/10/26	Mon 23/11/26	791
793	Signage	14 days	Mon 19/10/26	Tue 3/11/26	791
794	**Upon TC3 Dismantling**	**21 days**	**Fri 30/10/26**	**Tue 24/11/26**	
795	Waterproofing to planter box	7 days	Fri 30/10/26	Fri 6/11/26	302
796	Landscaping	14 days	Sat 7/11/26	Tue 24/11/26	795
797					
798	**M&E Works (Site Installation)**	**674 days**	**Thu 8/8/24**	**Wed 28/10/26**	
799	**Part 1 - GL I-RW/RW to 8**	**668 days**	**Thu 8/8/24**	**Wed 21/10/26**	
800	**Basement**	**564 days**	**Thu 8/8/24**	**Sat 20/6/26**	
801	Mat'l & Shopdrawing Submission/Approval	90 days	Thu 8/8/24	Fri 22/11/24	
802	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**387 days**	**Sat 11/1/25**	**Fri 24/4/26**	
803	1st Fix (concealed piping & conduit, pipe sleeve)	60 days	Sat 11/1/25	Mon 24/3/25	197SS+14 days
804	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Fri 5/9/25	Thu 9/10/25	319SS+14 days
805	3rd Fix (fittings)	30 days	Thu 19/3/26	Fri 24/4/26	325SS+7 days
806	**Electrical/PA/IT/Fire alarm**	**433 days**	**Sat 11/1/25**	**Sat 20/6/26**	
807	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Sat 11/1/25	Mon 17/2/25	197SS+14 days
808	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Fri 5/9/25	Thu 9/10/25	319SS+14 days
809	3rd Fix (fittings)	30 days	Fri 15/5/26	Sat 20/6/26	325SS+7 days
810	**ACMV**	**414 days**	**Wed 5/2/25**	**Sat 20/6/26**	

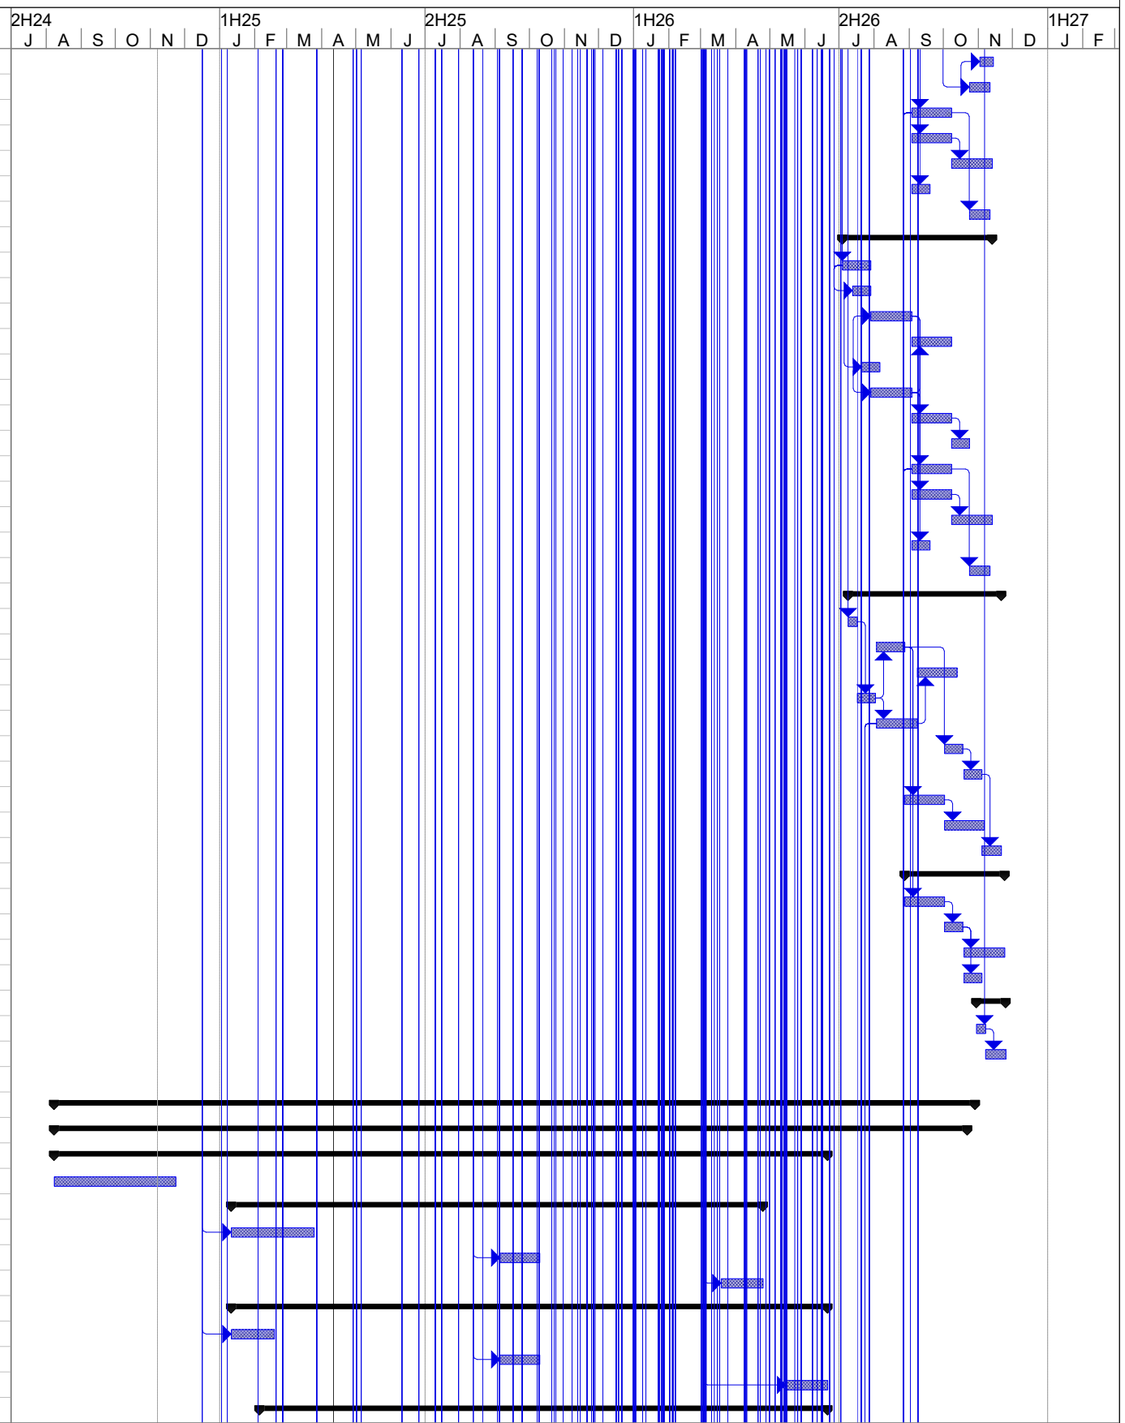

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	


ID	Task Name	Duration	Start	Finish	Predecessors
811	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Wed 5/2/25	Tue 11/3/25	197SS+14 days
812	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Fri 5/9/25	Thu 9/10/25	319SS+14 days
813	3rd Fix (fittings)	30 days	Fri 15/5/26	Sat 20/6/26	325SS+7 days
814	**Fire Protection - Sprinkler System**	**368 days**	**Wed 5/2/25**	**Fri 24/4/26**	
815	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Wed 5/2/25	Tue 11/3/25	197SS+14 days
816	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Fri 5/9/25	Thu 9/10/25	319SS+14 days
817	3rd Fix (fittings)	30 days	Thu 19/3/26	Fri 24/4/26	325SS+7 days
818	**Level 1**	**415 days**	**Thu 17/10/24**	**Mon 2/3/26**	
819	Mat'l & Shopdrawing Submission/Approval	90 days	Thu 17/10/24	Mon 3/2/25	
820	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**286 days**	**Fri 21/3/25**	**Mon 2/3/26**	
821	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Fri 21/3/25	Sat 26/4/25	205SS+14 days
822	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Fri 10/10/25	Fri 14/11/25	329SS+14 days
823	3rd Fix (fittings)	30 days	Sat 24/1/26	Mon 2/3/26	336SS+7 days
824	**Electrical/PA/IT/Fire alarm**	**286 days**	**Fri 21/3/25**	**Mon 2/3/26**	
825	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Fri 21/3/25	Sat 26/4/25	205SS+14 days
826	2nd Fix (concealed/surface (pipes/conduit),cable containment, wirings)	30 days	Fri 10/10/25	Fri 14/11/25	329SS+14 days
827	3rd Fix (fittings)	30 days	Sat 24/1/26	Mon 2/3/26	336SS+7 days
828	**ACMV**	**286 days**	**Fri 21/3/25**	**Mon 2/3/26**	
829	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Fri 21/3/25	Sat 26/4/25	205SS+14 days
830	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Fri 10/10/25	Fri 14/11/25	329SS+14 days
831	3rd Fix (fittings)	30 days	Sat 24/1/26	Mon 2/3/26	336SS+7 days
832	**Fire Protection - Sprinkler System**	**286 days**	**Fri 21/3/25**	**Mon 2/3/26**	
833	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Fri 21/3/25	Sat 26/4/25	205SS+14 days
834	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Fri 10/10/25	Fri 14/11/25	329SS+14 days
835	3rd Fix (fittings)	30 days	Sat 24/1/26	Mon 2/3/26	336SS+7 days
836	**Level 2**	**408 days**	**Thu 14/11/24**	**Sat 21/3/26**	
837	Mat'l & Shopdrawing Submission/Approval	90 days	Thu 14/11/24	Sat 1/3/25	
838	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**249 days**	**Tue 27/5/25**	**Sat 21/3/26**	
839	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Tue 27/5/25	Tue 1/7/25	206SS+14 days
840	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Sat 15/11/25	Fri 19/12/25	343SS+14 days
841	3rd Fix (fittings)	30 days	Thu 12/2/26	Sat 21/3/26	350SS+7 days
842	**Electrical/PA/IT/Fire alarm**	**249 days**	**Tue 27/5/25**	**Sat 21/3/26**	
843	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Tue 27/5/25	Tue 1/7/25	206SS+14 days
844	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Sat 15/11/25	Fri 19/12/25	343SS+14 days
845	3rd Fix (fittings)	30 days	Thu 12/2/26	Sat 21/3/26	350SS+7 days
846	**ACMV**	**249 days**	**Tue 27/5/25**	**Sat 21/3/26**	
847	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Tue 27/5/25	Tue 1/7/25	206SS+14 days
848	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Sat 15/11/25	Fri 19/12/25	343SS+14 days
849	3rd Fix (fittings)	30 days	Thu 12/2/26	Sat 21/3/26	350SS+7 days
850	**Fire Protection - Sprinkler System**	**249 days**	**Tue 27/5/25**	**Sat 21/3/26**	
851	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Tue 27/5/25	Tue 1/7/25	206SS+14 days
852	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Sat 15/11/25	Fri 19/12/25	343SS+14 days
853	3rd Fix (fittings)	30 days	Thu 12/2/26	Sat 21/3/26	350SS+7 days
854	**Level 3**	**413 days**	**Thu 12/12/24**	**Mon 27/4/26**	
855	Mat'l & Shopdrawing Submission/Approval	90 days	Thu 12/12/24	Tue 1/4/25	
856	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**234 days**	**Sat 19/7/25**	**Mon 27/4/26**	
857	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Sat 19/7/25	Sat 23/8/25	207SS+14 days
858	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Sat 20/12/25	Mon 26/1/26	357SS+14 days
859	3rd Fix (fittings)	30 days	Mon 23/3/26	Mon 27/4/26	365SS+7 days

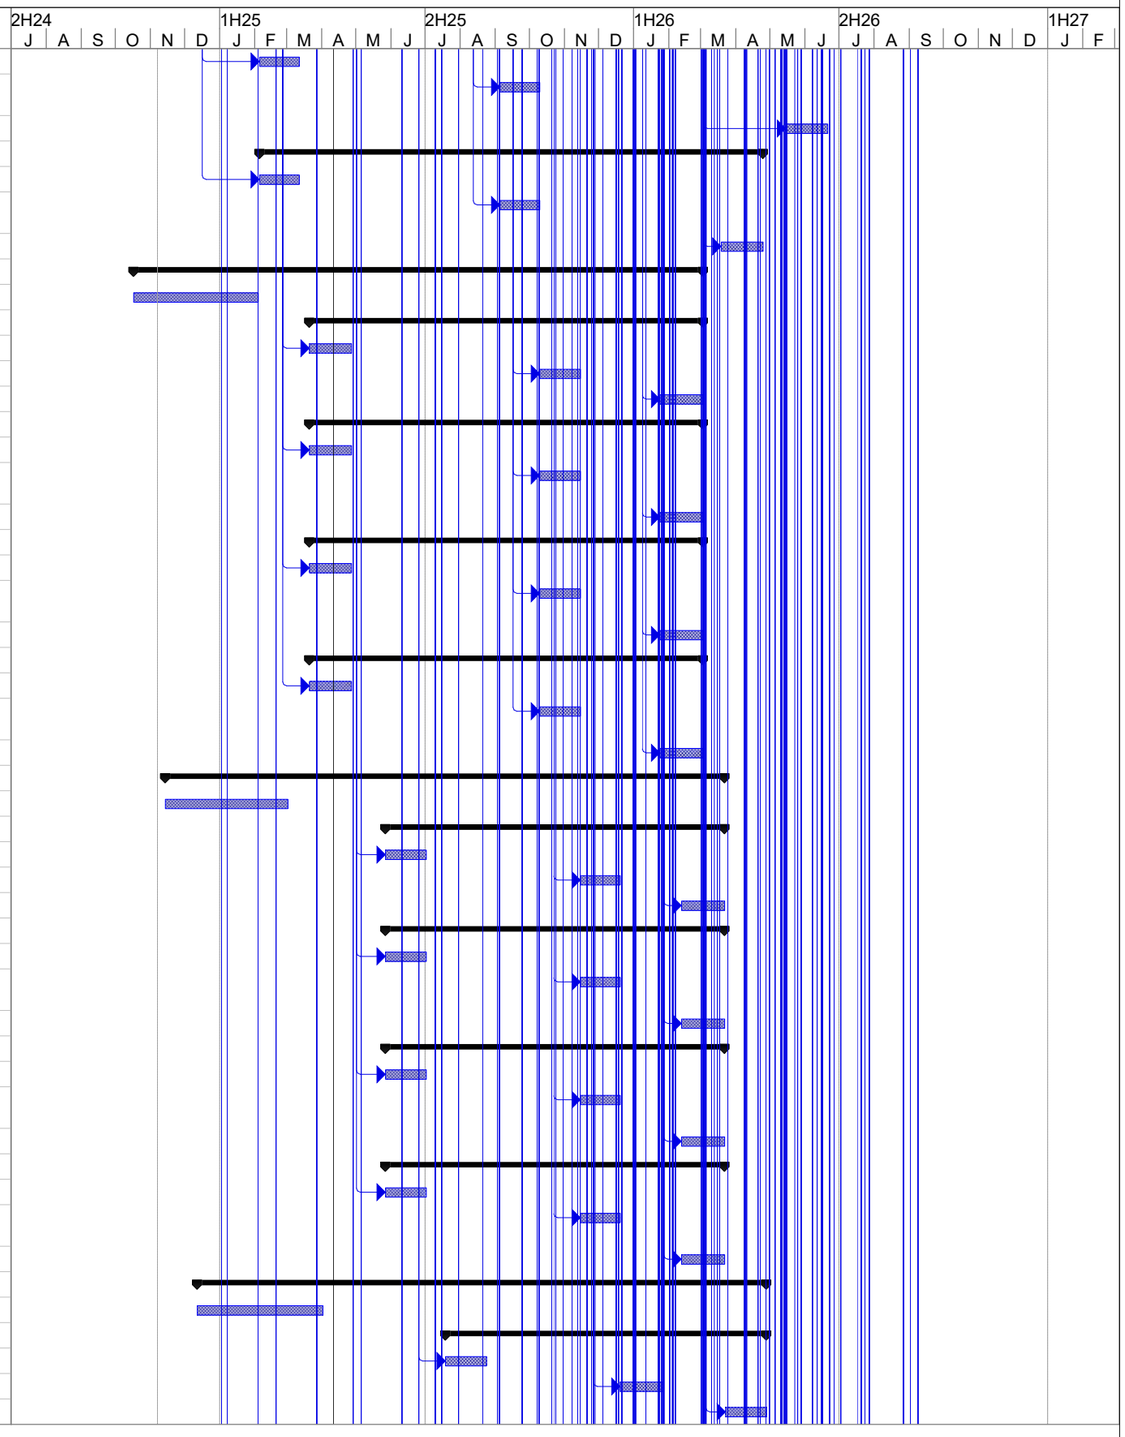

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Progress | Deadline


ID	Task Name	Duration	Start	Finish	Predecessors
860	**Electrical/PA/IT/Fire alarm**	**234 days**	**Sat 19/7/25**	**Mon 27/4/26**	
861	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Sat 19/7/25	Sat 23/8/25	207SS+14 days
862	2nd Fix (concealed/surface (pipes/conduit),cable containment, wirings)	30 days	Sat 20/12/25	Mon 26/1/26	357SS+14 days
863	3rd Fix (fittings)	30 days	Mon 23/3/26	Mon 27/4/26	365SS+7 days
864	**ACMV**	**234 days**	**Sat 19/7/25**	**Mon 27/4/26**	
865	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Sat 19/7/25	Sat 23/8/25	207SS+14 days
866	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Sat 20/12/25	Mon 26/1/26	357SS+14 days
867	3rd Fix (fittings)	30 days	Mon 23/3/26	Mon 27/4/26	365SS+7 days
868	**Fire Protection - Sprinkler System**	**234 days**	**Sat 19/7/25**	**Mon 27/4/26**	
869	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Sat 19/7/25	Sat 23/8/25	207SS+14 days
870	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Sat 20/12/25	Mon 26/1/26	357SS+14 days
871	3rd Fix (fittings)	30 days	Mon 23/3/26	Mon 27/4/26	365SS+7 days
872	**Level 4**	**402 days**	**Mon 13/1/25**	**Thu 14/5/26**	
873	Mat'l & Shopdrawing Submission/Approval	90 days	Mon 13/1/25	Fri 2/5/25	
874	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**218 days**	**Mon 25/8/25**	**Thu 14/5/26**	
875	1st Fix (concealed piping& conduit, pipe sleeve)	30 days	Mon 25/8/25	Sat 27/9/25	208SS+14 days
876	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Tue 27/1/26	Wed 4/3/26	372SS+14 days
877	3rd Fix (fittings)	30 days	Thu 9/4/26	Thu 14/5/26	381SS+14 days
878	**Electrical/PA/IT/Fire alarm**	**218 days**	**Mon 25/8/25**	**Thu 14/5/26**	
879	1st Fix (concealed piping& conduit, pipe sleeve)	30 days	Mon 25/8/25	Sat 27/9/25	208SS+14 days
880	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Tue 27/1/26	Wed 4/3/26	372SS+14 days
881	3rd Fix (fittings)	30 days	Thu 9/4/26	Thu 14/5/26	381SS+14 days
882	**ACMV**	**218 days**	**Mon 25/8/25**	**Thu 14/5/26**	
883	1st Fix (concealed piping& conduit, pipe sleeve)	30 days	Mon 25/8/25	Sat 27/9/25	208SS+14 days
884	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Tue 27/1/26	Wed 4/3/26	372SS+14 days
885	3rd Fix (fittings)	30 days	Thu 9/4/26	Thu 14/5/26	381SS+14 days
886	**Fire Protection - Sprinkler System**	**218 days**	**Mon 25/8/25**	**Thu 14/5/26**	
887	1st Fix (concealed piping& conduit, pipe sleeve)	30 days	Mon 25/8/25	Sat 27/9/25	208SS+14 days
888	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Tue 27/1/26	Wed 4/3/26	372SS+14 days
889	3rd Fix (fittings)	30 days	Thu 9/4/26	Thu 14/5/26	381SS+14 days
890	**Level 5**	**407 days**	**Thu 13/2/25**	**Sat 20/6/26**	
891	Mat'l & Shopdrawing Submission/Approval	90 days	Thu 13/2/25	Mon 2/6/25	
892	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**218 days**	**Mon 29/9/25**	**Sat 20/6/26**	
893	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Mon 29/9/25	Mon 3/11/25	209SS+14 days
894	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Thu 5/3/26	Fri 10/4/26	387SS+14 days
895	3rd Fix (fittings)	30 days	Fri 15/5/26	Sat 20/6/26	396SS+14 days
896	**Electrical/PA/IT/Fire alarm**	**218 days**	**Mon 29/9/25**	**Sat 20/6/26**	
897	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Mon 29/9/25	Mon 3/11/25	209SS+14 days
898	2nd Fix (concealed/surface (pipes/conduit),cable containment, wirings)	30 days	Thu 5/3/26	Fri 10/4/26	387SS+14 days
899	3rd Fix (fittings)	30 days	Fri 15/5/26	Sat 20/6/26	396SS+14 days
900	**ACMV**	**218 days**	**Mon 29/9/25**	**Sat 20/6/26**	
901	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Mon 29/9/25	Mon 3/11/25	209SS+14 days
902	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Thu 5/3/26	Fri 10/4/26	387SS+14 days
903	3rd Fix (fittings)	30 days	Fri 15/5/26	Sat 20/6/26	396SS+14 days
904	**Fire Protection - Sprinkler System**	**218 days**	**Mon 29/9/25**	**Sat 20/6/26**	
905	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Mon 29/9/25	Mon 3/11/25	209SS+14 days
906	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Thu 5/3/26	Fri 10/4/26	387SS+14 days
907	3rd Fix (fittings)	30 days	Fri 15/5/26	Sat 20/6/26	396SS+14 days
908	**Level 6**	**386 days**	**Tue 15/4/25**	**Sat 25/7/26**	

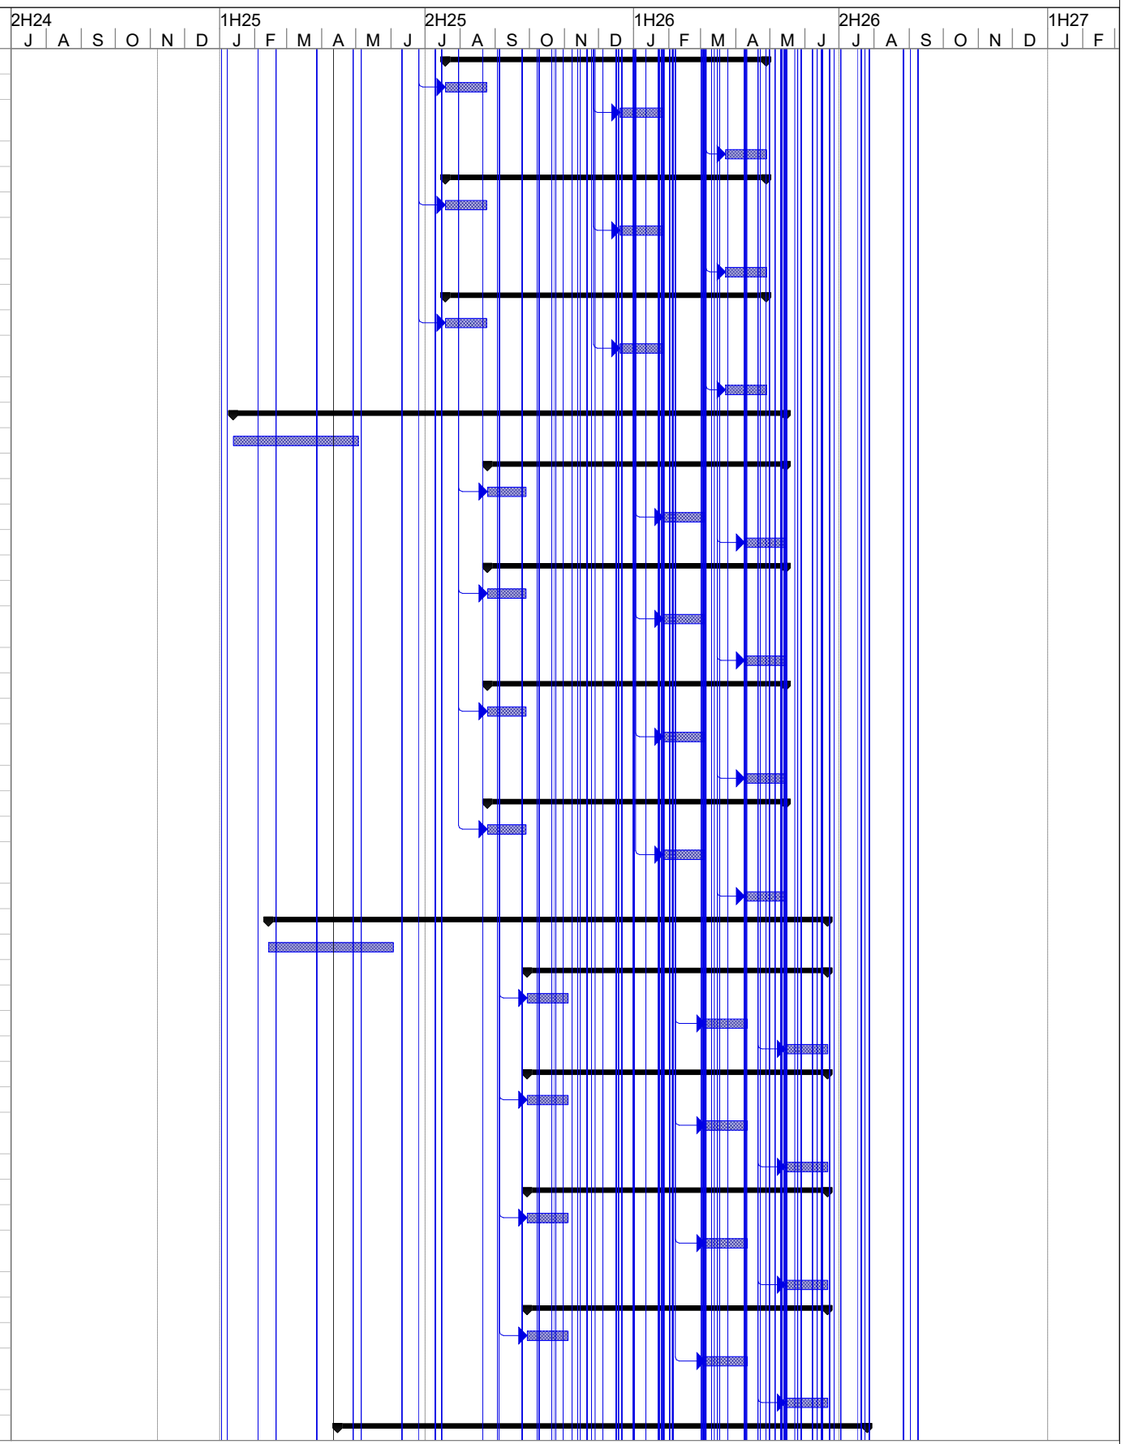

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	


ID	Task Name	Duration	Start	Finish	Predecessors
909	Mat'l & Shopdrawing Submission/Approval	90 days	Tue 15/4/25	Fri 1/8/25	
910	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**218 days**	**Tue 4/11/25**	**Sat 25/7/26**	
911	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Tue 4/11/25	Mon 8/12/25	210SS+14 days
912	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Sat 11/4/26	Sat 16/5/26	402SS+14 days
913	3rd Fix (fittings)	30 days	Mon 22/6/26	Sat 25/7/26	411SS+14 days
914	**Electrical/PA/IT/Fire alarm**	**218 days**	**Tue 4/11/25**	**Sat 25/7/26**	
915	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Tue 4/11/25	Mon 8/12/25	210SS+14 days
916	2nd Fix (concealed/surface (pipes/conduit),cable containment, wirings)	30 days	Sat 11/4/26	Sat 16/5/26	402SS+14 days
917	3rd Fix (fittings)	30 days	Mon 22/6/26	Sat 25/7/26	411SS+14 days
918	**ACMV**	**218 days**	**Tue 4/11/25**	**Sat 25/7/26**	
919	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Tue 4/11/25	Mon 8/12/25	210SS+14 days
920	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Sat 11/4/26	Sat 16/5/26	402SS+14 days
921	3rd Fix (fittings)	30 days	Mon 22/6/26	Sat 25/7/26	411SS+14 days
922	**Fire Protection - Sprinkler System**	**218 days**	**Tue 4/11/25**	**Sat 25/7/26**	
923	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Tue 4/11/25	Mon 8/12/25	210SS+14 days
924	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Sat 11/4/26	Sat 16/5/26	402SS+14 days
925	3rd Fix (fittings)	30 days	Mon 22/6/26	Sat 25/7/26	411SS+14 days
926	**Level 7**	**391 days**	**Sat 17/5/25**	**Mon 31/8/26**	
927	Mat'l & Shopdrawing Submission/Approval	90 days	Sat 17/5/25	Mon 1/9/25	
928	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**218 days**	**Tue 9/12/25**	**Mon 31/8/26**	
929	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Tue 9/12/25	Wed 14/1/26	211SS+14 days
930	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Mon 18/5/26	Tue 23/6/26	417SS+14 days
931	3rd Fix (fittings)	30 days	Mon 27/7/26	Mon 31/8/26	426SS+14 days
932	**Electrical/PA/IT/Fire alarm**	**218 days**	**Tue 9/12/25**	**Mon 31/8/26**	
933	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Tue 9/12/25	Wed 14/1/26	211SS+14 days
934	2nd Fix (concealed/surface (pipes/conduit),cable containment, wirings)	30 days	Mon 18/5/26	Tue 23/6/26	417SS+14 days
935	3rd Fix (fittings)	30 days	Mon 27/7/26	Mon 31/8/26	426SS+14 days
936	**ACMV**	**218 days**	**Tue 9/12/25**	**Mon 31/8/26**	
937	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Tue 9/12/25	Wed 14/1/26	211SS+14 days
938	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Mon 18/5/26	Tue 23/6/26	417SS+14 days
939	3rd Fix (fittings)	30 days	Mon 27/7/26	Mon 31/8/26	426SS+14 days
940	**Fire Protection - Sprinkler System**	**218 days**	**Tue 9/12/25**	**Mon 31/8/26**	
941	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Tue 9/12/25	Wed 14/1/26	211SS+14 days
942	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Mon 18/5/26	Tue 23/6/26	417SS+14 days
943	3rd Fix (fittings)	30 days	Mon 27/7/26	Mon 31/8/26	426SS+14 days
944	**Level 8**	**380 days**	**Wed 18/6/25**	**Thu 17/9/26**	
945	Mat'l & Shopdrawing Submission/Approval	90 days	Wed 18/6/25	Wed 1/10/25	
946	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**203 days**	**Thu 15/1/26**	**Thu 17/9/26**	
947	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Thu 15/1/26	Fri 20/2/26	212SS+14 days
948	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Sat 6/6/26	Fri 10/7/26	432SS+14 days
949	3rd Fix (fittings)	30 days	Fri 14/8/26	Thu 17/9/26	441SS+14 days
950	**Electrical/PA/IT/Fire alarm**	**203 days**	**Thu 15/1/26**	**Thu 17/9/26**	
951	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Thu 15/1/26	Fri 20/2/26	212SS+14 days
952	2nd Fix (concealed/surface (pipes/conduit),cable containment, wirings)	30 days	Sat 6/6/26	Fri 10/7/26	432SS+14 days
953	3rd Fix (fittings)	30 days	Fri 14/8/26	Thu 17/9/26	441SS+14 days
954	**ACMV**	**203 days**	**Thu 15/1/26**	**Thu 17/9/26**	
955	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Thu 15/1/26	Fri 20/2/26	212SS+14 days
956	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Sat 6/6/26	Fri 10/7/26	432SS+14 days
957	3rd Fix (fittings)	30 days	Fri 14/8/26	Thu 17/9/26	441SS+14 days

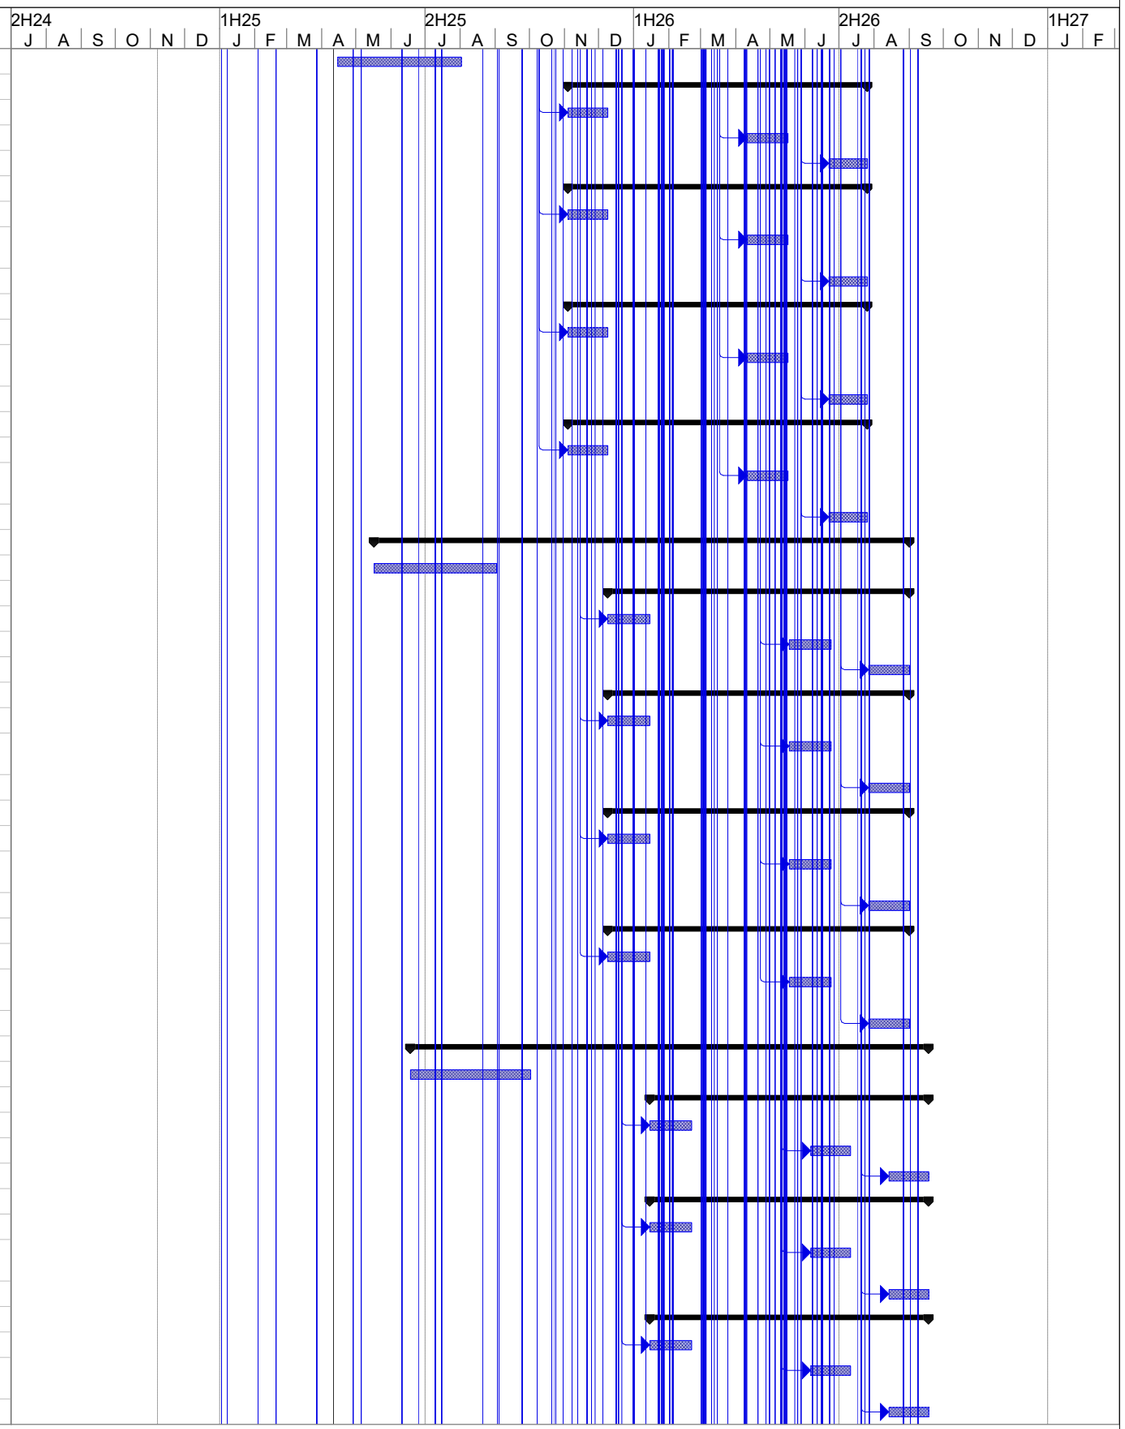

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	


ID	Task Name	Duration	Start	Finish	Predecessors
958	**Fire Protection - Sprinkler System**	**203 days**	**Thu 15/1/26**	**Thu 17/9/26**	
959	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Thu 15/1/26	Fri 20/2/26	212SS+14 days
960	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Sat 6/6/26	Fri 10/7/26	432SS+14 days
961	3rd Fix (fittings)	30 days	Fri 14/8/26	Thu 17/9/26	441SS+14 days
962	**Level 9**	**345 days**	**Fri 18/7/25**	**Mon 7/9/26**	
963	Mat'l & Shopdrawing Submission/Approval	90 days	Fri 18/7/25	Sat 1/11/25	
964	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**164 days**	**Sat 21/2/26**	**Mon 7/9/26**	
965	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Sat 21/2/26	Sat 28/3/26	213SS+14 days
966	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Sat 6/6/26	Fri 10/7/26	447SS+14 days
967	3rd Fix (fittings)	21 days	Fri 14/8/26	Mon 7/9/26	455SS+14 days
968	**Electrical/PA/IT/Fire alarm**	**164 days**	**Sat 21/2/26**	**Mon 7/9/26**	
969	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Sat 21/2/26	Sat 28/3/26	213SS+14 days
970	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Sat 6/6/26	Fri 10/7/26	447SS+14 days
971	3rd Fix (fittings)	21 days	Fri 14/8/26	Mon 7/9/26	455SS+14 days
972	**ACMV**	**164 days**	**Sat 21/2/26**	**Mon 7/9/26**	
973	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Sat 21/2/26	Sat 28/3/26	213SS+14 days
974	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Sat 6/6/26	Fri 10/7/26	447SS+14 days
975	3rd Fix (fittings)	21 days	Fri 14/8/26	Mon 7/9/26	455SS+14 days
976	**Fire Protection - Sprinkler System**	**164 days**	**Sat 21/2/26**	**Mon 7/9/26**	
977	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Sat 21/2/26	Sat 28/3/26	213SS+14 days
978	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Sat 6/6/26	Fri 10/7/26	447SS+14 days
979	3rd Fix (fittings)	21 days	Fri 14/8/26	Mon 7/9/26	455SS+14 days
980	**Lower Roof**	**298 days**	**Wed 17/9/25**	**Fri 11/9/26**	
981	Mat'l & Shopdrawing Submission/Approval	90 days	Wed 17/9/25	Fri 2/1/26	
982	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**138 days**	**Mon 30/3/26**	**Fri 11/9/26**	
983	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Mon 30/3/26	Tue 5/5/26	214SS+14 days
984	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Thu 11/6/26	Wed 15/7/26	461SS+14 days
985	3rd Fix (fittings)	21 days	Wed 19/8/26	Fri 11/9/26	466
986	**Electrical/PA/IT/Fire alarm**	**138 days**	**Mon 30/3/26**	**Fri 11/9/26**	
987	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Mon 30/3/26	Tue 5/5/26	214SS+14 days
988	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Thu 11/6/26	Wed 15/7/26	461SS+14 days
989	3rd Fix (fittings)	21 days	Wed 19/8/26	Fri 11/9/26	466
990	**ACMV**	**138 days**	**Mon 30/3/26**	**Fri 11/9/26**	
991	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Mon 30/3/26	Tue 5/5/26	214SS+14 days
992	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Thu 11/6/26	Wed 15/7/26	461SS+14 days
993	3rd Fix (fittings)	21 days	Wed 19/8/26	Fri 11/9/26	466
994	**Fire Protection - Sprinkler System**	**138 days**	**Mon 30/3/26**	**Fri 11/9/26**	
995	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Mon 30/3/26	Tue 5/5/26	214SS+14 days
996	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Thu 11/6/26	Wed 15/7/26	461SS+14 days
997	3rd Fix (fittings)	21 days	Wed 19/8/26	Fri 11/9/26	466
998	**Upper Roof**	**306 days**	**Fri 17/10/25**	**Wed 21/10/26**	
999	Mat'l & Shopdrawing Submission/Approval	90 days	Fri 17/10/25	Mon 2/2/26	
1000	**Electrical/PA/IT/Fire alarm**	**142 days**	**Wed 6/5/26**	**Wed 21/10/26**	
1001	1st Fix (concealed piping&conduit, pipe sleeve)	21 days	Wed 6/5/26	Sat 30/5/26	215SS+14 days
1002	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Thu 17/9/26	Wed 21/10/26	474SS+7 days
1003	3rd Fix (fittings)	14 days	Thu 17/9/26	Fri 2/10/26	474SS+7 days
1004	**Fire Protection - Sprinkler System**	**142 days**	**Wed 6/5/26**	**Wed 21/10/26**	
1005	1st Fix (concealed piping&conduit, pipe sleeve)	21 days	Wed 6/5/26	Sat 30/5/26	215SS+14 days
1006	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Thu 17/9/26	Wed 21/10/26	474SS+7 days

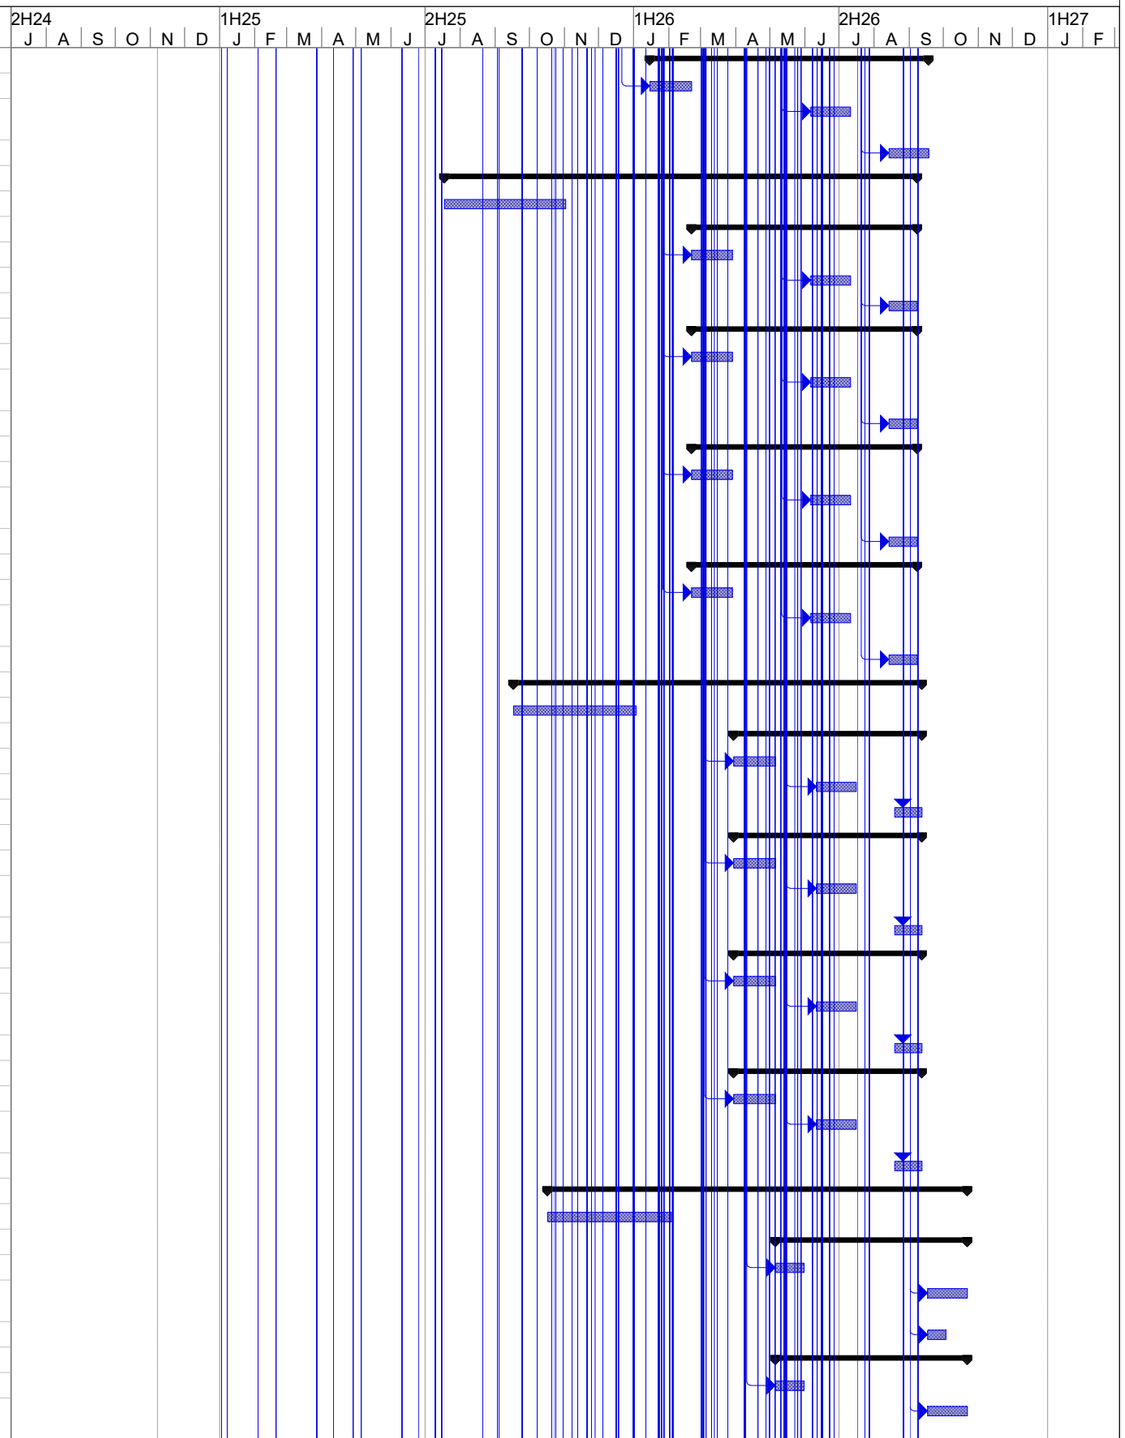

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task | Split | Milestone | Summary
Project Summary | External Tasks | External Milestone | Inactive Milestone
Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup
Manual Summary | Start-only | Finish-only | External Tasks
External Milestone | Progress | Deadline


ID	Task Name	Duration	Start	Finish	Predecessors
1007	3rd Fix (fittings)	14 days	Thu 17/9/26	Fri 2/10/26	474SS+7 days
1008	**Lifts (3 Nos) -FL2, BL2, FL3/BL3**	**588 days**	**Tue 1/10/24**	**Thu 10/9/26**	
1009	Submissions/Approval	77 days	Tue 1/10/24	Mon 30/12/24	
1010	Procurement/fabrication/shipment	240 days	Fri 29/8/25	Tue 16/6/26	1009FS+198 days
1011	**Site installations including T&C**	**92 days**	**Sat 23/5/26**	**Thu 10/9/26**	
1012	Lift shafts handover	7 days	Sat 23/5/26	Tue 2/6/26	215FS+14 days
1013	Preparation works inclu. Lift shaft verticality check & rectification work if any	15 days	Wed 3/6/26	Fri 19/6/26	1012
1014	Guardrails installations	19 days	Sat 20/6/26	Sat 11/7/26	1013,1010
1015	Landing sill, door frames installations, lift door & door jambs installations	13 days	Mon 13/7/26	Mon 27/7/26	1014
1016	Slow speed testing	12 days	Tue 28/7/26	Tue 11/8/26	1015
1017	Lift interior decorations & high speed testing	13 days	Wed 12/8/26	Wed 26/8/26	1016
1018	Final T&C (Including hot test)	13 days	Thu 27/8/26	Thu 10/9/26	1017
1019	**Part 2 - GL PE-RW/RW-8**	**614 days**	**Thu 8/8/24**	**Wed 19/8/26**	
1020	**Basement**	**562 days**	**Thu 8/8/24**	**Thu 18/6/26**	
1021	Mat'l & Shopdrawing Submission/Approval	90 days	Thu 8/8/24	Fri 22/11/24	
1022	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**421 days**	**Thu 23/1/25**	**Thu 18/6/26**	
1023	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Thu 23/1/25	Fri 28/2/25	230SS+7 days
1024	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Fri 21/11/25	Fri 26/12/25	482FS+14 days
1025	3rd Fix (fittings)	30 days	Wed 13/5/26	Thu 18/6/26	488SS+7 days
1026	**Electrical/PA/IT/Fire alarm**	**414 days**	**Mon 3/2/25**	**Thu 18/6/26**	
1027	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Mon 3/2/25	Sat 8/3/25	230SS+14 days
1028	2nd Fix (concealed/surface (pipes/conduit),cable containment, wirings)	30 days	Fri 21/11/25	Fri 26/12/25	482FS+14 days
1029	3rd Fix (fittings)	30 days	Wed 13/5/26	Thu 18/6/26	488SS+7 days
1030	**ACMV**	**414 days**	**Mon 3/2/25**	**Thu 18/6/26**	
1031	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Mon 3/2/25	Sat 8/3/25	230SS+14 days
1032	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Fri 21/11/25	Fri 26/12/25	482FS+14 days
1033	3rd Fix (fittings)	30 days	Wed 13/5/26	Thu 18/6/26	488SS+7 days
1034	**Fire Protection - Sprinkler System**	**414 days**	**Mon 3/2/25**	**Thu 18/6/26**	
1035	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Mon 3/2/25	Sat 8/3/25	230SS+14 days
1036	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Fri 21/11/25	Fri 26/12/25	482FS+14 days
1037	3rd Fix (fittings)	30 days	Wed 13/5/26	Thu 18/6/26	488SS+7 days
1038	**Level 1**	**508 days**	**Wed 18/9/24**	**Sat 23/5/26**	
1039	Mat'l & Shopdrawing Submission/Approval	90 days	Wed 18/9/24	Thu 2/1/25	
1040	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**359 days**	**Sat 15/3/25**	**Sat 23/5/26**	
1041	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Sat 15/3/25	Mon 21/4/25	234SS+14 days
1042	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Mon 12/1/26	Sat 14/2/26	491SS+14 days
1043	3rd Fix (fittings)	30 days	Sat 18/4/26	Sat 23/5/26	500SS+14 days
1044	**Electrical/PA/IT/Fire alarm**	**359 days**	**Sat 15/3/25**	**Sat 23/5/26**	
1045	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Sat 15/3/25	Mon 21/4/25	234SS+14 days
1046	2nd Fix (concealed/surface (pipes/conduit),cable containment, wirings)	30 days	Mon 12/1/26	Sat 14/2/26	491SS+14 days
1047	3rd Fix (fittings)	30 days	Sat 18/4/26	Sat 23/5/26	500SS+14 days
1048	**ACMV**	**359 days**	**Sat 15/3/25**	**Sat 23/5/26**	
1049	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Sat 15/3/25	Mon 21/4/25	234SS+14 days
1050	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Mon 12/1/26	Sat 14/2/26	491SS+14 days
1051	2nd Fix (piping/conduit, cable containment, wirings, flex. sprinkler)	30 days	Mon 12/1/26	Sat 14/2/26	491SS+14 days
1052	3rd Fix (fittings)	30 days	Sat 18/4/26	Sat 23/5/26	500SS+14 days
1053	**Fire Protection - Sprinkler System**	**359 days**	**Sat 15/3/25**	**Sat 23/5/26**	
1054	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Sat 15/3/25	Mon 21/4/25	234SS+14 days
1055	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Mon 12/1/26	Sat 14/2/26	491SS+14 days

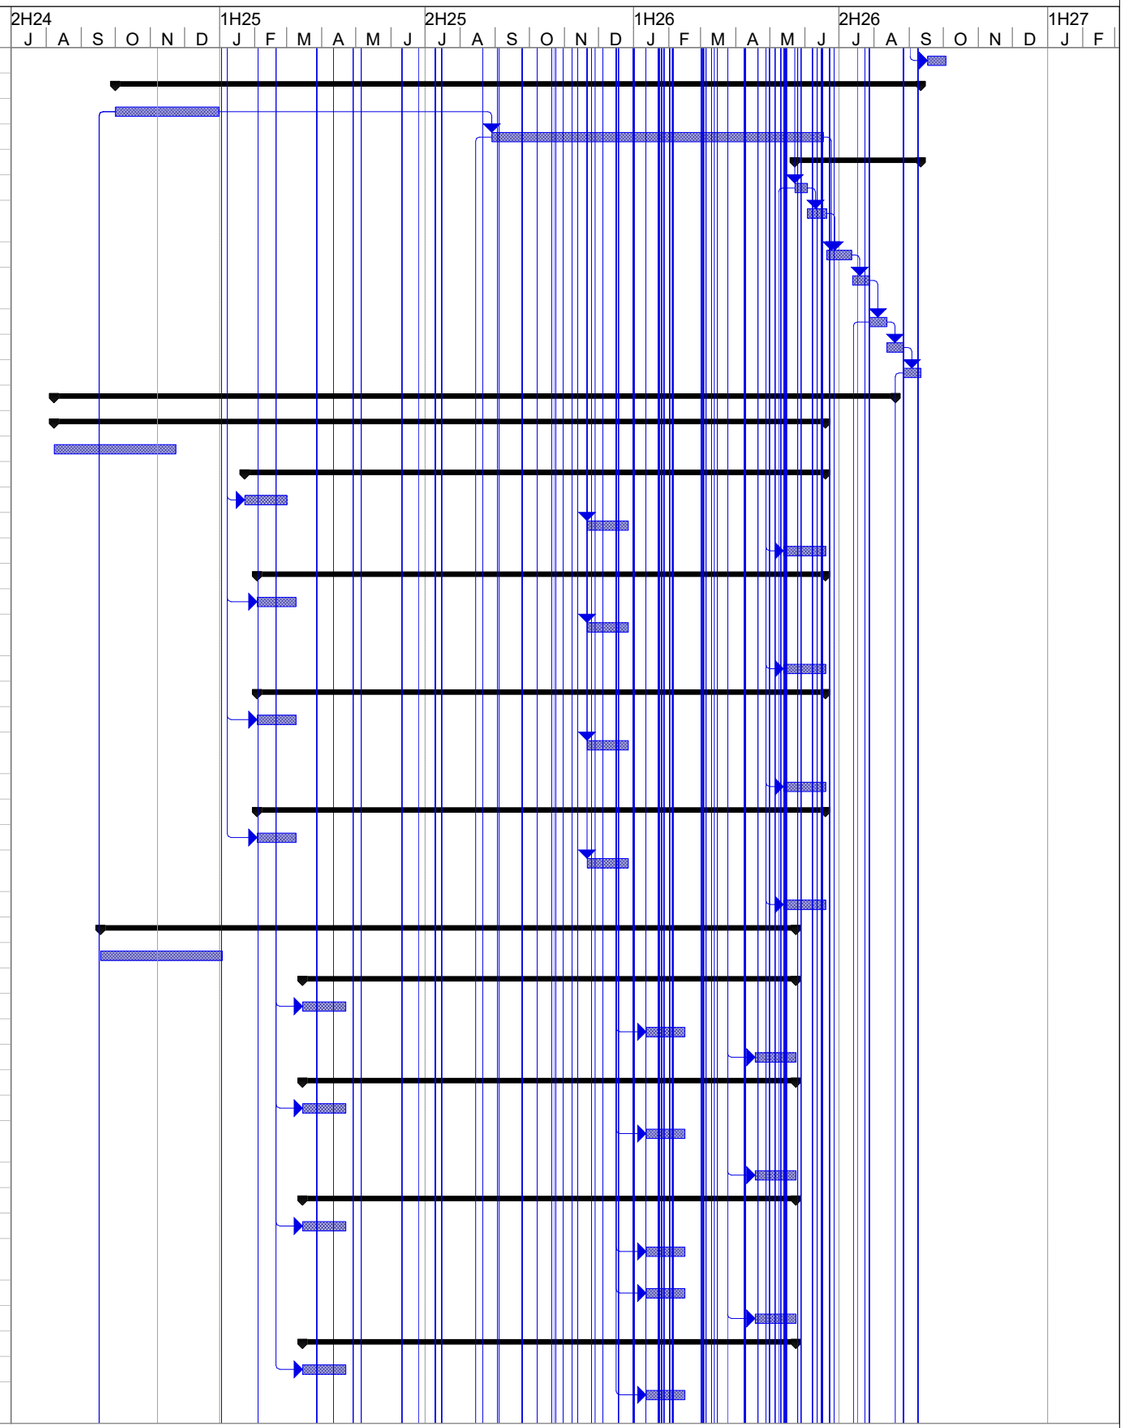

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone	
Split	External Tasks	Manual Task	Start-only	Progress	
Milestone	External Milestone	Duration-only	Finish-only	Deadline	
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks		


ID	Task Name	Duration	Start	Finish	Predecessors
1056	3rd Fix (fittings)	30 days	Sat 18/4/26	Sat 23/5/26	500SS+14 days
1057	**Level 2**	**514 days**	**Wed 16/10/24**	**Tue 30/6/26**	
1058	Mat'l & Shopdrawing Submission/Approval	90 days	Wed 16/10/24	Sat 1/2/25	
1059	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**329 days**	**Thu 29/5/25**	**Tue 30/6/26**	
1060	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Thu 29/5/25	Thu 3/7/25	235SS+14 days
1061	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Mon 16/2/26	Wed 25/3/26	506SS+14 days
1062	3rd Fix (fittings)	30 days	Mon 25/5/26	Tue 30/6/26	515SS+14 days
1063	**Electrical/PA/IT/Fire alarm**	**329 days**	**Thu 29/5/25**	**Tue 30/6/26**	
1064	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Thu 29/5/25	Thu 3/7/25	235SS+14 days
1065	2nd Fix (concealed/surface (pipes/conduit),cable containment, wirings)	30 days	Mon 16/2/26	Wed 25/3/26	506SS+14 days
1066	3rd Fix (fittings)	30 days	Mon 25/5/26	Tue 30/6/26	515SS+14 days
1067	**ACMV**	**329 days**	**Thu 29/5/25**	**Tue 30/6/26**	
1068	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Thu 29/5/25	Thu 3/7/25	235SS+14 days
1069	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Mon 16/2/26	Wed 25/3/26	506SS+14 days
1070	2nd Fix (piping/conduit, cable containment, wirings, flex. sprinkler)	30 days	Mon 16/2/26	Wed 25/3/26	506SS+14 days
1071	3rd Fix (fittings)	30 days	Mon 25/5/26	Tue 30/6/26	515SS+14 days
1072	**Fire Protection - Sprinkler System**	**329 days**	**Thu 29/5/25**	**Tue 30/6/26**	
1073	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Thu 29/5/25	Thu 3/7/25	235SS+14 days
1074	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Mon 16/2/26	Wed 25/3/26	506SS+14 days
1075	3rd Fix (fittings)	30 days	Mon 25/5/26	Tue 30/6/26	515SS+14 days
1076	**Level 3**	**444 days**	**Mon 13/1/25**	**Sat 4/7/26**	
1077	Mat'l & Shopdrawing Submission/Approval	90 days	Mon 13/1/25	Fri 2/5/25	
1078	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**273 days**	**Fri 8/8/25**	**Sat 4/7/26**	
1079	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Fri 8/8/25	Fri 12/9/25	236SS+14 days
1080	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Mon 23/2/26	Mon 30/3/26	521SS+14 days
1081	3rd Fix (fittings)	30 days	Sat 30/5/26	Sat 4/7/26	529SS+14 days
1082	**Electrical/PA/IT/Fire alarm**	**273 days**	**Fri 8/8/25**	**Sat 4/7/26**	
1083	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Fri 8/8/25	Fri 12/9/25	236SS+14 days
1084	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Mon 23/2/26	Mon 30/3/26	521SS+14 days
1085	3rd Fix (fittings)	30 days	Sat 30/5/26	Sat 4/7/26	529SS+14 days
1086	**ACMV**	**273 days**	**Fri 8/8/25**	**Sat 4/7/26**	
1087	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Fri 8/8/25	Fri 12/9/25	236SS+14 days
1088	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Mon 23/2/26	Mon 30/3/26	521SS+14 days
1089	2nd Fix (piping/conduit, cable containment, wirings, flex. sprinkler)	30 days	Mon 23/2/26	Mon 30/3/26	521SS+14 days
1090	3rd Fix (fittings)	30 days	Sat 30/5/26	Sat 4/7/26	529SS+14 days
1091	**Fire Protection - Sprinkler System**	**273 days**	**Fri 8/8/25**	**Sat 4/7/26**	
1092	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Fri 8/8/25	Fri 12/9/25	236SS+14 days
1093	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Mon 23/2/26	Mon 30/3/26	521SS+14 days
1094	3rd Fix (fittings)	30 days	Sat 30/5/26	Sat 4/7/26	529SS+14 days
1095	**Lower Roof**	**399 days**	**Thu 13/3/25**	**Thu 9/7/26**	
1096	Mat'l & Shopdrawing Submission/Approval incl. Cooling Tower	90 days	Thu 13/3/25	Tue 1/7/25	
1097	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**217 days**	**Sat 18/10/25**	**Thu 9/7/26**	
1098	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Sat 18/10/25	Sat 22/11/25	237SS+14 days
1099	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Fri 27/2/26	Sat 4/4/26	536SS+14 days
1100	3rd Fix (fittings)	30 days	Fri 5/6/26	Thu 9/7/26	541SS+14 days
1101	**Electrical/PA/IT/Fire alarm**	**217 days**	**Sat 18/10/25**	**Thu 9/7/26**	
1102	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Sat 18/10/25	Sat 22/11/25	237SS+14 days
1103	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Fri 27/2/26	Sat 4/4/26	536SS+14 days
1104	3rd Fix (fittings)	30 days	Fri 5/6/26	Thu 9/7/26	541SS+14 days
1105	**ACMV**	**217 days**	**Sat 18/10/25**	**Thu 9/7/26**	

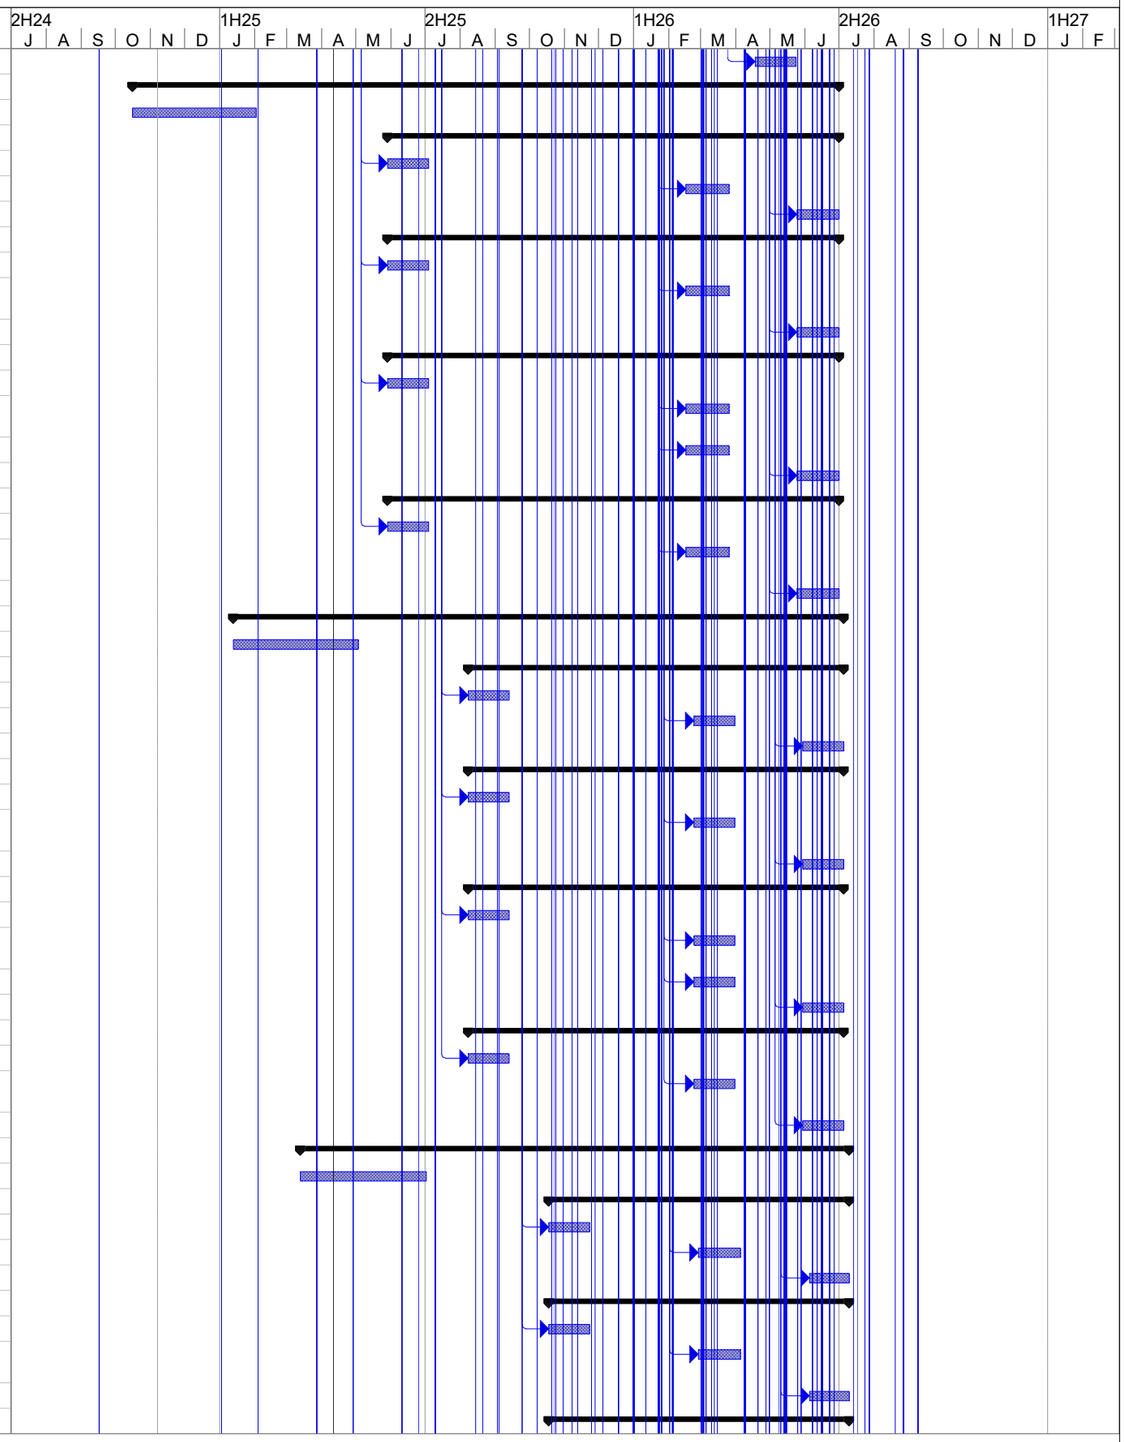

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Progress
Deadline


ID	Task Name	Duration	Start	Finish	Predecessors
1106	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Sat 18/10/25	Sat 22/11/25	237SS+14 days
1107	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Fri 27/2/26	Sat 4/4/26	536SS+14 days
1108	3rd Fix (fittings)	30 days	Fri 5/6/26	Thu 9/7/26	541SS+14 days
1109	**Fire Protection - Sprinkler System**	**217 days**	**Sat 18/10/25**	**Thu 9/7/26**	
1110	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Sat 18/10/25	Sat 22/11/25	237SS+14 days
1111	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Fri 27/2/26	Sat 4/4/26	536SS+14 days
1112	3rd Fix (fittings)	30 days	Fri 5/6/26	Thu 9/7/26	541SS+14 days
1113	**Upper Roof**	**381 days**	**Sat 17/5/25**	**Wed 19/8/26**	
1114	Mat'l & Shopdrawing Submission/Approval	90 days	Sat 17/5/25	Mon 1/9/25	
1115	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**191 days**	**Tue 30/12/25**	**Wed 19/8/26**	
1116	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Tue 30/12/25	Tue 3/2/26	238SS+14 days
1117	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Wed 10/6/26	Tue 14/7/26	551SS+7 days
1118	3rd Fix (fittings)	30 days	Wed 15/7/26	Wed 19/8/26	1117
1119	**Electrical/PA/IT/Fire alarm**	**191 days**	**Tue 30/12/25**	**Wed 19/8/26**	
1120	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Tue 30/12/25	Tue 3/2/26	238SS+14 days
1121	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Wed 10/6/26	Tue 14/7/26	551SS+7 days
1122	3rd Fix (fittings)	30 days	Wed 15/7/26	Wed 19/8/26	1121
1123	**ACMV**	**191 days**	**Tue 30/12/25**	**Wed 19/8/26**	
1124	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Tue 30/12/25	Tue 3/2/26	238SS+14 days
1125	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Wed 10/6/26	Tue 14/7/26	551SS+7 days
1126	3rd Fix (fittings)	30 days	Wed 15/7/26	Wed 19/8/26	1125
1127	**Fire Protection - Sprinkler System**	**191 days**	**Tue 30/12/25**	**Wed 19/8/26**	
1128	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Tue 30/12/25	Tue 3/2/26	238SS+14 days
1129	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Wed 10/6/26	Tue 14/7/26	551SS+7 days
1130	3rd Fix (fittings)	30 days	Wed 15/7/26	Wed 19/8/26	1129
1131	**Lifts (1 No) - FL4**	**492 days**	**Tue 1/10/24**	**Mon 18/5/26**	
1132	Submissions/Approval	77 days	Tue 1/10/24	Mon 30/12/24	
1133	Procurement/fabrication/shipment	240 days	Fri 14/3/25	Sat 27/12/25	1132FS+60 days
1134	**Site installations including T&C**	**84 days**	**Wed 4/2/26**	**Mon 18/5/26**	
1135	Lift shafts handover	7 days	Wed 4/2/26	Wed 11/2/26	238FS+14 days
1136	Preparation works inclu. Lift shaft verticality check & rectification work if any	11 days	Thu 12/2/26	Thu 26/2/26	1135
1137	Guardrails installations	18 days	Fri 27/2/26	Thu 19/3/26	1133,1136
1138	Landing sill, door frames installations, lift door & door jambs installations	12 days	Sat 21/3/26	Sat 4/4/26	1137
1139	Slow speed testing	12 days	Mon 6/4/26	Sat 18/4/26	1138
1140	Lift interior decorations & high speed testing	12 days	Mon 20/4/26	Mon 4/5/26	1139
1141	Final T&C (Including hot test)	12 days	Tue 5/5/26	Mon 18/5/26	1140
1142	**Part 3 - GL RW-PE/RW-8**	**674 days**	**Thu 8/8/24**	**Wed 28/10/26**	
1143	**Basement**	**562 days**	**Thu 8/8/24**	**Thu 18/6/26**	
1144	Mat'l & Shopdrawing Submission/Approval including Chiller System & AHUs	90 days	Thu 8/8/24	Fri 22/11/24	
1145	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**418 days**	**Mon 27/1/25**	**Thu 18/6/26**	
1146	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Mon 27/1/25	Tue 4/3/25	253SS+14 days
1147	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Tue 2/12/25	Wed 7/1/26	556SS+14 days
1148	3rd Fix (fittings)	30 days	Wed 13/5/26	Thu 18/6/26	562SS+7 days
1149	**Electrical/PA/IT/Fire alarm**	**411 days**	**Thu 6/2/25**	**Thu 18/6/26**	
1150	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Thu 6/2/25	Wed 12/3/25	253SS+14 days
1151	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Tue 2/12/25	Wed 7/1/26	556SS+14 days
1152	3rd Fix (fittings)	30 days	Wed 13/5/26	Thu 18/6/26	562SS+7 days
1153	**ACMV**	**418 days**	**Mon 27/1/25**	**Thu 18/6/26**	
1154	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Mon 27/1/25	Tue 4/3/25	253SS+14 days

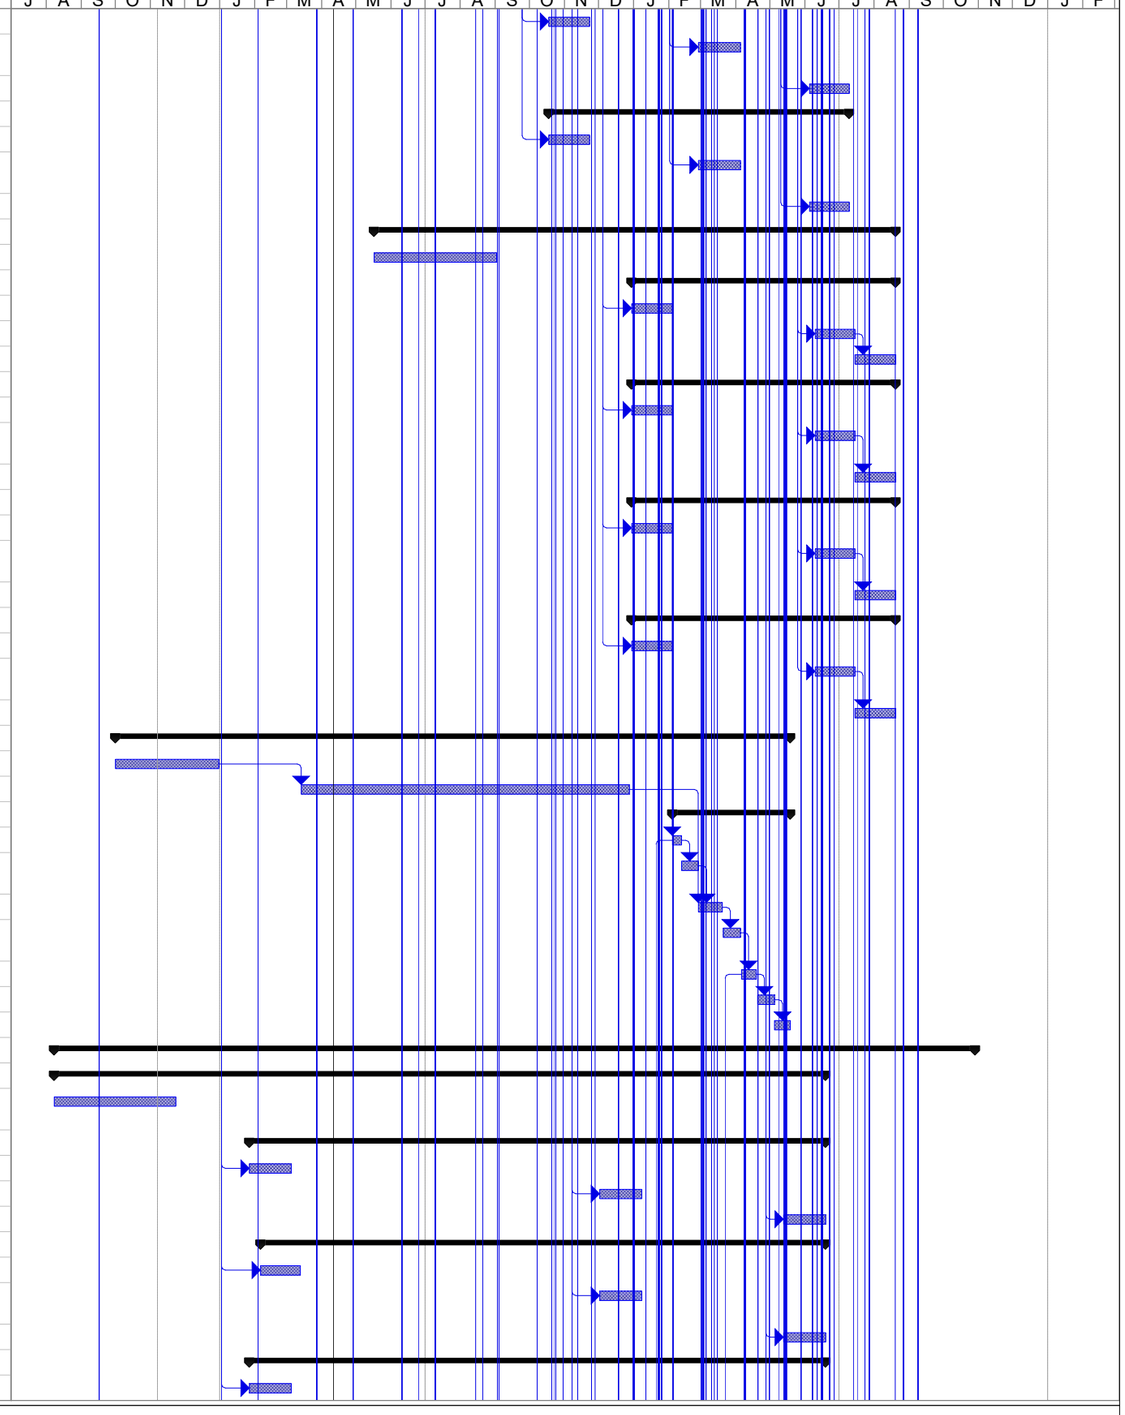

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Progress
Deadline


ID	Task Name	Duration	Start	Finish	Predecessors
1155	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Tue 2/12/25	Wed 7/1/26	556SS+14 days
1156	3rd Fix (fittings)	30 days	Wed 13/5/26	Thu 18/6/26	562SS+7 days
1157	**Fire Protection - Sprinkler System**	**418 days**	**Mon 27/1/25**	**Thu 18/6/26**	
1158	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Mon 27/1/25	Tue 4/3/25	253SS+14 days
1159	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Tue 2/12/25	Wed 7/1/26	556SS+14 days
1160	3rd Fix (fittings)	30 days	Wed 13/5/26	Thu 18/6/26	562SS+7 days
1161	**Level 1**	**538 days**	**Wed 18/9/24**	**Tue 30/6/26**	
1162	Mat'l & Shopdrawing Submission/Approval	90 days	Wed 18/9/24	Thu 2/1/25	
1163	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**359 days**	**Tue 22/4/25**	**Tue 30/6/26**	
1164	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Tue 22/4/25	Wed 28/5/25	261SS+14 days
1165	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Mon 16/2/26	Wed 25/3/26	565SS+14 days
1166	3rd Fix (fittings)	30 days	Mon 25/5/26	Tue 30/6/26	573SS+14 days
1167	**Electrical/PA/IT/Fire alarm**	**359 days**	**Tue 22/4/25**	**Tue 30/6/26**	
1168	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Tue 22/4/25	Wed 28/5/25	261SS+14 days
1169	2nd Fix (concealed/surface (pipes/conduit),cable containment, wirings)	30 days	Mon 16/2/26	Wed 25/3/26	565SS+14 days
1170	3rd Fix (fittings)	30 days	Mon 25/5/26	Tue 30/6/26	573SS+14 days
1171	**ACMV**	**359 days**	**Tue 22/4/25**	**Tue 30/6/26**	
1172	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Tue 22/4/25	Wed 28/5/25	261SS+14 days
1173	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Mon 16/2/26	Wed 25/3/26	565SS+14 days
1174	3rd Fix (fittings)	30 days	Mon 25/5/26	Tue 30/6/26	573SS+14 days
1175	**Fire Protection - Sprinkler System**	**359 days**	**Tue 22/4/25**	**Tue 30/6/26**	
1176	1st Fix (concealed piping & conduit, pipe sleeve)	30 days	Tue 22/4/25	Wed 28/5/25	261SS+14 days
1177	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Mon 16/2/26	Wed 25/3/26	565SS+14 days
1178	3rd Fix (fittings)	30 days	Mon 25/5/26	Tue 30/6/26	573SS+14 days
1179	**Level 2**	**495 days**	**Thu 12/12/24**	**Tue 4/8/26**	
1180	Mat'l & Shopdrawing Submission/Approval	90 days	Thu 12/12/24	Tue 1/4/25	
1181	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**329 days**	**Fri 4/7/25**	**Tue 4/8/26**	
1182	1st Fix (concealed piping& conduit, pipe sleeve)	30 days	Fri 4/7/25	Thu 7/8/25	262SS+14 days
1183	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Thu 26/3/26	Thu 30/4/26	579SS+14 days
1184	3rd Fix (fittings)	30 days	Wed 1/7/26	Tue 4/8/26	588SS+14 days
1185	**Electrical/PA/IT/Fire alarm**	**329 days**	**Fri 4/7/25**	**Tue 4/8/26**	
1186	1st Fix (concealed piping& conduit, pipe sleeve)	30 days	Fri 4/7/25	Thu 7/8/25	262SS+14 days
1187	2nd Fix (concealed/surface (pipes/conduit),cable containment, wirings)	30 days	Thu 26/3/26	Thu 30/4/26	579SS+14 days
1188	3rd Fix (fittings)	30 days	Wed 1/7/26	Tue 4/8/26	588SS+14 days
1189	**ACMV**	**329 days**	**Fri 4/7/25**	**Tue 4/8/26**	
1190	1st Fix (concealed piping& conduit, pipe sleeve)	30 days	Fri 4/7/25	Thu 7/8/25	262SS+14 days
1191	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Thu 26/3/26	Thu 30/4/26	579SS+14 days
1192	3rd Fix (fittings)	30 days	Wed 1/7/26	Tue 4/8/26	588SS+14 days
1193	**Fire Protection - Sprinkler System**	**329 days**	**Fri 4/7/25**	**Tue 4/8/26**	
1194	1st Fix (concealed piping& conduit, pipe sleeve)	30 days	Fri 4/7/25	Thu 7/8/25	262SS+14 days
1195	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Thu 26/3/26	Thu 30/4/26	579SS+14 days
1196	3rd Fix (fittings)	30 days	Wed 1/7/26	Tue 4/8/26	588SS+14 days
1197	**Level 3**	**449 days**	**Thu 13/2/25**	**Sat 8/8/26**	
1198	Mat'l & Shopdrawing Submission/Approval	90 days	Thu 13/2/25	Mon 2/6/25	
1199	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**273 days**	**Sat 13/9/25**	**Sat 8/8/26**	
1200	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Sat 13/9/25	Fri 17/10/25	263SS+14 days
1201	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Tue 31/3/26	Wed 6/5/26	594SS+14 days
1202	3rd Fix (fittings)	30 days	Mon 6/7/26	Sat 8/8/26	602SS+14 days
1203	**Electrical/PA/IT/Fire alarm**	**273 days**	**Sat 13/9/25**	**Sat 8/8/26**	

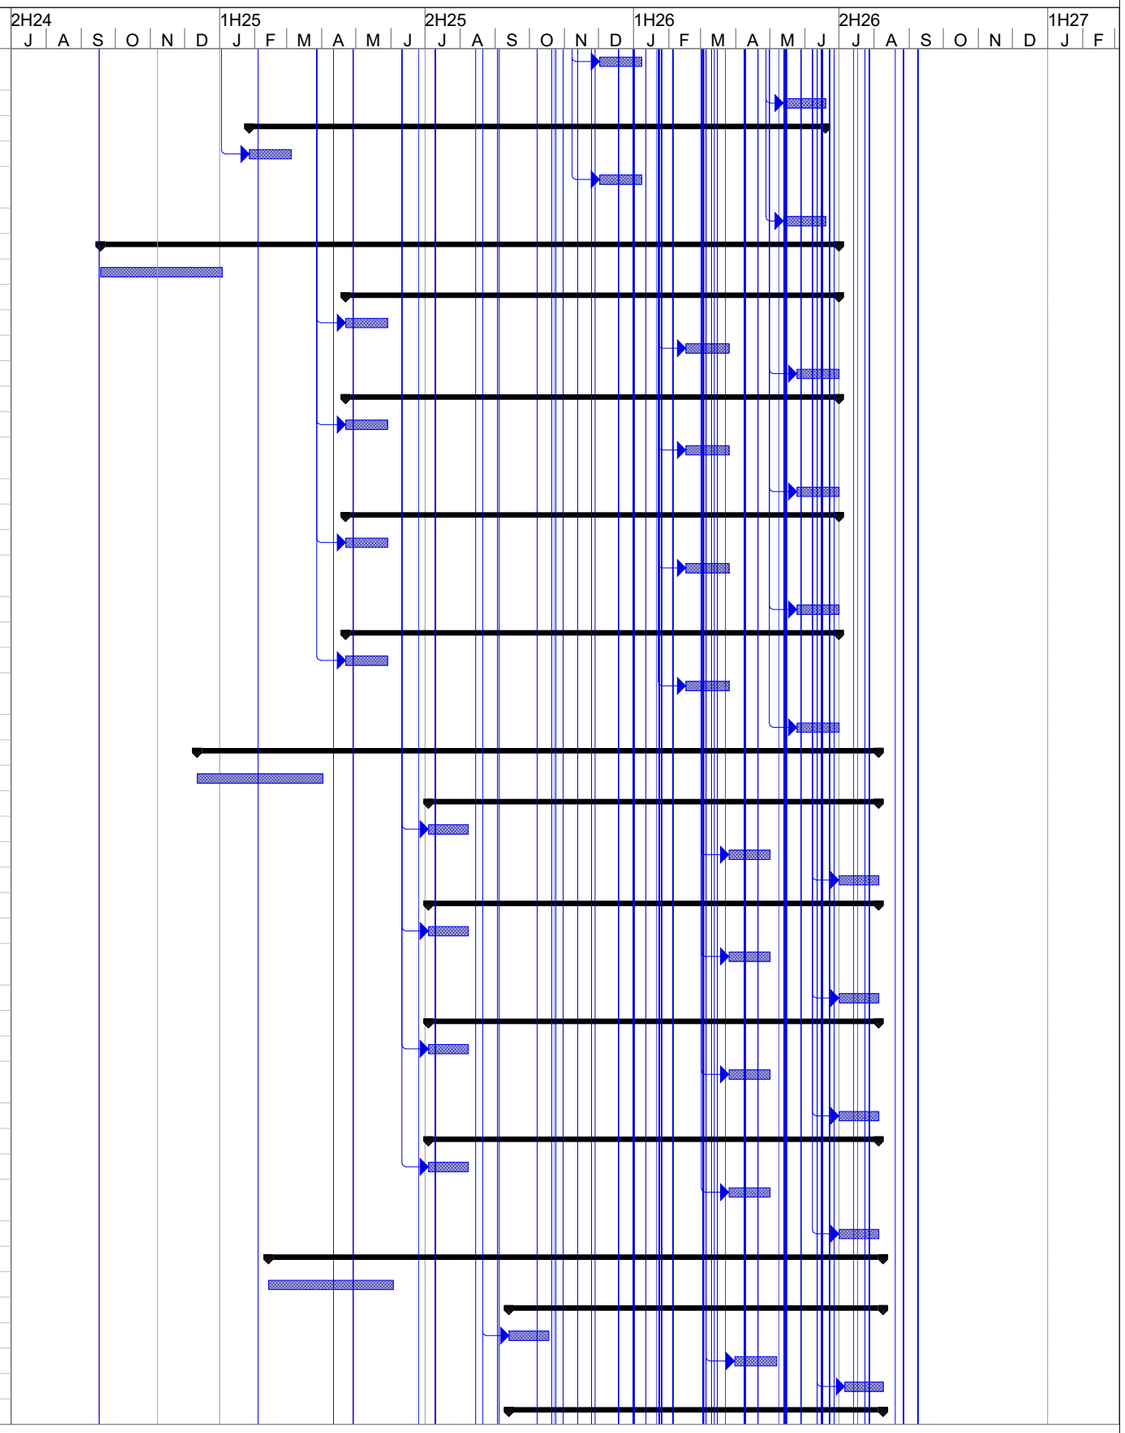

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Progress | Deadline


ID	Task Name	Duration	Start	Finish	Predecessors
1204	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Sat 13/9/25	Fri 17/10/25	263SS+14 days
1205	2nd Fix (concealed/surface (pipes/conduit),cable containment, wirings)	30 days	Tue 31/3/26	Wed 6/5/26	594SS+14 days
1206	3rd Fix (fittings)	30 days	Mon 6/7/26	Sat 8/8/26	602SS+14 days
1207	**ACMV**	**273 days**	**Sat 13/9/25**	**Sat 8/8/26**	
1208	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Sat 13/9/25	Fri 17/10/25	263SS+14 days
1209	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Tue 31/3/26	Wed 6/5/26	594SS+14 days
1210	3rd Fix (fittings)	30 days	Mon 6/7/26	Sat 8/8/26	602SS+14 days
1211	**Fire Protection - Sprinkler System**	**273 days**	**Sat 13/9/25**	**Sat 8/8/26**	
1212	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Sat 13/9/25	Fri 17/10/25	263SS+14 days
1213	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Tue 31/3/26	Wed 6/5/26	594SS+14 days
1214	3rd Fix (fittings)	30 days	Mon 6/7/26	Sat 8/8/26	602SS+14 days
1215	**Lower Roof**	**351 days**	**Wed 18/6/25**	**Fri 14/8/26**	
1216	Mat'l & Shopdrawing Submission/Approval	90 days	Wed 18/6/25	Wed 1/10/25	
1217	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**217 days**	**Mon 24/11/25**	**Fri 14/8/26**	
1218	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Mon 24/11/25	Mon 29/12/25	264SS+14 days
1219	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Mon 6/4/26	Mon 11/5/26	608SS+14 days
1220	3rd Fix (fittings)	30 days	Fri 10/7/26	Fri 14/8/26	613SS+14 days
1221	**Electrical/PA/IT/Fire alarm**	**217 days**	**Mon 24/11/25**	**Fri 14/8/26**	
1222	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Mon 24/11/25	Mon 29/12/25	264SS+14 days
1223	2nd Fix (concealed/surface (pipes/conduit),cable containment, wirings)	30 days	Mon 6/4/26	Mon 11/5/26	608SS+14 days
1224	3rd Fix (fittings)	30 days	Fri 10/7/26	Fri 14/8/26	613SS+14 days
1225	**ACMV**	**217 days**	**Mon 24/11/25**	**Fri 14/8/26**	
1226	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Mon 24/11/25	Mon 29/12/25	264SS+14 days
1227	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Mon 6/4/26	Mon 11/5/26	608SS+14 days
1228	3rd Fix (fittings)	30 days	Fri 10/7/26	Fri 14/8/26	613SS+14 days
1229	**Fire Protection - Sprinkler System**	**217 days**	**Mon 24/11/25**	**Fri 14/8/26**	
1230	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Mon 24/11/25	Mon 29/12/25	264SS+14 days
1231	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Mon 6/4/26	Mon 11/5/26	608SS+14 days
1232	3rd Fix (fittings)	30 days	Fri 10/7/26	Fri 14/8/26	613SS+14 days
1233	**Upper Roof**	**389 days**	**Fri 18/7/25**	**Wed 28/10/26**	
1234	Mat'l & Shopdrawing Submission/Approval	90 days	Fri 18/7/25	Sat 1/11/25	
1235	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**212 days**	**Wed 4/2/26**	**Sat 17/10/26**	
1236	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Wed 4/2/26	Thu 12/3/26	265SS+14 days
1237	2nd Fix (concealed/ surface(piping & conduit) with accessories)	21 days	Thu 24/9/26	Sat 17/10/26	623SS+7 days
1238	3rd Fix (fittings)	21 days	Thu 24/9/26	Sat 17/10/26	623SS+7 days
1239	**Electrical/PA/IT/Fire alarm**	**221 days**	**Wed 4/2/26**	**Wed 28/10/26**	
1240	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Wed 4/2/26	Thu 12/3/26	265SS+14 days
1241	2nd Fix (concealed/surface (pipes/conduit),cable containment, wirings)	30 days	Thu 24/9/26	Wed 28/10/26	623SS+7 days
1242	3rd Fix (fittings)	21 days	Thu 24/9/26	Sat 17/10/26	623SS+7 days
1243	**ACMV**	**221 days**	**Wed 4/2/26**	**Wed 28/10/26**	
1244	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Wed 4/2/26	Thu 12/3/26	265SS+14 days
1245	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Thu 24/9/26	Wed 28/10/26	623SS+7 days
1246	3rd Fix (fittings)	21 days	Thu 24/9/26	Sat 17/10/26	623SS+7 days
1247	**Fire Protection - Sprinkler System**	**221 days**	**Wed 4/2/26**	**Wed 28/10/26**	
1248	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Wed 4/2/26	Thu 12/3/26	265SS+14 days
1249	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Thu 24/9/26	Wed 28/10/26	623SS+7 days
1250	3rd Fix (fittings)	21 days	Thu 24/9/26	Sat 17/10/26	623SS+7 days
1251	**Lifts (4 Nos) - FL5, PL1, PL2 & PL3**	**526 days**	**Tue 1/10/24**	**Mon 29/6/26**	
1252	Submissions/Approval	77 days	Tue 1/10/24	Mon 30/12/24	

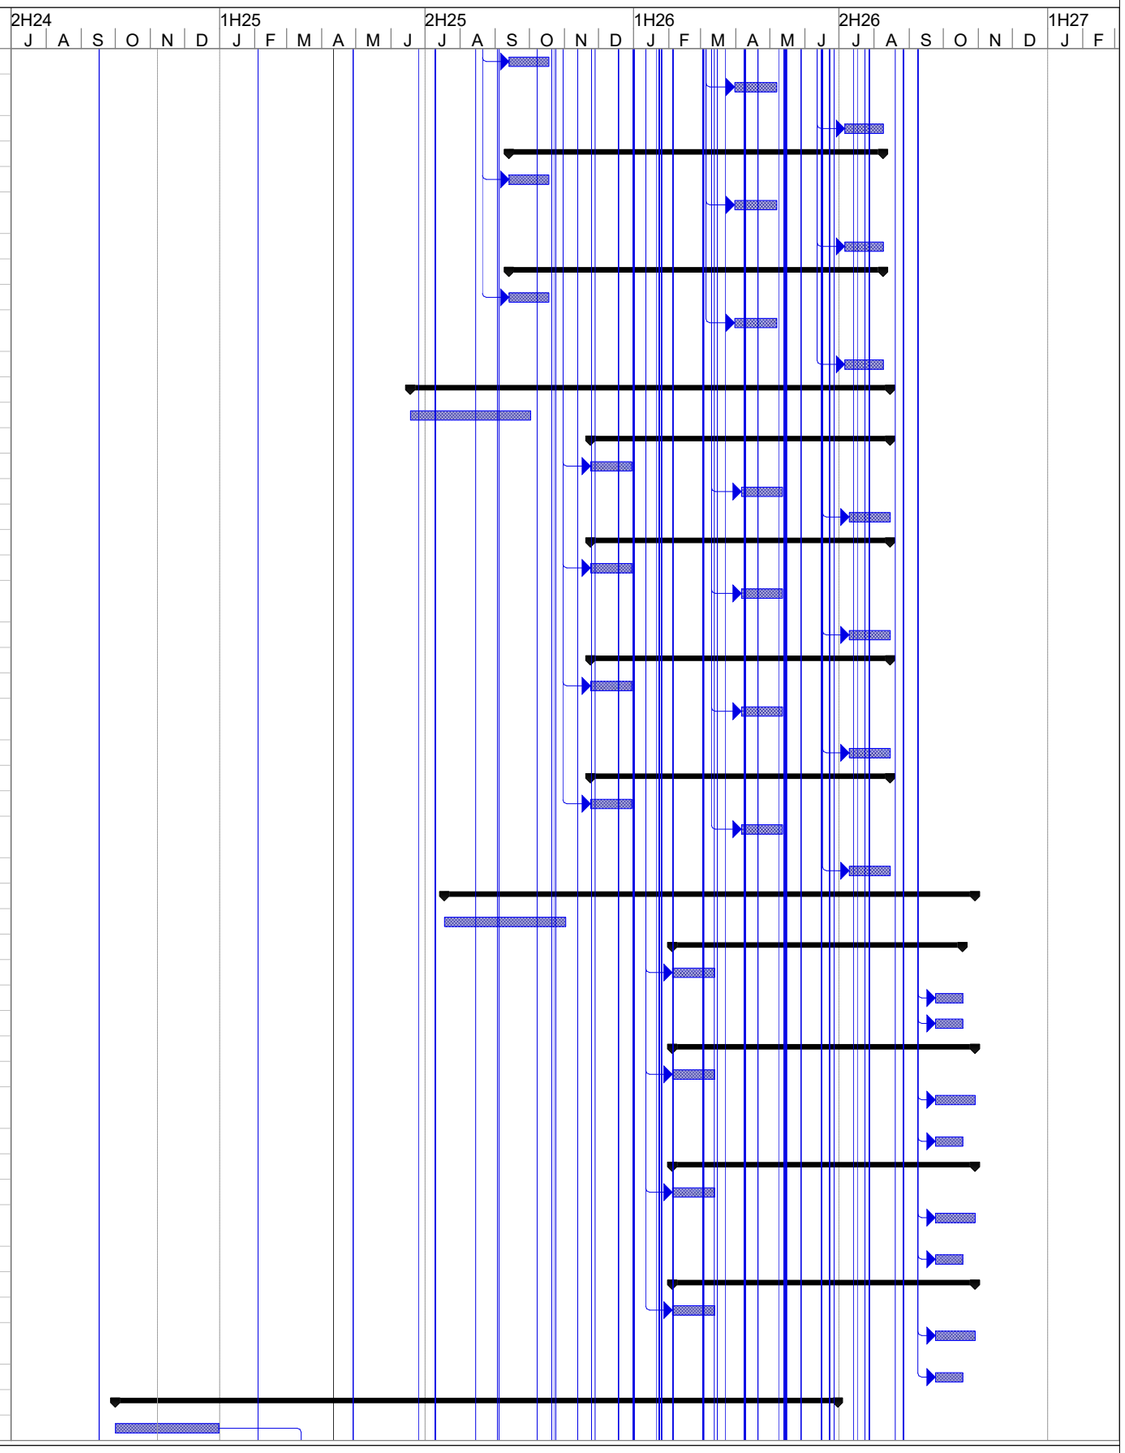

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Progress
Deadline


ID	Task Name	Duration	Start	Finish	Predecessors
1253	Procurement/fabrication/shipment	240 days	Fri 14/3/25	Sat 27/12/25	1252FS+60 days
1254	**Site installations including T&C**	**88 days**	**Fri 13/3/26**	**Mon 29/6/26**	
1255	Lift shafts handover	7 days	Fri 13/3/26	Sat 21/3/26	265FS+14 days
1256	Preparation works inclu. Lift shaft verticality check & rectification work if any	12 days	Mon 23/3/26	Mon 6/4/26	1255
1257	Guardrails installations	13 days	Tue 7/4/26	Tue 21/4/26	1253,1256
1258	Landing sill, door frames installations, lift door & door jambs installations	12 days	Wed 22/4/26	Wed 6/5/26	1257
1259	Slow speed testing	12 days	Thu 7/5/26	Wed 20/5/26	1258
1260	Lift interior decorations & high speed testing	19 days	Thu 21/5/26	Sat 13/6/26	1259
1261	Final T&C (Including hot test)	13 days	Mon 15/6/26	Mon 29/6/26	1260
1262	**Part 4 - GL RW-I/RW-20**	**670 days**	**Thu 8/8/24**	**Fri 23/10/26**	
1263	**Basement**	**594 days**	**Thu 8/8/24**	**Sat 25/7/26**	
1264	Mat'l & Shopdrawing Submission/Approval	90 days	Thu 8/8/24	Fri 22/11/24	
1265	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**425 days**	**Thu 27/2/25**	**Sat 25/7/26**	
1266	1st Fix (concealed piping, pipe sleeve)	30 days	Thu 27/2/25	Thu 3/4/25	282SS+14 days
1267	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Thu 13/11/25	Wed 17/12/25	637SS+14 days
1268	3rd Fix (fittings)	30 days	Mon 22/6/26	Sat 25/7/26	643SS+14 days
1269	**Electrical/PA/IT/Fire alarm**	**408 days**	**Thu 6/3/25**	**Mon 13/7/26**	
1270	1st Fix (concealed piping, pipe sleeve)	30 days	Thu 6/3/25	Thu 10/4/25	282SS+14 days
1271	2nd Fix (concealed/surface (pipes/conduit),cable containment, wirings)	30 days	Thu 13/11/25	Wed 17/12/25	637SS+14 days
1272	3rd Fix (fittings)	30 days	Tue 9/6/26	Mon 13/7/26	643SS+14 days
1273	**ACMV**	**408 days**	**Thu 6/3/25**	**Mon 13/7/26**	
1274	1st Fix (concealed piping, pipe sleeve)	30 days	Thu 6/3/25	Thu 10/4/25	282SS+14 days
1275	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Thu 13/11/25	Wed 17/12/25	637SS+14 days
1276	3rd Fix (fittings)	30 days	Tue 9/6/26	Mon 13/7/26	643SS+14 days
1277	**Fire Protection - Sprinkler System**	**213 days**	**Tue 28/10/25**	**Mon 13/7/26**	
1278	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Tue 28/10/25	Mon 1/12/25	282SS+14 days
1279	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Thu 13/11/25	Wed 17/12/25	637SS+14 days
1280	3rd Fix (fittings)	30 days	Tue 9/6/26	Mon 13/7/26	643SS+14 days
1281	**Level 1**	**437 days**	**Wed 16/10/24**	**Fri 27/3/26**	
1282	Mat'l & Shopdrawing Submission/Approval	90 days	Wed 16/10/24	Sat 1/2/25	
1283	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**257 days**	**Fri 23/5/25**	**Fri 27/3/26**	
1284	1st Fix (concealed piping, pipe sleeve)	30 days	Fri 23/5/25	Fri 27/6/25	290SS+14 days
1285	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Thu 18/12/25	Fri 23/1/26	647SS+14 days
1286	3rd Fix (fittings)	30 days	Fri 20/2/26	Fri 27/3/26	655SS+14 days
1287	**Electrical/PA/IT/Fire alarm**	**257 days**	**Fri 23/5/25**	**Fri 27/3/26**	
1288	1st Fix (concealed piping, pipe sleeve)	30 days	Fri 23/5/25	Fri 27/6/25	290SS+14 days
1289	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Thu 18/12/25	Fri 23/1/26	647SS+14 days
1290	3rd Fix (fittings)	30 days	Fri 20/2/26	Fri 27/3/26	655SS+14 days
1291	**ACMV**	**257 days**	**Fri 23/5/25**	**Fri 27/3/26**	
1292	1st Fix (concealed piping, pipe sleeve)	30 days	Fri 23/5/25	Fri 27/6/25	290SS+14 days
1293	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Thu 18/12/25	Fri 23/1/26	647SS+14 days
1294	3rd Fix (fittings)	30 days	Fri 20/2/26	Fri 27/3/26	655SS+14 days
1295	**Fire Protection - Sprinkler System**	**257 days**	**Fri 23/5/25**	**Fri 27/3/26**	
1296	1st Fix (concealed piping, pipe sleeve)	30 days	Fri 23/5/25	Fri 27/6/25	290SS+14 days
1297	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Thu 18/12/25	Fri 23/1/26	647SS+14 days
1298	3rd Fix (fittings)	30 days	Fri 20/2/26	Fri 27/3/26	655SS+14 days
1299	**Level 2**	**393 days**	**Mon 13/1/25**	**Mon 4/5/26**	
1300	Mat'l & Shopdrawing Submission/Approval	90 days	Mon 13/1/25	Fri 2/5/25	
1301	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**227 days**	**Sat 2/8/25**	**Mon 4/5/26**	

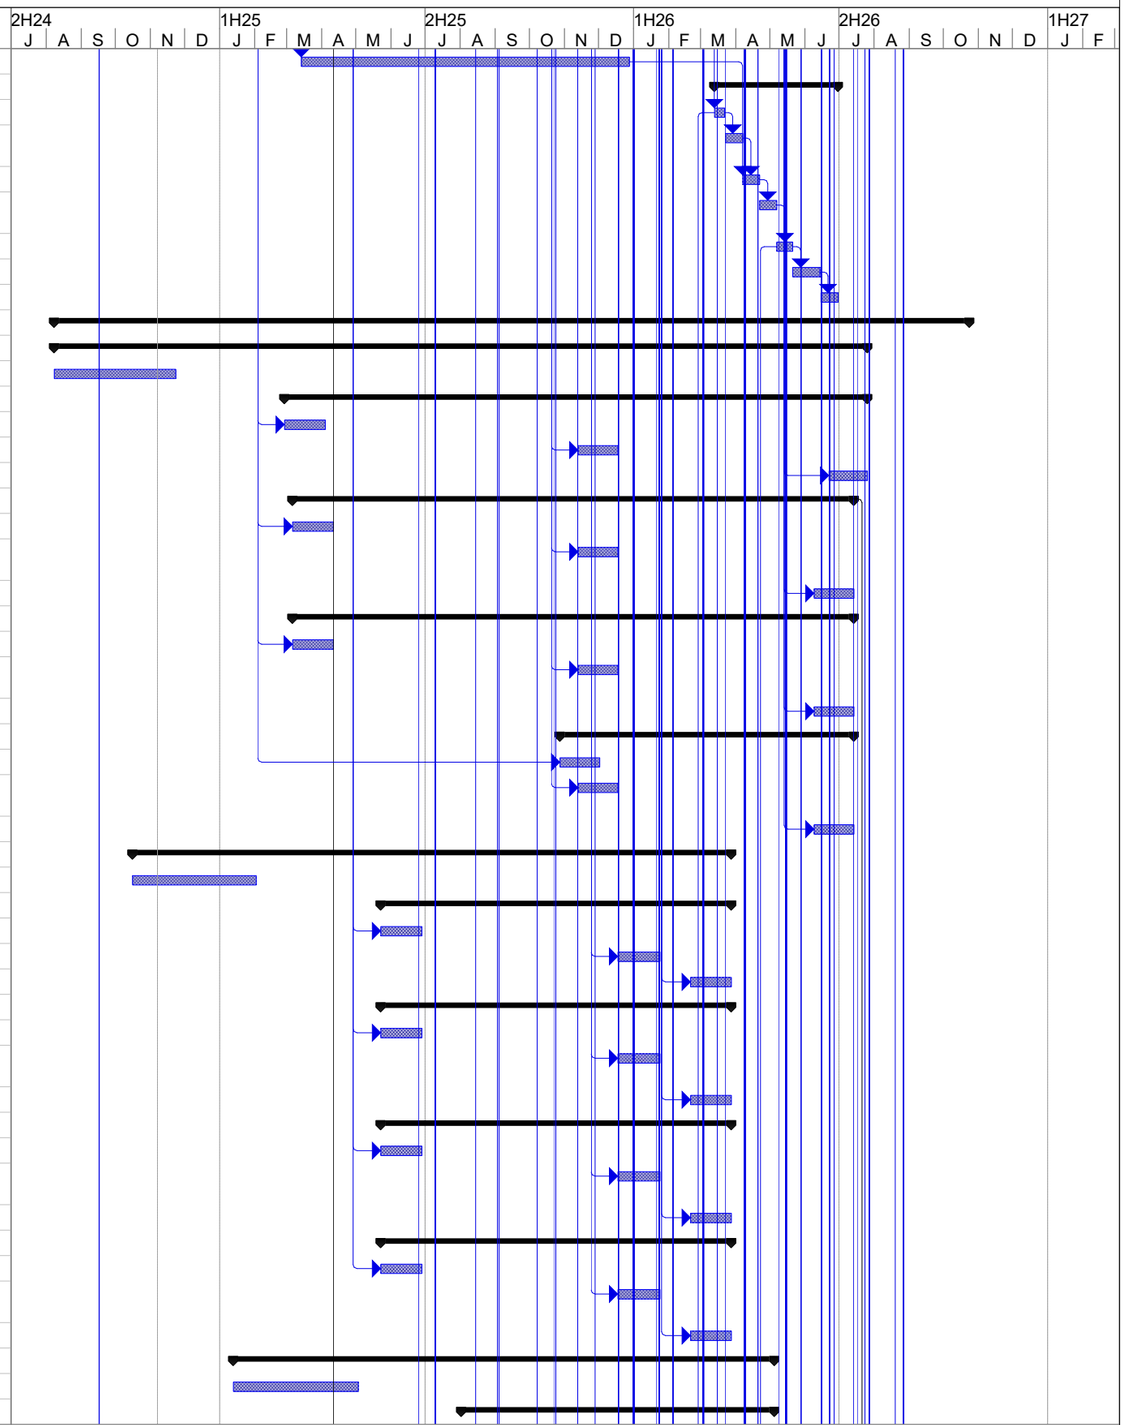

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	


ID	Task Name	Duration	Start	Finish	Predecessors
1302	1st Fix (concealed piping, pipe sleeve)	30 days	Sat 2/8/25	Sat 6/9/25	291SS+14 days
1303	2nd Fix (concealed/surface (pipes/conduit),cable containment, wirings)	30 days	Sat 24/1/26	Mon 2/3/26	661SS+14 days
1304	3rd Fix (fittings)	30 days	Sat 28/3/26	Mon 4/5/26	669SS+14 days
1305	**Electrical/PA/IT/Fire alarm**	**227 days**	**Sat 2/8/25**	**Mon 4/5/26**	
1306	1st Fix (concealed piping, pipe sleeve)	30 days	Sat 2/8/25	Sat 6/9/25	291SS+14 days
1307	2nd Fix (surface pipes,cable containment, wirings)	30 days	Sat 24/1/26	Mon 2/3/26	661SS+14 days
1308	3rd Fix (fittings)	30 days	Sat 28/3/26	Mon 4/5/26	669SS+14 days
1309	**ACMV**	**227 days**	**Sat 2/8/25**	**Mon 4/5/26**	
1310	1st Fix (concealed piping, pipe sleeve)	30 days	Sat 2/8/25	Sat 6/9/25	291SS+14 days
1311	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Sat 24/1/26	Mon 2/3/26	661SS+14 days
1312	3rd Fix (fittings)	30 days	Sat 28/3/26	Mon 4/5/26	669SS+14 days
1313	**Fire Protection - Sprinkler System**	**227 days**	**Sat 2/8/25**	**Mon 4/5/26**	
1314	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Sat 2/8/25	Sat 6/9/25	291SS+14 days
1315	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Sat 24/1/26	Mon 2/3/26	661SS+14 days
1316	3rd Fix (fittings)	30 days	Sat 28/3/26	Mon 4/5/26	669SS+14 days
1317	**Level 3**	**398 days**	**Thu 13/2/25**	**Wed 10/6/26**	
1318	Mat'l & Shopdrawing Submission/Approval	90 days	Thu 13/2/25	Mon 2/6/25	
1319	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**211 days**	**Fri 26/9/25**	**Wed 10/6/26**	
1320	1st Fix (concealed piping, pipe sleeve)	30 days	Fri 26/9/25	Fri 31/10/25	292SS+14 days
1321	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Tue 3/3/26	Wed 8/4/26	675SS+14 days
1322	3rd Fix (fittings)	30 days	Tue 5/5/26	Wed 10/6/26	684SS+14 days
1323	**Electrical/PA/IT/Fire alarm**	**211 days**	**Fri 26/9/25**	**Wed 10/6/26**	
1324	1st Fix (concealed piping, pipe sleeve)	30 days	Fri 26/9/25	Fri 31/10/25	292SS+14 days
1325	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Tue 3/3/26	Wed 8/4/26	675SS+14 days
1326	3rd Fix (fittings)	30 days	Tue 5/5/26	Wed 10/6/26	684SS+14 days
1327	**ACMV**	**211 days**	**Fri 26/9/25**	**Wed 10/6/26**	
1328	1st Fix (concealed piping, pipe sleeve)	30 days	Fri 26/9/25	Fri 31/10/25	292SS+14 days
1329	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Tue 3/3/26	Wed 8/4/26	675SS+14 days
1330	3rd Fix (fittings)	30 days	Tue 5/5/26	Wed 10/6/26	684SS+14 days
1331	**Fire Protection - Sprinkler System**	**211 days**	**Fri 26/9/25**	**Wed 10/6/26**	
1332	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Fri 26/9/25	Fri 31/10/25	292SS+14 days
1333	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Tue 3/3/26	Wed 8/4/26	675SS+14 days
1334	3rd Fix (fittings)	30 days	Tue 5/5/26	Wed 10/6/26	684SS+14 days
1335	**Level 4**	**404 days**	**Thu 13/3/25**	**Wed 15/7/26**	
1336	Mat'l & Shopdrawing Submission/Approval	90 days	Thu 13/3/25	Tue 1/7/25	
1337	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**211 days**	**Sat 1/11/25**	**Wed 15/7/26**	
1338	1st Fix (concealed piping, pipe sleeve)	30 days	Sat 1/11/25	Fri 5/12/25	293SS+14 days
1339	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Thu 9/4/26	Thu 14/5/26	690SS+14 days
1340	3rd Fix (fittings)	30 days	Thu 11/6/26	Wed 15/7/26	699SS+14 days
1341	**Electrical/PA/IT/Fire alarm**	**211 days**	**Sat 1/11/25**	**Wed 15/7/26**	
1342	1st Fix (concealed piping, pipe sleeve)	30 days	Sat 1/11/25	Fri 5/12/25	293SS+14 days
1343	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Thu 9/4/26	Thu 14/5/26	690SS+14 days
1344	3rd Fix (fittings)	30 days	Thu 11/6/26	Wed 15/7/26	699SS+14 days
1345	**ACMV**	**211 days**	**Sat 1/11/25**	**Wed 15/7/26**	
1346	1st Fix (concealed piping, pipe sleeve)	30 days	Sat 1/11/25	Fri 5/12/25	293SS+14 days
1347	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Thu 9/4/26	Thu 14/5/26	690SS+14 days
1348	3rd Fix (fittings)	30 days	Thu 11/6/26	Wed 15/7/26	699SS+14 days
1349	**Fire Protection - Sprinkler System**	**211 days**	**Sat 1/11/25**	**Wed 15/7/26**	
1350	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Sat 1/11/25	Fri 5/12/25	293SS+14 days

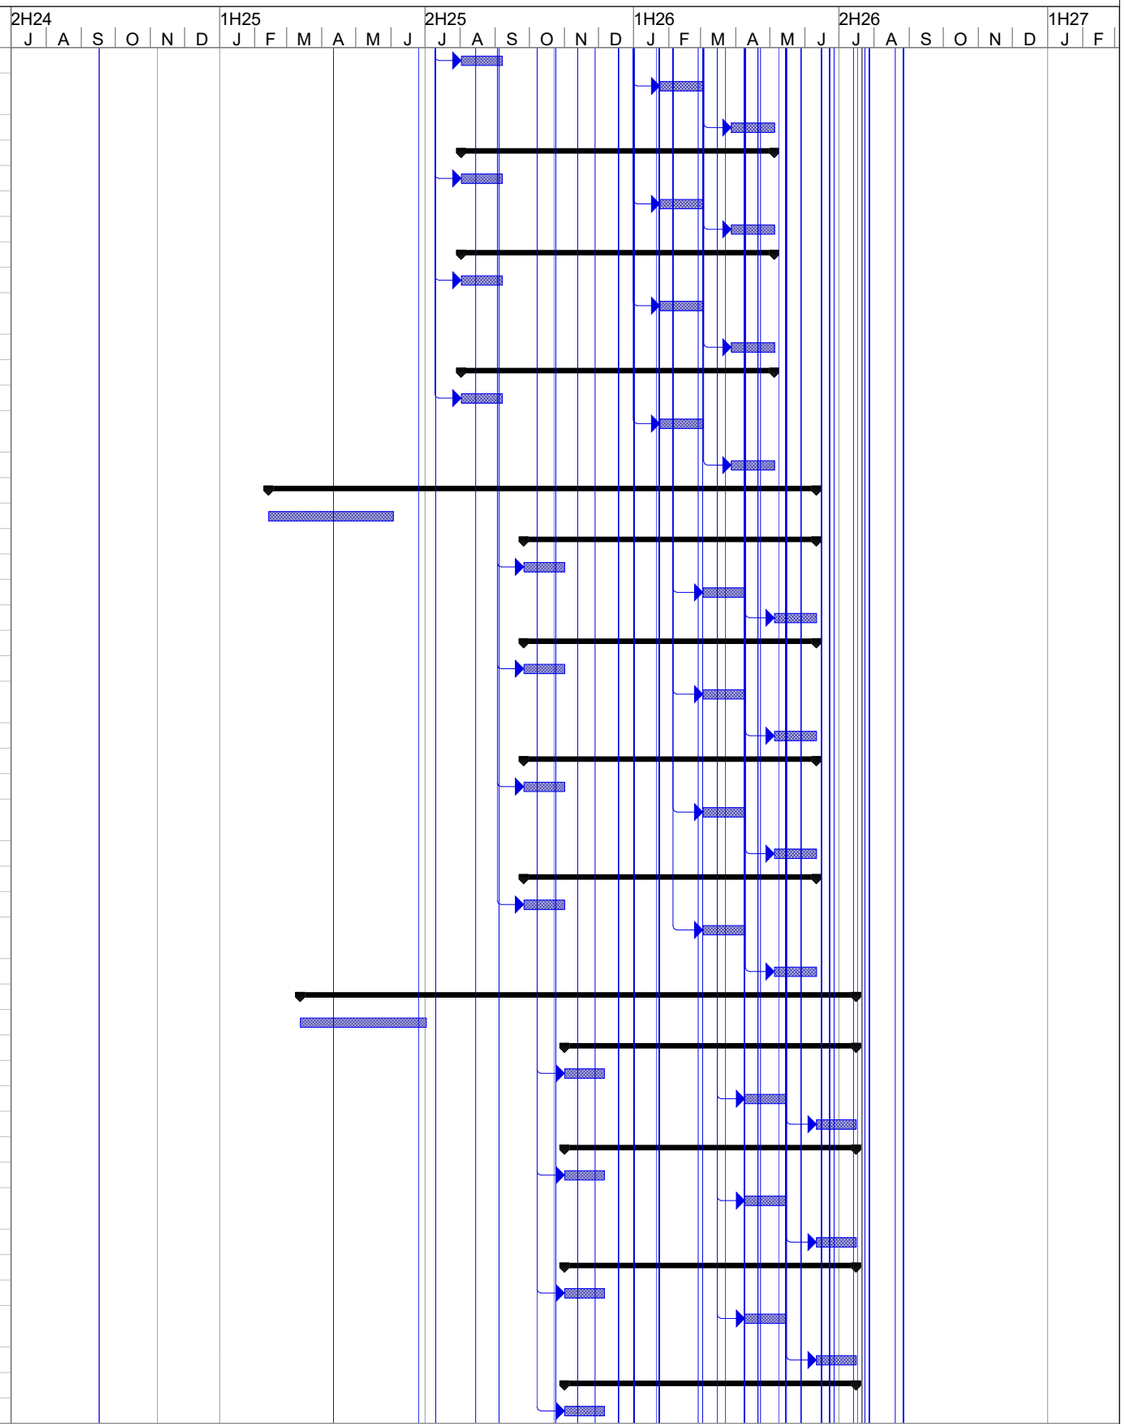

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	


ID	Task Name	Duration	Start	Finish	Predecessors
1351	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Thu 9/4/26	Thu 14/5/26	690SS+14 days
1352	3rd Fix (fittings)	30 days	Thu 11/6/26	Wed 15/7/26	699SS+14 days
1353	**Level 5**	**407 days**	**Tue 15/4/25**	**Thu 20/8/26**	
1354	Mat'l & Shopdrawing Submission/Approval	90 days	Tue 15/4/25	Fri 1/8/25	
1355	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**211 days**	**Sat 6/12/25**	**Thu 20/8/26**	
1356	1st Fix (concealed piping, pipe sleeve)	30 days	Sat 6/12/25	Mon 12/1/26	294SS+14 days
1357	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Fri 15/5/26	Sat 20/6/26	705SS+14 days
1358	3rd Fix (fittings)	30 days	Thu 16/7/26	Thu 20/8/26	714SS+14 days
1359	**Electrical/PA/IT/Fire alarm**	**211 days**	**Sat 6/12/25**	**Thu 20/8/26**	
1360	1st Fix (concealed piping, pipe sleeve)	30 days	Sat 6/12/25	Mon 12/1/26	294SS+14 days
1361	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Fri 15/5/26	Sat 20/6/26	705SS+14 days
1362	3rd Fix (fittings)	30 days	Thu 16/7/26	Thu 20/8/26	714SS+14 days
1363	**ACMV**	**211 days**	**Sat 6/12/25**	**Thu 20/8/26**	
1364	1st Fix (concealed piping, pipe sleeve)	30 days	Sat 6/12/25	Mon 12/1/26	294SS+14 days
1365	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Fri 15/5/26	Sat 20/6/26	705SS+14 days
1366	3rd Fix (fittings)	30 days	Thu 16/7/26	Thu 20/8/26	714SS+14 days
1367	**Fire Protection - Sprinkler System**	**211 days**	**Sat 6/12/25**	**Thu 20/8/26**	
1368	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Sat 6/12/25	Mon 12/1/26	294SS+14 days
1369	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Fri 15/5/26	Sat 20/6/26	705SS+14 days
1370	3rd Fix (fittings)	30 days	Thu 16/7/26	Thu 20/8/26	714SS+14 days
1371	**Level 6**	**412 days**	**Sat 17/5/25**	**Thu 24/9/26**	
1372	Mat'l & Shopdrawing Submission/Approval	90 days	Sat 17/5/25	Mon 1/9/25	
1373	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**211 days**	**Tue 13/1/26**	**Thu 24/9/26**	
1374	1st Fix (concealed piping, pipe sleeve)	30 days	Tue 13/1/26	Mon 16/2/26	295SS+14 days
1375	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Mon 22/6/26	Sat 25/7/26	720SS+14 days
1376	3rd Fix (fittings)	30 days	Fri 21/8/26	Thu 24/9/26	730SS+14 days
1377	**Electrical/PA/IT/Fire alarm**	**211 days**	**Tue 13/1/26**	**Thu 24/9/26**	
1378	1st Fix (concealed piping, pipe sleeve)	30 days	Tue 13/1/26	Mon 16/2/26	295SS+14 days
1379	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Mon 22/6/26	Sat 25/7/26	720SS+14 days
1380	3rd Fix (fittings)	30 days	Fri 21/8/26	Thu 24/9/26	730SS+14 days
1381	**ACMV**	**211 days**	**Tue 13/1/26**	**Thu 24/9/26**	
1382	1st Fix (concealed piping, pipe sleeve)	30 days	Tue 13/1/26	Mon 16/2/26	295SS+14 days
1383	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Mon 22/6/26	Sat 25/7/26	720SS+14 days
1384	3rd Fix (fittings)	30 days	Fri 21/8/26	Thu 24/9/26	730SS+14 days
1385	**Fire Protection - Sprinkler System**	**211 days**	**Tue 13/1/26**	**Thu 24/9/26**	
1386	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Tue 13/1/26	Mon 16/2/26	295SS+14 days
1387	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Mon 22/6/26	Sat 25/7/26	720SS+14 days
1388	3rd Fix (fittings)	30 days	Fri 21/8/26	Thu 24/9/26	730SS+14 days
1389	**Level 7**	**385 days**	**Fri 18/7/25**	**Fri 23/10/26**	
1390	Mat'l & Shopdrawing Submission/Approval	90 days	Fri 18/7/25	Sat 1/11/25	
1391	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**206 days**	**Thu 19/2/26**	**Fri 23/10/26**	
1392	1st Fix (concealed piping, pipe sleeve)	30 days	Thu 19/2/26	Thu 26/3/26	296SS+14 days
1393	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Tue 21/7/26	Tue 25/8/26	735SS+14 days
1394	3rd Fix (fittings)	30 days	Sat 19/9/26	Fri 23/10/26	744SS+14 days
1395	**Electrical/PA/IT/Fire alarm**	**206 days**	**Thu 19/2/26**	**Fri 23/10/26**	
1396	1st Fix (concealed piping, pipe sleeve)	30 days	Thu 19/2/26	Thu 26/3/26	296SS+14 days
1397	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Tue 21/7/26	Tue 25/8/26	735SS+14 days
1398	3rd Fix (fittings)	30 days	Sat 19/9/26	Fri 23/10/26	744SS+14 days
1399	**ACMV**	**206 days**	**Thu 19/2/26**	**Fri 23/10/26**	

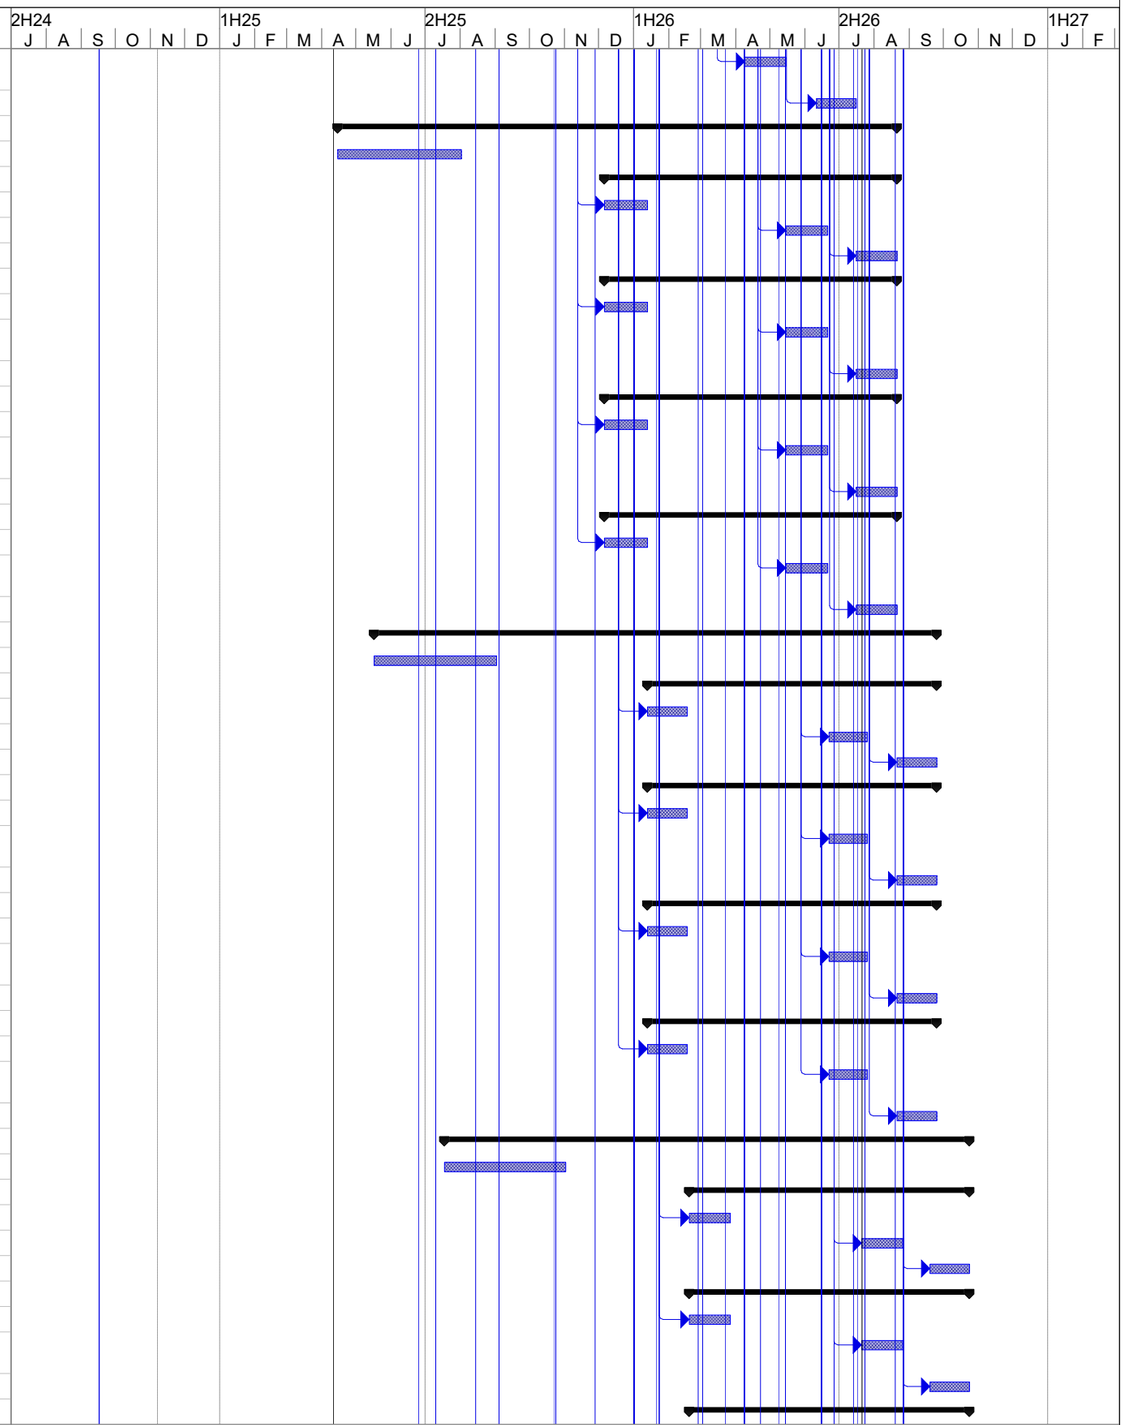

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	


ID	Task Name	Duration	Start	Finish	Predecessors
1400	1st Fix (concealed piping, pipe sleeve)	30 days	Thu 19/2/26	Thu 26/3/26	296SS+14 days
1401	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Tue 21/7/26	Tue 25/8/26	735SS+14 days
1402	3rd Fix (fittings)	30 days	Sat 19/9/26	Fri 23/10/26	744SS+14 days
1403	**Fire Protection - Sprinkler System**	**206 days**	**Thu 19/2/26**	**Fri 23/10/26**	
1404	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Thu 19/2/26	Thu 26/3/26	296SS+14 days
1405	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Tue 21/7/26	Tue 25/8/26	735SS+14 days
1406	3rd Fix (fittings)	30 days	Sat 19/9/26	Fri 23/10/26	744SS+14 days
1407	**Level 8**	**360 days**	**Mon 18/8/25**	**Fri 23/10/26**	
1408	Mat'l & Shopdrawing Submission/Approval	90 days	Mon 18/8/25	Mon 1/12/25	
1409	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**176 days**	**Fri 27/3/26**	**Fri 23/10/26**	
1410	1st Fix (concealed piping, pipe sleeve)	30 days	Fri 27/3/26	Sat 2/5/26	297SS+14 days
1411	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Tue 21/7/26	Tue 25/8/26	750SS+14 days
1412	3rd Fix (fittings)	30 days	Sat 19/9/26	Fri 23/10/26	759SS+14 days
1413	**Electrical/PA/IT/Fire alarm**	**176 days**	**Fri 27/3/26**	**Fri 23/10/26**	
1414	1st Fix (concealed piping, pipe sleeve)	30 days	Fri 27/3/26	Sat 2/5/26	297SS+14 days
1415	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Tue 21/7/26	Tue 25/8/26	750SS+14 days
1416	3rd Fix (fittings)	30 days	Sat 19/9/26	Fri 23/10/26	759SS+14 days
1417	**ACMV**	**176 days**	**Fri 27/3/26**	**Fri 23/10/26**	
1418	1st Fix (concealed piping, pipe sleeve)	30 days	Fri 27/3/26	Sat 2/5/26	297SS+14 days
1419	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Tue 21/7/26	Tue 25/8/26	750SS+14 days
1420	3rd Fix (fittings)	30 days	Sat 19/9/26	Fri 23/10/26	759SS+14 days
1421	**Fire Protection - Sprinkler System**	**176 days**	**Fri 27/3/26**	**Fri 23/10/26**	
1422	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Fri 27/3/26	Sat 2/5/26	297SS+14 days
1423	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Tue 21/7/26	Tue 25/8/26	750SS+14 days
1424	3rd Fix (fittings)	30 days	Sat 19/9/26	Fri 23/10/26	759SS+14 days
1425	**Level 9**	**325 days**	**Wed 17/9/25**	**Tue 13/10/26**	
1426	Mat'l & Shopdrawing Submission/Approval	90 days	Wed 17/9/25	Fri 2/1/26	
1427	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**137 days**	**Mon 4/5/26**	**Tue 13/10/26**	
1428	1st Fix (concealed piping, pipe sleeve)	30 days	Mon 4/5/26	Tue 9/6/26	298SS+14 days
1429	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Tue 21/7/26	Tue 25/8/26	765SS+14 days
1430	3rd Fix (fittings)	21 days	Sat 19/9/26	Tue 13/10/26	773SS+14 days
1431	**Electrical/PA/IT/Fire alarm**	**137 days**	**Mon 4/5/26**	**Tue 13/10/26**	
1432	1st Fix (concealed piping, pipe sleeve)	30 days	Mon 4/5/26	Tue 9/6/26	298SS+14 days
1433	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Tue 21/7/26	Tue 25/8/26	765SS+14 days
1434	3rd Fix (fittings)	21 days	Sat 19/9/26	Tue 13/10/26	773SS+14 days
1435	**ACMV**	**137 days**	**Mon 4/5/26**	**Tue 13/10/26**	
1436	1st Fix (concealed piping, pipe sleeve)	30 days	Mon 4/5/26	Tue 9/6/26	298SS+14 days
1437	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Tue 21/7/26	Tue 25/8/26	765SS+14 days
1438	3rd Fix (fittings)	21 days	Sat 19/9/26	Tue 13/10/26	773SS+14 days
1439	**Fire Protection - Sprinkler System**	**137 days**	**Mon 4/5/26**	**Tue 13/10/26**	
1440	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Mon 4/5/26	Tue 9/6/26	298SS+14 days
1441	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Tue 21/7/26	Tue 25/8/26	765SS+14 days
1442	3rd Fix (fittings)	21 days	Sat 19/9/26	Tue 13/10/26	773SS+14 days
1443	**Lower Roof**	**271 days**	**Thu 13/11/25**	**Tue 6/10/26**	
1444	Mat'l & Shopdrawing Submission/Approval	90 days	Thu 13/11/25	Mon 2/3/26	
1445	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**101 days**	**Wed 10/6/26**	**Tue 6/10/26**	
1446	1st Fix (concealed piping, pipe sleeve)	30 days	Wed 10/6/26	Tue 14/7/26	299SS+14 days
1447	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Fri 7/8/26	Fri 11/9/26	783SS+4 days
1448	3rd Fix (fittings)	21 days	Sat 12/9/26	Tue 6/10/26	1447

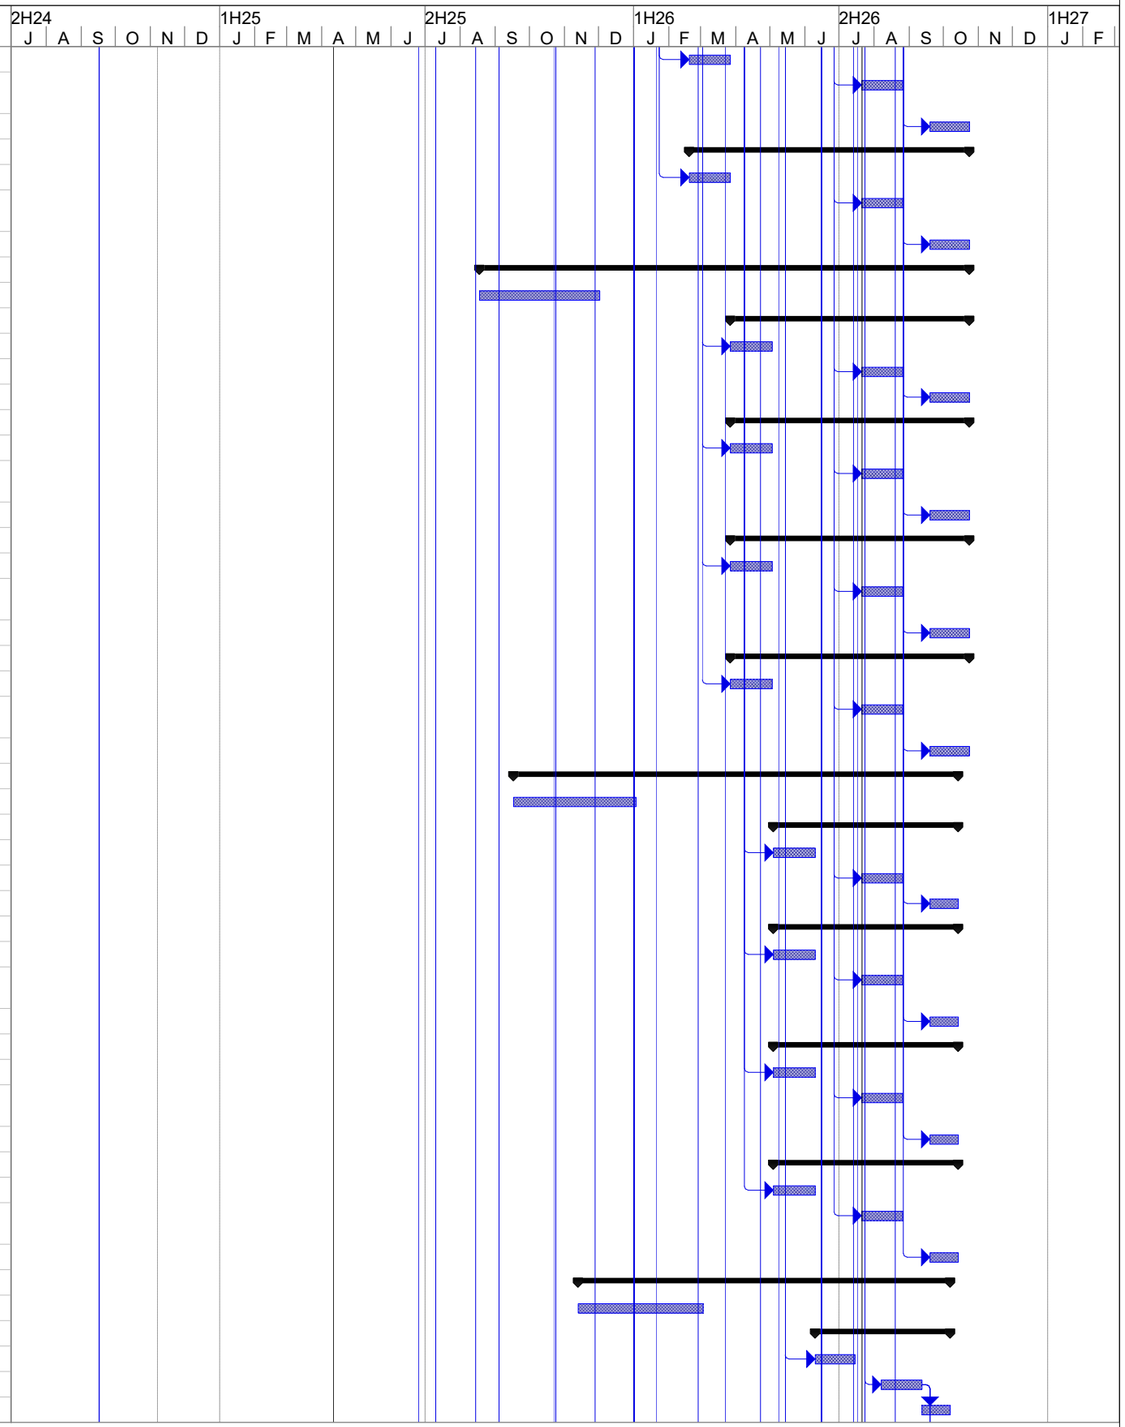

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task | Project Summary | Inactive Summary | Manual Summary | External Milestone
Split | External Tasks | Manual Task | Start-only | Progress
Milestone | External Milestone | Duration-only | Finish-only | Deadline
Summary | Inactive Milestone | Manual Summary Rollup | External Tasks

ID	Task Name	Duration	Start	Finish	Predecessors
1449	**Electrical/PA/IT/Fire alarm**	**101 days**	**Wed 10/6/26**	**Tue 6/10/26**	
1450	1st Fix (concealed piping, pipe sleeve)	30 days	Wed 10/6/26	Tue 14/7/26	299SS+14 days
1451	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Fri 7/8/26	Fri 11/9/26	783SS+4 days
1452	3rd Fix (fittings)	21 days	Sat 12/9/26	Tue 6/10/26	1447
1453	**ACMV**	**76 days**	**Wed 10/6/26**	**Mon 7/9/26**	
1454	1st Fix (concealed piping, pipe sleeve)	30 days	Wed 10/6/26	Tue 14/7/26	299SS+14 days
1455	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	12 days	Fri 7/8/26	Fri 21/8/26	783SS+4 days
1456	3rd Fix (fittings)	14 days	Sat 22/8/26	Mon 7/9/26	1455
1457	**Fire Protection - Sprinkler System**	**101 days**	**Wed 10/6/26**	**Tue 6/10/26**	
1458	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Wed 10/6/26	Tue 14/7/26	299SS+14 days
1459	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Fri 7/8/26	Fri 11/9/26	783SS+4 days
1460	3rd Fix (fittings)	21 days	Sat 12/9/26	Tue 6/10/26	1447
1461	**Upper Roof**	**283 days**	**Sat 15/11/25**	**Thu 22/10/26**	
1462	Mat'l & Shopdrawing Submission/Approval	90 days	Fri 12/12/25	Wed 1/4/26	
1463	**Plumbing & Sanitary / Gas / Hosereels / Dry risers etc.**	**90 days**	**Thu 9/7/26**	**Thu 22/10/26**	
1464	1st Fix (concealed piping, pipe sleeve)	30 days	Thu 9/7/26	Thu 13/8/26	300SS+14 days
1465	2nd Fix (concealed/ surface(piping & conduit) with accessories)	30 days	Fri 14/8/26	Thu 17/9/26	1464
1466	3rd Fix (fittings)	30 days	Fri 18/9/26	Thu 22/10/26	1465
1467	**Electrical/PA/IT/Fire alarm**	**283 days**	**Sat 15/11/25**	**Thu 22/10/26**	
1468	1st Fix (concealed piping, pipe sleeve)	30 days	Thu 9/7/26	Thu 13/8/26	300SS+14 days
1469	2nd Fix (concealed/surface (pipes/condui),cable containment, wirings)	30 days	Sat 15/11/25	Fri 19/12/25	343SS+14 days
1470	2nd Fix (surface pipes,cable containment, wirings)	30 days	Fri 14/8/26	Thu 17/9/26	1464
1471	3rd Fix (fittings)	30 days	Fri 18/9/26	Thu 22/10/26	1465
1472	**ACMV**	**90 days**	**Thu 9/7/26**	**Thu 22/10/26**	
1473	1st Fix (concealed piping, pipe sleeve)	30 days	Thu 9/7/26	Thu 13/8/26	300SS+14 days
1474	2nd Fix (concealed/surface (piping/conduit),cable containment, ducting, wirings)	30 days	Fri 14/8/26	Thu 17/9/26	1464
1475	3rd Fix (fittings)	30 days	Fri 18/9/26	Thu 22/10/26	1465
1476	**Fire Protection - Sprinkler System**	**90 days**	**Thu 9/7/26**	**Thu 22/10/26**	
1477	1st Fix (concealed piping&conduit, pipe sleeve)	30 days	Thu 9/7/26	Thu 13/8/26	300SS+14 days
1478	2nd Fix (Concealed/surface conduit, cable containment, wirings, flex. sprinkler)	30 days	Fri 14/8/26	Thu 17/9/26	1464
1479	3rd Fix (fittings)	30 days	Fri 18/9/26	Thu 22/10/26	1465
1480	**Lifts (4 Nos) - FL1, BL1, PL4 & PL5**	**622 days**	**Tue 1/10/24**	**Tue 20/10/26**	
1481	Submissions/Approval	77 days	Tue 1/10/24	Mon 30/12/24	
1482	Procurement/fabrication/shipment	240 days	Fri 29/8/25	Tue 16/6/26	1010SS
1483	**Site installations including T&C**	**84 days**	**Tue 14/7/26**	**Tue 20/10/26**	
1484	Lift shafts handover	7 days	Tue 14/7/26	Tue 21/7/26	300FS+3 days
1485	Preparation works inclu. Lift shaft verticality check & rectification work if any	12 days	Wed 22/7/26	Tue 4/8/26	1484
1486	Guardrails installations	18 days	Wed 5/8/26	Wed 26/8/26	1482,1485
1487	Landing sill, door frames installations, lift door & door jambs installations	12 days	Thu 27/8/26	Wed 9/9/26	1486
1488	Slow speed testing	12 days	Thu 10/9/26	Wed 23/9/26	1487
1489	Lift interior decorations & high speed testing	12 days	Thu 24/9/26	Wed 7/10/26	1488
1490	Final T&C (Including hot test)	11 days	Thu 8/10/26	Tue 20/10/26	1489
1491					
1492	**Electrical Sub-station (20 months)**	**503 days**	**Thu 8/8/24**	**Tue 7/4/26**	
1493	Contract Duration	503 days	Thu 8/8/24	Tue 7/4/26	
1494	**Structural Works**	**60 days**	**Mon 7/10/24**	**Sat 14/12/24**	
1495	Piling Works	60 days	Mon 7/10/24	Sat 14/12/24	
1496	**Substructure**	**90 days**	**Mon 16/12/24**	**Fri 4/4/25**	
1497	ERSS pilecaps & basement	90 days	Mon 16/12/24	Fri 4/4/25	1495

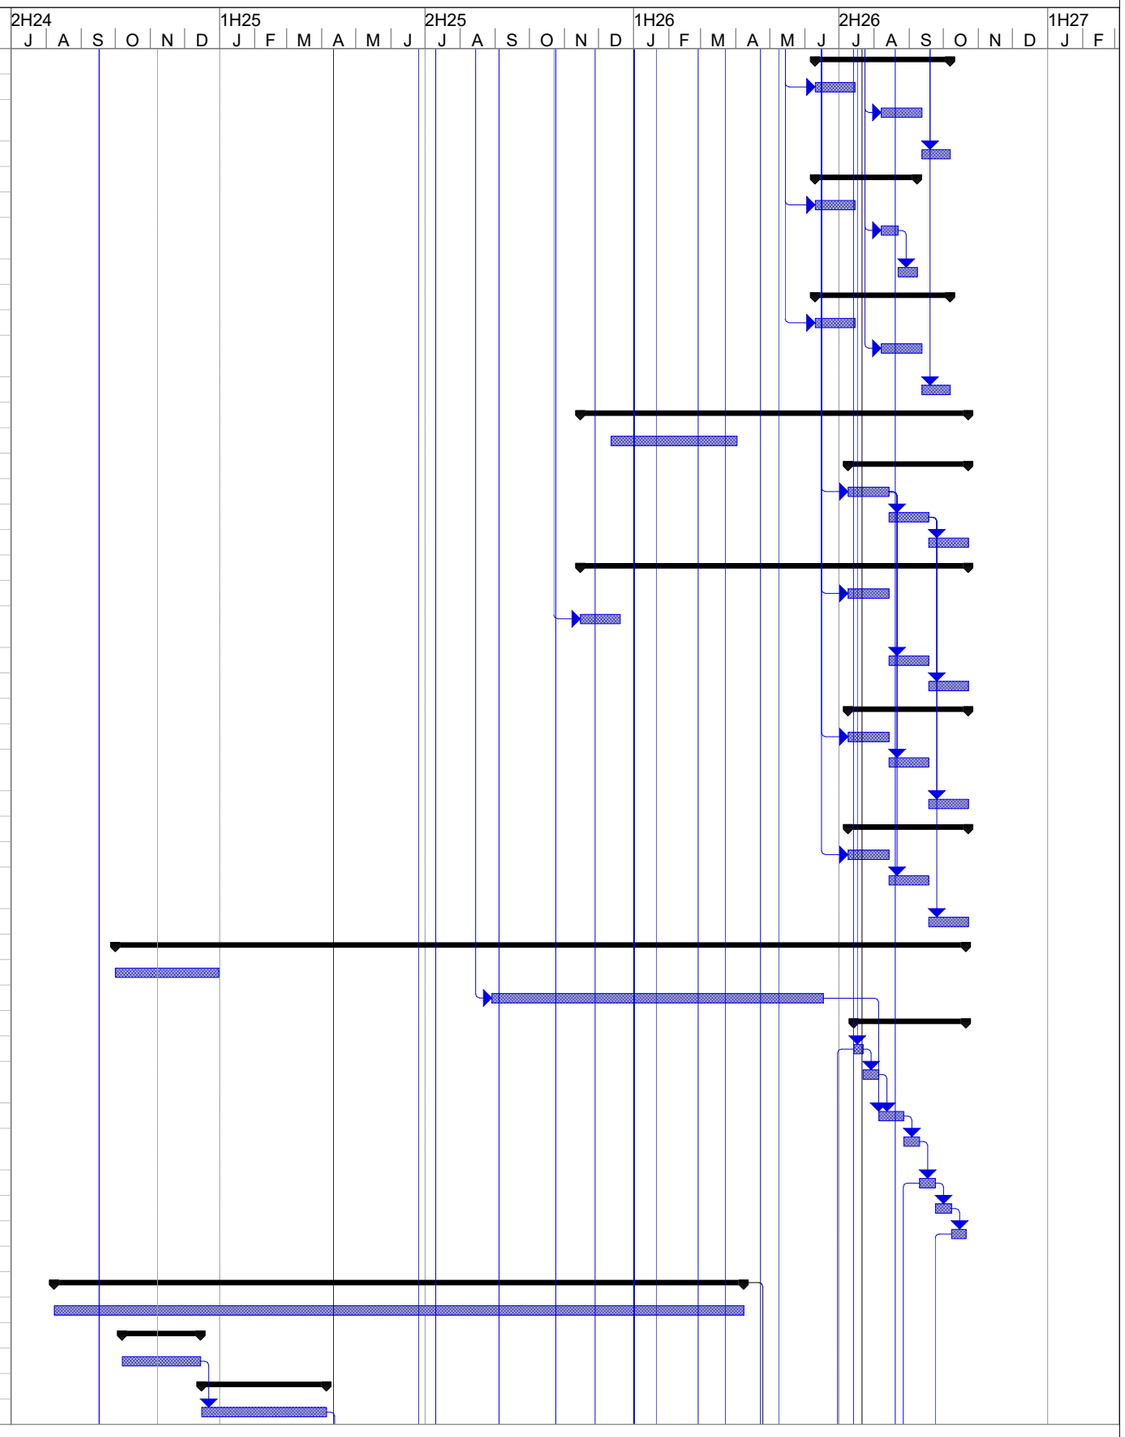


Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	

Kwan Yong Construction Pte Ltd — **Master Programme For Co-Located Polyclinic & Nursing Home At 200 Jurong East Ave 1**


ID	Task Name	Duration	Start	Finish	Predecessors
1498	**Superstructure**	**105 days**	**Sat 5/4/25**	**Mon 11/8/25**	
1499	1st storey	60 days	Sat 5/4/25	Wed 18/6/25	1497
1500	2nd storey	45 days	Thu 19/6/25	Mon 11/8/25	1499
1501	**Architectural Works**	**111 days**	**Tue 12/8/25**	**Fri 19/12/25**	
1502	Prefab walls	30 days	Tue 12/8/25	Mon 15/9/25	1500
1503	Plastering	30 days	Tue 16/9/25	Tue 21/10/25	1502
1504	Floor finishes	15 days	Wed 22/10/25	Fri 7/11/25	1503
1505	Doors and windows	30 days	Tue 12/8/25	Fri 14/11/25	1502SS
1506	Railings & gratings	15 days	Sat 8/11/25	Tue 25/11/25	1504
1507	Painting	21 days	Wed 26/11/25	Fri 19/12/25	1506
1508	**M&E**	**229 days**	**Tue 1/4/25**	**Wed 31/12/25**	
1509	Underground lead-in-pipes (within site boundary)	45 days	Tue 1/4/25	Mon 26/5/25	
1510	M&E fixtures (Switchboard, DBs, etc.)	30 days	Wed 26/11/25	Wed 31/12/25	1506
1511	**External works**	**30 days**	**Wed 1/10/25**	**Wed 5/11/25**	
1512	Drains	15 days	Wed 1/10/25	Fri 17/10/25	
1513	Driveway (Temporary)	15 days	Sat 18/10/25	Wed 5/11/25	1512
1514	Inspections & handover to Powergrid	30 days	Mon 2/3/26	Tue 7/4/26	1513
1515					
1516	**External Works**	**609 days**	**Mon 2/12/24**	**Mon 7/12/26**	
1517	**Detention Tank & ACMV Exhaust Duct Compartment**	**75 days**	**Fri 4/4/25**	**Fri 4/7/25**	
1518	**Wall - Lower Part**	**22 days**	**Fri 4/4/25**	**Wed 30/4/25**	
1519	Rebar laying	14 days	Fri 4/4/25	Mon 21/4/25	249
1520	Formwork closing	14 days	Sat 12/4/25	Tue 29/4/25	1519SS+7 days
1521	Casting	1 day	Wed 30/4/25	Wed 30/4/25	1520
1522	**Wall - Upper Part**	**17 days**	**Mon 5/5/25**	**Sat 24/5/25**	
1523	Rebar laying	10 days	Mon 5/5/25	Fri 16/5/25	1521FS+2 days
1524	Formwork closing	9 days	Wed 14/5/25	Fri 23/5/25	1523SS+7 days
1525	Casting	1 day	Sat 24/5/25	Sat 24/5/25	1524
1526	**Top slab construction Incl. rc M&E trench**	**18 days**	**Wed 28/5/25**	**Wed 18/6/25**	
1527	Falsework erection	7 days	Wed 28/5/25	Wed 4/6/25	1525FS+2 days
1528	Rebar laying	10 days	Thu 5/6/25	Tue 17/6/25	1527
1529	Formwork closing	4 days	Sat 14/6/25	Wed 18/6/25	1528SS+7 days
1530	Casting	1 day	Wed 18/6/25	Wed 18/6/25	261
1531	Discharge drain (boxed drain) construction	14 days	Thu 19/6/25	Fri 4/7/25	1530
1532	Aprons & drains	90 days	Fri 30/5/25	Sat 13/9/25	
1533	**Roadworks**	**130 days**	**Mon 15/6/26**	**Sat 14/11/26**	
1534	Boundary & roadside drains and kerbs	90 days	Mon 15/6/26	Mon 28/9/26	
1535	Driveway construction/carpark & road markings	60 days	Sat 5/9/26	Sat 14/11/26	
1536	**Miscellaneous**	**609 days**	**Mon 2/12/24**	**Mon 7/12/26**	
1537	Telcoms manhole & underground pipes	60 days	Tue 1/4/25	Fri 13/6/25	
1538	IC and underground sanitary works	61 days	Mon 2/12/24	Fri 14/2/25	
1539	Gas incoming & underground pipes	30 days	Mon 3/3/25	Mon 7/4/25	
1540	Covered linkways	30 days	Mon 2/11/26	Mon 7/12/26	
1541	Bicycle lots	14 days	Fri 23/10/26	Sat 7/11/26	
1542	Side table landscape & turfing	30 days	Thu 15/10/26	Thu 19/11/26	
1543	**Milestone Dates**	**712 days**	**Tue 1/10/24**	**Sun 7/2/27**	
1544	**Handover area to LTA**	**30 days**	**Mon 3/11/25**	**Sat 6/12/25**	
1545	Shifting of hoardings	29 days	Mon 3/11/25	Fri 5/12/25	
1546	Handover to LTA	1 day	Sat 6/12/25	Sat 6/12/25	1545
1547					
1548	**Mock-ups**	**622 days**	**Tue 1/10/24**	**Tue 20/10/26**	
1549	**Off Site Mock-up (Corridor screen, Curtain track, Bedhead panel, M&E items, Paper signages (for basement, Level 1 to Level 3 common areas for NH & PC)**	**122 days**	**Tue 1/10/24**	**Mon 24/2/25**	

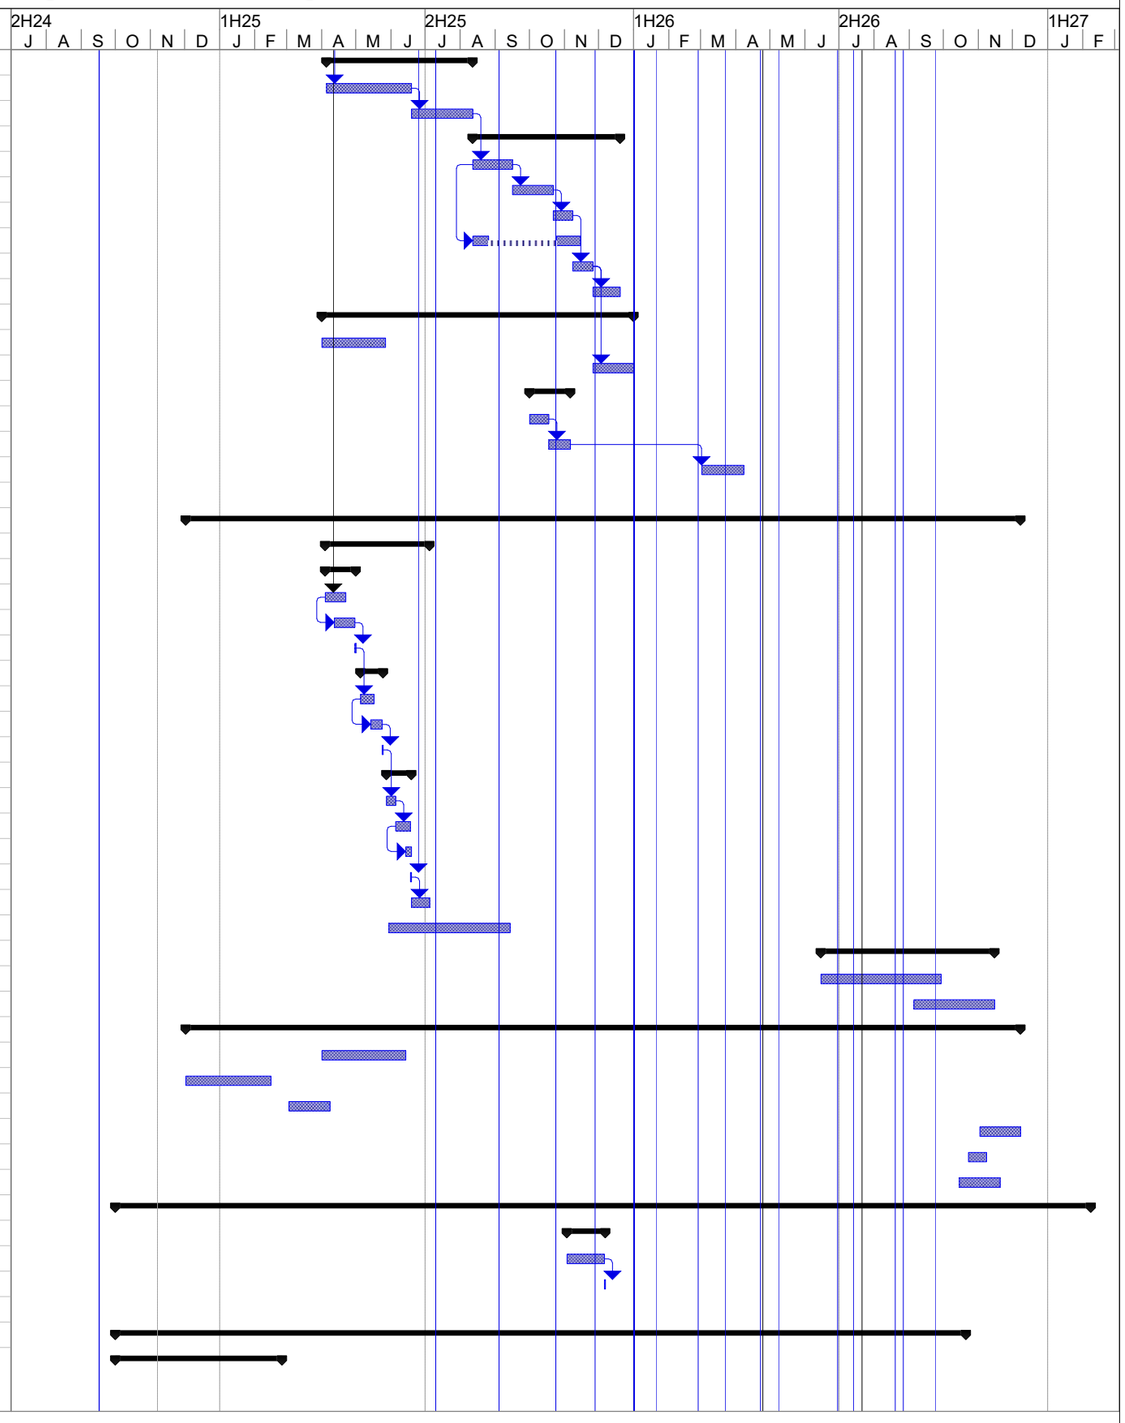

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Progress | Deadline


ID	Task Name	Duration	Start	Finish	Predecessors
1550	Material/shop-drwgs submissions, review, selection & approval	90 days	Tue 1/10/24	Wed 15/1/25	
1551	Procurement	30 days	Wed 6/11/24	Mon 9/12/24	1550SS+30 days
1552	Installation	30 days	Thu 2/1/25	Fri 7/2/25	1551
1553	Review, comments, rectifications & approval	14 days	Sat 8/2/25	Mon 24/2/25	1552
1554	**Nursing Home Block**	**69 days**	**Fri 17/10/25**	**Thu 8/1/26**	
1555	**Mock-up 1**	**69 days**	**Fri 17/10/25**	**Thu 8/1/26**	
1556	**Bedroom 1-1, 1-2, 1-3, 1-4**	**69 days**	**Fri 17/10/25**	**Thu 8/1/26**	
1557	Falsework Dismantling	10 days	Fri 17/10/25	Wed 29/10/25	209
1558	Wall Erection	12 days	Thu 30/10/25	Wed 12/11/25	1557
1559	Wall Plastering & Skimming	14 days	Thu 13/11/25	Fri 28/11/25	1558
1560	Drywall Installation	14 days	Fri 7/11/25	Sat 22/11/25	1558SS+7 days
1561	Floor Screeding	14 days	Fri 21/11/25	Sat 6/12/25	1559SS+7 days
1562	M&E Works Above Ceiling	14 days	Sat 29/11/25	Mon 15/12/25	1561SS+7 days
1563	False Ceiling Works	14 days	Mon 8/12/25	Tue 23/12/25	1562SS+7 days
1564	Painting	14 days	Tue 16/12/25	Fri 2/1/26	1563SS+7 days
1565	Window Installation	7 days	Sat 29/11/25	Sat 6/12/25	1559
1566	Curtain Track Installation	3 days	Sat 3/1/26	Tue 6/1/26	1564
1567	Grab Bar Installation	3 days	Sat 3/1/26	Tue 6/1/26	1564
1568	Vinyl Flooring	7 days	Mon 8/12/25	Mon 15/12/25	1561
1569	Fitments Installation	19 days	Tue 16/12/25	Thu 8/1/26	1568
1570	M&E 2nd Fix	7 days	Fri 7/11/25	Fri 14/11/25	1558SS+7 days
1571	M&E 3rd Fix	7 days	Wed 24/12/25	Fri 2/1/26	1569SS+7 days
1572	**Assisted Bath 1, Toilet 1, Bath 1**	**69 days**	**Fri 17/10/25**	**Thu 8/1/26**	
1573	Falsework Dismantling	10 days	Fri 17/10/25	Wed 29/10/25	209
1574	Wall Erection	10 days	Thu 30/10/25	Mon 10/11/25	1573
1575	Wall Plastering & Skimming	10 days	Fri 7/11/25	Tue 18/11/25	1574SS+7 days
1576	Sanitary Piping	7 days	Fri 7/11/25	Fri 14/11/25	1574SS+7 days
1577	Application of Waterproofing	5 days	Tue 11/11/25	Sat 15/11/25	1574
1578	Floor Screeding	10 days	Mon 17/11/25	Thu 27/11/25	1577
1579	Wall Tiling	12 days	Fri 28/11/25	Thu 11/12/25	1578
1580	Floor Tiling	10 days	Sat 6/12/25	Wed 17/12/25	1579SS+7 days
1581	Door Frame/Sliding Door /Bi-Fold Door Track Installation	7 days	Fri 28/11/25	Fri 5/12/25	1578
1582	M&E Works Above Ceiling	14 days	Wed 10/12/25	Fri 26/12/25	1580SS+3 days
1583	False Ceiling Works	14 days	Thu 18/12/25	Mon 5/1/26	1582SS+7 days
1584	Painting	3 days	Tue 6/1/26	Thu 8/1/26	1583
1585	Window Installation	7 days	Fri 12/12/25	Fri 19/12/25	1579
1586	Grab Bar Installation	5 days	Thu 18/12/25	Tue 23/12/25	1580
1587	Door Panel Installation	3 days	Thu 18/12/25	Sat 20/12/25	1580
1588	Sanitary Wares Installation	5 days	Thu 18/12/25	Tue 23/12/25	1580
1589	M&E 2nd Fix	7 days	Fri 7/11/25	Fri 14/11/25	1574SS+7 days
1590	M&E 3rd Fix	5 days	Fri 12/12/25	Wed 17/12/25	1579
1591	**Decentralise Day Room 1**	**69 days**	**Fri 17/10/25**	**Thu 8/1/26**	
1592	Falsework Dismantling	10 days	Fri 17/10/25	Wed 29/10/25	209
1593	Wall Erection	7 days	Thu 30/10/25	Thu 6/11/25	1592
1594	Wall Plastering & Skimming	8 days	Fri 7/11/25	Sat 15/11/25	1593
1595	Sanitary Piping	7 days	Fri 7/11/25	Fri 14/11/25	1593SS+7 days
1596	Floor Screeding	5 days	Mon 17/11/25	Fri 21/11/25	1594
1597	M&E Works Above Ceiling	10 days	Sat 22/11/25	Wed 3/12/25	1596
1598	False Ceiling Works	12 days	Thu 4/12/25	Wed 17/12/25	1597
1599	Painting	3 days	Thu 18/12/25	Sat 20/12/25	1598
1600	Grab Bar Installation	3 days	Mon 22/12/25	Wed 24/12/25	1599
1601	Vinyl Flooring	5 days	Thu 18/12/25	Tue 23/12/25	1598
1602	Fitments Installation	12 days	Wed 24/12/25	Thu 8/1/26	1601
1603	Solid Surface Installation	3 days	Sat 3/1/26	Tue 6/1/26	1602SS+7 days

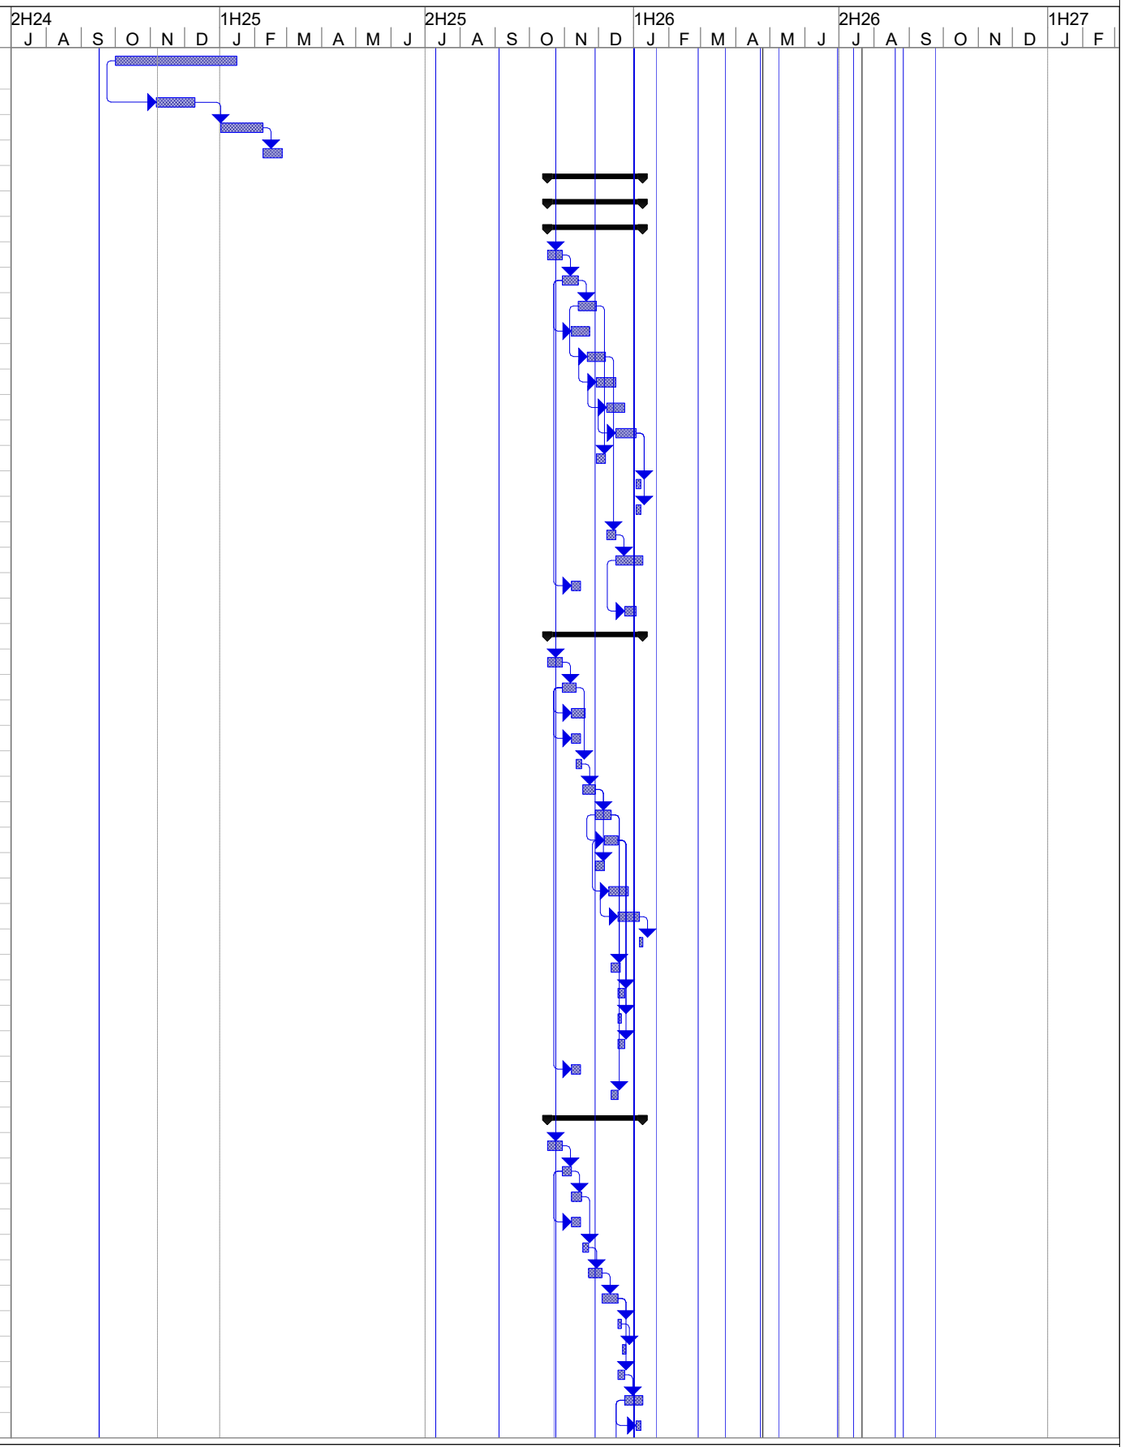

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone	
Split	External Tasks	Manual Task	Start-only	Progress	
Milestone	External Milestone	Duration-only	Finish-only	Deadline	
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks		


ID	Task Name	Duration	Start	Finish	Predecessors
1604	M&E 2nd Fix	7 days	Fri 7/11/25	Fri 14/11/25	1593SS+7 days
1605	M&E 3rd Fix	5 days	Sat 3/1/26	Thu 8/1/26	1602SS+7 days
1606	**Main Day Room 2 & Resident's Pantry 2**	**69 days**	**Fri 17/10/25**	**Thu 8/1/26**	
1607	Falsework Dismantling	10 days	Fri 17/10/25	Wed 29/10/25	209
1608	Wall Erection	10 days	Thu 30/10/25	Mon 10/11/25	1607
1609	Wall Plastering & Skimming	14 days	Tue 11/11/25	Wed 26/11/25	1608
1610	Sanitary Piping	14 days	Wed 19/11/25	Thu 4/12/25	1608FS+7 days
1611	Floor Screeding	10 days	Fri 5/12/25	Tue 16/12/25	1612
1612	M&E Works Above Ceiling	14 days	Wed 19/11/25	Thu 4/12/25	1609SS+7 days
1613	False Ceiling Works	14 days	Wed 17/12/25	Sat 3/1/26	1611
1614	Painting	3 days	Mon 5/1/26	Wed 7/1/26	1613
1615	Grab Bar Installation	1 day	Thu 8/1/26	Thu 8/1/26	1614
1616	Vinyl Flooring	7 days	Fri 5/12/25	Fri 12/12/25	1612
1617	Sanitary Wares Installation	7 days	Wed 31/12/25	Thu 8/1/26	1619
1618	Fitments Installation	12 days	Wed 17/12/25	Wed 31/12/25	1611
1619	Solid Surface Installation	4 days	Fri 26/12/25	Tue 30/12/25	1618SS+7 days
1620	M&E 2nd Fix	7 days	Tue 11/11/25	Tue 18/11/25	1608
1621	M&E 3rd Fix	6 days	Fri 2/1/26	Thu 8/1/26	1618
1622	**Nurse Station 2, WC Park 2, Staff Pantry 2**	**69 days**	**Fri 17/10/25**	**Thu 8/1/26**	
1623	Falsework Dismantling	10 days	Fri 17/10/25	Wed 29/10/25	209
1624	Wall Erection	10 days	Thu 30/10/25	Mon 10/11/25	1623
1625	Wall Plastering & Skimming	12 days	Tue 11/11/25	Mon 24/11/25	1624
1626	Sanitary Piping	4 days	Fri 7/11/25	Tue 11/11/25	1624SS+7 days
1627	Floor Screeding	6 days	Wed 12/11/25	Tue 18/11/25	1626
1628	M&E Works Above Ceiling	9 days	Wed 19/11/25	Fri 28/11/25	1627
1629	False Ceiling Works	14 days	Sat 29/11/25	Mon 15/12/25	1628
1630	Painting	3 days	Tue 16/12/25	Thu 18/12/25	1629
1631	Floor Tiling	7 days	Tue 16/12/25	Tue 23/12/25	1629
1632	Vinyl Flooring	5 days	Mon 8/12/25	Fri 12/12/25	1629SS+7 days
1633	Sanitary Wares Installation	3 days	Tue 6/1/26	Thu 8/1/26	1635SS+1 day
1634	Fitments Installation	10 days	Sat 13/12/25	Wed 24/12/25	1632
1635	Solid Surface Installation	3 days	Mon 5/1/26	Wed 7/1/26	1634FS+7 days
1636	M&E 2nd Fix	7 days	Fri 7/11/25	Fri 14/11/25	1624SS+7 days
1637	M&E 3rd Fix	6 days	Fri 26/12/25	Fri 2/1/26	1634
1638	**Prep Room 2**	**69 days**	**Fri 17/10/25**	**Thu 8/1/26**	
1639	Falsework Dismantling	10 days	Fri 17/10/25	Wed 29/10/25	209
1640	Wall Erection	10 days	Thu 30/10/25	Mon 10/11/25	1639
1641	Wall Plastering & Skimming	12 days	Tue 11/11/25	Mon 24/11/25	1640
1642	Door Frame Installation	2 days	Fri 7/11/25	Sat 8/11/25	1640SS+7 days
1643	Sanitary Piping	5 days	Tue 25/11/25	Sat 29/11/25	1641
1644	Floor Screeding	7 days	Tue 25/11/25	Tue 2/12/25	1641
1645	M&E Works Above Ceiling	10 days	Wed 19/11/25	Sat 29/11/25	1641SS+7 days
1646	False Ceiling Works	10 days	Mon 1/12/25	Thu 11/12/25	1645
1647	Painting	3 days	Fri 12/12/25	Mon 15/12/25	1646
1648	Door Panel Installation	1 day	Mon 8/12/25	Mon 8/12/25	1649
1649	Floor Tiling	4 days	Wed 3/12/25	Sat 6/12/25	1644
1650	Sanitary Wares Installation	3 days	Wed 24/12/25	Sat 27/12/25	1651
1651	Fitments Installation	14 days	Mon 8/12/25	Tue 23/12/25	1649
1652	Solid Surface Installation	5 days	Sat 3/1/26	Thu 8/1/26	1651FS+7 days
1653	M&E 2nd Fix	7 days	Fri 7/11/25	Fri 14/11/25	1640SS+7 days
1654	M&E 3rd Fix	6 days	Wed 24/12/25	Wed 31/12/25	1651
1655	**Quiet Room 2**	**69 days**	**Fri 17/10/25**	**Thu 8/1/26**	
1656	Falsework Dismantling	10 days	Fri 17/10/25	Wed 29/10/25	209
1657	Wall Erection	10 days	Thu 30/10/25	Mon 10/11/25	1656

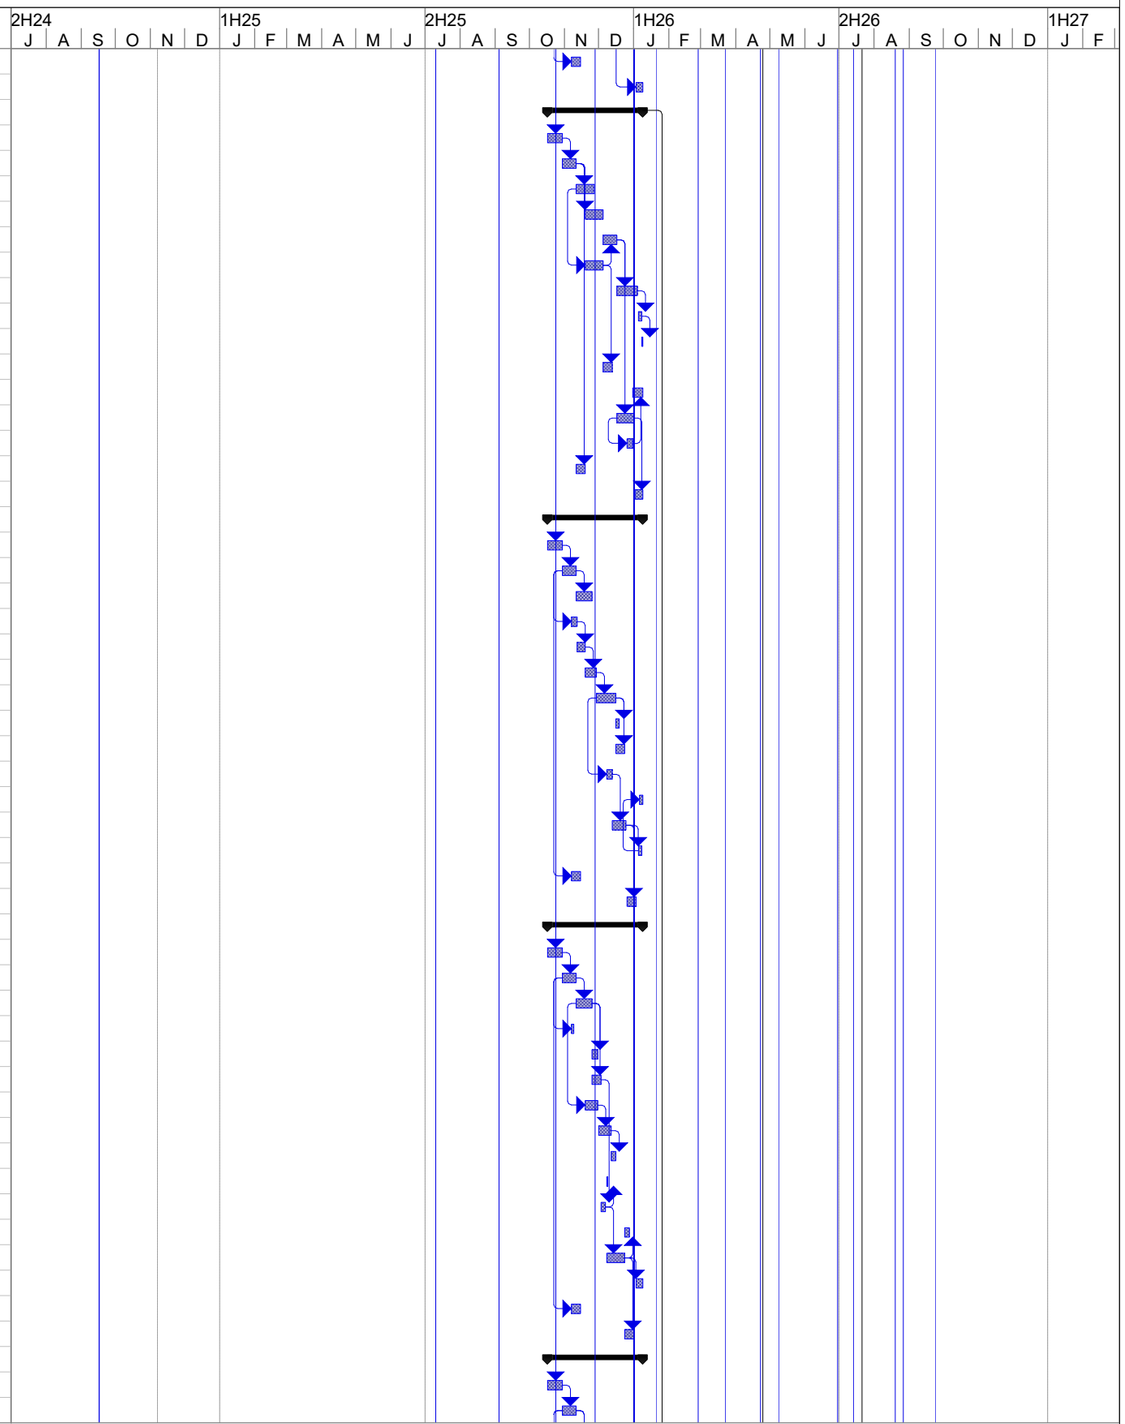

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	


ID	Task Name	Duration	Start	Finish	Predecessors
1658	Wall Plastering & Skimming	10 days	Tue 11/11/25	Fri 21/11/25	1657
1659	Door Frame Installation	2 days	Fri 7/11/25	Sat 8/11/25	1657SS+7 days
1660	Window Frame Installation	2 days	Fri 7/11/25	Sat 8/11/25	1657SS+7 days
1661	Floor Screeding	7 days	Sat 22/11/25	Sat 29/11/25	1658
1662	M&E Works Above Ceiling	12 days	Mon 1/12/25	Sat 13/12/25	1661
1663	False Ceiling Works	12 days	Mon 15/12/25	Mon 29/12/25	1662
1664	Painting	2 days	Tue 30/12/25	Wed 31/12/25	1663
1665	Door Panel Installation	1 day	Fri 2/1/26	Fri 2/1/26	1664
1666	Window Panel Installation	1 day	Sat 3/1/26	Sat 3/1/26	1665
1667	M&E 2nd Fix	7 days	Tue 11/11/25	Tue 18/11/25	1657
1668	M&E 3rd Fix	6 days	Fri 2/1/26	Thu 8/1/26	1664
1669	**Sluice Room 2**	**69 days**	**Fri 17/10/25**	**Thu 8/1/26**	
1670	Falsework Dismantling	10 days	Fri 17/10/25	Wed 29/10/25	209
1671	Wall Erection	10 days	Thu 30/10/25	Mon 10/11/25	1670
1672	Wall Plastering & Skimming	14 days	Tue 11/11/25	Wed 26/11/25	1671
1673	Door Frame Installation	2 days	Fri 7/11/25	Sat 8/11/25	1671SS+7 days
1674	Window Frame Installation	2 days	Mon 10/11/25	Tue 11/11/25	1673
1675	Sanitary Piping	7 days	Fri 7/11/25	Fri 14/11/25	1671SS+7 days
1676	Floor Screeding	7 days	Fri 7/11/25	Fri 14/11/25	1671SS+7 days
1677	M&E Works Above Ceiling	10 days	Sat 15/11/25	Wed 26/11/25	1676
1678	False Ceiling Works	9 days	Thu 27/11/25	Sat 6/12/25	1677
1679	Painting	3 days	Mon 8/12/25	Wed 10/12/25	1678
1680	Door Panel Installation	1 day	Thu 11/12/25	Thu 11/12/25	1679
1681	Window Panel Installation	1 day	Thu 11/12/25	Thu 11/12/25	1679
1682	Floor Tiling	4 days	Mon 8/12/25	Thu 11/12/25	1678
1683	Sanitary Wares Installation	5 days	Fri 12/12/25	Wed 17/12/25	1682
1684	Fitments Installation	12 days	Fri 12/12/25	Fri 26/12/25	1682
1685	Solid Surface Installation	3 days	Tue 6/1/26	Thu 8/1/26	1684FS+7 days
1686	M&E 2nd Fix	7 days	Tue 11/11/25	Tue 18/11/25	1671
1687	M&E 3rd Fix	6 days	Sat 27/12/25	Sat 3/1/26	1684
1688	**Common Area/Common Corridor/Lift Lobby**	**69 days**	**Fri 17/10/25**	**Thu 8/1/26**	
1689	Falsework Dismantling	10 days	Fri 17/10/25	Wed 29/10/25	209
1690	Wall Erection	10 days	Thu 30/10/25	Mon 10/11/25	1689
1691	Wall Plastering & Skimming	10 days	Tue 11/11/25	Fri 21/11/25	1690
1692	Floor Screeding	10 days	Tue 2/12/25	Fri 12/12/25	1693
1693	M&E Works Above Ceiling	11 days	Wed 19/11/25	Mon 1/12/25	1691SS+7 days
1694	False Ceiling Works	12 days	Sat 13/12/25	Sat 27/12/25	1692
1695	Painting	7 days	Mon 29/12/25	Tue 6/1/26	1694
1696	Floor Tiling	7 days	Sat 13/12/25	Sat 20/12/25	1692
1697	Vinyl Flooring	7 days	Mon 29/12/25	Tue 6/1/26	1694
1698	M&E 2nd Fix	7 days	Fri 7/11/25	Fri 14/11/25	1690SS+7 days
1699	M&E 3rd Fix	6 days	Fri 2/1/26	Thu 8/1/26	1695SS+3 days
1700	**Larger 4 Bedder 2-2**	**69 days**	**Fri 17/10/25**	**Thu 8/1/26**	
1701	Falsework Dismantling	10 days	Fri 17/10/25	Wed 29/10/25	209
1702	Wall Erection	14 days	Thu 30/10/25	Fri 14/11/25	1701
1703	Wall Plastering & Skimming	14 days	Fri 7/11/25	Sat 22/11/25	1702SS+7 days
1704	Drywall Installation	14 days	Mon 24/11/25	Tue 9/12/25	1703
1705	Floor Screeding	10 days	Tue 16/12/25	Sat 27/12/25	1707
1706	M&E Works Above Ceiling	12 days	Sat 15/11/25	Fri 28/11/25	1703SS+7 days
1707	False Ceiling Works	14 days	Sat 29/11/25	Mon 15/12/25	1706
1708	Painting	12 days	Tue 16/12/25	Tue 30/12/25	1707
1709	Window Installation	7 days	Sat 15/11/25	Sat 22/11/25	1702
1710	Curtain Track Installation	3 days	Wed 31/12/25	Sat 3/1/26	1708
1711	Vinyl Flooring	7 days	Tue 16/12/25	Tue 23/12/25	1707

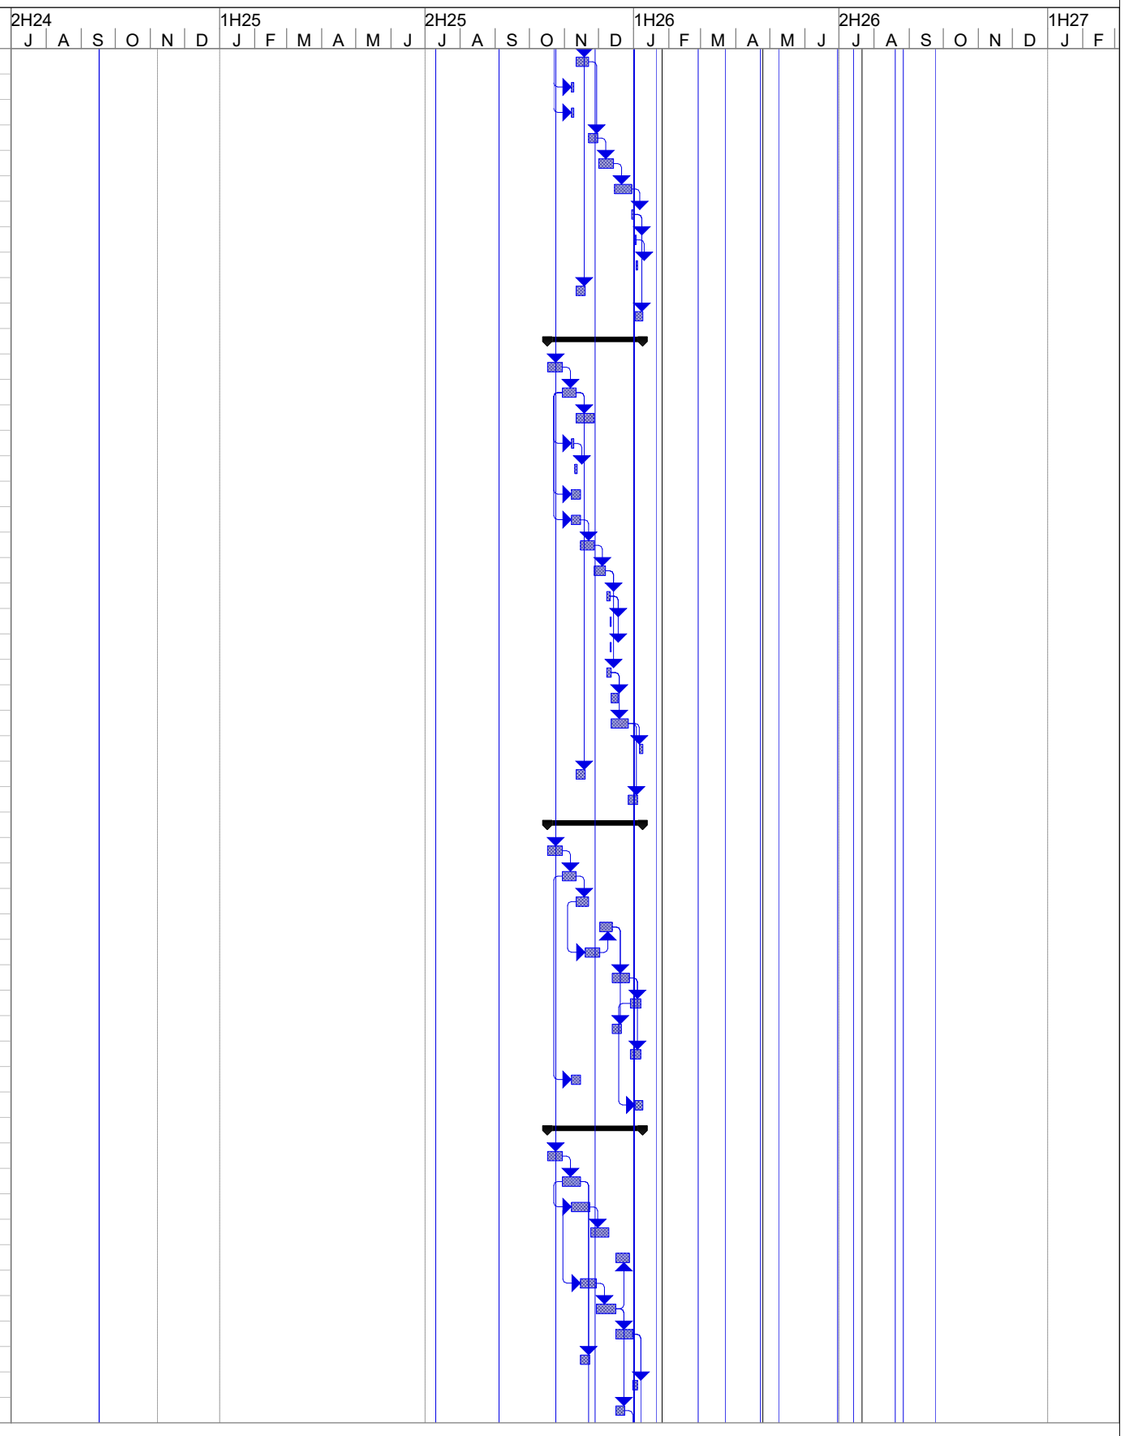

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	


ID	Task Name	Duration	Start	Finish	Predecessors
1712	Fitments Installation	12 days	Wed 24/12/25	Thu 8/1/26	1711
1713	M&E 2nd Fix	7 days	Sat 15/11/25	Sat 22/11/25	1702
1714	M&E 3rd Fix	7 days	Wed 31/12/25	Thu 8/1/26	1708
1715	**Single Bed 1 & 2**	**69 days**	**Fri 17/10/25**	**Thu 8/1/26**	
1716	Falsework Dismantling	10 days	Fri 17/10/25	Wed 29/10/25	209
1717	Wall Erection	14 days	Thu 30/10/25	Fri 14/11/25	1716
1718	Wall Plastering & Skimming	14 days	Fri 7/11/25	Sat 22/11/25	1717SS+7 days
1719	Drywall Installation	14 days	Mon 24/11/25	Tue 9/12/25	1718
1720	Floor Screeding	10 days	Tue 16/12/25	Sat 27/12/25	1722
1721	M&E Works Above Ceiling	12 days	Sat 15/11/25	Fri 28/11/25	1718SS+7 days
1722	False Ceiling Works	14 days	Sat 29/11/25	Mon 15/12/25	1721
1723	Painting	12 days	Tue 16/12/25	Tue 30/12/25	1722
1724	Window Installation	4 days	Wed 31/12/25	Mon 5/1/26	1723
1725	Curtain Track Installation	3 days	Wed 31/12/25	Sat 3/1/26	1723
1726	Vinyl Flooring	7 days	Tue 16/12/25	Tue 23/12/25	1722
1727	Fitments Installation	12 days	Wed 24/12/25	Thu 8/1/26	1726
1728	M&E 2nd Fix	7 days	Sat 15/11/25	Sat 22/11/25	1717
1729	M&E 3rd Fix	7 days	Wed 31/12/25	Thu 8/1/26	1727SS+5 days
1730	**Isolation Room 2**	**69 days**	**Fri 17/10/25**	**Thu 8/1/26**	
1731	Falsework Dismantling	10 days	Fri 17/10/25	Wed 29/10/25	209
1732	Wall Erection	14 days	Thu 30/10/25	Fri 14/11/25	1731
1733	Wall Plastering & Skimming	14 days	Fri 7/11/25	Sat 22/11/25	1732SS+7 days
1734	Drywall Installation	14 days	Mon 24/11/25	Tue 9/12/25	1733
1735	Floor Screeding	10 days	Tue 16/12/25	Sat 27/12/25	1737
1736	M&E Works Above Ceiling	12 days	Sat 15/11/25	Fri 28/11/25	1733SS+7 days
1737	False Ceiling Works	14 days	Sat 29/11/25	Mon 15/12/25	1736
1738	Painting	12 days	Tue 16/12/25	Tue 30/12/25	1737
1739	Window Installation	4 days	Wed 31/12/25	Mon 5/1/26	1738
1740	Curtain Track Installation	3 days	Wed 31/12/25	Sat 3/1/26	1738
1741	Vinyl Flooring	7 days	Tue 16/12/25	Tue 23/12/25	1737
1742	Fitments Installation	12 days	Wed 24/12/25	Thu 8/1/26	1741
1743	M&E 2nd Fix	7 days	Sat 15/11/25	Sat 22/11/25	1732
1744	M&E 3rd Fix	7 days	Wed 31/12/25	Thu 8/1/26	1742SS+5 days
1745	**Isolation Bath 2**	**69 days**	**Fri 17/10/25**	**Thu 8/1/26**	
1746	Falsework Dismantling	10 days	Fri 17/10/25	Wed 29/10/25	209
1747	Wall Erection	10 days	Thu 30/10/25	Mon 10/11/25	1746
1748	Wall Plastering & Skimming	10 days	Fri 7/11/25	Tue 18/11/25	1747SS+7 days
1749	Sanitary Piping	7 days	Fri 7/11/25	Fri 14/11/25	1747SS+7 days
1750	Application of Waterproofing	5 days	Tue 11/11/25	Sat 15/11/25	1747
1751	Floor Screeding	7 days	Mon 17/11/25	Mon 24/11/25	1750
1752	Wall Tiling	7 days	Tue 25/11/25	Tue 2/12/25	1751
1753	Floor Tiling	7 days	Wed 3/12/25	Wed 10/12/25	1752
1754	Door Frame/Sliding Door /Bi-Fold Door Track Installation	7 days	Fri 21/11/25	Fri 28/11/25	1751SS+4 days
1755	M&E Works Above Ceiling	11 days	Thu 11/12/25	Tue 23/12/25	1753
1756	False Ceiling Works	10 days	Wed 24/12/25	Tue 6/1/26	1755
1757	Painting	2 days	Wed 7/1/26	Thu 8/1/26	1756
1758	Window Installation	7 days	Wed 19/11/25	Wed 26/11/25	1748
1759	Grab Bar Installation	5 days	Thu 11/12/25	Tue 16/12/25	1753
1760	Door Panel Installation	3 days	Thu 11/12/25	Sat 13/12/25	1753
1761	Sanitary Wares Installation	5 days	Thu 11/12/25	Tue 16/12/25	1753
1762	M&E 2nd Fix	7 days	Tue 11/11/25	Tue 18/11/25	1747
1763	M&E 3rd Fix	5 days	Wed 17/12/25	Mon 22/12/25	1761
1764	**Decentralise Day Room 2**	**69 days**	**Fri 17/10/25**	**Thu 8/1/26**	
1765	Falsework Dismantling	10 days	Fri 17/10/25	Wed 29/10/25	209

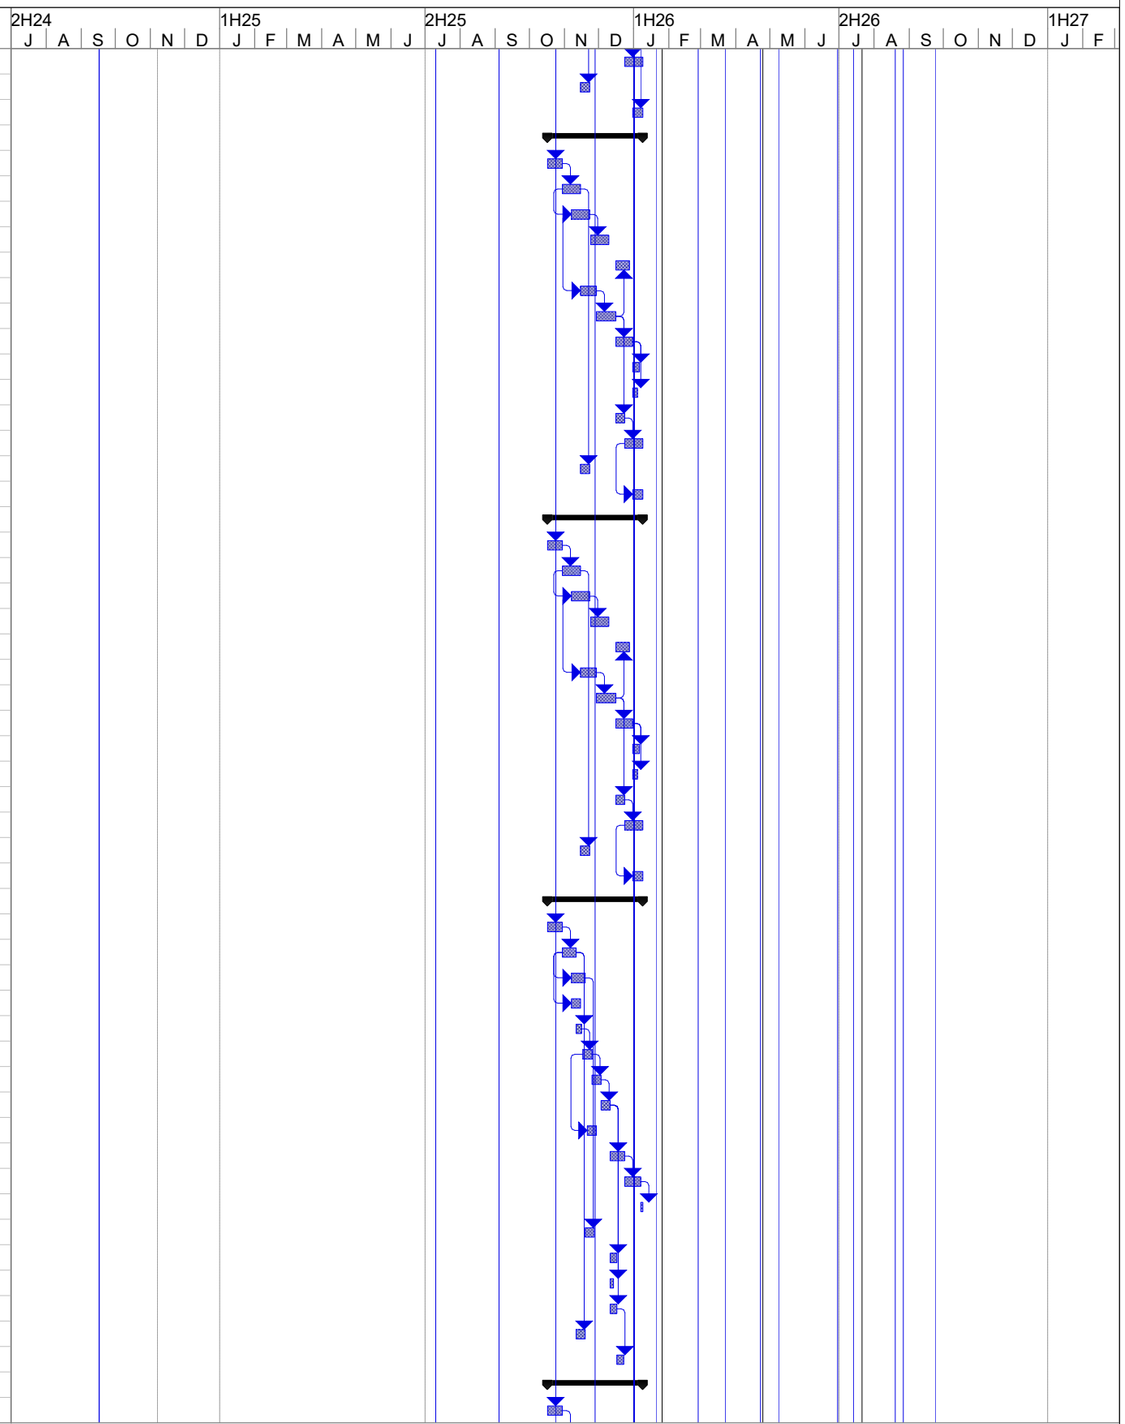

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	


ID	Task Name	Duration	Start	Finish	Predecessors
1766	Wall Erection	10 days	Thu 30/10/25	Mon 10/11/25	1765
1767	Wall Plastering & Skimming	10 days	Fri 7/11/25	Tue 18/11/25	1766SS+7 days
1768	Sanitary Piping	7 days	Fri 7/11/25	Fri 14/11/25	1766SS+7 days
1769	Floor Screeding	5 days	Wed 19/11/25	Mon 24/11/25	1767
1770	M&E Works Above Ceiling	10 days	Tue 25/11/25	Fri 5/12/25	1769
1771	False Ceiling Works	12 days	Sat 6/12/25	Fri 19/12/25	1770
1772	Painting	3 days	Sat 20/12/25	Tue 23/12/25	1771
1773	Grab Bar Installation	3 days	Wed 24/12/25	Sat 27/12/25	1772
1774	Vinyl Flooring	7 days	Sat 6/12/25	Sat 13/12/25	1770
1775	Fitments Installation	12 days	Mon 15/12/25	Mon 29/12/25	1774
1776	Solid Surface Installation	3 days	Tue 6/1/26	Thu 8/1/26	1775FS+5 days
1777	M&E 2nd Fix	7 days	Tue 11/11/25	Tue 18/11/25	1766
1778	M&E 3rd Fix	5 days	Tue 30/12/25	Mon 5/1/26	1775
1779	**Sky Terrace & Planter**	**69 days**	**Fri 17/10/25**	**Thu 8/1/26**	
1780	Falsework Dismantling	12 days	Fri 17/10/25	Fri 31/10/25	209
1781	Wall Plastering & Skimming	12 days	Sat 1/11/25	Fri 14/11/25	1780
1782	Application of Waterproofing	7 days	Sat 15/11/25	Sat 22/11/25	1781
1783	Floor Screeding	5 days	Mon 24/11/25	Fri 28/11/25	1782
1784	M&E Works Above Ceiling	9 days	Sat 29/11/25	Tue 9/12/25	1783
1785	False Ceiling Works	8 days	Wed 10/12/25	Thu 18/12/25	1784
1786	Painting	3 days	Fri 19/12/25	Mon 22/12/25	1785
1787	Railing Installation	14 days	Fri 19/12/25	Tue 6/1/26	1785
1788	Planter Water Discharge Pipe	1 day	Wed 7/1/26	Wed 7/1/26	1787
1789	Planting Soil	1 day	Thu 8/1/26	Thu 8/1/26	1788
1790	M&E 2nd Fix	7 days	Wed 5/11/25	Wed 12/11/25	1781SS+3 days
1791	M&E 3rd Fix	5 days	Tue 23/12/25	Mon 29/12/25	1786
1792	MOHH/Consultants/Operator Review	1 day	Mon 26/1/26	Mon 26/1/26	1606FS+14 days
1793	Approval to proceed with materials procurment	7 days	Tue 27/1/26	Tue 3/2/26	1792
1794	**Mock-up 2**	**622 days**	**Tue 1/10/24**	**Tue 20/10/26**	
1795	**Bedroom 5-1, 5-2, 5-3 & 5-4**	**49 days**	**Fri 26/12/25**	**Tue 24/2/26**	
1796	Falsework Dismantling	10 days	Fri 26/12/25	Wed 7/1/26	294
1797	Wall Erection	7 days	Thu 8/1/26	Thu 15/1/26	1796
1798	Wall Plastering & Skimming	10 days	Mon 12/1/26	Thu 22/1/26	1797SS+3 days
1799	Drywall Installation	7 days	Sat 31/1/26	Sat 7/2/26	1800
1800	Floor Screeding	7 days	Fri 23/1/26	Fri 30/1/26	1798
1801	M&E Works Above Ceiling	12 days	Tue 27/1/26	Mon 9/2/26	1800SS+3 days
1802	False Ceiling Works	12 days	Fri 30/1/26	Thu 12/2/26	1801SS+3 days
1803	Painting	10 days	Tue 3/2/26	Fri 13/2/26	1802SS+3 days
1804	Window Installation	2 days	Sat 31/1/26	Mon 2/2/26	1800
1805	Curtain Track Installation	3 days	Sat 7/2/26	Tue 10/2/26	1802SS+7 days
1806	Grab Bar Installation	2 days	Sat 14/2/26	Mon 16/2/26	1803
1807	Vinyl Flooring	3 days	Fri 13/2/26	Mon 16/2/26	1802
1808	Fitments Installation	6 days	Mon 16/2/26	Tue 24/2/26	1807SS+2 days
1809	M&E 2nd Fix	7 days	Fri 16/1/26	Fri 23/1/26	1797
1810	M&E 3rd Fix	5 days	Sat 14/2/26	Sat 21/2/26	1803
1811	**Decentralised Day Room 5**	**49 days**	**Fri 26/12/25**	**Tue 24/2/26**	
1812	Falsework Dismantling	10 days	Fri 26/12/25	Wed 7/1/26	294
1813	Wall Erection	7 days	Thu 8/1/26	Thu 15/1/26	1812
1814	Wall Plastering & Skimming	10 days	Mon 12/1/26	Thu 22/1/26	1813SS+3 days
1815	Sanitary Piping	3 days	Mon 12/1/26	Wed 14/1/26	1813SS+3 days
1816	Floor Screeding	3 days	Fri 23/1/26	Mon 26/1/26	1814
1817	M&E Works Above Ceiling	12 days	Tue 27/1/26	Mon 9/2/26	1816SS+3 days
1818	False Ceiling Works	5 days	Fri 30/1/26	Wed 4/2/26	1817SS+3 days
1819	Painting	3 days	Thu 5/2/26	Sat 7/2/26	1818

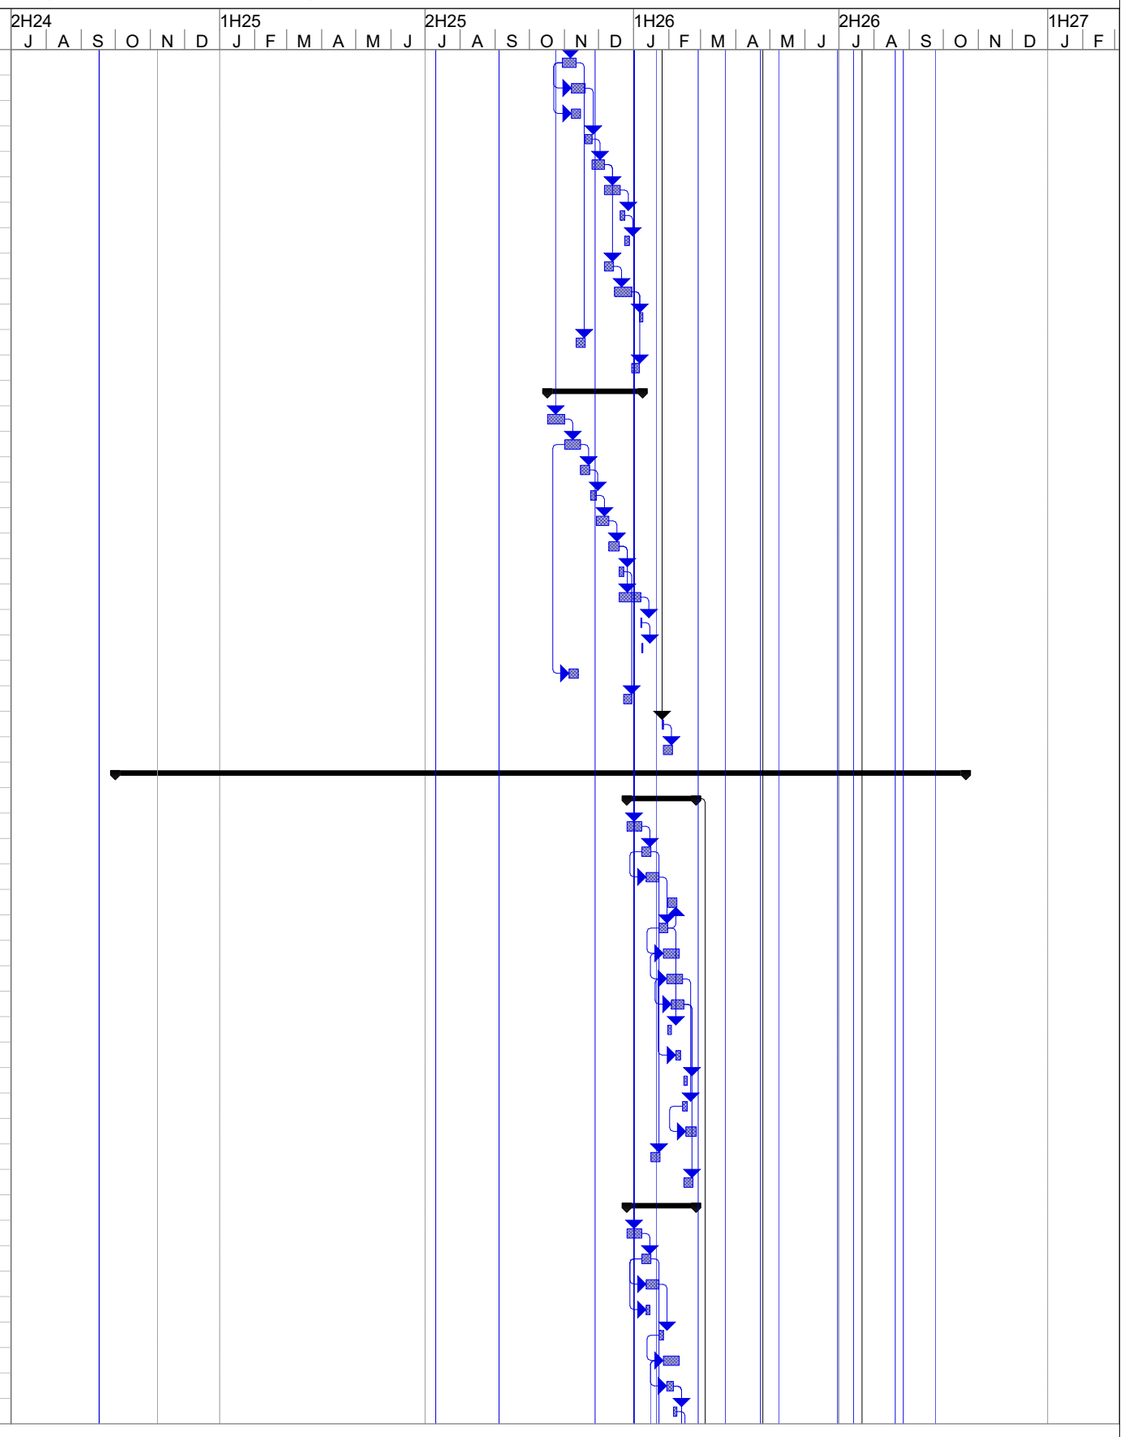

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Progress | Deadline


ID	Task Name	Duration	Start	Finish	Predecessors
1820	Grab Bar Installation	2 days	Mon 9/2/26	Tue 10/2/26	1819
1821	Vinyl Flooring	3 days	Thu 5/2/26	Sat 7/2/26	1818
1822	Fitments Installation	12 days	Fri 30/1/26	Thu 12/2/26	1817SS+3 days
1823	Solid Surface Installation	3 days	Sat 21/2/26	Tue 24/2/26	1822FS+5 days
1824	Installation of Sanitary Ware	1 day	Sat 21/2/26	Sat 21/2/26	1823SS
1825	M&E 2nd Fix	7 days	Fri 16/1/26	Fri 23/1/26	1813
1826	M&E 3rd Fix	5 days	Fri 13/2/26	Fri 20/2/26	1822
1827	**Bath 5, Toilet 5, Assisted Bath 5**	**49 days**	**Fri 26/12/25**	**Tue 24/2/26**	
1828	Falsework Dismantling	10 days	Fri 26/12/25	Wed 7/1/26	294
1829	Wall Erection	7 days	Thu 8/1/26	Thu 15/1/26	1828
1830	Wall Plastering & Skimming	7 days	Mon 12/1/26	Mon 19/1/26	1829SS+3 days
1831	Sanitary Piping	3 days	Mon 12/1/26	Wed 14/1/26	1829SS+3 days
1832	Application of Waterproofing	3 days	Thu 15/1/26	Sat 17/1/26	1831
1833	Floor Screeding	3 days	Mon 19/1/26	Wed 21/1/26	1832
1834	Wall Tiling	6 days	Thu 22/1/26	Wed 28/1/26	1833
1835	Floor Tiling	5 days	Thu 29/1/26	Tue 3/2/26	1834
1836	Door Frame/Sliding Door /Bi-Fold Door Track Installation	1 day	Wed 21/1/26	Wed 21/1/26	1833SS+2 days
1837	M&E Works Above Ceiling	12 days	Wed 4/2/26	Thu 19/2/26	1835
1838	False Ceiling Works	13 days	Sat 7/2/26	Tue 24/2/26	1837SS+3 days
1839	Painting	3 days	Tue 10/2/26	Thu 12/2/26	1838SS+2 days
1840	Window Installation	2 days	Thu 29/1/26	Fri 30/1/26	1834
1841	Grab Bar Installation	2 days	Thu 29/1/26	Fri 30/1/26	1834
1842	Door Panel Installation	2 days	Thu 29/1/26	Fri 30/1/26	1834
1843	Sanitary Wares Installation	1 day	Wed 4/2/26	Wed 4/2/26	1835
1844	M&E 2nd Fix	7 days	Mon 12/1/26	Mon 19/1/26	1829SS+3 days
1845	M&E 3rd Fix	5 days	Fri 13/2/26	Fri 20/2/26	1839
1846	**Isolation Room 1**	**49 days**	**Fri 26/12/25**	**Tue 24/2/26**	
1847	Falsework Dismantling	10 days	Fri 26/12/25	Wed 7/1/26	294
1848	Wall Erection	7 days	Thu 8/1/26	Thu 15/1/26	1847
1849	Wall Plastering & Skimming	10 days	Mon 12/1/26	Thu 22/1/26	1848SS+3 days
1850	Drywall Installation	7 days	Fri 23/1/26	Fri 30/1/26	1849
1851	Floor Screeding	3 days	Fri 23/1/26	Mon 26/1/26	1849
1852	M&E Works Above Ceiling	12 days	Tue 27/1/26	Mon 9/2/26	1851
1853	False Ceiling Works	12 days	Fri 30/1/26	Thu 12/2/26	1852SS+3 days
1854	Painting	3 days	Fri 13/2/26	Mon 16/2/26	1853
1855	Window Installation	1 day	Thu 19/2/26	Thu 19/2/26	1854
1856	Curtain Track Installation	2 days	Fri 13/2/26	Sat 14/2/26	1853
1857	Vinyl Flooring	3 days	Tue 27/1/26	Thu 29/1/26	1851
1858	Fitments Installation	12 days	Fri 30/1/26	Thu 12/2/26	1857
1859	M&E 2nd Fix	7 days	Mon 12/1/26	Mon 19/1/26	1848SS+3 days
1860	M&E 3rd Fix	8 days	Fri 13/2/26	Tue 24/2/26	1858
1861	**Isolation Bath 1**	**49 days**	**Fri 26/12/25**	**Tue 24/2/26**	
1862	Falsework Dismantling	10 days	Fri 26/12/25	Wed 7/1/26	294
1863	Wall Erection	7 days	Thu 8/1/26	Thu 15/1/26	1862
1864	Wall Plastering & Skimming	10 days	Mon 12/1/26	Thu 22/1/26	1863SS+3 days
1865	Sanitary Piping	3 days	Mon 12/1/26	Wed 14/1/26	1863SS+3 days
1866	Application of Waterproofing	3 days	Thu 15/1/26	Sat 17/1/26	1865
1867	Floor Screeding	3 days	Mon 19/1/26	Wed 21/1/26	1866
1868	Wall Tiling	6 days	Thu 22/1/26	Wed 28/1/26	1867
1869	Floor Tiling	5 days	Thu 29/1/26	Tue 3/2/26	1868
1870	Door Frame/Sliding Door /Bi-Fold Door Track Installation	1 day	Wed 21/1/26	Wed 21/1/26	1867SS+2 days
1871	M&E Works Above Ceiling	12 days	Wed 4/2/26	Thu 19/2/26	1869
1872	False Ceiling Works	12 days	Sat 7/2/26	Mon 23/2/26	1871SS+3 days
1873	Painting	3 days	Tue 10/2/26	Thu 12/2/26	1872SS+2 days

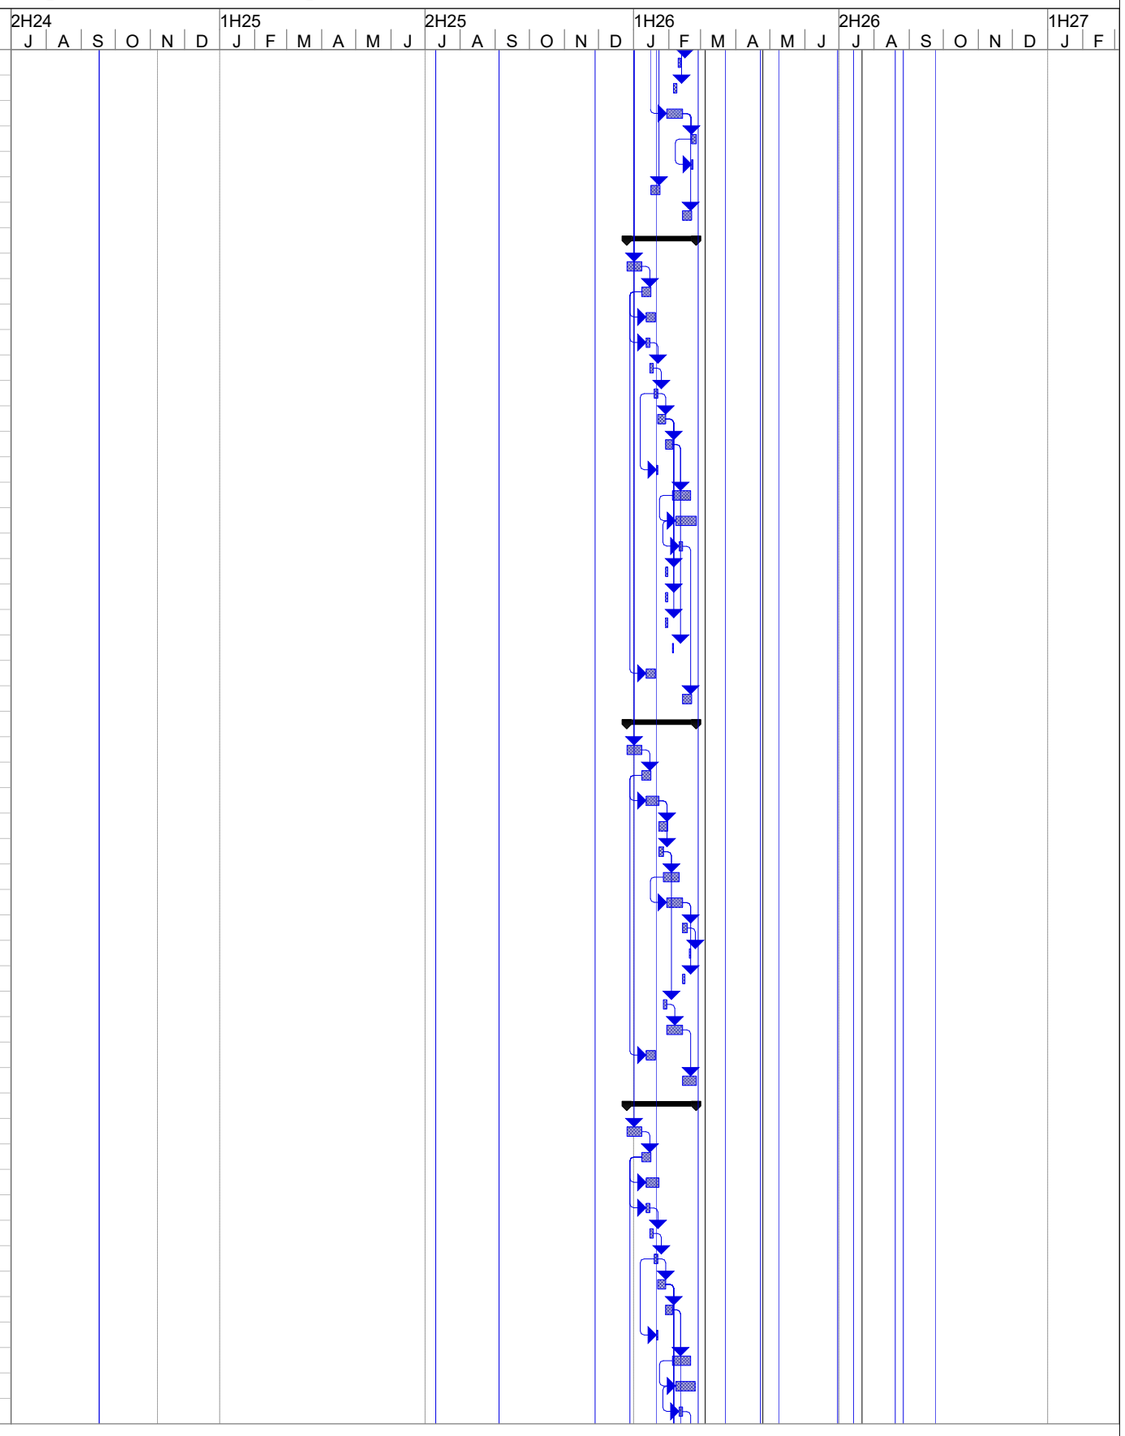

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task | Split | Milestone | Summary
Project Summary | External Tasks | External Milestone | Inactive Milestone
Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup
Manual Summary | Start-only | Finish-only | External Tasks
External Milestone | Progress | Deadline


ID	Task Name	Duration	Start	Finish	Predecessors
1874	Window Installation	2 days	Thu 29/1/26	Fri 30/1/26	1868
1875	Grab Bar Installation	2 days	Thu 29/1/26	Fri 30/1/26	1868
1876	Door Panel Installation	3 days	Thu 29/1/26	Sat 31/1/26	1868
1877	Sanitary Wares Installation	1 day	Wed 4/2/26	Wed 4/2/26	1869
1878	M&E 2nd Fix	7 days	Mon 12/1/26	Mon 19/1/26	1863SS+3 days
1879	M&E 3rd Fix	8 days	Fri 13/2/26	Tue 24/2/26	1873
1880	MOHH/Consultants/Operator Review	14 days	Thu 5/3/26	Sat 21/3/26	1795FS+7 days
1881	Approval to proceed with materials procurment	7 days	Mon 23/3/26	Mon 30/3/26	1880
1882	**Mock-up 3 - Façade paint**	**72 days**	**Sat 13/9/25**	**Sat 6/12/25**	
1883	Material/shop-drwgs submissions, review, selection & approval	30 days	Sat 13/9/25	Fri 17/10/25	
1884	Procurement of materials	30 days	Sat 18/10/25	Sat 22/11/25	1883
1885	Site installation for mock up approval	8 days	Fri 28/11/25	Sat 6/12/25	293FS+7 days
1886	Review, comments, rectifications & approval	14 days	Mon 8/12/25	Tue 23/12/25	1885
1887	Approval to proceed with materials procurment	7 days	Wed 24/12/25	Fri 2/1/26	1886
1888	**Mock-up 1 - Lift car interior (Offsite)**	**108 days**	**Tue 1/10/24**	**Fri 7/2/25**	
1889	Material/shop-drwgs submissions, review, selection & approval	77 days	Tue 1/10/24	Mon 30/12/24	1009SS
1890	Procurement of materials & installation for site mock up approval	31 days	Tue 31/12/24	Fri 7/2/25	1889
1891	Review, comments, rectifications & approval	7 days	Sat 8/2/25	Sat 15/2/25	1890
1892	Approval to proceed with materials procurment	6 days	Mon 17/2/25	Sat 22/2/25	1891
1893	**Sky Signage (ECON)**	**327 days**	**Mon 22/9/25**	**Tue 20/10/26**	
1894	Shopdrawing Submission & Approval	60 days	Mon 22/9/25	Mon 1/12/25	
1895	Paper Mock Up Fabrication & Installation	30 days	Wed 1/7/26	Tue 4/8/26	
1896	Review & approval	14 days	Wed 5/8/26	Fri 21/8/26	1895
1897	Off-Site Fabrication & Installation	30 days	Sat 22/8/26	Fri 25/9/26	1896
1898	Review, comments, rectifications & approval	14 days	Sat 26/9/26	Mon 12/10/26	1897
1899	Approval to proceed with materials procurment	7 days	Tue 13/10/26	Tue 20/10/26	1898
1900	**Polyclinic Block**	**502 days**	**Tue 1/10/24**	**Sat 30/5/26**	
1901	**Mock-up**	**109 days**	**Thu 3/7/25**	**Sat 8/11/25**	
1902	**Acute Consultation Room**	**109 days**	**Thu 3/7/25**	**Sat 8/11/25**	
1903	Falsework Dismantling	10 days	Thu 3/7/25	Mon 14/7/25	206
1904	Carcass Erection	23 days	Tue 15/7/25	Mon 11/8/25	1903
1905	Drywall Installation	16 days	Tue 12/8/25	Fri 29/8/25	1904
1906	Sanitary Piping	5 days	Sat 30/8/25	Thu 4/9/25	1905
1907	Floor Screeding	5 days	Fri 5/9/25	Wed 10/9/25	1906
1908	Timber Sliding/Swing Door Frame Installation	1 day	Thu 11/9/25	Thu 11/9/25	1907
1909	M&E Works Above Ceiling	14 days	Sat 30/8/25	Mon 15/9/25	1905
1910	False Ceiling Works	14 days	Tue 16/9/25	Wed 1/10/25	1909
1911	Curtain Track Installation	5 days	Sat 4/10/25	Thu 9/10/25	1914
1912	Grab Bar Installation	1 day	Sat 4/10/25	Sat 4/10/25	1914
1913	Wall Protection Installation	1 day	Sat 4/10/25	Sat 4/10/25	1914
1914	Painting	2 days	Thu 2/10/25	Fri 3/10/25	1910
1915	Door Panel Installation	1 day	Sat 4/10/25	Sat 4/10/25	1914
1916	Vinyl Flooring	3 days	Mon 6/10/25	Wed 8/10/25	1915
1917	Fitments Installation	21 days	Thu 9/10/25	Mon 3/11/25	1916
1918	Solid Surface Fabrication & Installation	7 days	Fri 10/10/25	Fri 17/10/25	1919
1919	Sanitary Wares Installation	5 days	Sat 4/10/25	Thu 9/10/25	1914
1920	M&E 2nd Fix	7 days	Sat 30/8/25	Sat 6/9/25	1905
1921	M&E 3rd Fix	5 days	Tue 4/11/25	Sat 8/11/25	1917
1922	**Dental Consultation Room**	**109 days**	**Thu 3/7/25**	**Sat 8/11/25**	
1923	Falsework Dismantling	10 days	Thu 3/7/25	Mon 14/7/25	206
1924	Carcass Erection	23 days	Tue 15/7/25	Mon 11/8/25	1923
1925	Drywall Installation	7 days	Tue 12/8/25	Tue 19/8/25	1924

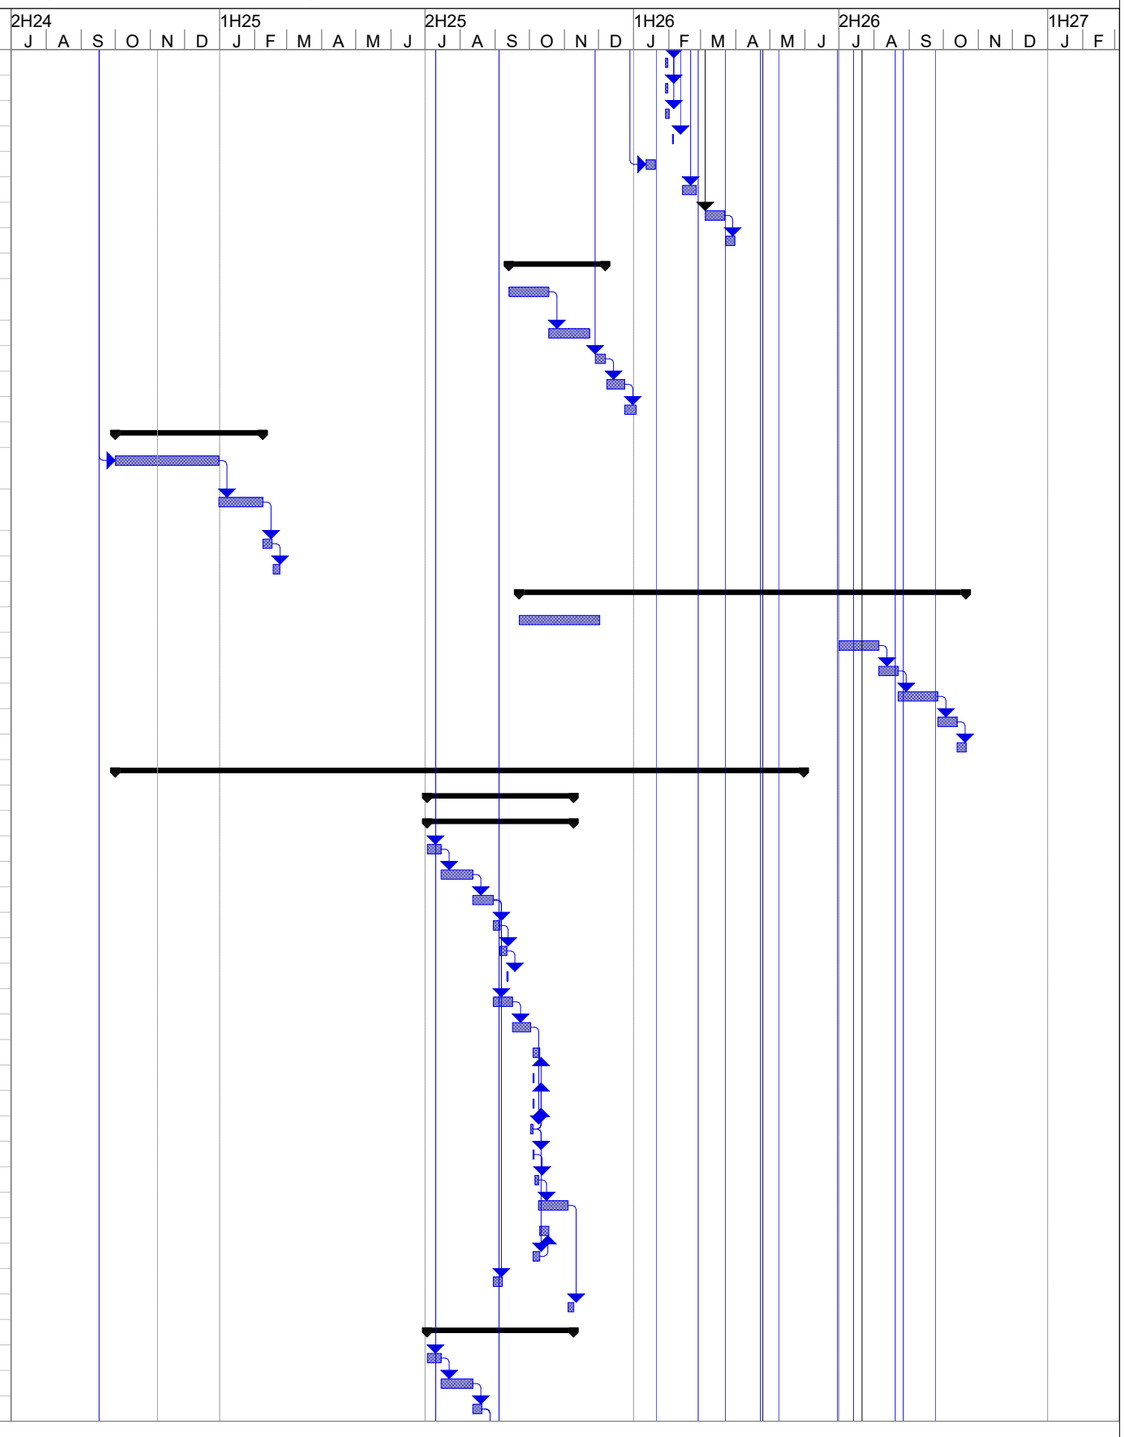

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	


ID	Task Name	Duration	Start	Finish	Predecessors
1926	Sanitary Piping	5 days	Wed 20/8/25	Mon 25/8/25	1925
1927	Window Frame Installation	1 day	Wed 20/8/25	Wed 20/8/25	1925
1928	Floor Screeding	7 days	Tue 26/8/25	Tue 2/9/25	1926
1929	Swing Door Frame	1 day	Wed 3/9/25	Wed 3/9/25	1928
1930	M&E Works Above Ceiling	12 days	Wed 3/9/25	Tue 16/9/25	1928
1931	False Ceiling Works	12 days	Wed 17/9/25	Tue 30/9/25	1930
1932	Window Installation	1 day	Wed 1/10/25	Wed 1/10/25	1931
1933	Painting	2 days	Wed 1/10/25	Thu 2/10/25	1931
1934	Door Panel Installation	1 day	Fri 3/10/25	Fri 3/10/25	1933
1935	Vinyl Flooring	3 days	Sat 4/10/25	Tue 7/10/25	1934
1936	Fitments Installation	14 days	Wed 8/10/25	Fri 24/10/25	1935
1937	Solid Surface Fabrication & Installation	7 days	Sat 25/10/25	Sat 1/11/25	1936
1938	Sanitary Wares Installation	6 days	Mon 3/11/25	Sat 8/11/25	1937
1939	M&E 2nd Fix	7 days	Wed 20/8/25	Wed 27/8/25	1925
1940	M&E 3rd Fix	5 days	Sat 25/10/25	Thu 30/10/25	1936
1941	**Chronic Consultation Room**	**109 days**	**Thu 3/7/25**	**Sat 8/11/25**	
1942	Falsework Dismantling	10 days	Thu 3/7/25	Mon 14/7/25	206
1943	Carcass Erection	23 days	Tue 15/7/25	Mon 11/8/25	1942
1944	Drywall Installation	7 days	Tue 12/8/25	Tue 19/8/25	1943
1945	Sanitary Piping	5 days	Wed 20/8/25	Mon 25/8/25	1944
1946	Window Frame Installation	1 day	Wed 20/8/25	Wed 20/8/25	1944
1947	Floor Screeding	7 days	Tue 26/8/25	Tue 2/9/25	1945
1948	Sliding Door Frame Installation	1 day	Wed 3/9/25	Wed 3/9/25	1947
1949	M&E Works Above Ceiling	12 days	Wed 3/9/25	Tue 16/9/25	1947
1950	False Ceiling Works	12 days	Wed 17/9/25	Tue 30/9/25	1949
1951	Window Installation	1 day	Wed 1/10/25	Wed 1/10/25	1950
1952	Curtain Track Installation	1 day	Fri 3/10/25	Fri 3/10/25	1954
1953	Wall Protection Installation	1 day	Fri 3/10/25	Fri 3/10/25	1954
1954	Painting	2 days	Wed 1/10/25	Thu 2/10/25	1950
1955	Door Panel Installation	1 day	Fri 3/10/25	Fri 3/10/25	1954
1956	Vinyl Flooring	3 days	Sat 4/10/25	Tue 7/10/25	1955
1957	Fitments Installation	14 days	Wed 8/10/25	Fri 24/10/25	1956
1958	Solid Surface Fabrication & Installation	7 days	Sat 25/10/25	Sat 1/11/25	1957
1959	Sanitary Wares Installation	6 days	Mon 3/11/25	Sat 8/11/25	1958
1960	M&E 2nd Fix	7 days	Wed 20/8/25	Wed 27/8/25	1944
1961	M&E 3rd Fix	5 days	Sat 25/10/25	Thu 30/10/25	1957
1962	**Phlebo Station**	**109 days**	**Thu 3/7/25**	**Sat 8/11/25**	
1963	Falsework Dismantling	10 days	Thu 3/7/25	Mon 14/7/25	206
1964	Carcass Erection	23 days	Tue 15/7/25	Mon 11/8/25	1963
1965	Drywall Installation	14 days	Tue 12/8/25	Wed 27/8/25	1964
1966	Sliding Timber Window Frame	1 day	Thu 28/8/25	Thu 28/8/25	1965
1967	Floor Screeding	7 days	Thu 28/8/25	Thu 4/9/25	1965
1968	M&E Works Above Ceiling	12 days	Fri 5/9/25	Thu 18/9/25	1967
1969	False Ceiling Works	12 days	Fri 19/9/25	Thu 2/10/25	1968
1970	Sliding Timber Window	1 day	Fri 3/10/25	Fri 3/10/25	1969
1971	Curtain Track Installation	1 day	Mon 6/10/25	Mon 6/10/25	1973
1972	Wall Protection Installation	1 day	Mon 6/10/25	Mon 6/10/25	1973
1973	Painting	2 days	Fri 3/10/25	Sat 4/10/25	1969
1974	Vinyl Flooring	3 days	Mon 6/10/25	Wed 8/10/25	1973
1975	Fitments Installation	21 days	Thu 9/10/25	Mon 3/11/25	1974
1976	M&E 2nd Fix	7 days	Thu 28/8/25	Thu 4/9/25	1965
1977	M&E 3rd Fix	5 days	Tue 4/11/25	Sat 8/11/25	1975
1978	**Pharmacy Dispensing Counter**	**109 days**	**Thu 3/7/25**	**Sat 8/11/25**	
1979	Falsework Dismantling	10 days	Thu 3/7/25	Mon 14/7/25	206

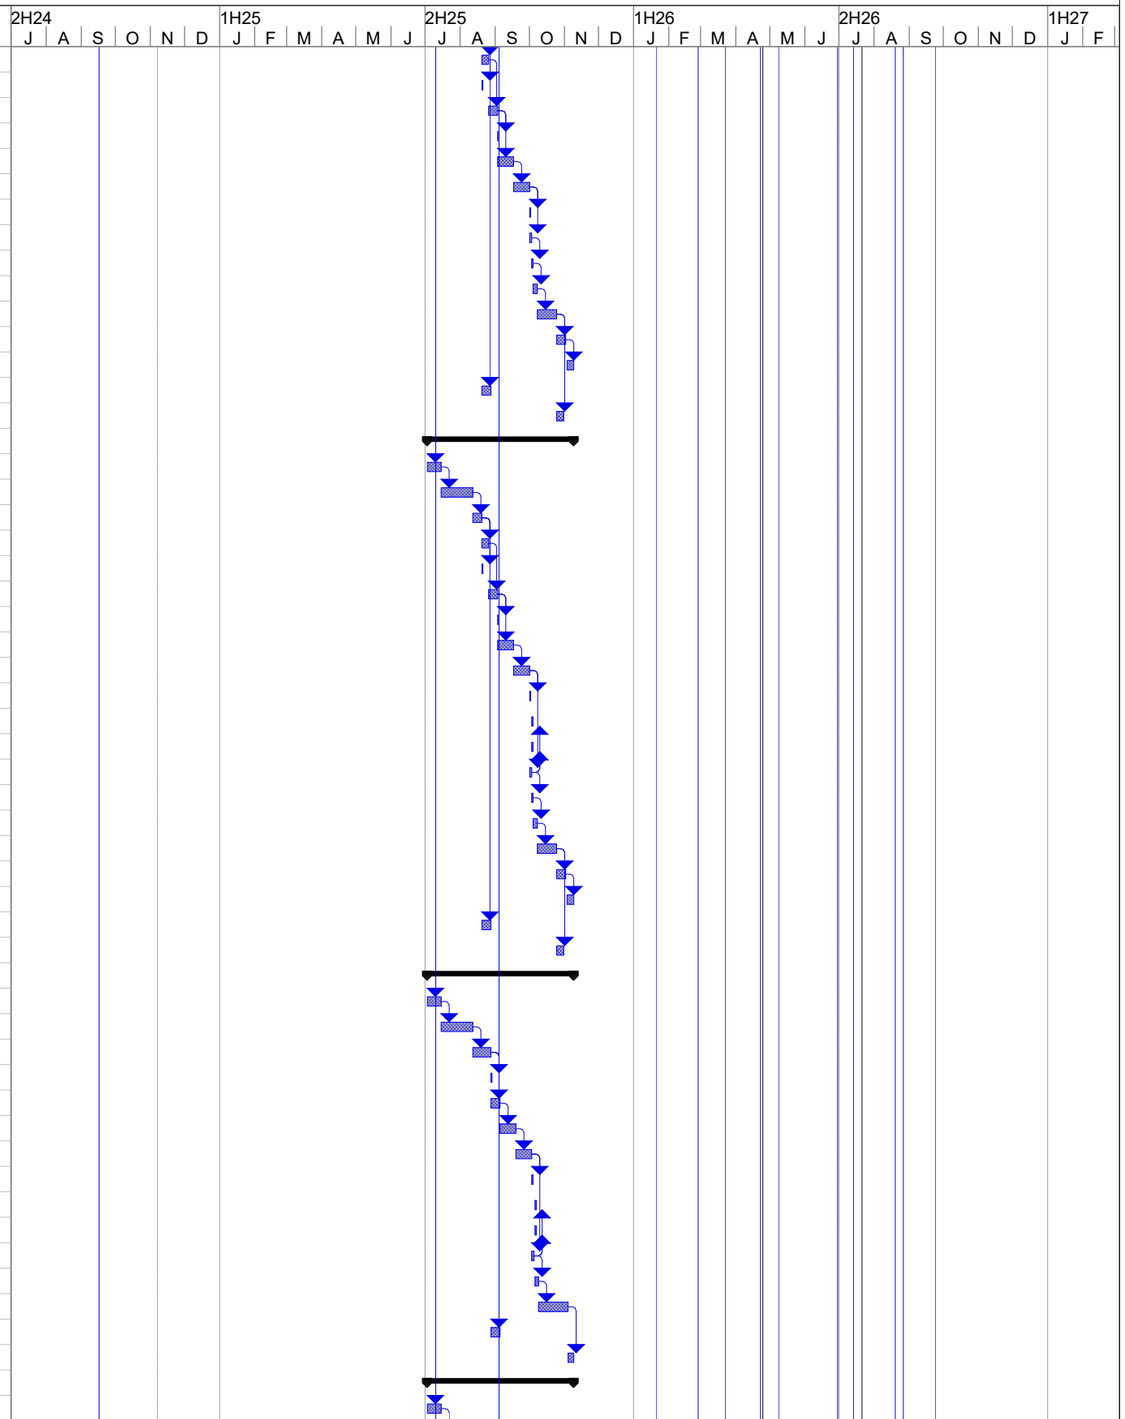

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Progress | Deadline

ID	Task Name	Duration	Start	Finish	Predecessors
1980	Carcass Erection	23 days	Tue 15/7/25	Mon 11/8/25	1979
1981	Floor Screeding	14 days	Tue 12/8/25	Wed 27/8/25	1980
1982	M&E Works Above Ceiling	12 days	Thu 28/8/25	Wed 10/9/25	1981
1983	False Ceiling Works	12 days	Thu 11/9/25	Wed 24/9/25	1982
1984	Vinyl Flooring	3 days	Thu 25/9/25	Sat 27/9/25	1983
1985	Fitments Installation	30 days	Mon 29/9/25	Mon 3/11/25	1984
1986	M&E 2nd Fix	7 days	Tue 12/8/25	Tue 19/8/25	1980
1987	M&E 3rd Fix	5 days	Tue 4/11/25	Sat 8/11/25	1985
1988	**Health Monitoring Station**	**109 days**	**Thu 3/7/25**	**Sat 8/11/25**	
1989	Falsework Dismantling	10 days	Thu 3/7/25	Mon 14/7/25	206
1990	Carcass Erection	23 days	Tue 15/7/25	Mon 11/8/25	1989
1991	Floor Screeding	7 days	Tue 12/8/25	Tue 19/8/25	1990
1992	M&E Works Above Ceiling	15 days	Wed 20/8/25	Fri 5/9/25	1991
1993	False Ceiling Works	16 days	Sat 6/9/25	Wed 24/9/25	1992
1994	Painting	2 days	Thu 25/9/25	Fri 26/9/25	1993
1995	Vinyl Flooring	3 days	Thu 25/9/25	Sat 27/9/25	1993
1996	Fitments Installation	30 days	Mon 29/9/25	Mon 3/11/25	1995
1997	M&E 2nd Fix	7 days	Tue 12/8/25	Tue 19/8/25	1990
1998	M&E 3rd Fix	5 days	Tue 4/11/25	Sat 8/11/25	1996
1999	**Toilet (F/M) & Accessible Toilet**	**109 days**	**Thu 3/7/25**	**Sat 8/11/25**	
2000	Falsework Dismantling	10 days	Thu 3/7/25	Mon 14/7/25	206
2001	Carcass Erection	23 days	Tue 15/7/25	Mon 11/8/25	2000
2002	Drywall Installation	14 days	Tue 12/8/25	Wed 27/8/25	2001
2003	Sanitary Piping	7 days	Thu 28/8/25	Thu 4/9/25	2002
2004	Window Frame Installation	2 days	Fri 5/9/25	Sat 6/9/25	2003
2005	Floor Screeding	7 days	Fri 5/9/25	Fri 12/9/25	2003
2006	Wall Tiling	10 days	Tue 16/9/25	Fri 26/9/25	2008
2007	Floor Tiling	7 days	Tue 16/9/25	Tue 23/9/25	2008
2008	Timber Sliding/Swing Door Frame Installation	2 days	Sat 13/9/25	Mon 15/9/25	2005
2009	M&E Works Above Ceiling	12 days	Wed 24/9/25	Tue 7/10/25	2007
2010	False Ceiling Works	13 days	Wed 8/10/25	Thu 23/10/25	2009
2011	Window Installation	2 days	Fri 24/10/25	Sat 25/10/25	2010
2012	Grab Bar Installation	2 days	Sat 1/11/25	Mon 3/11/25	2015
2013	Painting	2 days	Fri 24/10/25	Sat 25/10/25	2010
2014	Door Panel Installation	2 days	Mon 27/10/25	Tue 28/10/25	2013
2015	Sanitary Wares Installation	5 days	Mon 27/10/25	Fri 31/10/25	2013
2016	M&E 2nd Fix	7 days	Thu 28/8/25	Thu 4/9/25	2002
2017	M&E 3rd Fix	7 days	Sat 1/11/25	Sat 8/11/25	2015
2018	**Loose Furniture Couch**	**109 days**	**Thu 3/7/25**	**Sat 8/11/25**	
2019	Falsework Dismantling	10 days	Thu 3/7/25	Mon 14/7/25	206
2020	Carcass Fabricatio (Off site)	60 days	Tue 15/7/25	Tue 23/9/25	2019
2021	Site lamination	25 days	Wed 24/9/25	Thu 23/10/25	2020
2022	Final Finishes	14 days	Fri 24/10/25	Sat 8/11/25	2021
2023	MOHH/Consultants/Operator Review	14 days	Tue 18/11/25	Wed 3/12/25	1999FS+7 days
2024	Approval to proceed with materials procurment	7 days	Thu 4/12/25	Thu 11/12/25	2023
2025	**Mock-up 3 - External Façade & Drop-off Facade**	**125 days**	**Wed 9/4/25**	**Sat 6/9/25**	
2026	Material/shop-drwgs submissions, review, selection & approval	60 days	Wed 9/4/25	Sat 21/6/25	
2027	Procurements of materials	30 days	Mon 23/6/25	Sat 26/7/25	2026
2028	Installation for mock up approval	9 days	Thu 28/8/25	Sat 6/9/25	262
2029	Review, comments, rectifications & approval	14 days	Mon 8/9/25	Tue 23/9/25	2028
2030	Final approval	6 days	Wed 24/9/25	Tue 30/9/25	2029
2031	**Mock-up 1 - Lift car interior (Offsite)**	**108 days**	**Tue 1/10/24**	**Fri 7/2/25**	
2032	Material/shop-drwgs submissions, review, selection& approval	77 days	Tue 1/10/24	Mon 30/12/24	1009SS
2033	Procurement of materials& installation for site mock up approval	31 days	Tue 31/12/24	Fri 7/2/25	2032

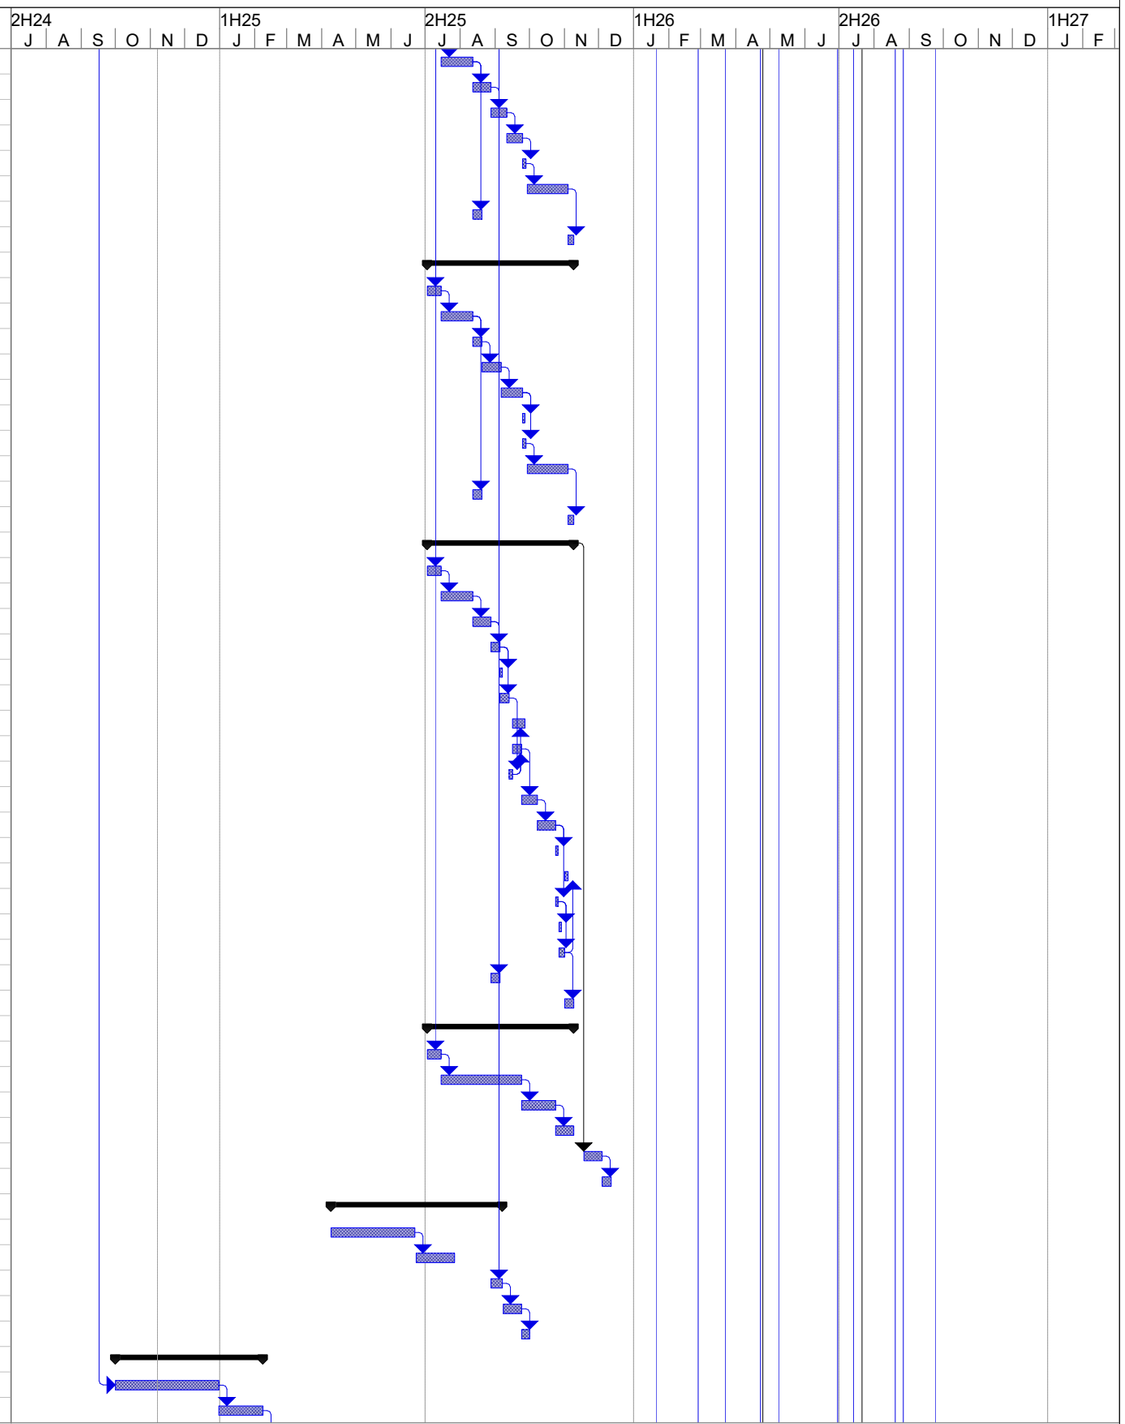


Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone			
Split	External Tasks	Manual Task	Start-only	Progress			
Milestone	External Milestone	Duration-only	Finish-only	Deadline			
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks				

Kwan Yong Construction Pte Ltd **Master Programme For Co-Located Polyclinic & Nursing Home At 200 Jurong East Ave 1**


ID	Task Name	Duration	Start	Finish	Predecessors
2034	Review, comments, rectifications& approval	7 days	Sat 8/2/25	Sat 15/2/25	2033
2035	Approval to proceed with materials procurment	6 days	Mon 17/2/25	Sat 22/2/25	2034
2036	**Sky Signage (National University Polyclinic)**	**148 days**	**Mon 1/12/25**	**Sat 30/5/26**	
2037	Shopdrawing Submission & Approval	60 days	Mon 1/12/25	Tue 10/2/26	
2038	Paper Mock Up Fabrication & Installation	30 days	Wed 11/2/26	Thu 19/3/26	2037
2039	Review & approval	14 days	Sat 21/3/26	Tue 7/4/26	2038
2040	Off-Site Fabrication & Installation	30 days	Wed 8/4/26	Wed 13/5/26	2039
2041	Review, comments, rectifications & approval	14 days	Thu 14/5/26	Sat 30/5/26	2040
2042	**External Boundary Signage & Drop-Off Logo Sign**	**118 days**	**Wed 1/7/26**	**Tue 17/11/26**	
2043	Shopdrawing Submission & Approval	30 days	Wed 1/7/26	Tue 4/8/26	
2044	Paper Mock Up Fabrication & Installation	30 days	Wed 5/8/26	Wed 9/9/26	2043
2045	Review & approval	14 days	Thu 10/9/26	Fri 25/9/26	2044
2046	Off-Site Fabrication & Installation	30 days	Sat 26/9/26	Fri 30/10/26	2045
2047	Review, comments, rectifications & approval	14 days	Sat 31/10/26	Tue 17/11/26	2046
2048	**Conquas Schedules**	**394 days**	**Wed 3/9/25**	**Sat 19/12/26**	
2049	Application to BCA	14 days	Mon 15/9/25	Tue 30/9/25	
2050	Approval & Payment	7 days	Wed 1/10/25	Wed 8/10/25	2049
2051	**Assessment Schedules**	**394 days**	**Wed 3/9/25**	**Sat 19/12/26**	
2052	**Installation Method Verification**	**115 days**	**Wed 3/9/25**	**Sat 17/1/26**	
2053	Waterproofing works	14 days	Wed 3/9/25	Thu 18/9/25	
2054	Window Installation Works	14 days	Tue 2/12/25	Wed 17/12/25	
2055	Tiling Works	14 days	Fri 2/1/26	Sat 17/1/26	
2056	**Internal Finishes**	**287 days**	**Wed 7/1/26**	**Thu 17/12/26**	
2057	Tile pull-out test	14 days	Wed 7/1/26	Thu 22/1/26	
2058	Wet area water-tightness test	14 days	Tue 11/8/26	Wed 26/8/26	
2059	Window water-tighness test	14 days	Wed 2/9/26	Thu 17/9/26	
2060	Roof	14 days	Thu 15/10/26	Fri 30/10/26	
2061	Internal Finishes	30 days	Fri 13/11/26	Thu 17/12/26	
2062	**External Finishes**	**17 days**	**Tue 1/12/26**	**Sat 19/12/26**	
2063	External walls	14 days	Fri 4/12/26	Sat 19/12/26	
2064	External works	14 days	Tue 1/12/26	Wed 16/12/26	
2065	**Rooms handover**	**230 days**	**Wed 4/2/26**	**Sat 7/11/26**	
2066	MDF room handover including 1st sty telecom riser	14 days	Mon 22/6/26	Tue 7/7/26	
2067	Telecom risers -2nd storey to lower roof	14 days	Mon 22/6/26	Tue 7/7/26	2066SS
2068	Central Server Room	14 days	Fri 23/10/26	Sat 7/11/26	
2069	Staff accomodation	14 days	Fri 23/10/26	Sat 7/11/26	
2070	Kitchen & Laundry	14 days	Fri 23/10/26	Sat 7/11/26	
2071	Substation handover to Powergrid	30 days	Mon 2/3/26	Tue 7/4/26	
2072	**Lift shafts handover (to lift contractor)**	**137 days**	**Wed 4/2/26**	**Tue 21/7/26**	
2073	Lifts FL2, BL2, FL3/BL3	7 days	Sat 23/5/26	Tue 2/6/26	1012SS
2074	Lift FL4	7 days	Wed 4/2/26	Wed 11/2/26	1135SS
2075	Lifts FL5, PL1, PL2 & PL3	7 days	Fri 13/3/26	Sat 21/3/26	1255SS
2076	Lifts FL1, BL1, PL4 & PL5	7 days	Tue 14/7/26	Tue 21/7/26	1484SS
2077	**Services turn-on dates**	**131 days**	**Sat 25/4/26**	**Tue 29/9/26**	
2078	Electrical turn on (By Powergrid)	90 days	Sat 25/4/26	Wed 12/8/26	1492FS+15 days
2079	Water turn on (By PUB)	7 days	Tue 7/7/26	Tue 14/7/26	
2080	Gas turn on (By Powergas)	7 days	Tue 22/9/26	Tue 29/9/26	
2081	**M&E T&C**	**191 days**	**Mon 6/4/26**	**Thu 19/11/26**	
2082	**Sanitary & Plumbing**	**30 days**	**Tue 11/8/26**	**Mon 14/9/26**	
2083	Domestic Water Transfer Tank/Pump (1st sty)	7 days	Mon 24/8/26	Mon 31/8/26	
2084	Domestic Water Booster Tank/Pump (Roof)	7 days	Mon 24/8/26	Mon 31/8/26	
2085	Water Tightness Test to U/G Sanitary Pipe Lines,Ics & Waste Sump	7 days	Mon 24/8/26	Mon 31/8/26	
2086	Other T&C (Sanitizer Water Booster Pump, Irrigation System, Water Heater,Water Reticulation System at Kitchen&Laundry)	30 days	Tue 11/8/26	Mon 14/9/26	

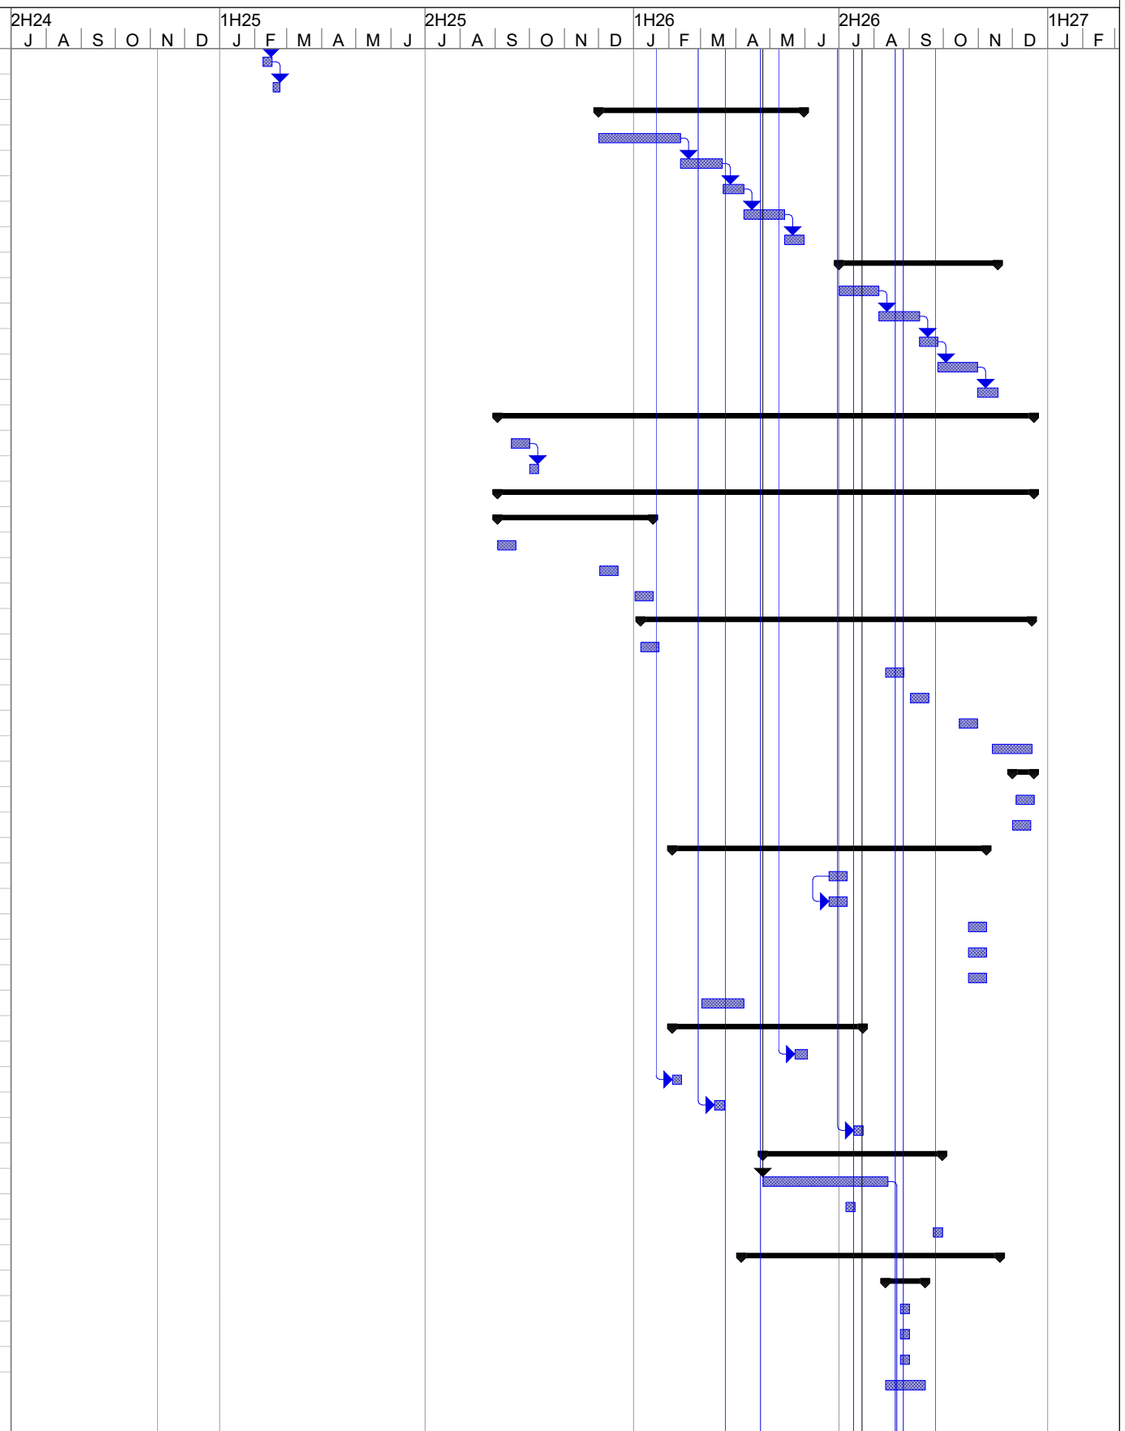

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	

ID	Task Name	Duration	Start	Finish	Predecessors
2087	**Electrical**	**39 days**	**Tue 18/8/26**	**Thu 1/10/26**	
2088	Meggering, Continuity, Trip & Polarity Test @ All Rooms	30 days	Tue 18/8/26	Mon 21/9/26	
2089	MSB/EMSB - Electrical turn-on to building	7 days	Fri 21/8/26	Fri 28/8/26	2078FS+7 days
2090	Genset	7 days	Thu 24/9/26	Thu 1/10/26	
2091	Lightning Protection System	7 days	Thu 24/9/26	Thu 1/10/26	
2092	ELV System (PA System, Card Access, Fireman Intercom)	14 days	Tue 8/9/26	Wed 23/9/26	
2093	Other T&C (Solar system, Actual Lux Measuring, MATV system, Nurse Call system, CCTV system, Guard Tour & Car Barrier system, Hearing Enhancement System, Data & Wifi System, Telephone System etc.)	28 days	Mon 24/8/26	Thu 24/9/26	
2094	**Fire Protection**	**32 days**	**Sat 12/9/26**	**Mon 19/10/26**	
2095	Sprinkler Pumpset (Meggering, Pressure Test, Cut in & out)	3 days	Sat 12/9/26	Tue 15/9/26	
2096	Hosereel Pumpset (Meggering, Pressure Test, Cut in & out)	3 days	Fri 16/10/26	Mon 19/10/26	
2097	Control Valve (Flow Test)	3 days	Mon 21/9/26	Wed 23/9/26	
2098	MAP/SAP	7 days	Thu 24/9/26	Thu 1/10/26	
2099	Dry Riser (Pressure Test)	7 days	Thu 24/9/26	Thu 1/10/26	
2100	**ACMV**	**51 days**	**Tue 8/9/26**	**Thu 5/11/26**	
2101	MV system tests	7 days	Thu 29/10/26	Thu 5/11/26	
2102	Aircon T&C incl. Chiller System	14 days	Tue 8/9/26	Wed 23/9/26	
2103	Kitchen (Air Flow Test)	7 days	Wed 30/9/26	Wed 7/10/26	
2104	**IDM**	**30 days**	**Thu 24/9/26**	**Wed 28/10/26**	
2105	PAHU Functional Test	30 days	Thu 24/9/26	Wed 28/10/26	2102
2106	FAF Functional Test	30 days	Thu 24/9/26	Wed 28/10/26	2105SS
2107	EAF Functional Test	30 days	Thu 24/9/26	Wed 28/10/26	2105SS
2108	VV Test (Venturi Valve Test)	30 days	Thu 24/9/26	Wed 28/10/26	2105SS
2109	BTD Test (Bubble Tight Damper Test)	30 days	Thu 24/9/26	Wed 28/10/26	2105SS
2110	Duct Static Pressure Test	30 days	Thu 24/9/26	Wed 28/10/26	2105SS
2111	Room Temperature Test	30 days	Thu 24/9/26	Wed 28/10/26	2105SS
2112	Room RH% Test	30 days	Thu 24/9/26	Wed 28/10/26	2105SS
2113	Room Pressure Test	30 days	Thu 24/9/26	Wed 28/10/26	2105SS
2114	SCR Control & Feedback - VVH	30 days	Thu 24/9/26	Wed 28/10/26	2105SS
2115	**Lifts**	**175 days**	**Mon 6/4/26**	**Fri 30/10/26**	
2116	**Slow speed (by Temporary Supply)**	**152 days**	**Mon 6/4/26**	**Sat 3/10/26**	
2117	Lifts FL2, BL2, FL3/BL3	14 days	Tue 28/7/26	Thu 13/8/26	1016SS
2118	Lift FL4	10 days	Mon 6/4/26	Thu 16/4/26	1139SS
2119	Lifts FL5, PL1, PL2 & PL3	21 days	Thu 7/5/26	Tue 2/6/26	1259SS
2120	Lifts FL1, BL1, PL4 & PL5	21 days	Thu 10/9/26	Sat 3/10/26	1488SS
2121	**Final T&C (Including Hot Test)**	**49 days**	**Fri 4/9/26**	**Fri 30/10/26**	
2122	Lifts FL2, BL2, FL3/BL3	14 days	Fri 4/9/26	Sat 19/9/26	1018SS+7 days
2123	Lift FL4	12 days	Mon 21/9/26	Sat 3/10/26	2122
2124	Lifts FL5, PL1, PL2 & PL3	21 days	Mon 5/10/26	Wed 28/10/26	2123
2125	Lifts FL1, BL1, PL4 & PL5	20 days	Thu 8/10/26	Fri 30/10/26	1490SS
2126	**M&E combined T&C**	**16 days**	**Sat 31/10/26**	**Thu 19/11/26**	
2127	**Combine Test (1st) - Fire alarm system activation**	**3 days**	**Sat 31/10/26**	**Tue 3/11/26**	**2125**
2128	EVC System	2 days	Sat 31/10/26	Mon 2/11/26	
2129	Fireman intercom system test	1 day	Tue 3/11/26	Tue 3/11/26	2128
2130	**Combine Test (2nd) - Fire alarm system activation**	**6 days**	**Wed 4/11/26**	**Wed 11/11/26**	**2129**
2131	Fire roller shutter test	1 day	Wed 4/11/26	Wed 4/11/26	
2132	Security system and auto door system	2 days	Thu 5/11/26	Fri 6/11/26	2131
2133	Car Park MV system test	1 day	Sat 7/11/26	Sat 7/11/26	2132
2134	Essential MV system test	2 days	Sat 7/11/26	Tue 10/11/26	2133SS
2135	AHU test under somker detector activation	1 day	Wed 11/11/26	Wed 11/11/26	2134
2136	Lift homing test	1 day	Wed 11/11/26	Wed 11/11/26	2135SS

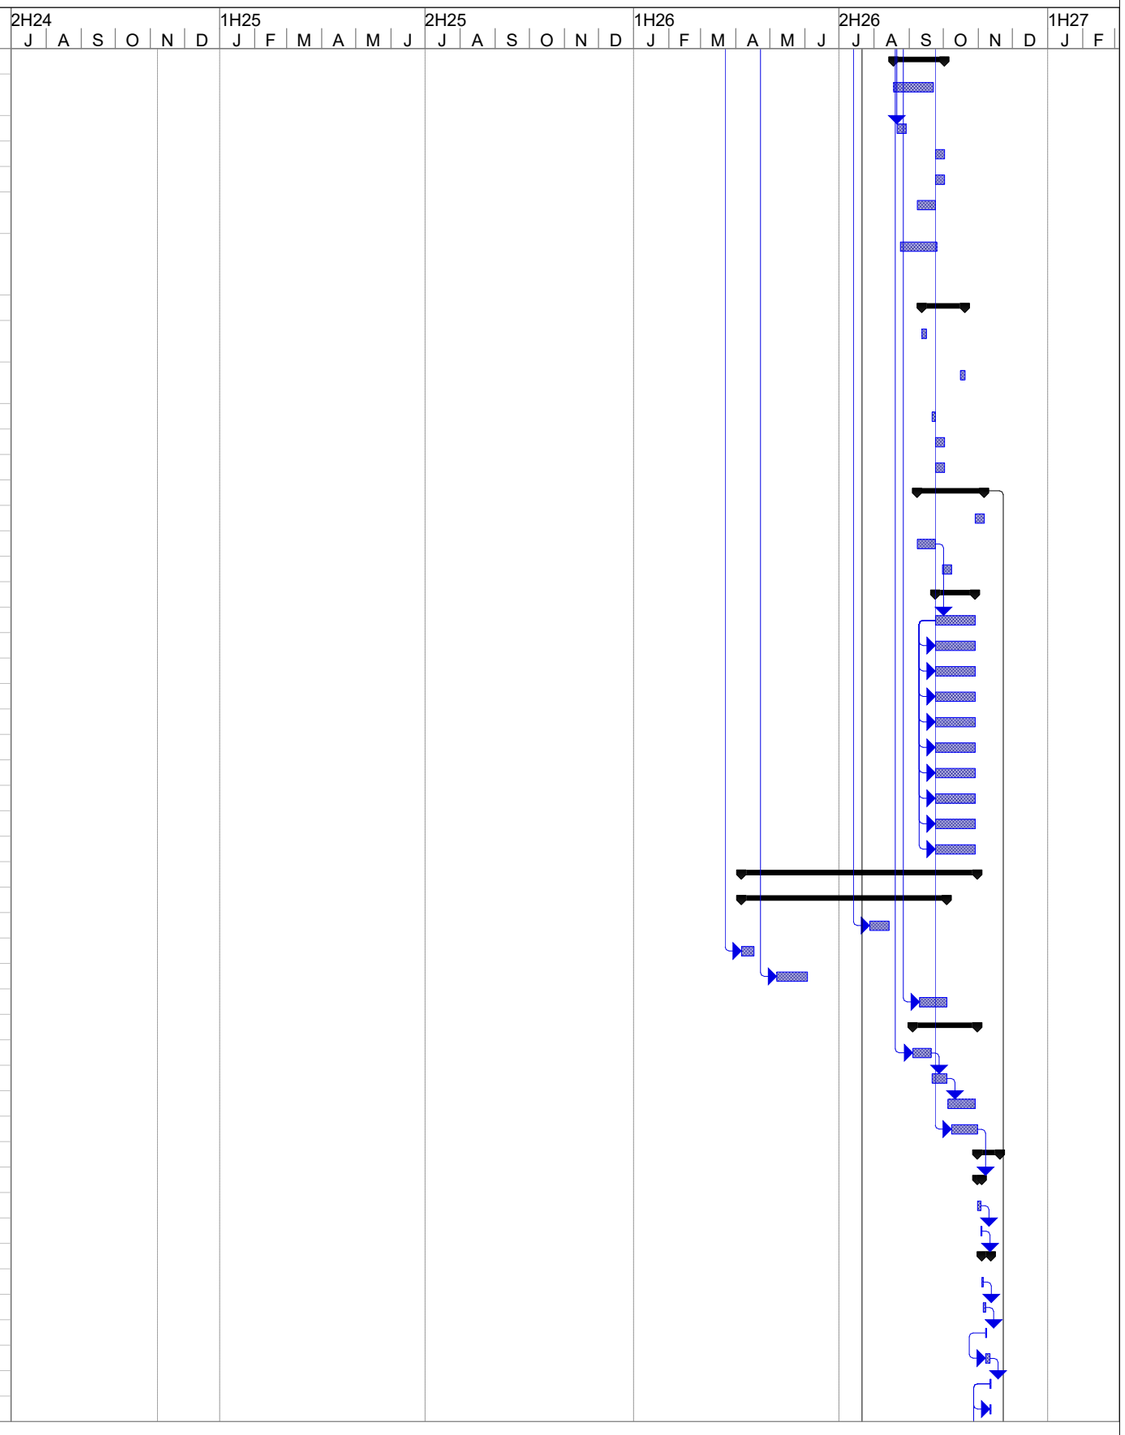


Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone
Split	External Tasks	Manual Task	Start-only	Progress
Milestone	External Milestone	Duration-only	Finish-only	Deadline
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks	

Kwan Yong Construction Pte Ltd **Master Programme For Co-Located Polyclinic & Nursing Home At 200 Jurong East Ave 1**

ID	Task Name	Duration	Start	Finish	Predecessors
2137	NN 100 system test (IT server room)	1 day	Wed 11/11/26	Wed 11/11/26	2135SS
2138	**Combine Test (3rd) - Power Failure Test**	**5 days**	**Thu 12/11/26**	**Tue 17/11/26**	
2139	E-light, EXIT light	1 day	Thu 12/11/26	Thu 12/11/26	2137
2140	Lift homing test	1 day	Fri 13/11/26	Fri 13/11/26	2139
2141	Fire Sprinker System Test	1 day	Sat 14/11/26	Sat 14/11/26	2140
2142	Fire Hosereel system test	1 day	Mon 16/11/26	Mon 16/11/26	2141
2143	Fire Hydrant test	1 day	Tue 17/11/26	Tue 17/11/26	2142
2144	Dry Riser Pressure Test	1 day	Tue 17/11/26	Tue 17/11/26	2143SS
2145	**Final Combined Test**	**2 days**	**Wed 18/11/26**	**Thu 19/11/26**	
2146	Test with all above services	2 days	Wed 18/11/26	Thu 19/11/26	2144
2147	**Documents submissions or RI/TOP**	**125 days**	**Tue 14/7/26**	**Tue 8/12/26**	
2148	Post CCTV(PUB/NEA)	21 days	Wed 26/8/26	Fri 18/9/26	
2149	Plumbing & sanitary clearance(PUB/NEA)	21 days	Sat 19/9/26	Tue 13/10/26	
2150	Submission of M&E equipment noise levels to NEA	14 days	Mon 23/11/26	Tue 8/12/26	2100
2151	Submission of LPS documents to BCA	14 days	Tue 14/7/26	Wed 29/7/26	1269
2152	Submission of Greenmark documents	14 days	Wed 4/11/26	Fri 20/11/26	
2153	Submission of all COC/fire certificates, etc.	14 days	Wed 4/11/26	Fri 20/11/26	
2154	Submission of CScore	14 days	Wed 4/11/26	Fri 20/11/26	
2155	COS for lift installations	7 days	Fri 20/11/26	Fri 27/11/26	
2156	Lift lodgement (Permit To Operate)	7 days	Sat 28/11/26	Sat 5/12/26	2155
2157	**Site Inspections for RI/TOP**	**54 days**	**Mon 16/11/26**	**Tue 19/1/27**	
2158	Pre-RI inspection (M & E)	5 days	Fri 20/11/26	Wed 25/11/26	2146
2159	Pre-RI inspection (Architectural)	7 days	Mon 16/11/26	Mon 23/11/26	
2160	Rectification to Pre-RIs comments	5 days	Thu 26/11/26	Tue 1/12/26	2158,2159
2161	RI inspection (M & E)	7 days	Mon 30/11/26	Mon 7/12/26	
2162	RI inspection (Architectural)	7 days	Mon 30/11/26	Mon 7/12/26	2161SS
2163	Rectification to RIs comments	7 days	Tue 8/12/26	Tue 15/12/26	2162
2164	RI Issuance of Form 2	14 days	Wed 16/12/26	Sat 2/1/27	2161,2163
2165	Submission to SCDF for TFP (including site audit)	14 days	Mon 4/1/27	Tue 19/1/27	2164
2166	T.O.P. inspection (BCA)	1 day	Thu 7/1/27	Thu 7/1/27	2162FS+24 days
2167	**Handover Process**	**41 days**	**Fri 18/12/26**	**Sun 7/2/27**	
2168	Cleaning & rectification	30 days	Fri 18/12/26	Sat 23/1/27	
2169	Inspections/Handover to client	21 days	Wed 13/1/27	Sat 6/2/27	2168SS
2170	Contractual completion date	0 days	Sun 7/2/27	Sun 7/2/27	2166

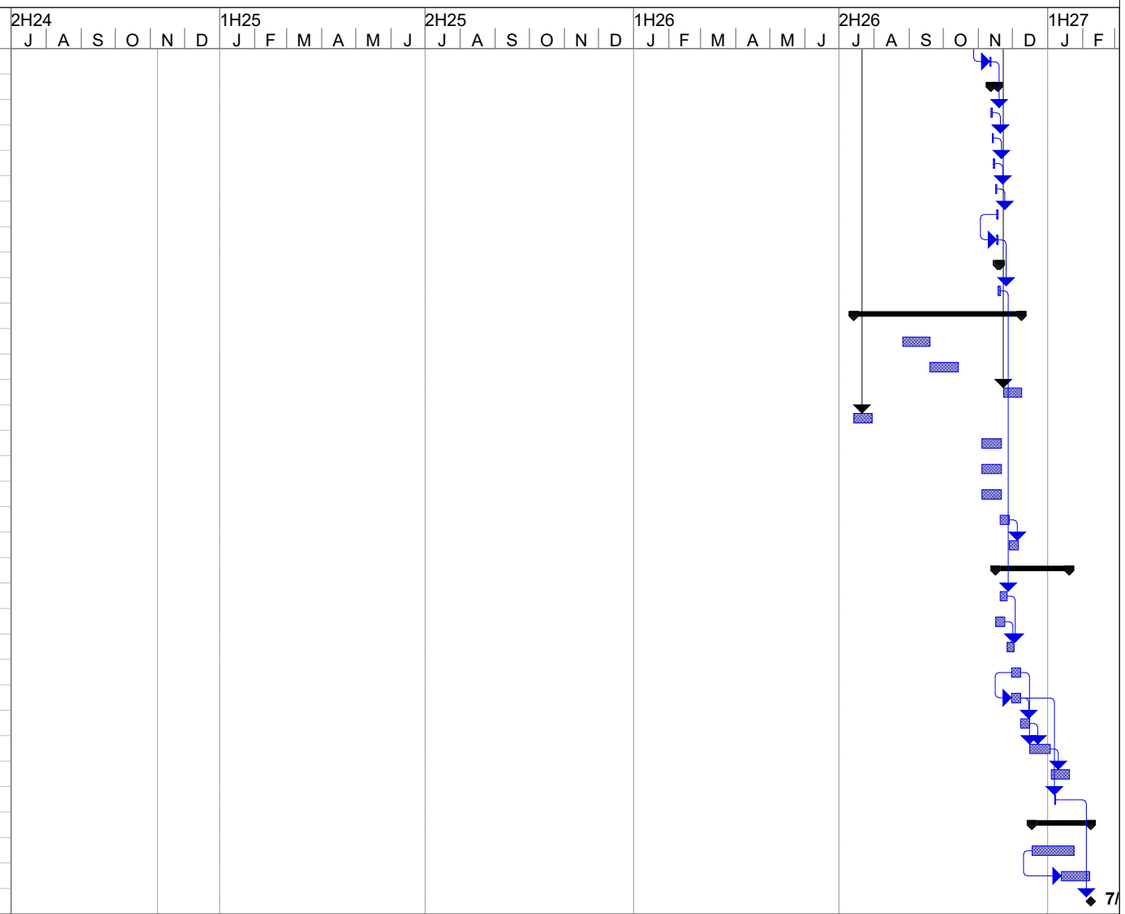

Project: JEPCNH - LCE - Proposed Sh
Date: Thu 7/11/24

Task	Project Summary	Inactive Summary	Manual Summary	External Milestone	
Split	External Tasks	Manual Task	Start-only	Progress	
Milestone	External Milestone	Duration-only	Finish-only	Deadline	
Summary	Inactive Milestone	Manual Summary Rollup	External Tasks		

SECTION 4

PROGRAMME

4.2 Authority Submission Status for M&E Services - 1st Submission

Service	Authority	Original Submission			Comments/Resubmission			Approval/		
		Scheduled	Actual	Comment	Resubmit	Comment	Resubmit	Comment	Resubmit	Clearance
Application for Electricity Supply	SP Services Ltd	15 Nov 2020	19 Nov 2020	19 Nov 2020	16 Dec 2020	16 Dec 2020				25 Jan 2021
Power Supply Substation	SP PowerGrid Ltd	13 May 2022	13 May 2022	6 Jul 2022	28 Oct 2022	4 Nov 2022	24 Nov 2022	8 Dec 2022	3 Jan 2023	6 Jan 2023
Metering Layout	SP Services Ltd	N.A								
Sanitary Installation	PUB Water Reclamation (Network) Dept	29 Jan 2025	18 Sep 2025							19 Sep 2025
Domestic Water Supply	PUB (Water Supply) Network Dept	15 Jan 2025	28 Feb 2025	30 Apr 2025	18 Jul 2025					29 Sept 2025
Gas Supply Installation	City Gas Pte Ltd	31 Mar 2023	9 May 2023	26 May 2023	18 Dec 2024	2 Jan 2025	11 Nov 2025	20 Nov 2025	1 Dec 2025	5 Dec 2025
Air Conditioning & Ventilation Inst.	FSSD	28 Feb 2025	11 Nov 2025							2 Dec 2025
Fire Fighting & Alarm Installation	FSSD	28 Feb 2025	11 Nov 2025							2 Dec 2025
Emergency Voice Communication	FSSD	28 Feb 2025	29 Aug 2025							9 Sept 2025
Telephone Installation	TFCC	29 Jul 2022	11 Aug 2022	22 Sep 2022	3 Nov 2022					7 Nov 2022
Broadband Co-axial Cable System (BCS)	Starhub Cable Vision	N.A								
Fuel Storage	FSSD	N.A								
	NEA (Pollution Control)									

SECTION 4

PROGRAMME

4.3 Authority Submission Status for M&E Services (Amendments) - 2nd Submission - NOT APPLICABLE

Service	Authority	Original Submission		Comments/Resubmission						Approval/
		Scheduled	Actual	Comment	Resubmit	Comment	Resubmit	Comment	Resubmit	Clearance
Application for Electricity Supply	SP Services Ltd									
Power Supply Substation	SP PowerGrid Ltd									
Metering Layout	SP Services Ltd									
Sanitary Installation	PUB Water Reclamation (Network) Dept									
Domestic Water Supply	PUB (Water Supply) Network Dept									
Gas Supply Installation	City Gas Pte Ltd									
Air Conditioning & Ventilation Inst.	FSSD									
Fire Fighting & Alarm Installation	FSSD									
Telephone Installation	TFCC									
Broadband Co-axial Cable System (BCS)	Starhub Cable Vision									
Fuel Storage	FSSD									
	NEA (Pollution Control)									

SECTION 5

PROJECT RECORDS

5.1 List of Internal Files

Standard Files

File Ref:		File Ref:	
- Owner		- Architect	
- Authorities	✓	- Other Consultants	
- Contractors		- CC	
- CF		- PQP/QSP	

Project Files to be initiated by PM as and when required

File Ref:		File Ref:		File Ref:	
- EC/MC					

(✓*where applicable*)

SECTION 5

PROJECT RECORDS

5.2 Filing of Drawings

The following team members shall take charge of filing of drawings, stamping "SUPERSEDED" drawings, etc.

Description	Team Member
Incoming Architectural Floor Plans	Saved in the server
Incoming Architectural Sketches/Details	Saved in the server
Incoming Structural Drawings	Saved in the server
M&E Drawings	
- Electrical Installation	Saved in the server
- Lift Installation	Saved in the server
- Air Conditioning & Ventilation Installation	Saved in the server
- Fire Fighting & Alarm Installation	Saved in the server
- Plumbing & Sanitary Installation	Saved in the server
- Swimming Pool & Filtration Installation	NA
Other Drawings	

SECTION 6

INTERFACING

6.1 Method of Interface

Description	Method of Interface	
Client's Review & Approval	M&E Design Report	✓
	Pre-planned meeting at fixed intervals	✓
	Telefax, letter and telephone	✓
	Email	✓
Interface With External Design Teams	M&E Design Report	✓
	Pre-planned meeting at fixed intervals	✓
	Telefax, letter and telephone	✓
	Email	✓
Interface Between Internal Design Teams	Telephone	✓
	Email	✓
	Internal Project Team Meeting	✓
	Circulation of Information	✓

(✓*where applicable*)

SECTION 6

INTERFACING

6.2 Internal Design Interface

Item No.	Description*	Required From	Required By	Date Required	Remarks
1	Equipment load	Mechanical	Electrical	13 Jan 2023	

** Information required by INTERNAL DESIGN TEAM MEMBERS*

SECTION 6

INTERFACING

6.3 Circulation of Documents to External Parties

	Code: A - Approval Required C - For Comments I - For Information Only	Client/ Client Rep.	* Client's Project Manager	Architect	Structural Engineer	Quantity Surveyor	
1.	**Letters/Fax:**						
a.	Project Design	A	I	C	C	I	
b.	Project Administration	A	I	I	I	I	
c.	Project Cost Estimate/Contract Cost	A	I	I	-	C	
2.	**Drawings**						
a.	Outline Design Drgs.	A	I	C	I	-	
b.	Sketch Design Drgs.	A	I	C	I	-	
c.	Final Design Drgs.	A	I	C	C	I	
d.	Shop Drawings	C	I	C	I	-	
e.	As Built Drgs.	I	I	I	I	I	
3.	**Other Document**						
a.	Specification	A	I	I	-	I	
b.	Tender Document	A	I	I	-	I	
c.	Tender Evaluation Report	A	I	I	-	I	
d.	Design Report	A	I	I	I	-	
e.	Progress Report	I	I	I	-	I	
f.	Financial Report	A	I	I	-	I	
g.	Minutes of Meeting	I	I	I	-	I	
h.	Inspection Report	I	I	I	-	-	
i.	Testing & Comm. Report	I	I	-	-	-	
j.	O & M Manual	I	I	-	-	-	

*Note: Applicable only, if the client engaged a Project Manager.

SECTION 7

WORK AUTHORISATION

Activity \ Authorised Signatories	PD	QP	PM	AE	SS
General Correspondences with Client			√	√	
General Correspondences with Other Consultants			√	√	
M&E Cost Estimate Report	√	√	√		
M&E Design Report	√	√	√		
Check Prints		√			
Tender Drawing Approval	√	√	√		
Tender Specification Approval	√	√	√		
List of Tenderers	√	√	√		
Tender Questionnaires	√	√	√		
Tender Reports	√	√	√		
Draft Letter of Award	√	√	√		
Review of Contractor's Shop Drawing			√	√	
Review of Contractor's Technical Submittal			√	√	
Review of Contractor's Sample Submittal			√	√	
Contractor's Request for Deviation		√	√		
Progress Payment Valuation Form	√		√		
Final Account Valuation	√		√		
Draft Variation Order	√		√		
Engineer/Architect's Instruction/Direction	√		√		
Site Instruction/Direction			√		
Correspondence/Submission to Authorities	√	√			

(✓*where authorised*)

Key to abbreviations:-

PD : Project Director
QP : Qualified Person
PM : Project Manager/Assistant Project Manager
AE : Assistant Engineer
SS : ACEPL Site Staff

SECTION 8

DESIGN INPUT & METHODOLOGY

8.1 List of Client's Standards, Reference Documents or Brief

ITEM	KEPT BY
Facility Guidelines for Nursing Homes	Soft Copy saved in Server
IT Infrastructure Guidelines for Nursing Homes	
IT Infrastructure Checklist (Design Requirement)	
IT Infrastructure Checklist (Infrastructure Requirement)	
MOH Licensing Requirements for Nursing Homes	
MEP Design Guide for Nursing Homes	
MEP Guidelines Checklist for Nursing Homes	
Precast Guidelines for Nursing Homes	
Design for Maintainability Checklist	
Project Brief (MEP Design Guide)	
SCC Design Brief	
Request for Approval to Order Variation	
Facility Guidelines for Polyclinics	
MEP Design Guide for Polyclinics	
MEP Design Guide Checklist for Polyclinics	
Physical Security Standards for Healthcare Institutions in Singapore	
IT Infrastructure Specifications for Polyclinics and Redevelopment Project	
Façade Access Design Guide	
Enhanced design for Maintainability Checklist	
Procedure for Design Review on Design for Maintainability	
Wayfinding Guidelines for Healthcare Facilities	

8.2 List of Applicable Code of Practice and Regulations

Services	Title of Code of Practice/Standard
Electrical Wiring	SS 638 : 2018
Lightning Protection System	SS 555 : 2018
Emergency Voice Communication System	SS 546 : 2009
Air Conditioning & Ventilation Installation	SS 553 : 2016
Lift & Escalator Installation	SS 550 : 2020
Sprinkler System	SS CP 52 : 2004
Wet Riser System	SS 575 : 2012
Automatic Fire Alarm System	SS 645 : 2019
Sanitary System	Code of Practice on Sewerage & Sanitary Works 2019
Plumbing System	SS 636 : 2018
Town Gas/LPG Supply System	SS 608 : 2015
Boiler and Steam Supply System	
Mechanical Smoke Control System	

SECTION 8

DESIGN INPUT & METHODOLOGY

8.3 List of Design Guide or Handbook Used

Carrier's Handbook of Air Conditioning System Design

ASHRAE Handbooks

Institute of Plumbing's Plumbing Services Design Guide

8.4 List of Pre-Consultation and Waiver

S/N	Description	Date of Application	Date of Approval	Remarks
1	Pre-Consultation Clause 4.4a in Code of Practice on Sewerage and Sanitary Works Usage of pump sump system for the discharge of wastewater from Refuse Rooms and Holding Rooms to 1st storey IC. Consultation Ref No. CR20220120-01588 Waiver Ref. No. NIL	02-12-2021	N.A	Ejector system shall be provided for new development.
2	*Clause number in Code of Practice for (Services) which require clarification or waiver. Consultation Ref No. Waiver Ref. No.			
3	*Clause number in Code of Practice for (Services) which require clarification or waiver. Consultation Ref No. Waiver Ref. No.			

*To fill in actual information

8.5 List of Applicable Quality System Procedures

Alpha Consulting Engineers Pte Ltd's Quality Management System Procedures

Section	Title	✓ where applicable
M1	Preparation of Consultancy Offer	✓
M2	Project Commissioning and Service Agreement	✓
M3	Design Control	✓
M4	Design Change Control	✓
M5	Tender Process and Evaluation	✓
M6	Authority Submission	✓
M7	Construction Process Control	✓
M8	Testing and Commissioning	✓
S1	Document Control	✓
S2	Documentation of Quality & Environmental Management System Procedure	✓
S3	Documentation of Project Quality Plan	✓
S4	Specification Control	✓
S5	Library Control	
S6	Archive Control	✓
S7	Filing Control	✓
S8	Drawing Control	✓
S9	Administration Control	✓
S10	Purchasing Control	
S11	Training Control	
S12	Computer Control	
S13	Non-Conformity and Corrective Action Procedures	✓
S14	Quality & Environmental System Audit	✓
S15	Feedback Reporting	✓
S16	Clients Feedback	✓
S17	Management Review	✓
S18	Risk Identification, Assessment & Control	✓

8.6 List of Software Used For Design/Analysis

DESCRIPTION/ PACKAGE NAME	VERSION	SUPPLIER/ SOURCE	PURPOSE	
Cophos	3.31	Zumtobel	Lighting design	
Carrier E20-II	5.11	Carrier	Programme for determination of heat load, duct size and its losses, etc.	✓
Gensize 2	2.1	Onan	Generator sizing	
Hyena	4.00.1	ACADS-BSG	Fire Sprinkler & Hydrant Analysis	
Dialux	4.11	Freeware	Lighting design	
Lift Traffic	7.18	Elevate	Lift traffic calculation	✓
Fault Level Calculation	11.11	ETAP	Calculation of fault level and voltage drop	

(✓*where applicable*)

SECTION 9

ENVIRONMENTAL CONSIDERATIONS

9.1 Sustainable Design Features / Criteria

Item	Remarks
Green Mark criteria	Platinum SLEB
Green Design Features	Installation of Solar PV System on roof

9.2 Site PPE Requirement

The necessary Personal Protective Equipment (detailed below) shall be provided by the main contractor / Company in accordance to the site EHS requirements prior to the site monitoring.


PPE	✓ where applicable
Safety Helmet	✓
Safety Shoes	✓
Eye Protection	
Ear Protection	
Safety Harness / Belt	
Others:	

9.3 Site Emergency Preparedness

Site staff shall comply with the site emergency preparedness and response procedure, established by the main contractor / owner, which shall include the following details.


Items	✓ where applicable
Evacuation Route	✓
Emergency Exit	✓
Assembly Point	✓
Emergency Contact List / Person	✓
Alarm system / methods	✓

4.0 Weekly WSH Activities [Updated Emergency Escape route as off 01 Dec 2025]

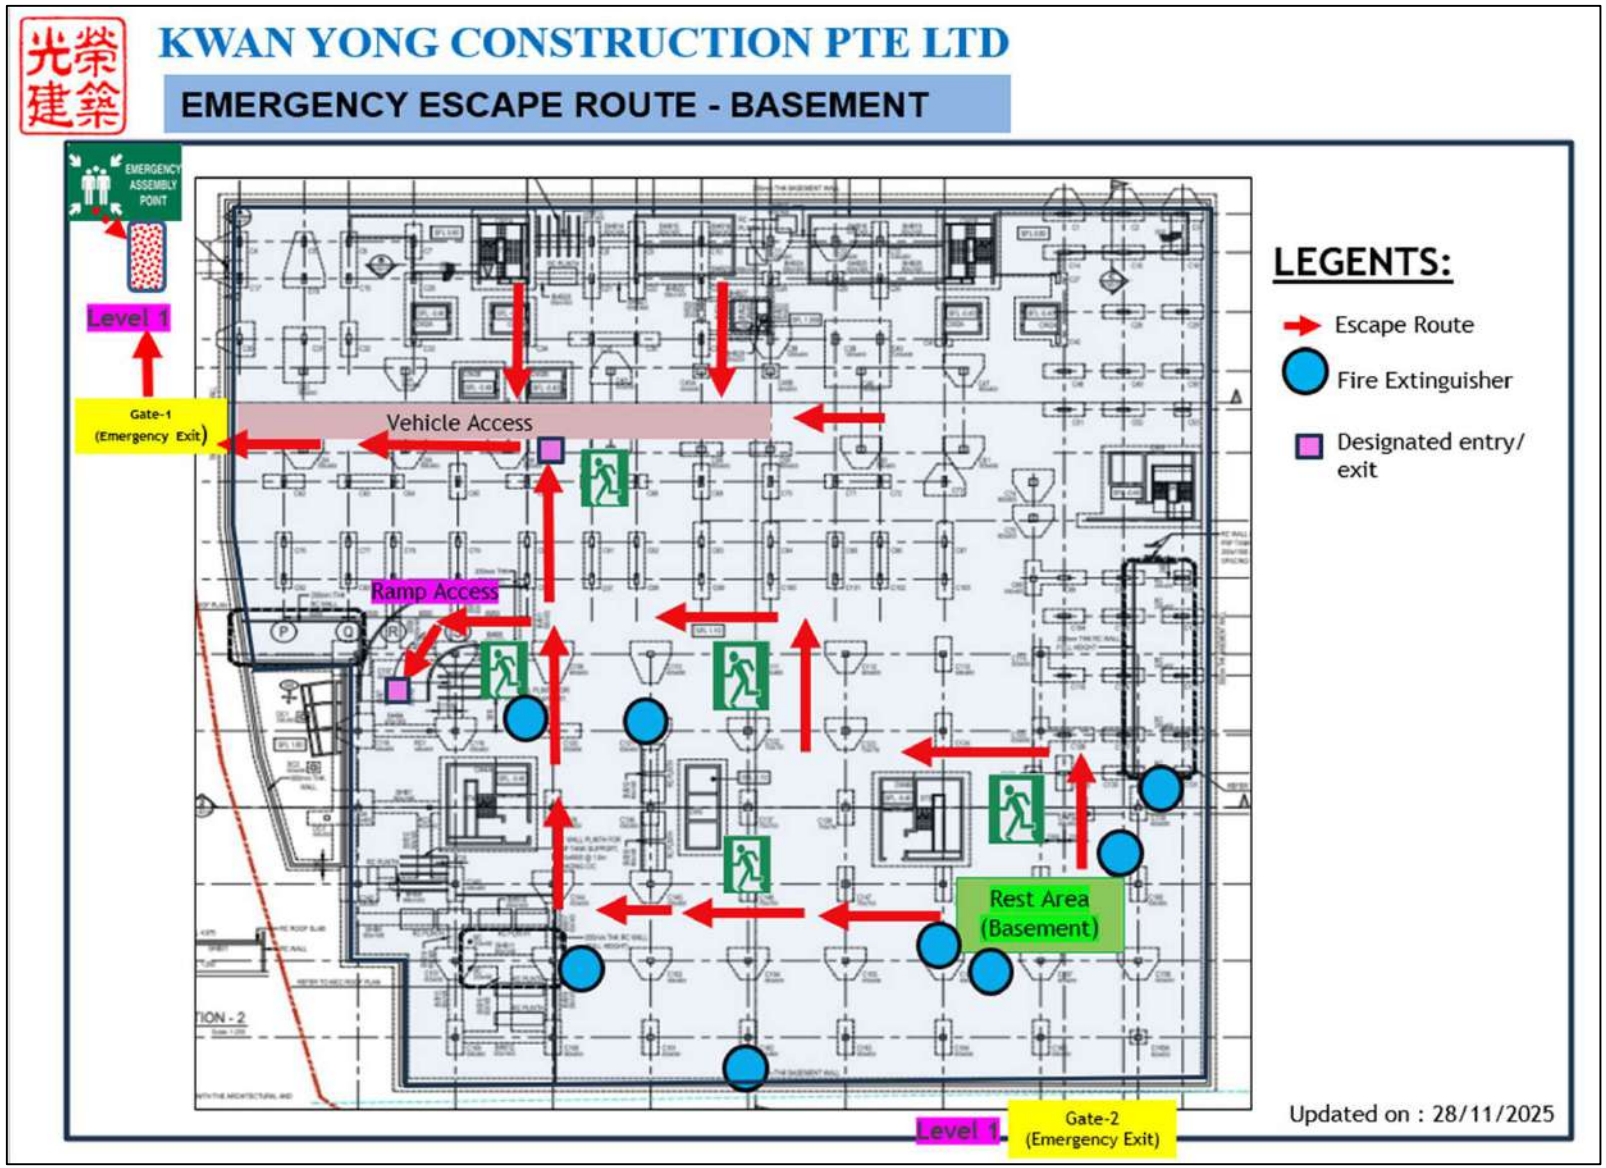


Basement Emergency Escape Route

4.0 Weekly WSH Activities [Updated Emergency Escape route as off 01 Dec 2025]

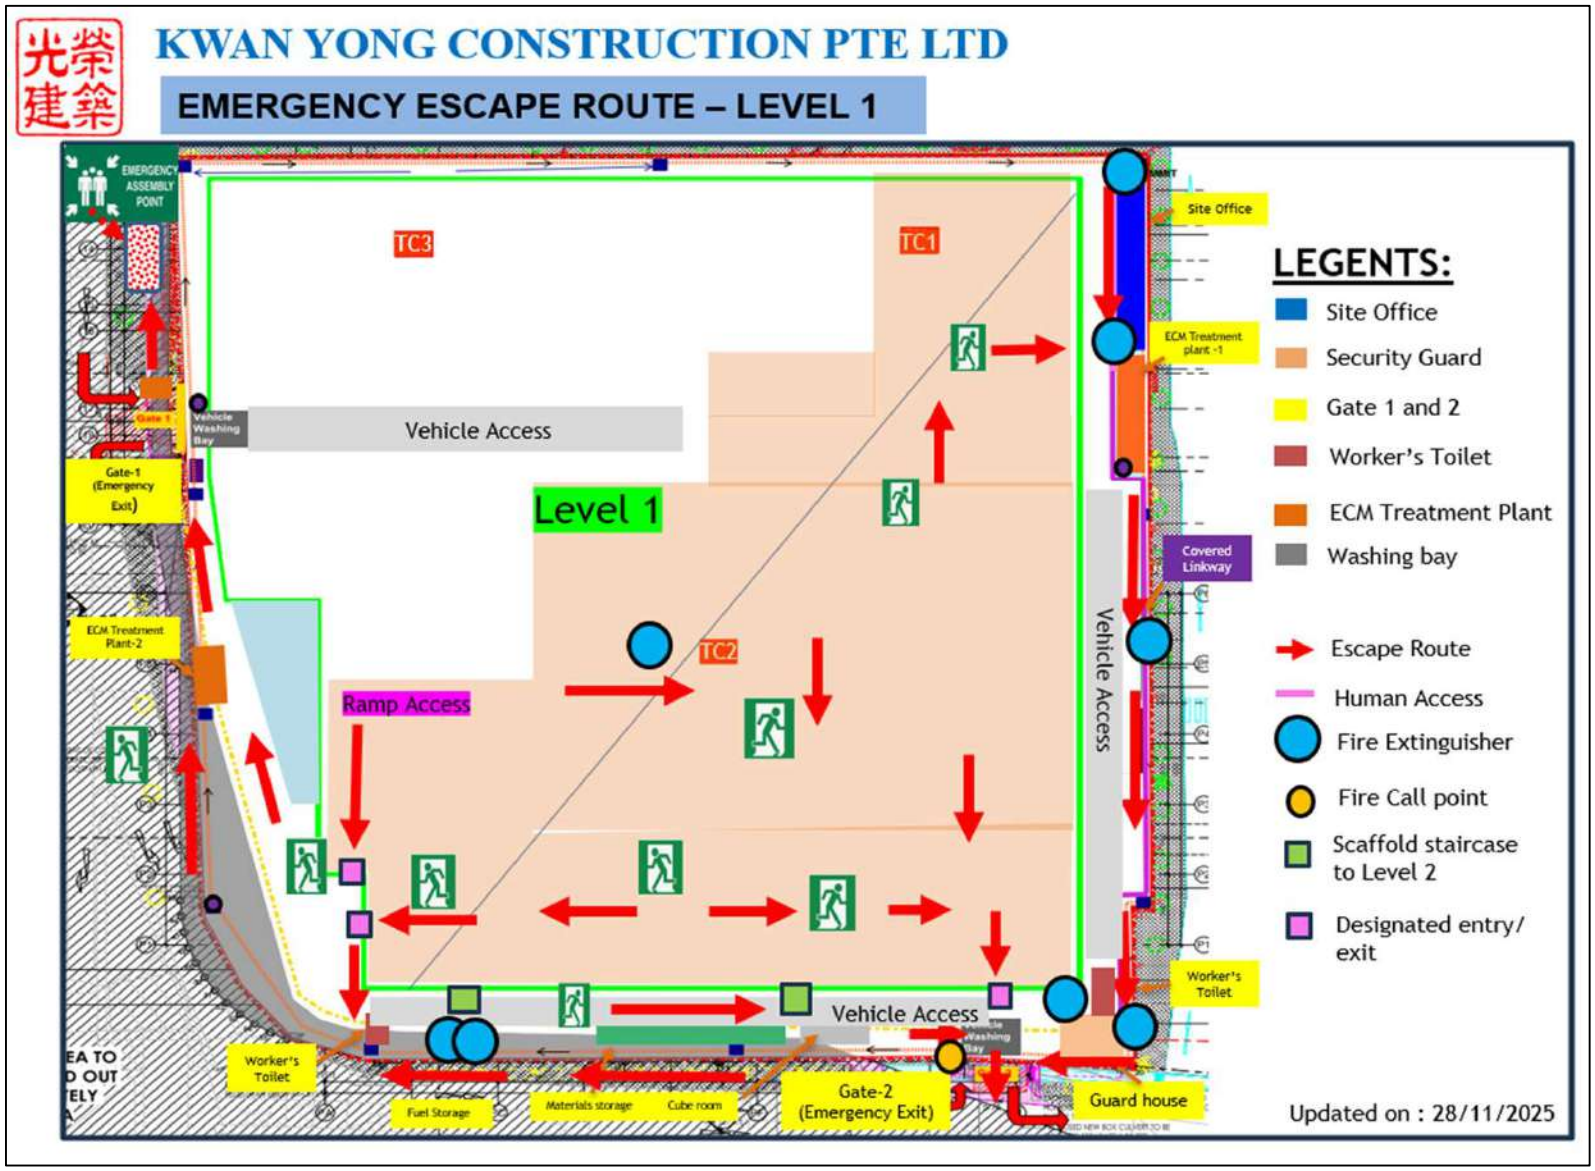

Level 1 - Emergency Escape Route

4.0 Weekly WSH Activities [Updated Emergency Escape route as off 01 Dec 2025]

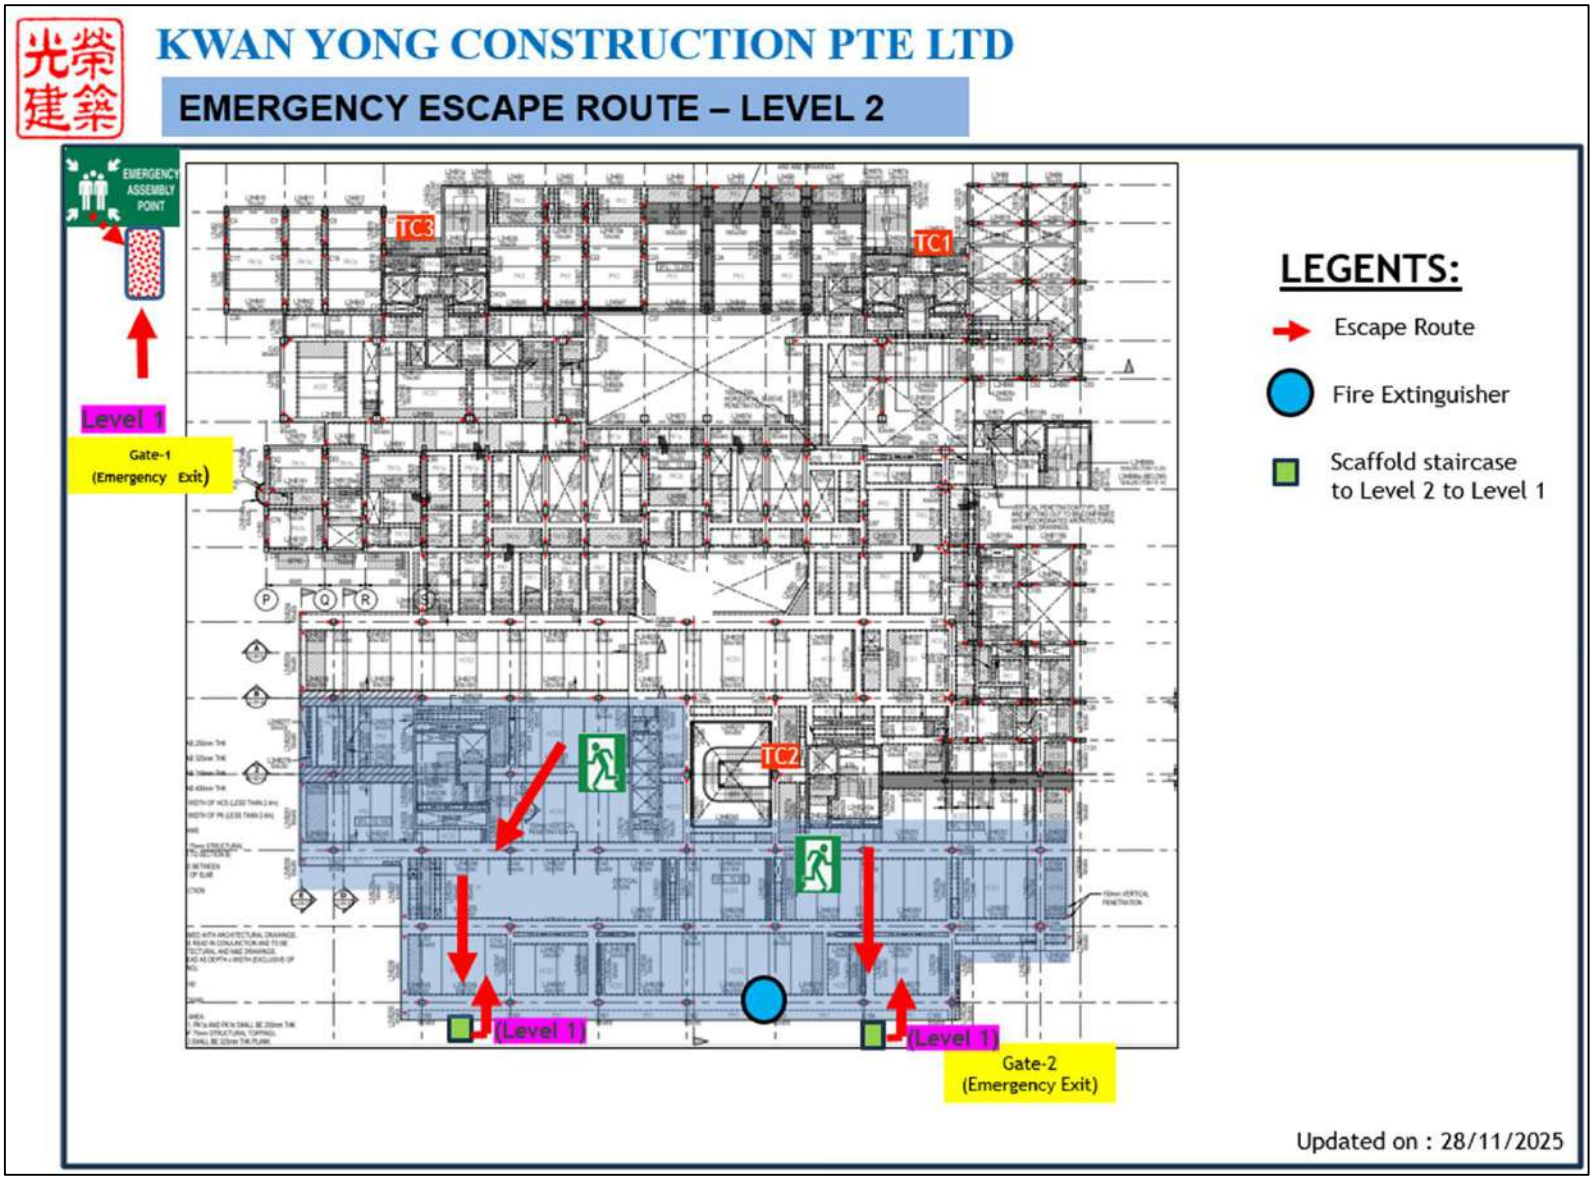

Level 2 - Emergency Escape Route

7.5 Emergency Contact No

KYC Site Personnel	Designation	Contact No
Mr. Tang Siew Tuck	Project Director	93822292
Mr. Lim Choon Ewe	Project Manager	90042435
Mr. Aung Theik	Assistant Project Manager	97709050
Mr. Fabian	Assistant Project Manager	93254231
Mr. Alexander	WSH Officer	81616747
Mr. Murugesan	Site Supervisor	93585923
Mr. Vinoth	WSH Co-Ordinator	98520372
Mr. Thamarai	Security	98110763

SECTION 9

ENVIRONMENTAL CONSIDERATIONS

9.4 Reporting of Environmental Non-conformances

When encountering environmental non-conformances, Site Staff shall be responsible to feedback to the main contractor.

9.5 List of Applicable Environmental management system Procedures – Not Applicable

Alpha Consulting Engineers Pte Ltd's Environmental Management System Procedures

Section	Title	✓ where applicable
E1	Aspect / Impact Identification, Risk Assessment & Risk Control	
E2	Identifying Legal & Other Requirements	
E3	Objectives, Targets & Programmes	
E4	Communication	
E5	Emergency Preparedness & Response	
E6	Monitoring & Measurement	
E7	Control of Air & Noise Pollution	
E8	Management of Wastes	

SECTION 10

CLIENT'S REQUIREMENTS

10.1 List of Output Required by Client:-

Item	* Remarks
M&E Design Report	A
M&E Cost Estimate Report	A
Pre-Qualification of Tenderers	NA
Tender Documents	A
Tender Report	A
Payment Valuation for QS	A
Certificates of Supervision for TOP/CSC	I

* *Remarks*

A: for approval *C: for comment* *I: for Information* *Re: for record*

Other purposes and for action: please specify.

10.2 Specific Procedures Required By Client *(If applicable)*

NOT APPLICABLE

SECTION 11

LIST OF SUB-JOB

11.1 List of Sub-Job Numbers

Sub Job No	Description	Allocation Details
