# PROJECT QUALITY PLAN

UNION SQUARE
PROPOSED MIXED-USE DEVELOPMENT COMPRISING 1 BLOCK 20-STOREY OFFICE TOWER WITH RETAIL UNITS, 1 BLOCK OF 3-STOREY HOTEL AND COMMERCIAL AND 1 BASEMENT CARPARKS, ADDITIONS & ALTERATIONS TO BLOCKS OF EXISTING CONSERVATION BUILDINGS, 1 BLOCK 40-STOREY RESIDENTIAL FLATS WITH COMMERCIAL UNITS AT 1ST AND 2ND STOREY AND 2 BASEMENT CARPARKS, REFURBISHMENT OF EXISTING POB ACROSS UPPER CROSS STREET AT TS08 ON LOTS 00327P, 00290T, 00289K, 00320N, 00337C, 00321X, 00334N, 00490L (PT), 99763X (PT), 99762N (PT), 99759N (PT), 99749M (PT), 99750L (PT), 00109X (PT), 99731N (PT), 99740V, 99741P, 99742T, 99735M, 99736W, 99737V, 99738P, 99739T AT MAGAZINE ROAD, HAVELOCK ROAD & KENG CHEOW STREET (SINGAPORE RIVER PLANNING AREA)

For

CDL LIBRA PTE LTD
CDL CONSERVO PTE LTD
CENTRO PROPERTY HOLDING PTE LTD

| | |
|---|---|
| Copy No. | 1 |

Prepared By : Chong Lai Meng/Yip Yoke Fun

Authorised By : Loh Fook Yuen

Date : 9 October 2026

**TABLE OF CONTENTS**


| SECTION | DESCRIPTION |
|---|---|
| – | **TITLE PAGE** |
| – | **TABLE OF CONTENTS** |
| **1** | **QUALITY PLAN CONTROL AND DISTRIBUTION** |
| 1.1 | List of Copy Holders |
| 1.2 | Revision Record |
| **2** | **PROJECT INFORMATION** |
| 2.1 | Project Description |
| 2.2 | Project Cost |
| 2.3 | Scope of Works |
| **3** | **ORGANISATION** |
| 3.1 | Organisation Chart |
| 3.2 | ACEPL's Project Team Member |
| 3.3 | Client/Client's Representative |
| 3.4 | Other Consultants<br>- Local<br>- Overseas – Not Applicable |
| 3.5 | Contractor/Sub-Contractors |
| 3.6 | Authorities |
| **4** | **PROGRAMME** |
| 4.1 | Overall Programme |
| 4.2 | Authority Submission Status for M&E Services – 1st Submission |
| 4.3 | Authority Submission Status for M&E Services (Amendment) – 2nd Submission – Not Applicable |
| **5** | **PROJECT RECORDS** |
| 5.1 | List of Internal Files |
| 5.2 | Filing of Drawings |

**TABLE OF CONTENTS**


| SECTION | DESCRIPTION |
|---|---|
| **6** | **INTERFACING** |
| 6.1 | Method of Interface |
| 6.2 | Internal Design Interface – Not Applicable |
| 6.3 | Circulation of Documents to External Parties |
| **7** | **WORK AUTHORISATION** |
| **8** | **DESIGN INPUT AND METHODOLOGY** |
| 8.1 | List of Client's Standards, Reference Documents or Brief – Not Applicable |
| 8.2 | List of Applicable Code of Practice and Regulations |
| 8.3 | List of Design Guide or Handbook Used |
| 8.4 | List of Pre-Consultation and Waiver – Not Applicable |
| 8.5 | List of Applicable Quality System Procedures |
| 8.6 | List of Software Used for Design/Analysis |
| **9** | **ENVIRONMENTAL CONSIDERATIONS** |
| 9.1 | Sustainable Design Features/Criteria – Not Applicable |
| 9.2 | Site PPE Requirement |
| 9.3 | Site Emergency Preparedness – Not Applicable |
| 9.4 | Reporting of Environmental Non-conformances |
| 9.5 | List of Applicable Environmental Management System Procedures |
| **10** | **CLIENT'S REQUIREMENTS** |
| 10.1 | List of Output Required by Client |
| 10.2 | Specific Procedures Required by Client – Not Applicable |
| **11** | **LIST OF SUB-JOB** |
| 11.1 | List of Sub-Job Numbers – Not Applicable |

**SECTION 1**

**QUALITY PLAN CONTROL AND DISTRIBUTION**

## 1.1 List of Copy Holders

| Copy No. | Copy Holder | Date of Issue |
|---|---|---|
| 1 | 6351 | 9 October 2026 |
| | | |
| | | |
| | | |
| | | |

## 1.2 Revision Record

| Revision | Date of Issue | Section Reference | Page(s) | Remarks |
|---|---|---|---|---|
| 0 | 13 November 2025 | 1 to 11 | 31 | + 20 page (Section 4.1 – Overall Master Programme) |
| 1 | 9 October 2026 | 1 to 11 | 31 | + 20 page (Section 4.1 – Overall Master Programme) |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |

**SECTION 2**

**PROJECT INFORMATION**

## 2.1 Project Description

| Type of Development | Residential with commercial (Union Square Residences & Retail) (USR & US1) | Office (Union Square Central) (USC) | Conservation (Union Square 3, 5, 7) (US3, US5 & US7) |
|---|---|---|---|
| Statistics of Development | | | |
| Site Area, m² | 6,238.00 | 2,800.80 | 4,785.80 |
| Nett Floor Area, m² | - | - | - |
| Gross Floor Area, m² | 31,758 | 28,368.75 | 8,203.25 |
| Covered Carpark, m² | - | - | - |
| No. of Covered Carpark Lots | 200 | 36 | - |
| No. of Apartments/Houses | 366 | - | - |
| No. of Beds (for Hospitals) | - | - | - |
| No. of Guestroom (for Hotels) | - | - | 134 |
| No. of Blocks / No. of Storeys | 40 | 21 | 3 |
| Green Mark Category | Super Low-E | | |
| No. of Phases | 1 | 1 | 1 |

## 2.2 Project Cost

| M&E Services Cost Plan (S$ x 1M) | | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|
| Services | EI | ACVI | LEI | FFAI | PSI | SPFI | | | | |
| Estimate | | | | | | | | | | |
| Awarded | 28.93 | 30.49 | 7.06 | 6.95 | 12.35 | | | | | |

| Total Project Construction Cost (S$ x1M) | | | |
|---|---|---|---|
| | Site Clearance | Piling Works | Main Contract |
| Estimate | | | |
| Awarded | 0.193 | 13.7 | US1 & USR: 202.369<br>USC, US3, US5 & US7: 273.484<br>TOTAL: 475.853 |

*Site Clearance shall include earth work, soil improvement, service diversion and termination.*

## 2.3 Scope of Works

### 2.3.1 Scope of Consultancy Services

| | |
|---|---|
| Conceptual/Schematic Design | – |
| Detailed Design | ✓ |
| Tender Documentation | – |
| Tender Evaluation | – |
| Contract Supervision | ✓ |
| M&E Costing | – |
| Submissions to Authority | ✓ |

(✓*where applicable*)

### 2.3.2 Scope of M&E Services

| | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|
| ELECTRICAL | ✓ | AIR CONDITIONING | ✓ | SPRINKLER | ✓ | SANITARY | ✓ | SWIMMING POOL | ✓ |
| LIFT | ✓ | MECHANICAL VENTILATION | ✓ | FIRE ALARM | ✓ | COLD WATER | ✓ | STEAM BOILER | |
| ESCALATOR | ✓ | MECHANICAL SMOKE EXTRACT | | HOSEREEL | ✓ | HOT WATER | ✓ | FUEL STORAGE | |
| PABX | | COMPUTER A/C | | WET RISER | ✓ | TOWN GAS | ✓ | | |
| SECURITY | ✓ | BST CARPARK EXH | ✓ | DRY RISER | ✓ | LPG GAS | | | |
| TELELIFT | | HEATING | | | | MEDICAL GAS | | | |
| DATA COMM. | ✓ | | | | | | | | |
| FLUSHFLOOR TRUNKING | | | | | | | | | |

(✓*where applicable*)

### 2.3.3 Submission to Relevant Authorities by Others

| | | | | | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| EJECTOR & DIVERTER | ✓ | SUMP PUMP | ✓ | FUEL OIL TANK | | LIFT & ESCALATOR | ✓ | PRESSURE VESSEL | | HOISTS | | FOAM | |

(✓*where applicable*)

**SECTION 3**

**ORGANISATION**

**3.1 Organisational Chart**



**SECTION 3**

**ORGANISATION**

### 3.2 ACEPL's Project Team Member

| TITLE | | NAME |
|---|---|---|
| Project Director | | Loh Fook Yuen (LFY) |
| Qualified Person | Mechanical | Choong Choon Guan (CCG) |
| | Electrical | Loh Fook Yuen (LFY) |
| Project Manager | | Chong Lai Meng (CLM) |
| Assistant Project Manager | | Yip Yoke Fun (YYF) |
| Project Assistant (Mech) | | Low Qi Fan (LQF) |
| Project Assistant (Elect) | | Thin Thin Tun (TTT) |
| Draughtsperson | | Common Pool |
| Resident Engineer (M&E) | | – |
| Assistant Resident Engineer (M&E) | | – |
| Clerk-of-Work (M&E) | | Koh Hai Chew (KHC) – USC, US3, US5 & US7<br>Ko Kok Chueen (KKC) – US1 & USR |
| | | |
| | | |

### 3.3 Client/Client's Representatives

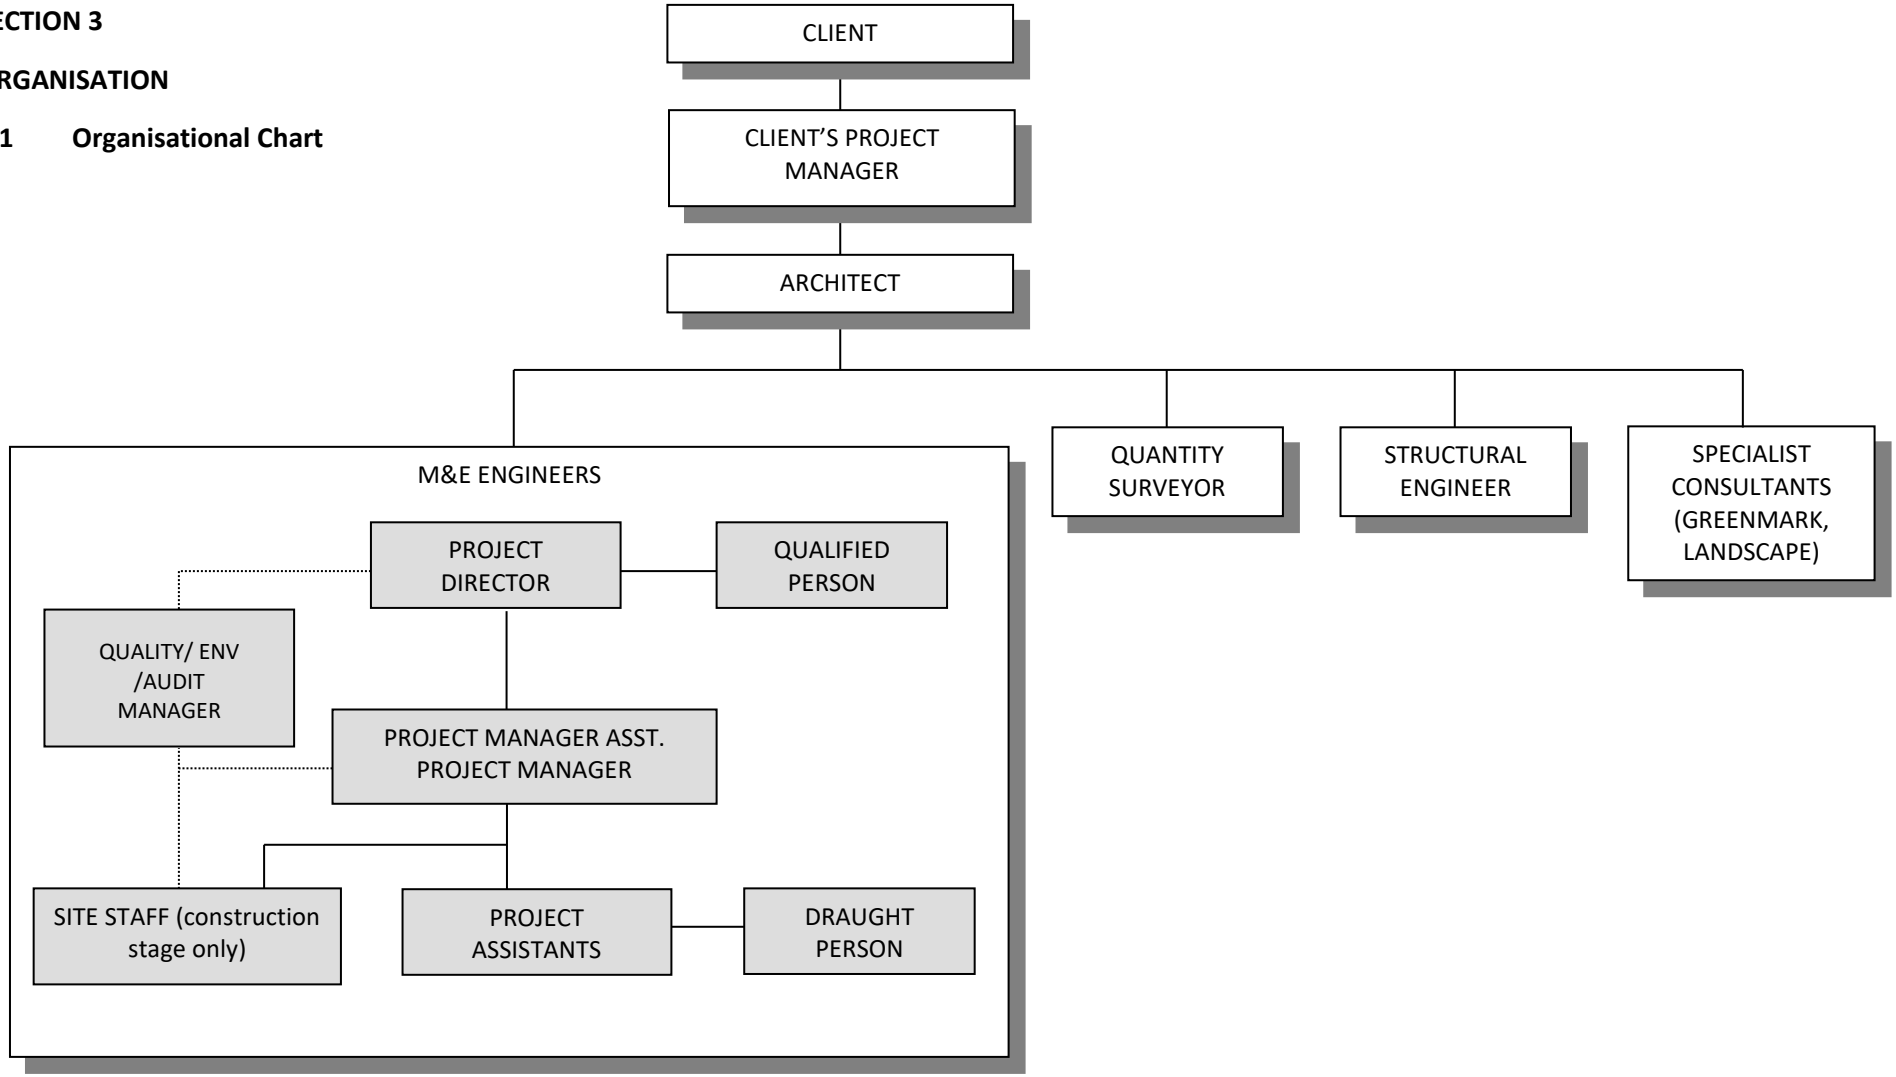Client: CDL Libra Pte Ltd
CDL Conservo Pte Ltd
Centro Property Holding Pte Ltd

Address: 9 Raffles Place
#12-01 Republic Plaza
Singapore 048619

Tel: 6877 8341

Fax: 6222 2293

Client's Representatives:

| Name of Company | Contact Person | Contact |
|---|---|---|
| CDL Libra Pte Ltd<br>CDL Conservo Pte Ltd<br>Centro Property Holding Pte Ltd | Name: Mr Francis Chan<br>Position: Assistant Vice President | Tel: –<br>Fax: 6222 2993<br>Handphone: 9875 7889<br>Email: francis.chan@cdl.com.sg |
| CDL Libra Pte Ltd<br>CDL Conservo Pte Ltd<br>Centro Property Holding Pte Ltd | Name: Mr Tan Choon Hong<br>Position: Project Manager | Tel: 6877 8305<br>Fax: 6222 2993<br>Handphone: 9450 1163<br>Email: choonhong@cdl.com.sg |
| | Name:<br>Position: | Tel:<br>Fax:<br>Handphone:<br>Email: |
| | Name:<br>Position: | Tel:<br>Fax:<br>Handphone:<br>Email: |
| | Name:<br>Position: | Tel:<br>Fax:<br>Handphone:<br>Email: |

### 3.4 **Other Consultants** (Local)

| Function / Name of Company | Contact Person | Contact |
|---|---|---|
| Architect<br><br>Aedas Pte Ltd | Name: Xue Wen Can<br>Position: Associate | Tel: 6464 1789<br>Fax: –<br>Handphone: 9758 9976<br>Email: aedassg210325@aedas.com |
| Quantity Surveyor<br><br>ThreeSixty Cost Management Pte Ltd | Name: Ms Claire Chow<br>Position: Senior Executive QS | Tel: –<br>Fax: –<br>Handphone: 8668 0821<br>Email: pj-360-centralmallqs@threesixtyconsultants.com |
| Structural Engineer<br><br>Mott MacDonald Singapore Pte Ltd | Name: Ms. Debbie Low<br>Position: Senior Structural Engineer | Tel: 6303 2032<br>Fax: –<br>Handphone: 9008 8571<br>Email: MM_425982@mottmac.com |
| Interior Designer<br><br>2nd Edition Pte Ltd | Name: Jlyn Yang<br>Position: Design Associate | Tel: –<br>Fax: –<br>Handphone:9792 1545<br>Email: jlyn@2ndedition.com.sg |
| Façade Consultant<br><br>Arup Singapore Pte Ltd | Name: Mr Paul Oyos<br>Position: Senior Consultant | Tel: 6411 2812<br>Fax: –<br>Handphone: 9671 9085<br>Email: Paul.Oyos@arup.com |
| Lighting Consultant<br><br>Lighting Planner Associates | Name: Mr Kek Hian Wee<br>Position: Senior Associate | Tel: 6734 3086<br>Fax: –<br>Handphone: 9796 2261<br>Email: lpa-pj-centralmall@lighting.co.jp |
| Landscape Consultant<br><br>Coen Design International Pte Ltd | Name: Ms Lynn Lee<br>Position: Project Director | Tel: 6844 988<br>Fax: –<br>Handphone: 9750 2523<br>Email: 415-centralmall@coen-design.com |
| Green Mark Consultant<br><br>DP Sustainable Design Pte Ltd | Name: Ms Stella Loo<br>Position: Senior ESD Analyst | Tel: 6829 3499<br>Fax: –<br>Handphone: 9624 9099<br>Email: ESD-Central@dpa.com.sg |
| Co-living Interior Designer<br><br>Farmwork Pte Ltd | Name: Ms Nina Arily<br>Position: Associate | Tel: 6336 1706<br>Fax: –<br>Handphone: 9649 4403<br>Email: cdlcoliving@farm.sg |

**3.4 Other Consultants** (Local) (Cont'd)

| Function / Name of Company | Contact Person | Contact |
|---|---|---|
| Wayfinding<br><br>Asylum Creative Pte Ltd | Name: Ms Cara Ang<br>Position: Design Director | Tel: –<br>Fax: –<br>Handphone: 9832 5044<br>Email: cara@theasylum.com.sg |
| Security Consultant<br><br>Prostruct Consulting Pte Ltd | Name: Mr Andrew Tan<br>Position: Principal Consultant | Tel: 6232 1360<br>Fax: –<br>Handphone: 9326 6353<br>Email: andrew.tanys@prostruct.com.sg |

**3.4 Other Consultants** (Overseas) – **NOT APPLICABLE**

| Function / Name of Company | Contact Person | Contact |
|---|---|---|
| Architect | Name:<br>Position: | Tel:<br>Fax:<br>Handphone:<br>Email: |
| M&E Consultant | Name:<br>Position: | Tel:<br>Fax:<br>Handphone:<br>Email: |
| Quantity Surveyor | Name:<br>Position: | Tel:<br>Fax:<br>Handphone:<br>Email: |
| Structural Engineer | Name:<br>Position: | Tel:<br>Fax:<br>Handphone:<br>Email: |
| Interior Designer | Name:<br>Position: | Tel:<br>Fax:<br>Handphone:<br>Email: |
| Lighting Consultant | Name:<br>Position: | Tel:<br>Fax:<br>Handphone:<br>Email: |
| Acoustic Consultant | Name:<br>Position: | Tel:<br>Fax:<br>Handphone:<br>Email: |
| _____ | Name:<br>Position: | Tel:<br>Fax:<br>Handphone:<br>Email: |

### 3.5 Contractors/Sub-Contractors

| Function / Name of Company | Contract * | Contact Person | Contact |
|---|---|---|---|
| Main Contractor<br>Woh Hup (Private) Limited | | Name: Ng Kim Han<br>Position: Senior M&E Manager | Tel: –<br>Fax: –<br>Handphone: 9850 0672<br>Email: ng_kimhan@wohhup.com |
| Air Conditioning & Ventilation Installation Sub-Contractor<br>Powen Engineering Pte Ltd | | Name: Mr Koh Kim San<br>Position: Senior Project Manager | Tel: –<br>Fax: –<br>Handphone: 8877 9062<br>Email: centralmall@powen.com.sg |
| Plumbing & Sanitary Installation Sub-Contractor<br>APP Engineering Pte Ltd | | Name: Mr Clement Li<br>Position: Senior Project Manager | Tel: –<br>Fax: –<br>Handphone: 9785 6106<br>Email: app.cm@appengrg.com.sg |
| Electrical Installation Sub-Contractor<br>BNL Engineering Pte Ltd | | Name: Chew Shong Link<br>Position: Operation Manager | Tel: 6684 8428<br>Fax: 6684 8598<br>Handphone: 9368 1550<br>Email: chew.sl@bnlengrg.com |
| Lift & Escalator Installation Sub-Contractor<br>Kone Pte Ltd | | Name: Mr Ng Yong Yi<br>Position: Senior Project Manager | Tel: 6424 6246<br>Fax: –<br>Handphone: 8998465<br>Email: yongyi.ng@kone.com |
| Fire Fighting & Alarm Installation Sub-Contractor<br>Rico Engineering Works Pte Ltd | | Name: Mr Dave Yeo<br>Position: Project Director | Tel: –<br>Fax: –<br>Handphone: 9847 0955<br>Email: CentralMall@ricoeng.com.sg |
| Swimming Pool Filtration Plant Installation Sub-Contractor<br>Aquatech Products & Services Pte Ltd | | Name: Mr Jonathan Teo<br>Position: Project Manager | Tel: –<br>Fax: –<br>Handphone: 8484 7548<br>Email: jteo@aquatech.com.sg |
| Carpark System Installation Sub-Contractor | | Name:<br>Position: | Tel:<br>Fax:<br>Handphone:<br>Email: |

** Type of Contract*
- *NSC (Nominated Sub-Contract)*
- *DSC (Domesticated Sub-Contract)*
- *DC (Direct Contract)*
- *NS (Nominated Supplier)*

### 3.6 Authorities

| Authorities/Department | Contact Person | Tel/Fax Nos./E-mail |
|---|---|---|
| SP PowerGrid:<br>(a) Sub-Station | Mr Goh Li Qing | 6916 8679<br>Email: LiQing@spgroup.com.sg |
| (b) Diversion | | |
| SP Services:<br>(a) Customer Supply | | |
| (b) Installation | | |
| (c) Meter Section | | |
| (d) Road Lighting | | |
| TFCC:<br>(a) SCV | | |
| (b) SingTel | | |
| (c) IMDA | Mr Gibson Tan | Email: Gibson_Tan@imda.gov.sg |
| BCA:<br>(a) Building Plan | | |
| (b) Green Mark | | |
| FSSD:<br>(a) Building Plan | MD Amin | Muhammad_Amin_Isa@scdf.gov.sg<br>DID: 6848 3236 |
| (b) M&E Plan | Jysica Liang | Jysica_liang@scdf.gov.sg<br>DID: 6848 1271 |
| PUB (Water Supply) Network Dept:<br>(a) Water Conservation | | |
| (b) Plumbing Plan | Muhd Aniq Aqil Bin A Rasid | muhd_aniq_aqil_a_rashid@pub.gov.sg<br>HP: 9877 4591 |
| (c) Diversion | | |
| (d) NEWater | | |
| PUB Water Reclamation (Network) Dept:<br>(a) Building Plan/CBPU | | |
| (b) M&E Plan | | |
| (c) Diversion | | |
| City Energy Pte Ltd:<br>(a) Planning/Submission | Mr Jackson Houng/Mr Koh Hwee Kang/Mr Jasper Ng | jacksonhoung@cityenergy.com.sg /<br>hweekang@cityenergy.com.sg /<br>jasperng@cityenergy.com.sg<br>HP: 9694 9383 / 96498515/8218 0082 |
| (b) Installation/Inspection | Mr Kamarulzaman Bin Rahman | kamarulzaman@cityenergy.com.sg /<br>HP: 8123 0342 |
| PowerGas Pte Ltd<br>(a) Diversion | Mr Dixon Loo | dixonloo@spgroup.com.sg |
| NEA (Pollution Control)<br>(a) Planning/Submission | | |
| (b) Inspection | | |

**SECTION 4**

**PROGRAMME**

**4.1 Overall Programme – To refer to the master programme attached.**

| | | | | | | | | | | | | | | | | | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| ID | TASK NAME | MONTHS | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D |
| 1. | Preliminary Planning | | | | | | | | | | | | | | | | | | | | | | | | | |
| 2. | Planning Submission | | | | | | | | | | | | | | | | | | | | | | | | | |
| 3. | Detail Design | | | | | | | | | | | | | | | | | | | | | | | | | |
| 4. | BP Submission | | | | | | | | | | | | | | | | | | | | | | | | | |
| 5. | BP Submission (Amendments) | | | | | | | | | | | | | | | | | | | | | | | | | |
| 6. | Tender Period for Piling | | | | | | | | | | | | | | | | | | | | | | | | | |
| 7. | Tender Period for Sub-Structure | | | | | | | | | | | | | | | | | | | | | | | | | |
| 8. | Tender Period for Super-Structure | | | | | | | | | | | | | | | | | | | | | | | | | |
| 9. | Piling Period | | | | | | | | | | | | | | | | | | | | | | | | | |
| 10. | Sub-Structure Construction Period | | | | | | | | | | | | | | | | | | | | | | | | | |
| 11. | Super-Structure Construction Period | | | | | | | | | | | | | | | | | | | | | | | | | |
| 12. | TOP | | | | | | | | | | | | | | | | | | | | | | | | | |
| 13. | CSC | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | | | | | | | | | |

| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 1 | **1724** | **Central Mall - Master Programme_R1_051024** | **1246 days** | **Thu 13/06/24** | **Tue 25/07/28** |
| 2 | **211** | **Project Key Dates** | **1246 days** | **Thu 13/06/24** | **Tue 25/07/28** |
| 3 | 363 | Target LOI Issuance | 0 days | Thu 13/06/24 | Thu 13/06/24 |
| 4 | 213 | Authority Submissions (ERSS/SI/Piling) | 90 days | Tue 20/08/24 | Tue 03/12/24 |
| 5 | 364 | Contract Commencement | 0 days | Mon 26/08/24 | Mon 26/08/24 |
| 6 | **354** | **Phase 1 (42 months)** | **686 days** | **Wed 19/11/25** | **Fri 25/02/28** |
| 7 | 357 | USC & Public Contributions Completion | 0 days | Fri 25/02/28 | Fri 25/02/28 |
| 8 | 358 | DCS Handover to operator (30 months) | 0 days | Fri 26/02/27 | Fri 26/02/27 |
| 9 | 1778 | Conservation Building Works commencement | 0 days | Wed 19/11/25 | Wed 19/11/25 |
| 10 | 361 | Conservation Buildings Completion | 0 days | Mon 25/10/27 | Mon 25/10/27 |
| 11 | 360 | External works & Road Improvements | 0 days | Fri 31/12/27 | Fri 31/12/27 |
| 12 | **359** | **Phase 2 (47 months)** | **246 days** | **Thu 30/09/27** | **Tue 25/07/28** |
| 13 | 356 | USR Completion | 0 days | Tue 25/07/28 | Tue 25/07/28 |
| 14 | 362 | Refurbishment of overhead Link way | 0 days | Thu 30/09/27 | Thu 30/09/27 |
| 15 | 1777 | Road Improvements, New Bus Stop & Shared Track | 0 days | Fri 31/12/27 | Fri 31/12/27 |
| 16 | **212** | **Project Major Milestone** | **683 days** | **Thu 23/04/26** | **Tue 25/07/28** |
| 17 | **381** | **USC/US3** | **559 days** | **Thu 23/04/26** | **Fri 25/02/28** |
| 18 | 436 | Full Basement Completion | 0 days | Thu 23/04/26 | Thu 23/04/26 |
| 19 | 437 | Superstructure Completion | 0 days | Thu 13/05/27 | Thu 13/05/27 |
| 20 | 382 | Full Water Tightness | 0 days | Sat 21/08/27 | Sat 21/08/27 |
| 21 | 383 | Substation handover to SPPG | 0 days | Sat 27/03/27 | Sat 27/03/27 |
| 22 | 380 | Power Turn-on | 0 days | Sat 26/06/27 | Sat 26/06/27 |
| 23 | 379 | Water Turn-on | 0 days | Thu 26/08/27 | Thu 26/08/27 |
| 24 | 1761 | Sanitary Clearance | 0 days | Sat 25/09/27 | Sat 25/09/27 |
| 25 | 384 | MDF Room Handover | 0 days | Mon 26/04/27 | Mon 26/04/27 |
| 26 | 1762 | Telecom Riser Handover | 0 days | Sat 26/06/27 | Sat 26/06/27 |
| 27 | 1764 | Minor Sewer Clearance | 0 days | Thu 26/08/27 | Thu 26/08/27 |
| 28 | 1763 | Aircon Turn On | 0 days | Fri 26/11/27 | Fri 26/11/27 |
| 29 | 385 | Lift Readiness | 0 days | Mon 20/09/27 | Mon 20/09/27 |
| 30 | 378 | TOP Inspection | 0 days | Wed 08/12/27 | Wed 08/12/27 |
| 31 | 377 | TOP Obtained | 0 days | Fri 25/02/28 | Fri 25/02/28 |
| 32 | **429** | **USR** | **303 days** | **Mon 26/07/27** | **Tue 25/07/28** |
| 33 | 1765 | Substation handover to SPPG | 0 days | Thu 26/08/27 | Thu 26/08/27 |
| 34 | 721 | Power Turn-on | 0 days | Tue 26/10/27 | Tue 26/10/27 |
| 35 | 722 | Water Turn-on | 0 days | Sat 26/02/28 | Sat 26/02/28 |
| 36 | 1769 | Sanitary Clearance | 0 days | Sat 25/03/28 | Sat 25/03/28 |
| 37 | 1767 | Minor Sewer Clearance | 0 days | Sat 26/02/28 | Sat 26/02/28 |
| 38 | 430 | MDF Room Handover | 0 days | Mon 26/07/27 | Mon 26/07/27 |
| 39 | 1768 | Telecom Riser Handover | 0 days | Sat 25/09/27 | Sat 25/09/27 |
| 40 | 1766 | Aircon Turn On | 0 days | Wed 26/04/28 | Wed 26/04/28 |
| 41 | 723 | Lift Readiness | 0 days | Thu 02/03/28 | Thu 02/03/28 |
| 42 | 719 | TOP Inspection | 0 days | Thu 11/05/28 | Thu 11/05/28 |
| 43 | 720 | TOP Obtained | 0 days | Tue 25/07/28 | Tue 25/07/28 |
| 44 | **210** | **Design Submission** | **907 days** | **Tue 20/08/24** | **Wed 18/08/27** |
| 45 | **438** | **ST Submission USC** | **285 days** | **Tue 20/08/24** | **Tue 29/07/25** |
| 46 | 419 | ERSS_USC | 25 days | Tue 20/08/24 | Tue 17/09/24 |
| 47 | 420 | ERSS_USC (Amendment) | 40 days | Wed 18/09/24 | Mon 04/11/24 |
| 48 | 421 | Foundation Piling Works | 50 days | Wed 18/09/24 | Fri 15/11/24 |
| 49 | 422 | Basement 1 | 50 days | Sat 16/11/24 | Wed 15/01/25 |
| 50 | 423 | Level 1 | 50 days | Wed 04/12/24 | Tue 04/02/25 |
| 51 | 424 | Level 2 | 50 days | Wed 05/02/25 | Fri 04/04/25 |
| 52 | 425 | Level 3 | 50 days | Sat 22/02/25 | Wed 23/04/25 |
| 53 | 426 | Typical Floors | 50 days | Thu 24/04/25 | Tue 24/06/25 |
| 54 | 415 | Level 18 | 50 days | Wed 14/05/25 | Fri 11/07/25 |
| 55 | 1995 | Roof_USC | 50 days | Sat 31/05/25 | Tue 29/07/25 |
| 56 | **1997** | **ST Submission US3** | **255 days** | **Tue 20/08/24** | **Tue 24/06/25** |
| 57 | 1745 | ERSS_US3 | 25 days | Tue 20/08/24 | Tue 17/09/24 |
| 58 | 2003 | ERSS_US3 (Amendment) | 40 days | Wed 18/09/24 | Mon 04/11/24 |
| 59 | 1998 | Foundation Piling Works | 50 days | Wed 18/09/24 | Fri 15/11/24 |
| 60 | 2002 | Basement 1 | 50 days | Sat 16/11/24 | Wed 15/01/25 |
| 61 | 2001 | Level 1 | 50 days | Wed 04/12/24 | Tue 04/02/25 |
| 62 | 2000 | Level 2 | 50 days | Wed 05/02/25 | Fri 04/04/25 |
| 63 | 1999 | Level 3 | 50 days | Sat 22/02/25 | Wed 23/04/25 |
| 64 | 1996 | Roof US3 | 50 days | Thu 24/04/25 | Tue 24/06/25 |
| 65 | **786** | **ST Submission USR** | **367 days** | **Wed 18/09/24** | **Wed 03/12/25** |
| 66 | 787 | ERSS | 50 days | Wed 18/09/24 | Fri 15/11/24 |
| 67 | 788 | ERSS (Amendment) | 40 days | Thu 17/10/24 | Tue 03/12/24 |
| 68 | 789 | Foundation Piling Works | 50 days | Sat 19/10/24 | Tue 17/12/24 |
| 69 | 790 | Basement 1 | 60 days | Wed 18/12/24 | Sat 01/03/25 |
| 70 | 791 | Level 1 | 60 days | Tue 07/01/25 | Wed 19/03/25 |
| 71 | 792 | Level 2 | 60 days | Thu 20/03/25 | Mon 02/06/25 |
| 72 | 793 | Level 3 | 60 days | Tue 08/04/25 | Fri 20/06/25 |
| 73 | 794 | Typical Floors (L4-L33) | 75 days | Sat 21/06/25 | Wed 17/09/25 |
| 74 | 807 | Typical Floors (L34-L40) | 50 days | Thu 18/09/25 | Sat 15/11/25 |
| 75 | 795 | Roof | 50 days | Mon 06/10/25 | Wed 03/12/25 |
| 76 | 808 | External Structure | 50 days | Sat 21/06/25 | Tue 19/08/25 |
| 77 | **1728** | **Façade Schedule** | **855 days** | **Mon 02/09/24** | **Wed 30/06/27** |
| 78 | 475 | Subcon Award:<br>Design, Supply and Installation of Curtain Walls (US3, USR & USC) | 0 days | Mon 02/09/24 | Mon 02/09/24 |
| 79 | **1990** | **USR** | **731 days** | **Mon 02/09/24** | **Sat 30/01/27** |
| 80 | 1992 | Material Submission & Approval | 126 days | Mon 02/09/24 | Fri 31/01/25 |
| 81 | 1725 | ST Submission_USR Façade | 75 days | Mon 02/09/24 | Thu 28/11/24 |
| 82 | 1729 | Façade Shopdrawing_USR (Residential Floors) | 100 days | Wed 04/09/24 | Tue 31/12/24 |
| 83 | 1771 | Facade Shopdrawing_USR (Podium) | 301 days | Wed 02/10/24 | Tue 30/09/25 |
| 84 | 1733 | Façade Production/Assembly/Delivery_USR (Residential Floors) | 581 days | Sat 01/03/25 | Sat 30/01/27 |
| 85 | 1772 | Façade Production/Assembly/Delivery_USR (Podium) | 404 days | Wed 01/10/25 | Sat 30/01/27 |



| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 86 | **1989** | **USC/C3** | **855 days** | **Mon 02/09/24** | **Wed 30/06/27** |
| 87 | 1991 | Façade Material Submission & Approval | 102 days | Mon 02/09/24 | Tue 31/12/24 |
| 88 | 416 | ST Submission_USC/US3 Façade | 100 days | Tue 01/10/24 | Tue 28/01/25 |
| 89 | 1730 | VMU_Façade Shopdrawing_USC/CM3 | 125 days | Tue 01/10/24 | Fri 28/02/25 |
| 90 | 2005 | Façade Shopdrawing submission and Approval | 101 days | Fri 02/05/25 | Sat 30/08/25 |
| 91 | 1734 | Façade Production/Assembly/Delivery_USC/US3 | 554 days | Mon 01/09/25 | Wed 30/06/27 |
| 92 | **417** | **M&E Design USC/US3** | **680 days** | **Tue 01/10/24** | **Wed 30/12/26** |
| 93 | 1752 | Electrical | 526 days | Tue 01/10/24 | Tue 30/06/26 |
| 94 | 1751 | ACMV | 680 days | Tue 01/10/24 | Wed 30/12/26 |
| 95 | 1750 | Fire | 224 days | Tue 01/10/24 | Mon 30/06/25 |
| 96 | 1749 | Plumbing | 302 days | Tue 01/10/24 | Tue 30/09/25 |
| 97 | 1748 | Sanitary | 302 days | Tue 01/10/24 | Tue 30/09/25 |
| 98 | 1747 | Gas | 302 days | Tue 01/10/24 | Tue 30/09/25 |
| 99 | 1746 | Lift | 224 days | Tue 01/10/24 | Mon 30/06/25 |
| 100 | **797** | **M&E Design USR** | **680 days** | **Tue 01/10/24** | **Wed 30/12/26** |
| 101 | 1753 | Electrical | 526 days | Tue 01/10/24 | Tue 30/06/26 |
| 102 | 1754 | ACMV | 680 days | Tue 01/10/24 | Wed 30/12/26 |
| 103 | 1755 | Fire | 224 days | Tue 01/10/24 | Mon 30/06/25 |
| 104 | 1756 | Plumbing | 302 days | Tue 01/10/24 | Tue 30/09/25 |
| 105 | 1757 | Sanitary | 302 days | Tue 01/10/24 | Tue 30/09/25 |
| 106 | 1758 | Gas | 302 days | Tue 01/10/24 | Tue 30/09/25 |
| 107 | 1759 | Lift + Escalator | 224 days | Tue 01/10/24 | Mon 30/06/25 |
| 108 | 1760 | PWCS | 76 days | Tue 01/10/24 | Mon 30/12/24 |
| 109 | **777** | **PPVC Schedule** | **902 days** | **Mon 26/08/24** | **Wed 18/08/27** |
| 110 | 778 | Design Coordination/Confirmation | 100 days | Mon 26/08/24 | Fri 20/12/24 |
| 111 | 779 | Shopdrawing preparation | 90 days | Tue 24/09/24 | Thu 09/01/25 |
| 112 | 780 | Shopdrawing approval | 90 days | Tue 29/10/24 | Sat 15/02/25 |
| 113 | 781 | Mould fabrication | 120 days | Wed 04/12/24 | Tue 29/04/25 |
| 114 | 782 | RC Carcass Fabrication | 648 days | Wed 05/02/25 | Tue 30/03/27 |
| 115 | 783 | Finishes | 642 days | Tue 15/04/25 | Mon 31/05/27 |
| 116 | 784 | Delivery to site | 592 days | Thu 04/09/25 | Wed 18/08/27 |
| 117 | **214** | **Mock-ups and Provisional Sum Award** | **847 days** | **Mon 01/07/24** | **Mon 19/04/27** |
| 118 | 1726 | VMU - External Façade_USR | 75 days | Fri 29/11/24 | Fri 28/02/25 |
| 119 | 470 | VMU - External Façade_USC | 75 days | Fri 31/01/25 | Wed 30/04/25 |
| 120 | 447 | PMU - External Façade_USC | 50 days | Tue 01/04/25 | Sat 31/05/25 |
| 121 | 448 | Railings (FOH&BOH) | 25 days | Wed 14/10/26 | Thu 12/11/26 |
| 122 | 449 | Covered Walkway | 25 days | Sat 20/03/27 | Mon 19/04/27 |
| 123 | 451 | Ceiling (Office) | 25 days | Tue 15/09/26 | Tue 13/10/26 |
| 124 | 450 | Toilet | 60 days | Sat 08/08/26 | Mon 19/10/26 |
| 125 | 452 | Office Lobby | 75 days | Wed 14/10/26 | Tue 12/01/27 |
| 126 | 453 | Residential Lobby | 75 days | Thu 23/04/26 | Wed 22/07/26 |
| 127 | **209** | **Award of Provisional Sum Items** | **759 days** | **Mon 01/07/24** | **Sat 02/01/27** |
| 128 | **471** | **MEP Item** | **98 days** | **Thu 02/01/25** | **Fri 02/05/25** |
| 129 | 472 | A. Design, Supply and Installation of IT Works (US3,US5,US7 & USC) | 0 days | Fri 02/05/25 | Fri 02/05/25 |
| 130 | 1779 | B. Design, Supply, and Installation of District Cooling System Routing \ | 0 days | Thu 02/01/25 | Thu 02/01/25 |
| 131 | **474** | **Architectural Items** | **507 days** | **Wed 30/04/25** | **Sat 02/01/27** |
| 132 | 476 | A. Design,<br>Supply and Delivery of Decorative/Special Light Fittings & Lighting Cor<br>(US3,US5,US7,USR & USC) | 0 days | Sat 01/11/25 | Sat 01/11/25 |
| 133 | 477 | B.<br>Design, Supply and Installation of Signage Works (non-statutory) (US3 | 0 days | Sat 02/05/26 | Sat 02/05/26 |
| 134 | 478 | C. Design,<br>Supply, Delivery and Installation of Artwork and Sculptures (US3,US5, | 0 days | Sat 02/01/27 | Sat 02/01/27 |
| 135 | 1780 | D. Design,Supply,and Installation of Commercial Design<br>Enhancement Works(US3,US5,US7,USR & USC) | 0 days | Wed 30/04/25 | Wed 30/04/25 |
| 136 | **481** | **USR (Residential)** | **205 days** | **Mon 26/08/24** | **Wed 30/04/25** |
| 137 | 482 | E. Design, Supply and Delivery of Sanitary Wares, Fittings and Accesso | 0 days | Mon 26/08/24 | Mon 26/08/24 |
| 138 | 483 | F. Design, Supply and Delivery Kitchen Appliances (USR) | 0 days | Mon 26/08/24 | Mon 26/08/24 |
| 139 | 486 | A. Design, Supply and Installation of Interior Decorations, Fitting Out \ | 0 days | Wed 30/04/25 | Wed 30/04/25 |
| 140 | **488** | **Conservation Buildings** | **307 days** | **Mon 26/08/24** | **Mon 01/09/25** |
| 141 | 489 | B. Design, Supply and Delivery of Sanitary Wares, Fittings and Accesso | 0 days | Mon 26/08/24 | Mon 26/08/24 |
| 142 | 490 | C. Design, Supply and Delivery Kitchen Appliances | 0 days | Mon 26/08/24 | Mon 26/08/24 |
| 143 | 492 | A. Design, Supply and Installation of Interior Decorations, Fitting Out \ | 0 days | Mon 30/06/25 | Mon 30/06/25 |
| 144 | 494 | B. Design, Supply and Installation of Interior Decorations, Fitting Out<br>Works and FF&E for Guestroom Mock up Unit | 0 days | Mon 02/06/25 | Mon 02/06/25 |
| 145 | 496 | A. A&A Works, Restoration and Conservation Works to Existing<br>Conservation Buildings to US5 & US7 | 0 days | Mon 02/06/25 | Mon 02/06/25 |
| 146 | 1770 | B. Design, Supply and Installation of Interior Lift Car Finishes | 0 days | Mon 01/09/25 | Mon 01/09/25 |
| 147 | **501** | **USC** | **0 days** | **Mon 01/09/25** | **Mon 01/09/25** |
| 148 | 502 | C. Design,Supply and Installation of Interior Decorations, Fitting Out<br>Works and FF&E (USC) | 0 days | Mon 01/09/25 | Mon 01/09/25 |
| 149 | **455** | **EXTERNAL WORKS ITEMS** | **76 days** | **Tue 30/09/25** | **Tue 30/12/25** |
| 150 | 456 | D. Design, Supply and Install of Softscape Works (US3,US5,US7,USR & | 0 days | Tue 30/09/25 | Tue 30/09/25 |
| 151 | 457 | A. Design,<br>Supply, Delivery and Installation of Gym Equipment (US3,US5,US7 & U | 0 days | Tue 30/12/25 | Tue 30/12/25 |
| 152 | 458 | B. Design,<br>Supply, Delivery and Installation of Playground and Outdoor Fitness E | 0 days | Tue 30/12/25 | Tue 30/12/25 |
| 153 | 459 | C. Design, Supply, Delivery and Installation of Water Play Equipment ( | 0 days | Tue 30/12/25 | Tue 30/12/25 |
| 154 | 460 | D. Design, Supply, Delivery and Installation of Outdoor / Pool Deck /<br>Indoor Furniture (US3,US5,US7,USR & USC) | 0 days | Tue 30/12/25 | Tue 30/12/25 |
| 155 | **461** | **OTHERS** | **47 days** | **Mon 01/07/24** | **Mon 26/08/24** |
| 156 | 462 | A. Ground Instrumentation and Monitoring Works | 0 days | Mon 26/08/24 | Mon 26/08/24 |
| 157 | 463 | E. Automated Tunnel Monitoring System | 0 days | Mon 26/08/24 | Mon 26/08/24 |
| 158 | 464 | M. Utilities Detection | 0 days | Mon 01/07/24 | Mon 01/07/24 |
| 159 | 465 | N. SiteSurvey / Investigation | 0 days | Mon 01/07/24 | Mon 01/07/24 |
| 160 | 466 | P. Geotechnical Investigation Works | 0 days | Mon 26/08/24 | Mon 26/08/24 |
| 161 | 467 | Q. Cadastral Survey | 0 days | Tue 20/08/24 | Tue 20/08/24 |
| 162 | 468 | R. Service Diversion | 0 days | Mon 26/08/24 | Mon 26/08/24 |




Project: Central Mall - Master P
Date: Mon 07/10/24

Task · Milestone · Project Summary · Inactive Milestone · Manual Task · Manual Summary Rollup · Start-only · External Tasks · Deadline · Critical Split · Manual Progress
Split · Summary · Inactive Task · Inactive Summary · Duration-only · Manual Summary · Finish-only · External Milestone · Critical · Progress

| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 163 | 469 | S. Service Connection | 0 days | Mon 26/08/24 | Mon 26/08/24 |
| 164 | 215 | **Site Setup & Mobilisation** | **338 days** | **Mon 26/08/24** | **Mon 06/10/25** |
| 165 | 1782 | **Conservation Building (US5 & US7)** | **338 days** | **Mon 26/08/24** | **Mon 06/10/25** |
| 166 | 1784 | Pre-conditon Survey | 50 days | Mon 26/08/24 | Tue 22/10/24 |
| 167 | 1785 | Site Instrumentation | 40 days | Tue 24/09/24 | Sat 09/11/24 |
| 168 | 1783 | Termite Investigation & Anti-termite treatment | 60 days | Sat 10/05/25 | Mon 21/07/25 |
| 169 | 1781 | Underground Service Detection | 40 days | Tue 22/07/25 | Sat 06/09/25 |
| 170 | 1793 | Trial pits prior to excavation | 25 days | Mon 08/09/25 | Mon 06/10/25 |
| 171 | 367 | **USC/US3** | **70 days** | **Mon 26/08/24** | **Fri 15/11/24** |
| 172 | 368 | **Soi Investigation** | **25 days** | **Mon 26/08/24** | **Mon 23/09/24** |
| 173 | 366 | SI | 25 days | Mon 26/08/24 | Mon 23/09/24 |
| 174 | 369 | **Site Set-up** | **70 days** | **Mon 26/08/24** | **Fri 15/11/24** |
| 175 | 376 | Site Hoarding (Alteration and new erection) | 38 days | Mon 26/08/24 | Tue 08/10/24 |
| 176 | 375 | ECM and Washing Bay | 27 days | Mon 30/09/24 | Wed 30/10/24 |
| 177 | 374 | Pre-conditon Survey | 44 days | Mon 26/08/24 | Tue 15/10/24 |
| 178 | 373 | Pre-Computation Plan | 20 days | Mon 26/08/24 | Tue 17/09/24 |
| 179 | 372 | Service Detection & Trial Trench Prior to Excavate | 40 days | Mon 26/08/24 | Thu 10/10/24 |
| 180 | 371 | Site Instrumentation | 40 days | Tue 24/09/24 | Sat 09/11/24 |
| 181 | 370 | Design & Erection of Site Office | 70 days | Mon 26/08/24 | Fri 15/11/24 |
| 182 | 216 | **Phase 1: Construction** | **1061 days** | **Mon 26/08/24** | **Fri 25/02/28** |
| 183 | 86 | **USC + US3** | **980 days** | **Tue 24/09/24** | **Fri 17/12/27** |
| 184 | 222 | **Temporary Works/Hacking** | **374 days** | **Tue 24/09/24** | **Wed 17/12/25** |
| 185 | 88 | Temporary Propping | 25 days | Tue 24/09/24 | Tue 22/10/24 |
| 186 | 89 | Localise hacking for piling | 25 days | Wed 23/10/24 | Thu 21/11/24 |
| 187 | 91 | Remove Temp Propping + Partial hack-off EB1 & EL1 | 40 days | Sat 10/05/25 | Fri 27/06/25 |
| 188 | 95 | Hack-off remaining EB1 | 40 days | Sat 01/11/25 | Wed 17/12/25 |
| 189 | 223 | **ERSS** | **281 days** | **Tue 01/04/25** | **Thu 05/03/26** |
| 190 | 94 | Install raker struts | 40 days | Mon 29/09/25 | Fri 14/11/25 |
| 191 | 97 | Remove Raker Strut | 25 days | Tue 03/02/26 | Thu 05/03/26 |
| 192 | 122 | Excavation + ERSS | 87 days | Tue 01/04/25 | Tue 15/07/25 |
| 193 | 90 | **Piling** | **138 days** | **Fri 22/11/24** | **Fri 09/05/25** |
| 194 | 224 | CBP600_USC_South | 75 days | Fri 22/11/24 | Fri 21/02/25 |
| 195 | 233 | CBP1200_USC_lift | 60 days | Tue 10/12/24 | Fri 21/02/25 |
| 196 | 121 | CBP_US3/DCS | 60 days | Thu 05/12/24 | Mon 17/02/25 |
| 197 | 225 | Foundation Piles_USC | 63 days | Sat 22/02/25 | Fri 09/05/25 |
| 198 | 228 | Foundation Piles_US3/DCS | 35 days | Tue 18/02/25 | Sat 29/03/25 |
| 199 | 226 | **Substructure** | **249 days** | **Sat 28/06/25** | **Thu 23/04/26** |
| 200 | 231 | **USC** | **249 days** | **Sat 28/06/25** | **Thu 23/04/26** |
| 201 | 92 | Construct Lift Pit | 50 days | Sat 28/06/25 | Tue 26/08/25 |
| 202 | 93 | Partial B1 | 40 days | Wed 27/08/25 | Sat 11/10/25 |
| 203 | 96 | Full New B1 | 50 days | Thu 04/12/25 | Mon 02/02/26 |
| 204 | 98 | New L1 | 40 days | Fri 06/03/26 | Thu 23/04/26 |
| 205 | 232 | **US3/DCS** | **167 days** | **Wed 16/07/25** | **Fri 30/01/26** |
| 206 | 123 | New B1 | 65 days | Wed 16/07/25 | Tue 30/09/25 |
| 207 | 124 | Vertical Element | 40 days | Wed 01/10/25 | Mon 17/11/25 |
| 208 | 125 | L1 | 62 days | Tue 18/11/25 | Fri 30/01/26 |
| 209 | 909 | **Vehicle Underpass** | **189 days** | **Sat 03/04/27** | **Fri 12/11/27** |
| 210 | 912 | **Stage 1** | **114 days** | **Sat 03/04/27** | **Mon 16/08/27** |
| 211 | 913 | Soldier pile | 15 days | Sat 03/04/27 | Tue 20/04/27 |
| 212 | 911 | Excavation | 20 days | Wed 21/04/27 | Fri 14/05/27 |
| 213 | 915 | Strutting (icluding steel decking) | 25 days | Sat 08/05/27 | Sat 05/06/27 |
| 214 | 914 | Concreting | 60 days | Mon 07/06/27 | Mon 16/08/27 |
| 215 | 919 | **Stage 2** | **114 days** | **Mon 07/06/27** | **Mon 18/10/27** |
| 216 | 917 | Soldier pile | 15 days | Mon 07/06/27 | Wed 23/06/27 |
| 217 | 918 | Excavation | 20 days | Thu 24/06/27 | Fri 16/07/27 |
| 218 | 916 | Strutting (icluding steel decking) | 25 days | Sat 10/07/27 | Sat 07/08/27 |
| 219 | 910 | Concreting | 60 days | Tue 10/08/27 | Mon 18/10/27 |
| 220 | 922 | Sewer Diversion | 75 days | Mon 07/06/27 | Thu 02/09/27 |
| 221 | 920 | Backfill and road reinstatement | 75 days | Tue 17/08/27 | Fri 12/11/27 |
| 222 | 227 | **Superstructure** | **415 days** | **Sat 31/01/26** | **Thu 17/06/27** |
| 223 | 229 | **USC** | **363 days** | **Tue 07/04/26** | **Thu 17/06/27** |
| 224 | 235 | **Core Wall** | **312 days** | **Tue 07/04/26** | **Sat 17/04/27** |
| 225 | 244 | L2 | 15 days | Tue 07/04/26 | Thu 23/04/26 |
| 226 | 245 | L3 | 14 days | Fri 24/04/26 | Mon 11/05/26 |
| 227 | 246 | L4 | 12 days | Tue 12/05/26 | Mon 25/05/26 |
| 228 | 247 | L5 | 12 days | Tue 26/05/26 | Wed 10/06/26 |
| 229 | 248 | L6 | 12 days | Fri 03/07/26 | Thu 16/07/26 |
| 230 | 249 | L7 | 15 days | Fri 17/07/26 | Mon 03/08/26 |
| 231 | 250 | L8 | 15 days | Sat 08/08/26 | Wed 26/08/26 |
| 232 | 251 | L9 | 15 days | Thu 27/08/26 | Sat 12/09/26 |
| 233 | 240 | L10 | 12 days | Tue 15/09/26 | Mon 28/09/26 |
| 234 | 241 | L11 | 12 days | Tue 29/09/26 | Mon 12/10/26 |
| 235 | 242 | L12 | 12 days | Wed 21/10/26 | Tue 03/11/26 |
| 236 | 243 | L13 | 12 days | Wed 04/11/26 | Wed 18/11/26 |
| 237 | 252 | L14 | 12 days | Fri 27/11/26 | Thu 10/12/26 |
| 238 | 253 | L15 | 15 days | Fri 11/12/26 | Tue 29/12/26 |
| 239 | 254 | L16 | 15 days | Wed 30/12/26 | Sat 16/01/27 |
| 240 | 255 | L17 | 15 days | Mon 18/01/27 | Wed 03/02/27 |
| 241 | 238 | L18 | 12 days | Thu 04/02/27 | Fri 19/02/27 |
| 242 | 239 | L19 | 12 days | Sat 20/02/27 | Fri 05/03/27 |
| 243 | 237 | L20 | 12 days | Sat 06/03/27 | Sat 20/03/27 |
| 244 | 236 | RF | 20 days | Thu 25/03/27 | Sat 17/04/27 |
| 245 | 810 | **Columns, Beams & Slabs** | **336 days** | **Sat 09/05/26** | **Thu 17/06/27** |
| 246 | 811 | **L2-L3** | **45 days** | **Sat 09/05/26** | **Thu 02/07/26** |
| 247 | 812 | L1-L3: Installation of Column | 5 days | Sat 09/05/26 | Thu 14/05/26 |
| 248 | 813 | **L2** | **35 days** | **Fri 15/05/26** | **Fri 26/06/26** |

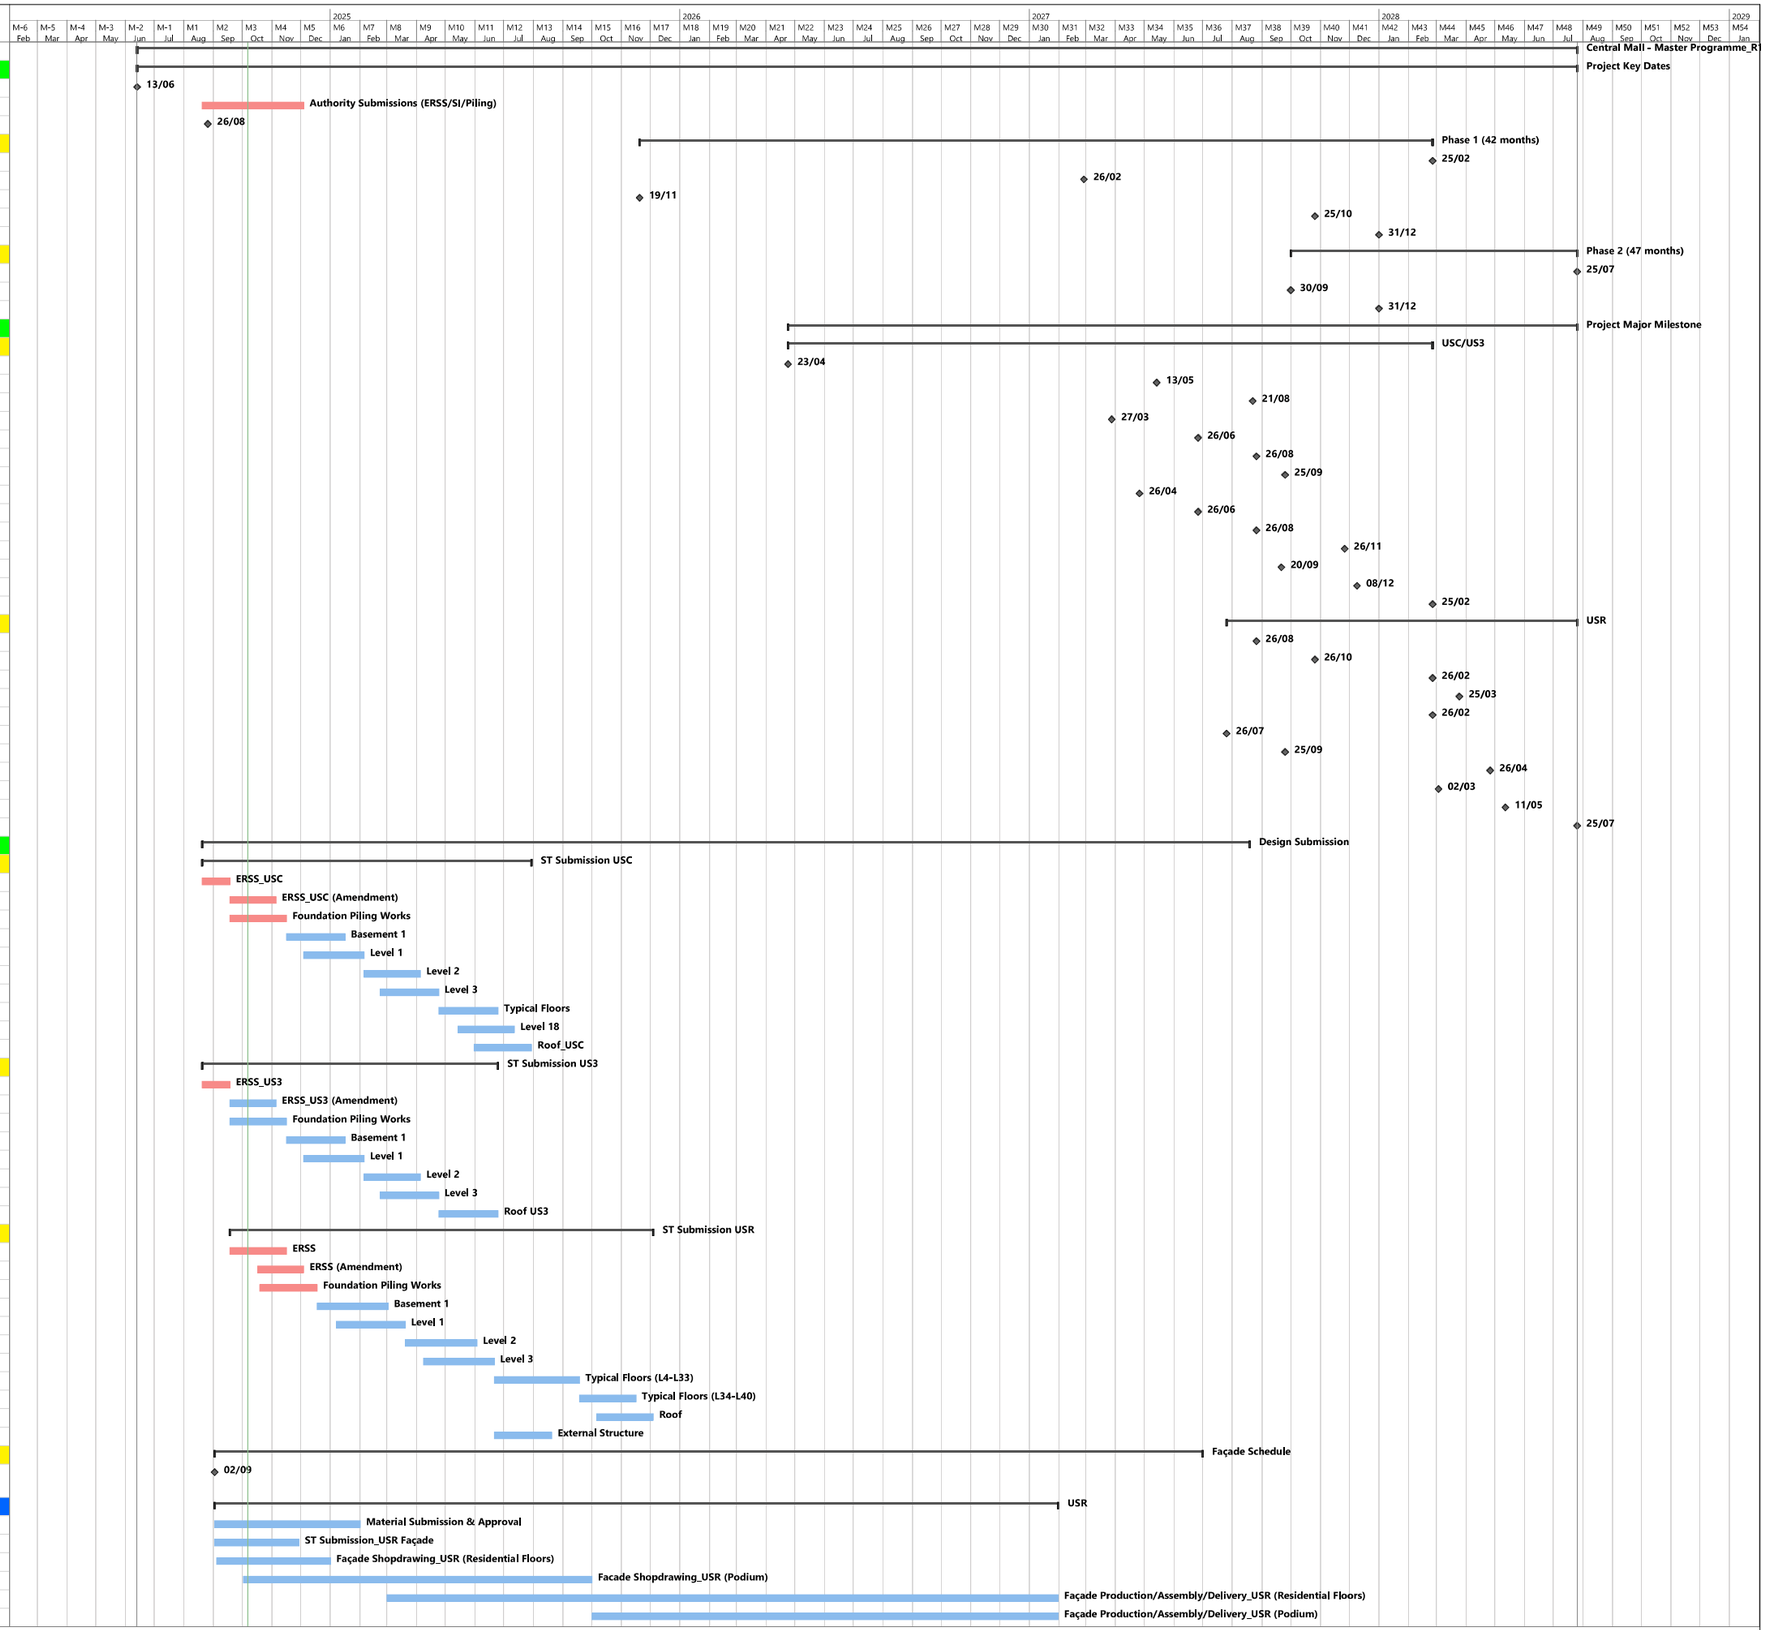


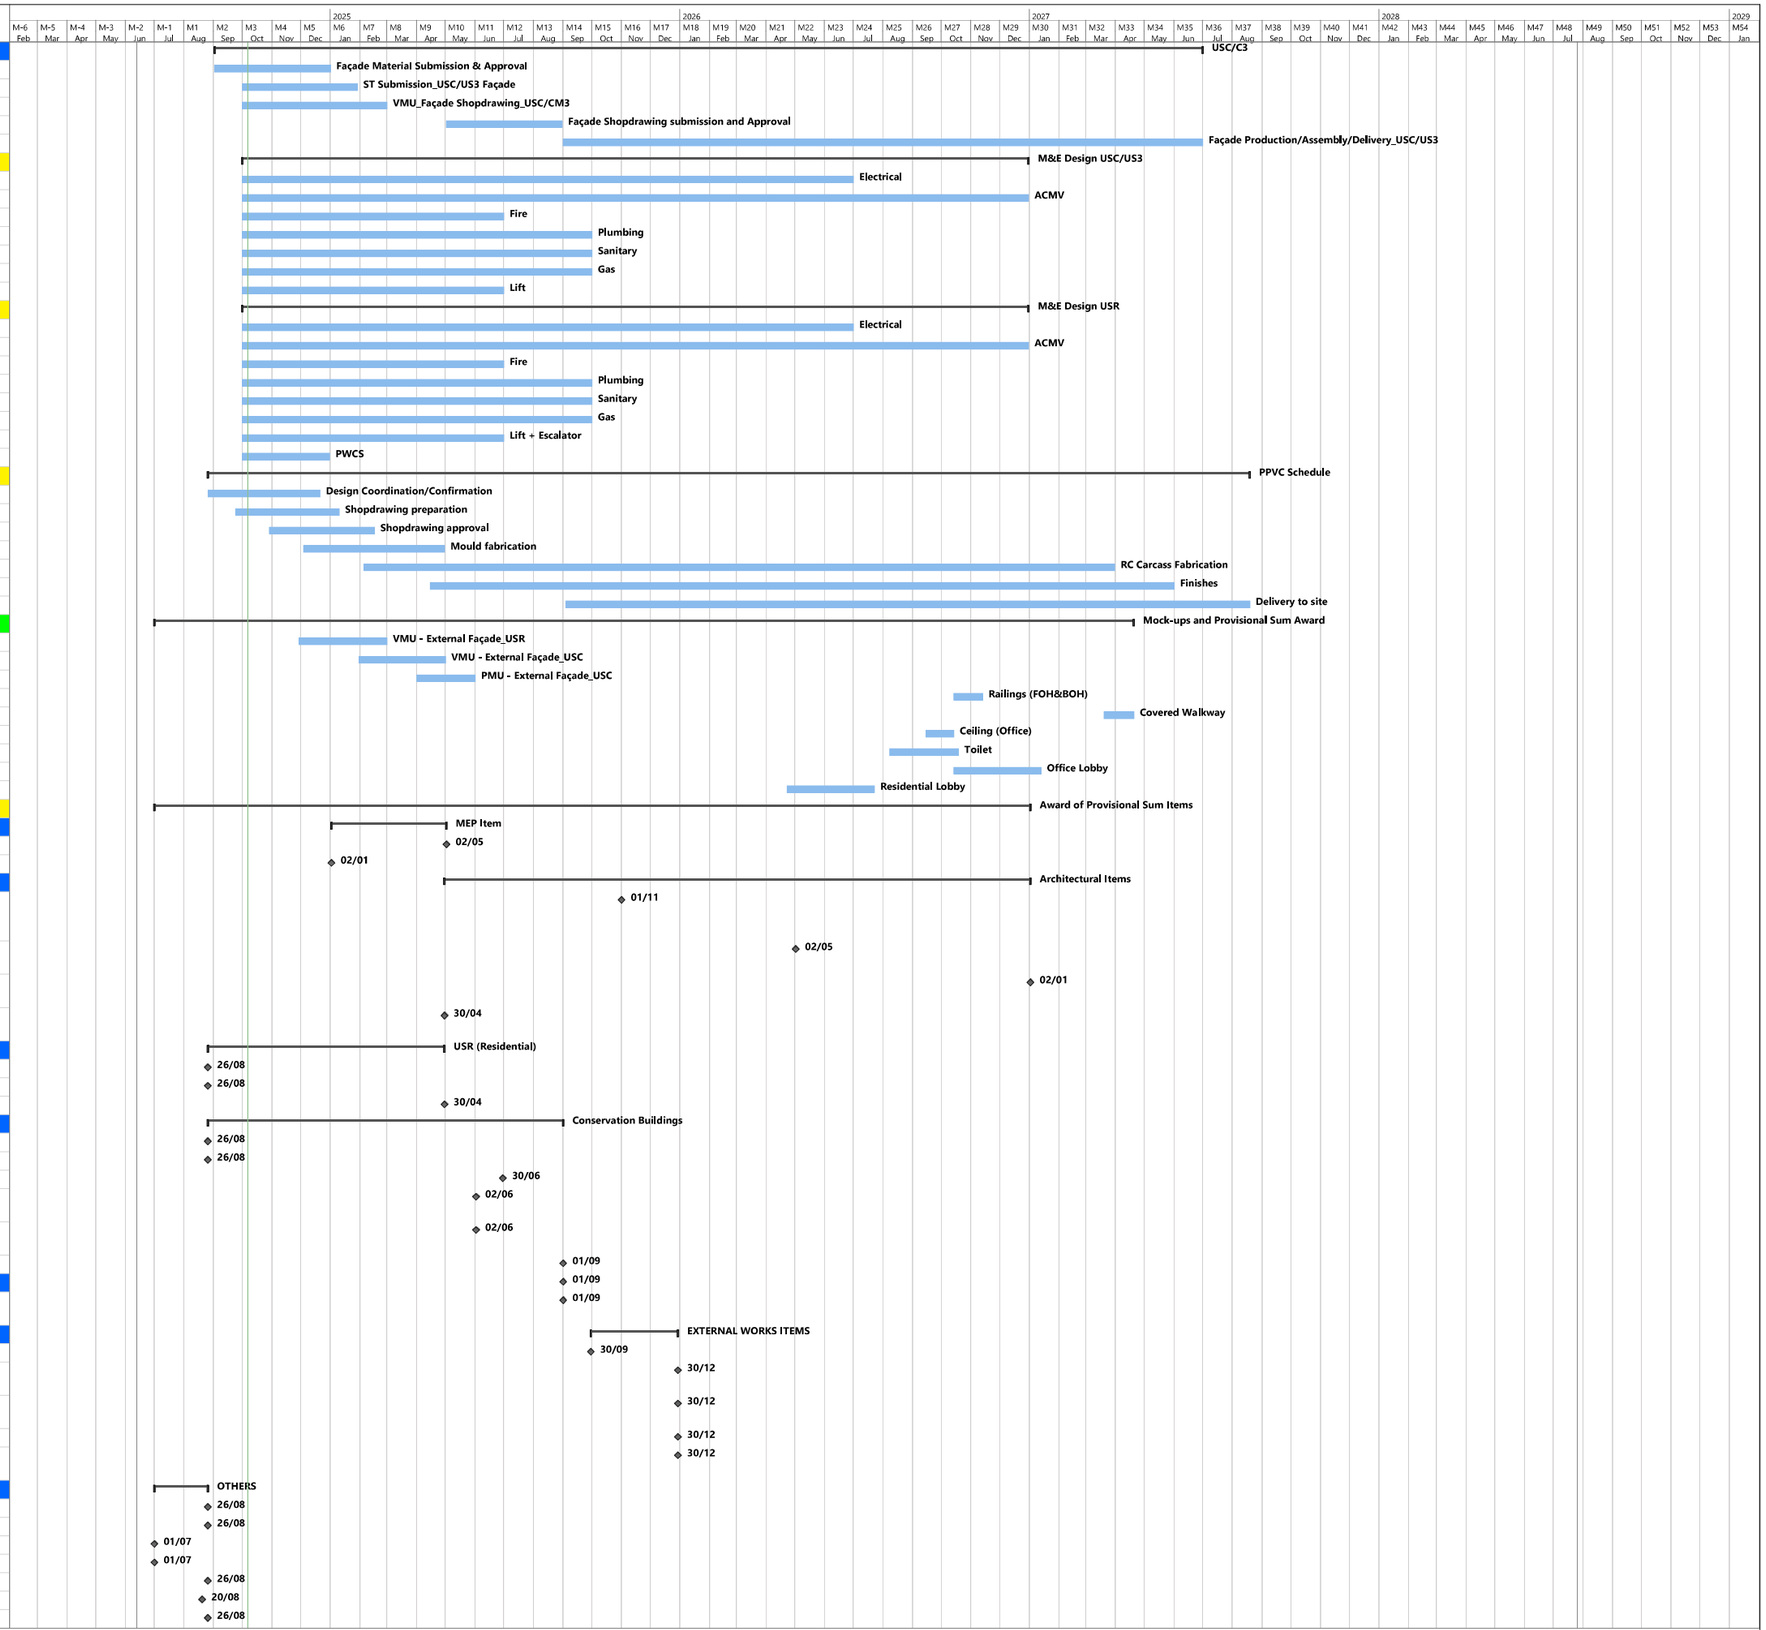Project: Central Mall - Master P
Date: Mon 07/10/24

Task · Split · Milestone · Summary · Project Summary · Inactive Task · Inactive Milestone · Inactive Summary · Manual Task · Duration-only · Manual Summary Rollup · Manual Summary · Start-only · Finish-only · External Tasks · External Milestone · Deadline · Critical · Critical Split · Progress · Manual Progress

| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 249 | 814 | L2: Erection of Steelworks | 15 days | Fri 15/05/26 | Wed 03/06/26 |
| 250 | 815 | L2: Installation of Bondek + Cast | 5 days | Mon 22/06/26 | Fri 26/06/26 |
| 251 | **816** | **L3** | **25 days** | **Thu 04/06/26** | **Thu 02/07/26** |
| 252 | 817 | L3: Erection of Steelworks | 15 days | Thu 04/06/26 | Sat 20/06/26 |
| 253 | 818 | L3: Installation of Bondek + Cast | 5 days | Sat 27/06/26 | Thu 02/07/26 |
| 254 | **819** | **L4-L5** | **31 days** | **Fri 03/07/26** | **Fri 07/08/26** |
| 255 | 820 | L3-L5: Installation of Column | 4 days | Fri 03/07/26 | Tue 07/07/26 |
| 256 | **821** | **L4** | **24 days** | **Wed 08/07/26** | **Tue 04/08/26** |
| 257 | 822 | L4: Erection of Steelworks | 11 days | Wed 08/07/26 | Mon 20/07/26 |
| 258 | 823 | L4: Installation of Bondek + Cast | 3 days | Sat 01/08/26 | Tue 04/08/26 |
| 259 | **824** | **L5** | **16 days** | **Tue 21/07/26** | **Fri 07/08/26** |
| 260 | 825 | L5: Erection of Steelworks | 10 days | Tue 21/07/26 | Fri 31/07/26 |
| 261 | 826 | L5: Installation of Bondek + Cast | 3 days | Wed 05/08/26 | Fri 07/08/26 |
| 262 | **827** | **L6-L7** | **31 days** | **Sat 08/08/26** | **Mon 14/09/26** |
| 263 | 828 | L5-L7: Installation of Column | 4 days | Sat 08/08/26 | Thu 13/08/26 |
| 264 | **829** | **L6** | **24 days** | **Fri 14/08/26** | **Thu 10/09/26** |
| 265 | 830 | L6: Erection of Steelworks | 11 days | Fri 14/08/26 | Wed 26/08/26 |
| 266 | 831 | L6: Installation of Bondek + Cast | 3 days | Tue 08/09/26 | Thu 10/09/26 |
| 267 | **832** | **L7** | **16 days** | **Thu 27/08/26** | **Mon 14/09/26** |
| 268 | 833 | L7: Erection of Steelworks | 10 days | Thu 27/08/26 | Mon 07/09/26 |
| 269 | 834 | L7: Installation of Bondek + Cast | 3 days | Fri 11/09/26 | Mon 14/09/26 |
| 270 | **835** | **L8-L9** | **31 days** | **Tue 15/09/26** | **Tue 20/10/26** |
| 271 | 836 | L7-L9: Installation of Column | 4 days | Tue 15/09/26 | Fri 18/09/26 |
| 272 | **837** | **L8** | **24 days** | **Sat 19/09/26** | **Fri 16/10/26** |
| 273 | 838 | L8: Erection of Steelworks | 11 days | Sat 19/09/26 | Thu 01/10/26 |
| 274 | 839 | L8: Installation of Bondek + Cast | 3 days | Wed 14/10/26 | Fri 16/10/26 |
| 275 | **840** | **L9** | **16 days** | **Fri 02/10/26** | **Tue 20/10/26** |
| 276 | 841 | L9: Erection of Steelworks | 10 days | Fri 02/10/26 | Tue 13/10/26 |
| 277 | 842 | L9: Installation of Bondek + Cast | 3 days | Sat 17/10/26 | Tue 20/10/26 |
| 278 | **843** | **L10-L11** | **31 days** | **Wed 21/10/26** | **Thu 26/11/26** |
| 279 | 844 | L9-L11: Installation of Column | 4 days | Wed 21/10/26 | Sat 24/10/26 |
| 280 | **845** | **L10** | **24 days** | **Mon 26/10/26** | **Mon 23/11/26** |
| 281 | 846 | L10: Erection of Steelworks | 11 days | Mon 26/10/26 | Fri 06/11/26 |
| 282 | 847 | L10: Installation of Bondek + Cast | 3 days | Fri 20/11/26 | Mon 23/11/26 |
| 283 | **848** | **L11** | **16 days** | **Sat 07/11/26** | **Thu 26/11/26** |
| 284 | 849 | L11: Erection of Steelworks | 10 days | Sat 07/11/26 | Thu 19/11/26 |
| 285 | 850 | L11: Installation of Bondek + Cast | 3 days | Tue 24/11/26 | Thu 26/11/26 |
| 286 | **851** | **L12-L13** | **24 days** | **Fri 27/11/26** | **Thu 24/12/26** |
| 287 | 852 | L11-L13: Installation of Column | 4 days | Fri 27/11/26 | Tue 01/12/26 |
| 288 | **853** | **L12** | **17 days** | **Wed 02/12/26** | **Mon 21/12/26** |
| 289 | 854 | L12: Erection of Steelworks | 7 days | Wed 02/12/26 | Wed 09/12/26 |
| 290 | 855 | L12: Installation of Bondek + Cast | 3 days | Fri 18/12/26 | Mon 21/12/26 |
| 291 | **856** | **L13** | **13 days** | **Thu 10/12/26** | **Thu 24/12/26** |
| 292 | 857 | L13: Erection of Steelworks | 7 days | Thu 10/12/26 | Thu 17/12/26 |
| 293 | 858 | L13: Installation of Bondek + Cast | 3 days | Tue 22/12/26 | Thu 24/12/26 |
| 294 | **859** | **L14-L15** | **24 days** | **Sat 26/12/26** | **Sat 23/01/27** |
| 295 | 860 | L13-L15: Installation of Column | 4 days | Sat 26/12/26 | Wed 30/12/26 |
| 296 | **861** | **L14** | **17 days** | **Thu 31/12/26** | **Wed 20/01/27** |
| 297 | 862 | L14: Erection of Steelworks | 7 days | Thu 31/12/26 | Fri 08/01/27 |
| 298 | 863 | L14: Installation of Bondek + Cast | 3 days | Mon 18/01/27 | Wed 20/01/27 |
| 299 | **864** | **L15** | **13 days** | **Sat 09/01/27** | **Sat 23/01/27** |
| 300 | 865 | L15: Erection of Steelworks | 7 days | Sat 09/01/27 | Sat 16/01/27 |
| 301 | 866 | L15: Installation of Bondek + Cast | 3 days | Thu 21/01/27 | Sat 23/01/27 |
| 302 | **867** | **L16-L17** | **24 days** | **Mon 25/01/27** | **Tue 23/02/27** |
| 303 | 868 | L15-L17: Installation of Column | 4 days | Mon 25/01/27 | Thu 28/01/27 |
| 304 | **869** | **L16** | **17 days** | **Fri 29/01/27** | **Fri 19/02/27** |
| 305 | 870 | L16: Erection of Steelworks | 7 days | Fri 29/01/27 | Fri 05/02/27 |
| 306 | 871 | L16: Installation of Bondek + Cast | 3 days | Wed 17/02/27 | Fri 19/02/27 |
| 307 | **872** | **L7** | **13 days** | **Tue 09/02/27** | **Tue 23/02/27** |
| 308 | 873 | L17: Erection of Steelworks | 7 days | Tue 09/02/27 | Tue 16/02/27 |
| 309 | 874 | L17: Installation of Bondek + Cast | 3 days | Sat 20/02/27 | Tue 23/02/27 |
| 310 | **875** | **L18-L19** | **31 days** | **Wed 24/02/27** | **Fri 02/04/27** |
| 311 | 876 | L17-L19: Installation of Column | 4 days | Wed 24/02/27 | Sat 27/02/27 |
| 312 | **877** | **L18** | **27 days** | **Mon 01/03/27** | **Fri 02/04/27** |
| 313 | 878 | L18: Erection of Steelworks | 7 days | Mon 01/03/27 | Mon 08/03/27 |
| 314 | 879 | L18: Installation of Bondek + Cast | 3 days | Thu 18/03/27 | Sat 20/03/27 |
| 315 | 880 | MEP | 10 days | Mon 22/03/27 | Fri 02/04/27 |
| 316 | **881** | **L19** | **13 days** | **Tue 09/03/27** | **Wed 24/03/27** |
| 317 | 882 | L19: Erection of Steelworks | 7 days | Tue 09/03/27 | Wed 17/03/27 |
| 318 | 883 | L19: Installation of Bondek + Cast | 3 days | Mon 22/03/27 | Wed 24/03/27 |
| 319 | **884** | **L20-RF** | **71 days** | **Thu 25/03/27** | **Thu 17/06/27** |
| 320 | 885 | L19-RF: Installation of Column | 6 days | Thu 25/03/27 | Thu 01/04/27 |
| 321 | **886** | **L20** | **30 days** | **Fri 02/04/27** | **Fri 07/05/27** |
| 322 | 887 | L20: Erection of Steelworks | 14 days | Fri 02/04/27 | Sat 17/04/27 |
| 323 | 888 | L20: Installation of Bondek + Cast | 5 days | Mon 03/05/27 | Fri 07/05/27 |
| 324 | **889** | **RF** | **21 days** | **Mon 19/04/27** | **Thu 13/05/27** |
| 325 | 890 | RF: Erection of Steelworks | 11 days | Mon 19/04/27 | Fri 30/04/27 |
| 326 | 891 | RF: Installation of Bondek + Cast | 5 days | Sat 08/05/27 | Thu 13/05/27 |
| 327 | **129** | **URF** | **30 days** | **Fri 14/05/27** | **Thu 17/06/27** |
| 328 | 2008 | LMR | 15 days | Fri 14/05/27 | Mon 31/05/27 |
| 329 | 2007 | URF (Upper Roof) | 30 days | Fri 14/05/27 | Thu 17/06/27 |
| 330 | **230** | **US3/DCS** | **110 days** | **Sat 31/01/26** | **Tue 16/06/26** |
| 331 | 126 | L2 | 30 days | Sat 31/01/26 | Mon 09/03/26 |
| 332 | 127 | L3 | 30 days | Tue 10/03/26 | Wed 15/04/26 |
| 333 | 1975 | Link Bridge at L3 to C5 | 50 days | Thu 16/04/26 | Tue 16/06/26 |
| 334 | 128 | RF | 40 days | Thu 16/04/26 | Thu 04/06/26 |

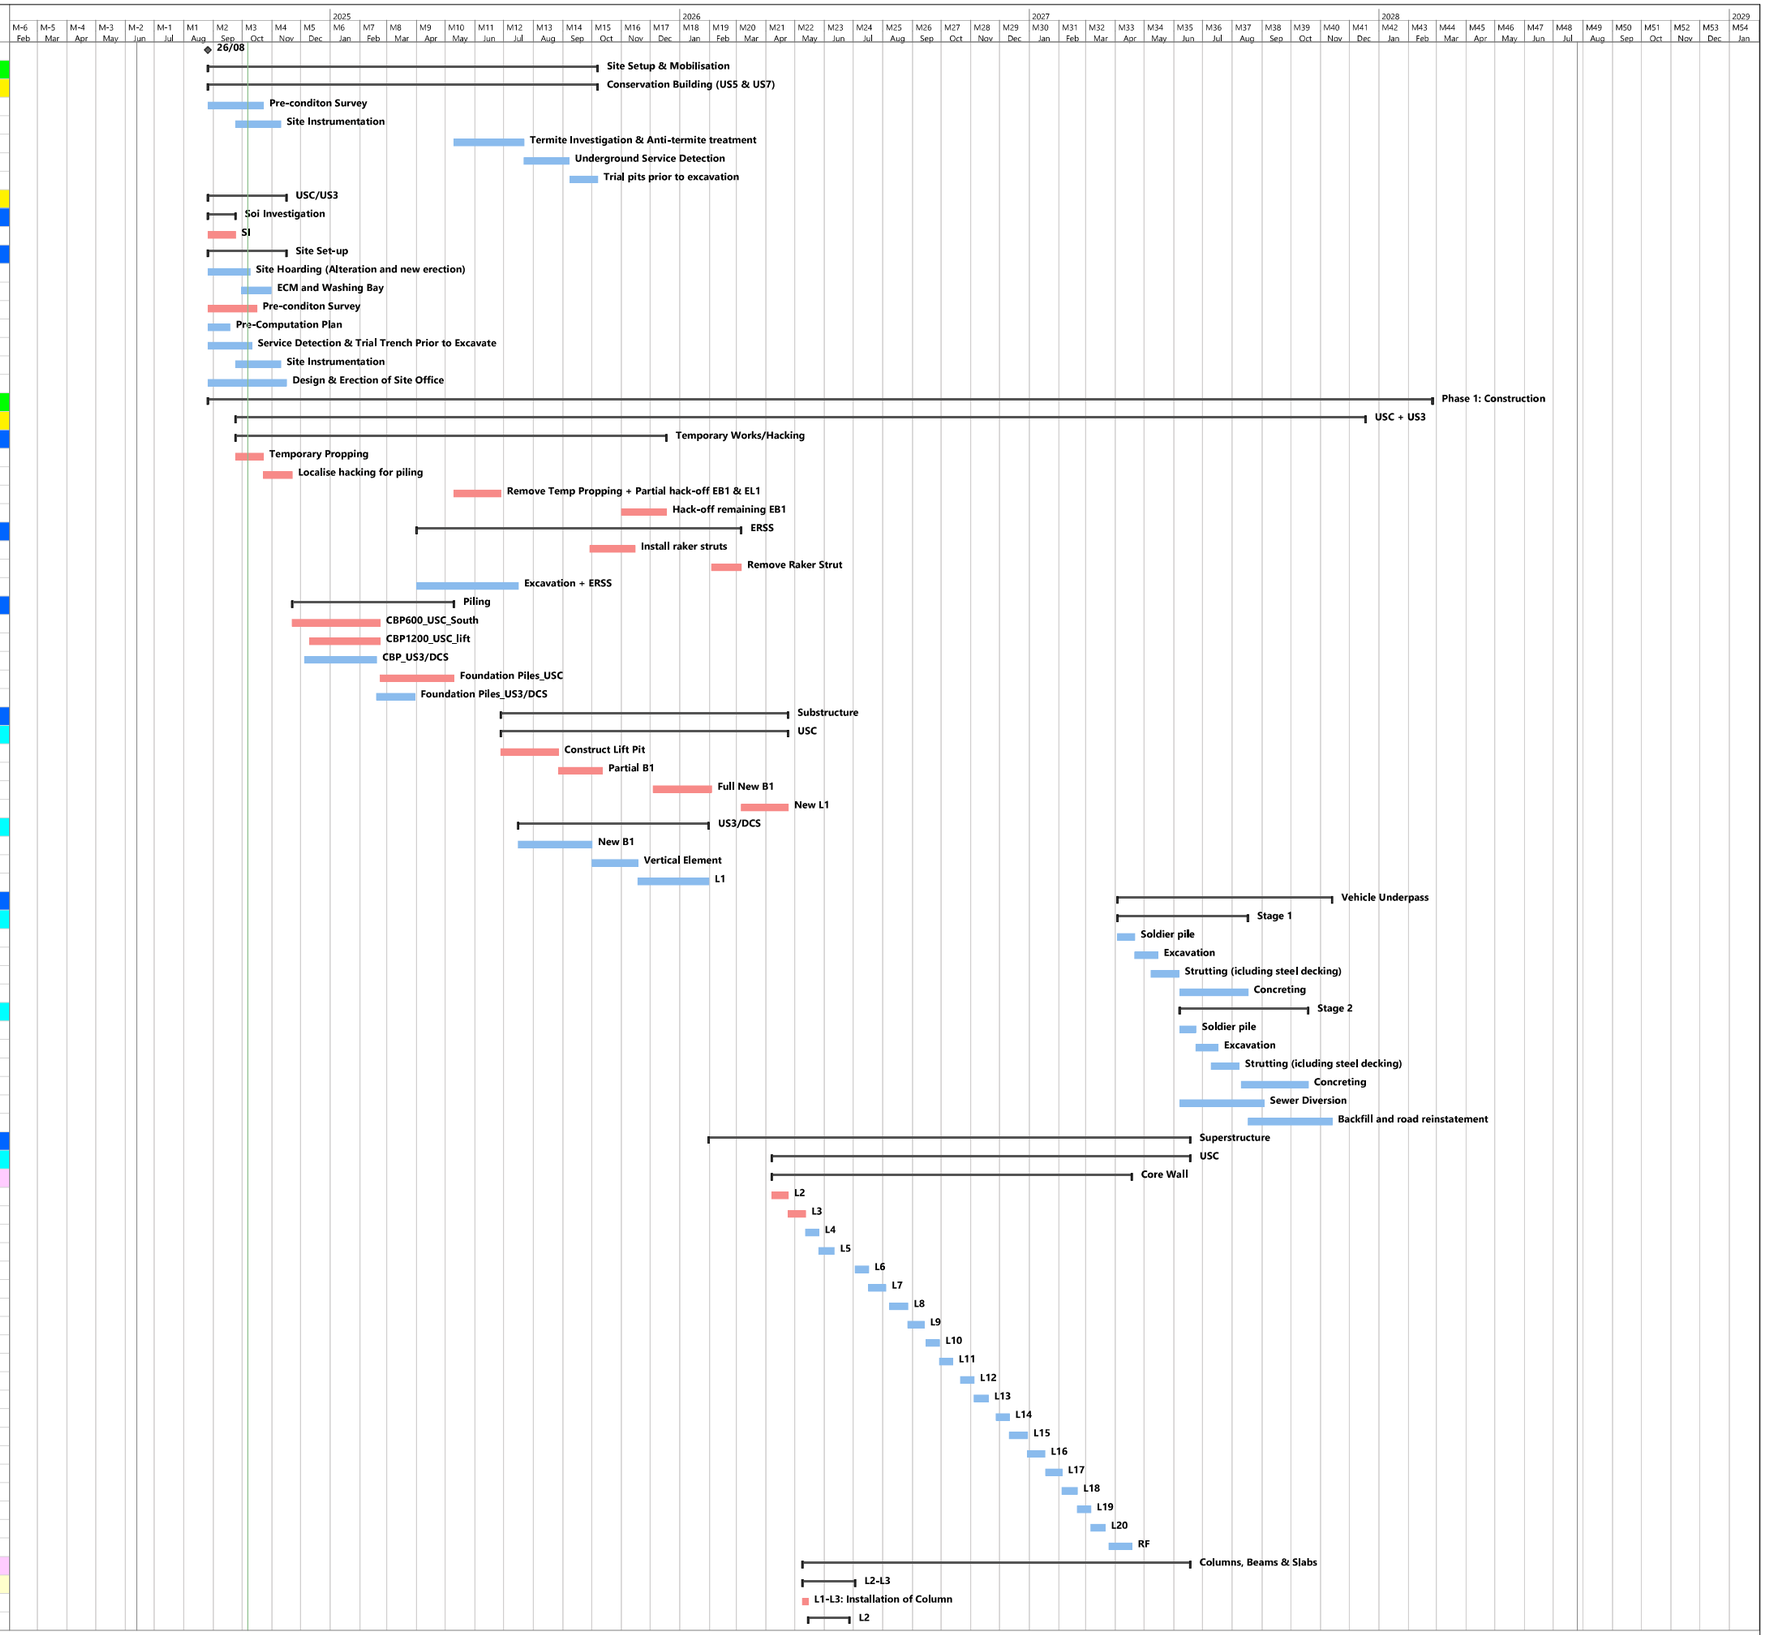


Project: Central Mall - Master P
Date: Mon 07/10/24

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress

| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 335 | **305** | **Façade** | **330 days** | **Thu 27/08/26** | **Sat 25/09/27** |
| 336 | 923 | L1 Façade/Shopfront | 44 days | Thu 04/02/27 | Wed 31/03/27 |
| 337 | 322 | L2 Façade | 30 days | Wed 30/12/26 | Wed 03/02/27 |
| 338 | 323 | L3 Façade | 25 days | Thu 27/08/26 | Thu 24/09/26 |
| 339 | 324 | L4 Façade | 25 days | Fri 25/09/26 | Fri 23/10/26 |
| 340 | 325 | L5 Façade | 15 days | Sat 24/10/26 | Wed 11/11/26 |
| 341 | 326 | L6 Façade | 15 days | Thu 12/11/26 | Sat 28/11/26 |
| 342 | 327 | L7 Façade | 15 days | Mon 30/11/26 | Wed 16/12/26 |
| 343 | 328 | L8 Façade | 15 days | Thu 17/12/26 | Tue 05/01/27 |
| 344 | 329 | L9 Façade | 15 days | Wed 06/01/27 | Fri 22/01/27 |
| 345 | 330 | L10 Façade | 15 days | Sat 23/01/27 | Thu 11/02/27 |
| 346 | 331 | L11 Façade | 15 days | Fri 12/02/27 | Mon 01/03/27 |
| 347 | 332 | L12 Façade | 15 days | Tue 02/03/27 | Fri 19/03/27 |
| 348 | 333 | L13 Façade | 15 days | Sat 20/03/27 | Wed 07/04/27 |
| 349 | 334 | L14 Façade | 15 days | Thu 08/04/27 | Sat 24/04/27 |
| 350 | 335 | L15 Façade | 15 days | Mon 26/04/27 | Thu 13/05/27 |
| 351 | 336 | L16 Façade | 15 days | Fri 14/05/27 | Mon 31/05/27 |
| 352 | 337 | L17 Façade | 15 days | Tue 01/06/27 | Thu 17/06/27 |
| 353 | 314 | L18 Façade | 15 days | Fri 18/06/27 | Mon 05/07/27 |
| 354 | 315 | L19 Façade | 15 days | Tue 06/07/27 | Thu 22/07/27 |
| 355 | 316 | L20 Façade | 25 days | Fri 23/07/27 | Sat 21/08/27 |
| 356 | 317 | Roof Crown | 40 days | Wed 11/08/27 | Sat 25/09/27 |
| 357 | **258** | **Finishing & MEP Works USC** | **431 days** | **Fri 03/07/26** | **Tue 30/11/27** |
| 358 | **259** | **Basement Finishing** | **220 days** | **Fri 03/07/26** | **Wed 24/03/27** |
| 359 | **282** | **M&E Rooms** | **85 days** | **Fri 03/07/26** | **Sat 10/10/26** |
| 360 | 287 | USC Consumer Switch HV Room | 50 days | Fri 03/07/26 | Mon 31/08/26 |
| 361 | 288 | USC Transformer Room | 50 days | Sat 01/08/26 | Tue 29/09/26 |
| 362 | 286 | HDC HT Switch Room | 50 days | Fri 14/08/26 | Sat 10/10/26 |
| 363 | 283 | M&E Tanks & Pump Rooms | 40 days | Tue 01/09/26 | Fri 16/10/26 |
| 364 | 285 | Greese Interceptor Room | 40 days | Sat 17/10/26 | Thu 03/12/26 |
| 365 | 284 | Ramp and Carprks | 90 days | Fri 04/12/26 | Wed 24/03/27 |
| 366 | **268** | **L1 Finishing** | **379 days** | **Fri 03/07/26** | **Wed 29/09/27** |
| 367 | 291 | SPPG Substation | 75 days | Fri 03/07/26 | Tue 29/09/26 |
| 368 | 292 | Transformer Room | 40 days | Tue 01/09/26 | Fri 16/10/26 |
| 369 | 2004 | SPPG Works | 132 days | Sat 17/10/26 | Sat 27/03/27 |
| 370 | 290 | MDF | 40 days | Sat 17/10/26 | Thu 03/12/26 |
| 371 | 293 | FCC/CMO | 40 days | Fri 04/12/26 | Thu 21/01/27 |
| 372 | 294 | Bin Centre | 40 days | Fri 22/01/27 | Fri 12/03/27 |
| 373 | 297 | Restaurants | 75 days | Thu 01/04/27 | Mon 28/06/27 |
| 374 | 296 | Waiting Lounge | 60 days | Fri 07/05/27 | Thu 15/07/27 |
| 375 | 301 | Toilets | 60 days | Tue 22/06/27 | Tue 31/08/27 |
| 376 | 289 | Drop-off | 45 days | Fri 16/07/27 | Tue 07/09/27 |
| 377 | 295 | Loading/Unloading | 40 days | Sat 14/08/27 | Wed 29/09/27 |
| 378 | **269** | **L2 Finishing** | **250 days** | **Wed 02/09/26** | **Tue 29/06/27** |
| 379 | 303 | Detention tank | 25 days | Wed 02/09/26 | Wed 30/09/26 |
| 380 | 299 | Genset | 40 days | Wed 02/09/26 | Sat 17/10/26 |
| 381 | 302 | Changing Room | 60 days | Mon 19/10/26 | Tue 29/12/26 |
| 382 | 300 | Management Office/Meeting Room/Store | 60 days | Thu 04/02/27 | Mon 19/04/27 |
| 383 | 298 | Bicycle park lots & Corridor | 60 days | Tue 20/04/27 | Tue 29/06/27 |
| 384 | **257** | **L3-L20 Finishing** | **334 days** | **Fri 25/09/26** | **Sat 30/10/27** |
| 385 | 270 | L3 | 60 days | Fri 25/09/26 | Fri 04/12/26 |
| 386 | 271 | L4 | 75 days | Mon 12/10/26 | Sat 09/01/27 |
| 387 | 272 | L5 | 75 days | Wed 28/10/26 | Tue 26/01/27 |
| 388 | 273 | L6 | 75 days | Sat 14/11/26 | Sat 13/02/27 |
| 389 | 274 | L7 | 75 days | Tue 01/12/26 | Tue 02/03/27 |
| 390 | 275 | L8 | 75 days | Thu 17/12/26 | Fri 19/03/27 |
| 391 | 264 | L9 | 75 days | Tue 05/01/27 | Tue 06/04/27 |
| 392 | 265 | L10 | 75 days | Thu 21/01/27 | Thu 22/04/27 |
| 393 | 276 | L11 | 75 days | Tue 09/02/27 | Mon 10/05/27 |
| 394 | 277 | L12 | 75 days | Thu 25/02/27 | Wed 26/05/27 |
| 395 | 278 | L13 | 75 days | Mon 15/03/27 | Fri 11/06/27 |
| 396 | 279 | L14 | 75 days | Thu 01/04/27 | Mon 28/06/27 |
| 397 | 280 | L15 | 75 days | Sat 17/04/27 | Wed 14/07/27 |
| 398 | 281 | L16 | 75 days | Wed 05/05/27 | Fri 30/07/27 |
| 399 | 266 | L17 | 75 days | Fri 21/05/27 | Tue 17/08/27 |
| 400 | 267 | L18 | 100 days | Mon 07/06/27 | Fri 01/10/27 |
| 401 | 262 | L19 | 75 days | Wed 23/06/27 | Sat 18/09/27 |
| 402 | 263 | L20 | 75 days | Tue 03/08/27 | Sat 30/10/27 |
| 403 | **256** | **Roof** | **110 days** | **Fri 23/07/27** | **Tue 30/11/27** |
| 404 | 261 | Restaurant | 90 days | Fri 23/07/27 | Sat 06/11/27 |
| 405 | 260 | Roof Garden/Planter/BMU | 55 days | Mon 27/09/27 | Tue 30/11/27 |
| 406 | **340** | **Finishing & MEP Works US3/DCS** | **414 days** | **Fri 05/06/26** | **Tue 12/10/27** |
| 407 | **341** | **Basement Finishes (DCS Core & Shell)** | **289 days** | **Fri 05/06/26** | **Tue 18/05/27** |
| 408 | 1985 | DCS Riser | 25 days | Fri 05/06/26 | Fri 03/07/26 |
| 409 | 339 | MEP Rooms | 90 days | Fri 05/06/26 | Fri 18/09/26 |
| 410 | 338 | Chiller Stations | 90 days | Sat 19/09/26 | Tue 05/01/27 |
| 411 | 342 | Carpark | 45 days | Thu 25/03/27 | Tue 18/05/27 |
| 412 | **343** | **L1 Finishing** | **389 days** | **Sat 04/07/26** | **Tue 12/10/27** |
| 413 | 1986 | DCS Riser | 25 days | Sat 04/07/26 | Sat 01/08/26 |
| 414 | 347 | Shops | 60 days | Thu 01/04/27 | Thu 10/06/27 |
| 415 | 346 | Restaurant | 60 days | Fri 11/06/27 | Fri 20/08/27 |
| 416 | 348 | Service Road | 45 days | Sat 21/08/27 | Tue 12/10/27 |
| 417 | **344** | **L2 - RF** | **220 days** | **Mon 03/08/26** | **Sat 24/04/27** |
| 418 | 1987 | Riser L2 to RF | 75 days | Mon 03/08/26 | Thu 29/10/26 |
| 419 | 349 | L2 | 90 days | Sat 19/09/26 | Tue 05/01/27 |
| 420 | 350 | L3 | 90 days | Wed 06/01/27 | Sat 24/04/27 |

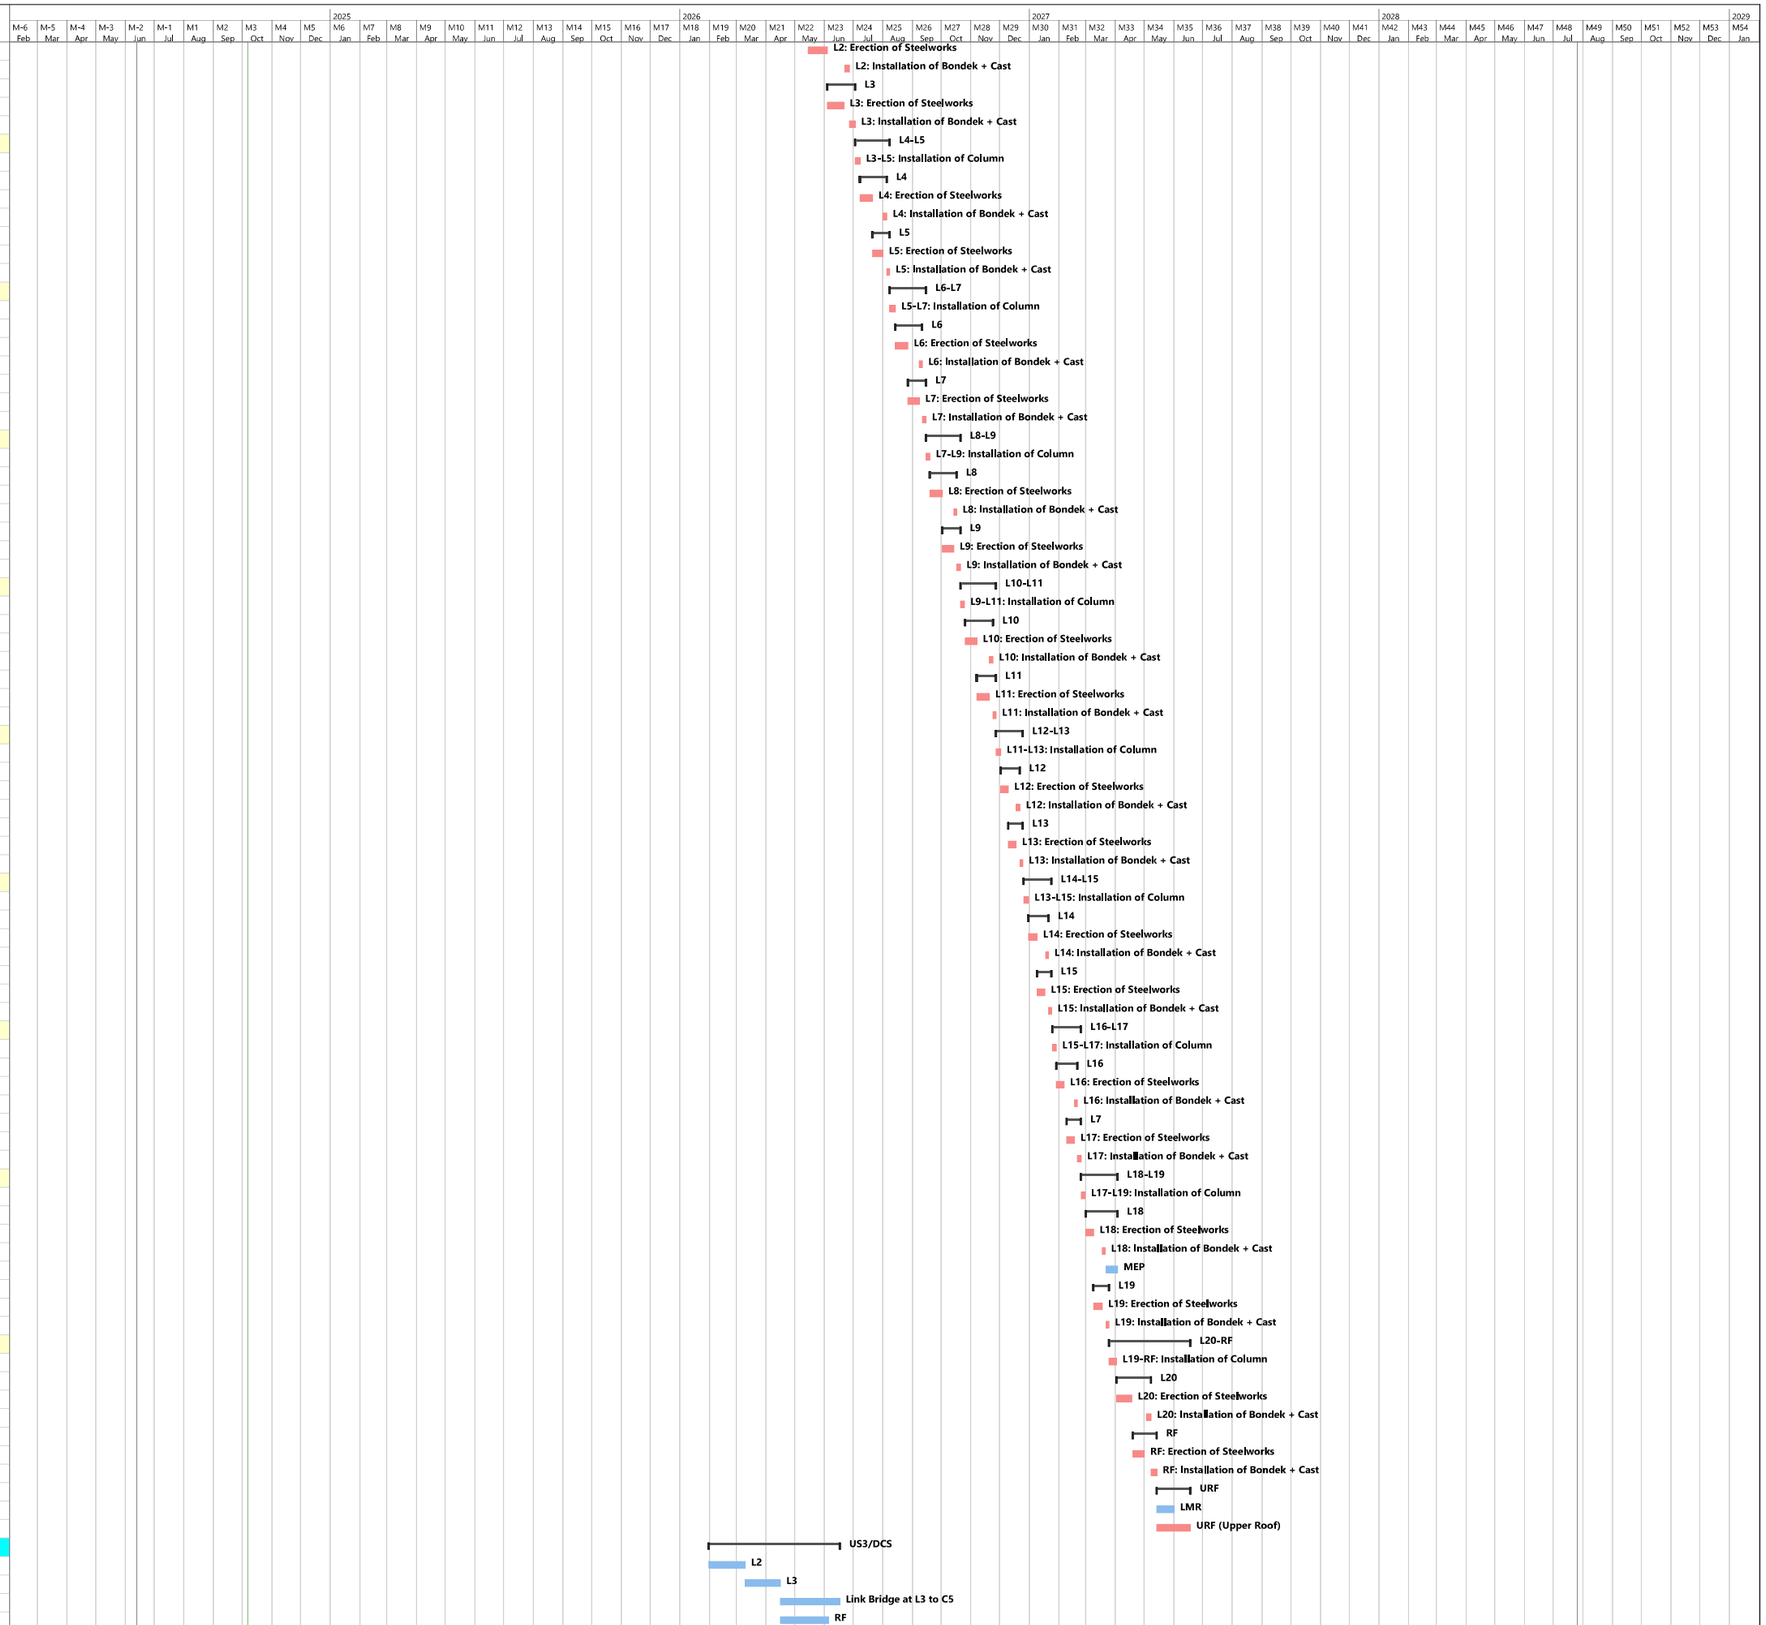


Project: Central Mall - Master P
Date: Mon 07/10/24

Task · Split · Milestone · Summary · Project Summary · Inactive Task · Inactive Milestone · Inactive Summary · Manual Task · Duration-only · Manual Summary Rollup · Manual Summary · Start-only · Finish-only · External Tasks · External Milestone · Deadline · Critical · Critical Split · Progress · Manual Progress

| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 421 | 1988 | Roof preparation for DCS Equipment | 75 days | Sat 19/09/26 | Wed 16/12/26 |
| 422 | 345 | Roofing/Roof Screen | 75 days | Fri 27/11/26 | Fri 26/02/27 |
| 423 | 1976 | Link Bridge at L3 to C5 | 60 days | Wed 06/01/27 | Fri 19/03/27 |
| 424 | **386** | **Common Area Finishes (Lift Lobbies + Staircase)** | **250 days** | **Wed 30/12/26** | **Mon 25/10/27** |
| 425 | 395 | Basement | 60 days | Thu 22/07/27 | Thu 30/09/27 |
| 426 | 396 | L1 | 60 days | Thu 13/05/27 | Wed 21/07/27 |
| 427 | 397 | L2 | 60 days | Wed 30/12/26 | Sat 13/03/27 |
| 428 | 398 | L3 | 40 days | Tue 12/01/27 | Mon 01/03/27 |
| 429 | 399 | L4 | 60 days | Sat 23/01/27 | Wed 07/04/27 |
| 430 | 400 | L5 | 60 days | Thu 04/02/27 | Mon 19/04/27 |
| 431 | 401 | L6 | 60 days | Thu 18/02/27 | Fri 30/04/27 |
| 432 | 402 | L7 | 60 days | Tue 02/03/27 | Thu 13/05/27 |
| 433 | 391 | L8 | 60 days | Mon 15/03/27 | Tue 25/05/27 |
| 434 | 392 | L9 | 60 days | Sat 27/03/27 | Sat 05/06/27 |
| 435 | 393 | L10 | 60 days | Thu 08/04/27 | Thu 17/06/27 |
| 436 | 394 | L11 | 60 days | Tue 20/04/27 | Tue 29/06/27 |
| 437 | 389 | L12 | 60 days | Mon 03/05/27 | Sat 10/07/27 |
| 438 | 390 | L13 | 60 days | Fri 14/05/27 | Thu 22/07/27 |
| 439 | 388 | L14 | 60 days | Wed 26/05/27 | Tue 03/08/27 |
| 440 | 387 | L15 | 60 days | Mon 07/06/27 | Mon 16/08/27 |
| 441 | 407 | L16 | 60 days | Fri 18/06/27 | Fri 27/08/27 |
| 442 | 408 | L17 | 60 days | Wed 30/06/27 | Wed 08/09/27 |
| 443 | 409 | L18 | 60 days | Mon 12/07/27 | Mon 20/09/27 |
| 444 | 410 | L19 | 60 days | Fri 23/07/27 | Fri 01/10/27 |
| 445 | 405 | L20 | 60 days | Wed 04/08/27 | Wed 13/10/27 |
| 446 | 406 | Roof | 60 days | Tue 17/08/27 | Mon 25/10/27 |
| 447 | 404 | LMR | 60 days | Mon 12/07/27 | Mon 20/09/27 |
| 448 | **352** | **External Finishes & Landscape** | **120 days** | **Thu 29/07/27** | **Fri 17/12/27** |
| 449 | **901** | **Conservation Buildings (US5 & US7)** | **747 days** | **Sat 10/05/25** | **Mon 25/10/27** |
| 450 | **1869** | **Coservation Building US5** | **747 days** | **Sat 10/05/25** | **Mon 25/10/27** |
| 451 | 906 | Erection of Building Protection structure | 150 days | Sat 10/05/25 | Wed 05/11/25 |
| 452 | **1848** | **US5-A: ROOF** | **72 days** | **Thu 06/11/25** | **Fri 30/01/26** |
| 453 | 1792 | Existing Services Termination/Removal/Protection | 12 days | Thu 06/11/25 | Wed 19/11/25 |
| 454 | 1794 | Removal of extg. Roof Ceiling | 7 days | Thu 20/11/25 | Thu 27/11/25 |
| 455 | 1795 | Inspection and Strengthening of existing roof truss | 15 days | Fri 28/11/25 | Mon 15/12/25 |
| 456 | 1796 | Restoration works (Roofing, facia and gutters) | 20 days | Tue 16/12/25 | Fri 09/01/26 |
| 457 | 1803 | Reinstate MEP services at roof | 18 days | Sat 10/01/26 | Fri 30/01/26 |
| 458 | **1849** | **US5-B: ROOF** | **72 days** | **Thu 20/11/25** | **Fri 13/02/26** |
| 459 | 1850 | Existing Services Termination/Removal/Protection | 12 days | Thu 20/11/25 | Wed 03/12/25 |
| 460 | 1851 | Removal of extg. Roof Ceiling | 7 days | Thu 04/12/25 | Thu 11/12/25 |
| 461 | 1852 | Inspection and Strengthening of existing roof truss | 15 days | Fri 12/12/25 | Tue 30/12/25 |
| 462 | 1853 | Restoration works (Roofing, facia and gutters) | 20 days | Wed 31/12/25 | Fri 23/01/26 |
| 463 | 1854 | Reinstate MEP services at roof | 18 days | Sat 24/01/26 | Fri 13/02/26 |
| 464 | 1856 | Repair works at concrete flat roof | 8 days | Sat 17/01/26 | Mon 26/01/26 |
| 465 | 1857 | Waterproofing works at concrete flat works | 7 days | Tue 27/01/26 | Tue 03/02/26 |
| 466 | 1858 | Install new roof tiles | 8 days | Wed 04/02/26 | Thu 12/02/26 |
| 467 | **1859** | **US5-C: ROOF** | **93 days** | **Thu 04/12/25** | **Fri 27/03/26** |
| 468 | 1860 | Existing Services Termination/Removal/Protection | 12 days | Thu 04/12/25 | Wed 17/12/25 |
| 469 | 1861 | Removal of extg. Roof Ceiling/Truss protection | 8 days | Thu 18/12/25 | Sat 27/12/25 |
| 470 | 1862 | Inspection and Strengthening of existing roof truss | 30 days | Mon 29/12/25 | Mon 02/02/26 |
| 471 | 1863 | Restoration works (Roofing, facia and gutters) | 30 days | Tue 03/02/26 | Wed 11/03/26 |
| 472 | 1865 | Installation of new skylights | 12 days | Thu 12/03/26 | Thu 26/03/26 |
| 473 | 1907 | Reinstate MEP services at roof | 25 days | Thu 26/02/26 | Fri 27/03/26 |
| 474 | **1870** | **US5-A: LEVEL 3** | **179 days** | **Sat 31/01/26** | **Sat 05/09/26** |
| 475 | 1801 | Existing Services Termination/Removal/Protection | 10 days | Sat 31/01/26 | Wed 11/02/26 |
| 476 | 1800 | Soft striffing of fixtures and furnishing | 8 days | Thu 12/02/26 | Mon 23/02/26 |
| 477 | 1806 | Removal of existing doors/windows/Wall panelling and framing | 6 days | Tue 24/02/26 | Mon 02/03/26 |
| 478 | 1805 | Removal of fittings and its associated pipe works | 8 days | Thu 12/02/26 | Mon 23/02/26 |
| 479 | 1804 | Strengthening/Repair works of Concrete/Steel Structure | 12 days | Tue 03/03/26 | Mon 16/03/26 |
| 480 | 1807 | Repair works of walls & Ceiling | 8 days | Tue 17/03/26 | Thu 26/03/26 |
| 481 | 1808 | Repair works of Floor Finishing | 10 days | Fri 27/03/26 | Wed 08/04/26 |
| 482 | 1809 | Glazing repairs | 6 days | Thu 09/04/26 | Wed 15/04/26 |
| 483 | 1811 | Metal work repair | 6 days | Thu 09/04/26 | Wed 15/04/26 |
| 484 | 1810 | Install new floor and wall Finishes, wall Paneling including timber w | 10 days | Thu 09/04/26 | Mon 20/04/26 |
| 485 | 1812 | Install new reinstated Doors, Windows, louvers or vents. | 8 days | Tue 21/04/26 | Wed 29/04/26 |
| 486 | 1813 | Reinstate MEP Sevices | 55 days | Tue 24/02/26 | Thu 30/04/26 |
| 487 | 2018 | Handover to Restoration Specialist | 6 days | Sat 02/05/26 | Fri 08/05/26 |
| 488 | 2009 | ID Fit-out Works by Restoration specialist | 100 days | Sat 09/05/26 | Sat 05/09/26 |
| 489 | **1872** | **US5-C: ATTICE** | **155 days** | **Fri 27/03/26** | **Tue 29/09/26** |
| 490 | 1875 | Existing Services Termination/Removal/Protection | 7 days | Fri 27/03/26 | Sat 04/04/26 |
| 491 | 1873 | Removal of existing walls doors/windows | 6 days | Mon 06/04/26 | Sat 11/04/26 |
| 492 | 1874 | Removal of Existing staircase, Beam & Slab | 12 days | Mon 13/04/26 | Sat 25/04/26 |
| 493 | 1876 | Reinstate surrounding structure | 20 days | Mon 27/04/26 | Wed 20/05/26 |
| 494 | 2020 | Handover to Restoration Specialist | 3 days | Tue 30/06/26 | Thu 02/07/26 |
| 495 | 2011 | ID Fit-out Works by Restoration specialist | 75 days | Fri 03/07/26 | Tue 29/09/26 |
| 496 | **1877** | **US5-A / US5-B: LEVEL 2** | **187 days** | **Sat 25/07/26** | **Sat 06/03/27** |
| 497 | 1814 | Existing Services Termination/Removal/Protection | 12 days | Sat 25/07/26 | Fri 07/08/26 |
| 498 | 1815 | Soft striffing of fixtures and furnishing | 10 days | Sat 08/08/26 | Thu 20/08/26 |
| 499 | 1816 | Removal of existing doors/windows/wall panelling and framing | 10 days | Fri 21/08/26 | Tue 01/09/26 |
| 500 | 1842 | Removal of Existing Timber flooring to be replaced with concrete sl | 8 days | Fri 21/08/26 | Sat 29/08/26 |
| 501 | 1817 | Removal of fittings and its associated pipe works | 18 days | Sat 08/08/26 | Sat 29/08/26 |
| 502 | 1818 | Strengthening/Repair works of Concrete Structure including casting | 35 days | Wed 02/09/26 | Mon 12/10/26 |
| 503 | 1819 | Repair works of walls & Ceiling | 15 days | Tue 13/10/26 | Thu 29/10/26 |
| 504 | 1820 | Repair works of Floor Finishing | 15 days | Fri 30/10/26 | Tue 17/11/26 |
| 505 | 1821 | Glazing repairs | 10 days | Wed 18/11/26 | Sat 28/11/26 |
| 506 | 1822 | Metal work repair | 8 days | Wed 18/11/26 | Thu 26/11/26 |

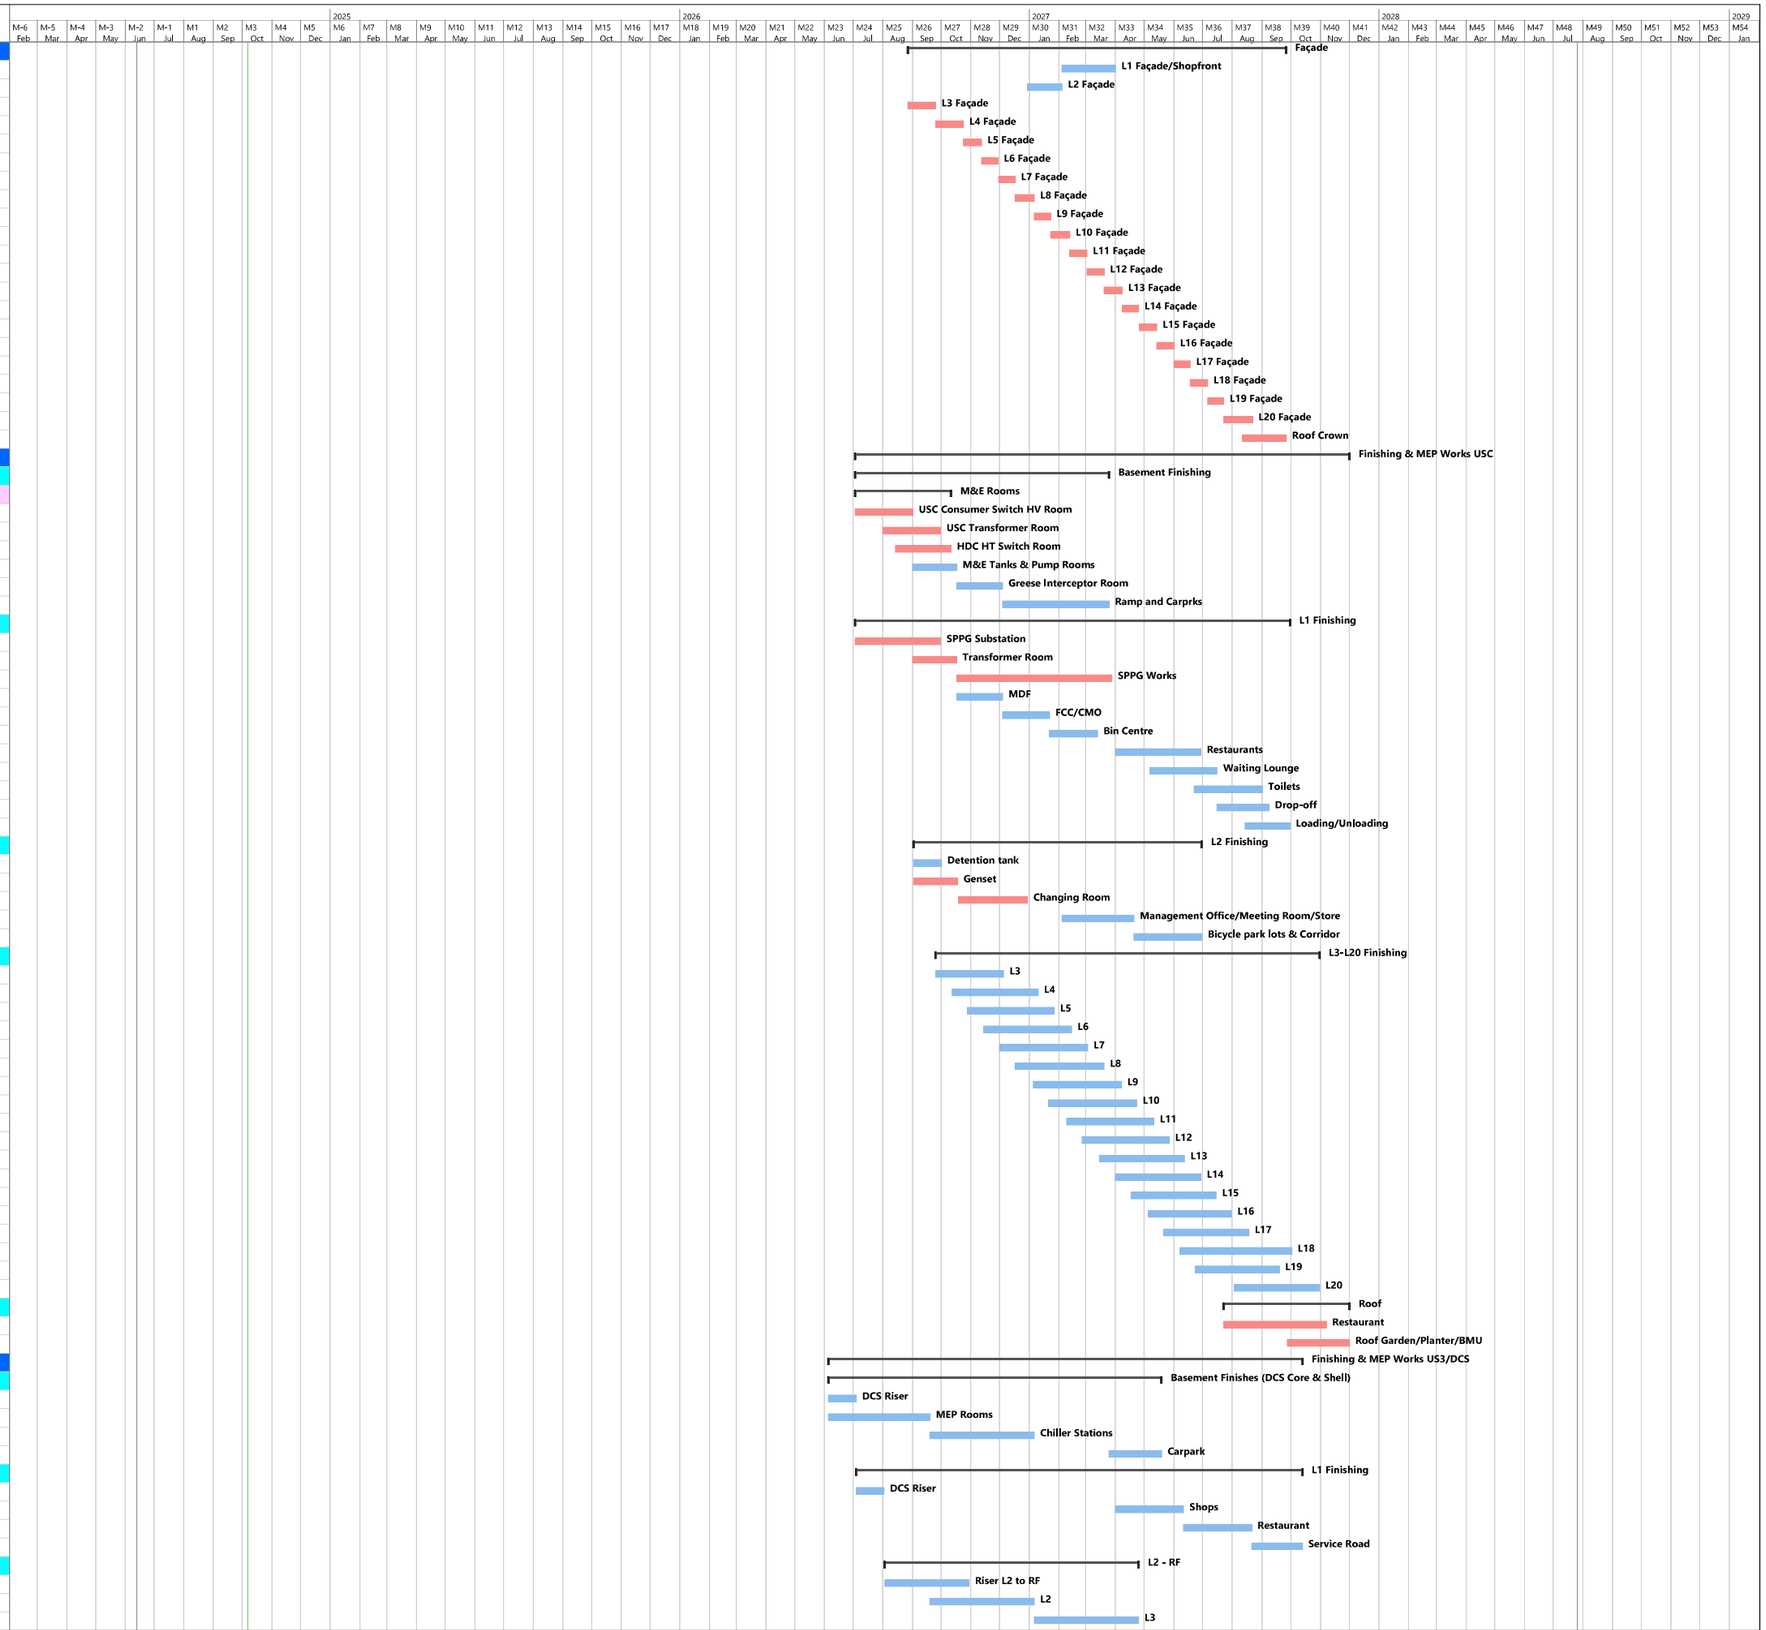


Project: Central Mall - Master P
Date: Mon 07/10/24

Task · Milestone · Project Summary · Inactive Milestone · Manual Task · Manual Summary Rollup · Start-only · External Tasks · Deadline · Critical Split · Manual Progress
Split · Summary · Inactive Task · Inactive Summary · Duration-only · Manual Summary · Finish-only · External Milestone · Critical · Progress

| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 507 | 1823 | Install new floor and wall Finishes, wall Paneling including timber w | 20 days | Wed 18/11/26 | Thu 10/12/26 |
| 508 | 1824 | Install new reinstated Doors, Windows, louvers or vents. | 12 days | Fri 11/12/26 | Thu 24/12/26 |
| 509 | 1825 | Reinstate MEP Sevices | 63 days | Tue 13/10/26 | Sat 26/12/26 |
| 510 | 2021 | Handover to Restoration Specialist | 6 days | Wed 30/09/26 | Tue 06/10/26 |
| 511 | 2014 | ID Fit-out Works by Restoration specialist | 125 days | Wed 07/10/26 | Sat 06/03/27 |
| 512 | **1879** | **US5-C: LEVEL 2** | **171 days** | **Tue 12/01/27** | **Wed 04/08/27** |
| 513 | 1880 | Existing Services Termination/Removal/Protection | 12 days | Tue 12/01/27 | Mon 25/01/27 |
| 514 | 1881 | Soft striffing of fixtures and furnishing | 10 days | Tue 26/01/27 | Fri 05/02/27 |
| 515 | 1882 | Removal of existing doors/windows/Wall panelling and framing/Tir | 10 days | Tue 09/02/27 | Fri 19/02/27 |
| 516 | 1883 | Removal of Existing Timber flooring to be replaced with concrete sl | 8 days | Tue 09/02/27 | Wed 17/02/27 |
| 517 | 1884 | Removal of fittings and its associated pipe works | 18 days | Tue 26/01/27 | Wed 17/02/27 |
| 518 | 1885 | Strengthening/Repair works of Concrete Structure including casting | 35 days | Sat 20/02/27 | Sat 03/04/27 |
| 519 | 1886 | Repair works of walls & Ceiling | 15 days | Mon 05/04/27 | Wed 21/04/27 |
| 520 | 1887 | Repair works of Floor Finishing | 15 days | Thu 22/04/27 | Mon 10/05/27 |
| 521 | 1888 | Glazing repairs | 10 days | Tue 11/05/27 | Fri 21/05/27 |
| 522 | 1889 | Metal work repair | 8 days | Tue 11/05/27 | Wed 19/05/27 |
| 523 | 1890 | Install new floor and wall Finishes, wall Paneling including timber w | 20 days | Tue 11/05/27 | Wed 02/06/27 |
| 524 | 1891 | Install new reinstated Doors, Windows, louvers or vents. | 12 days | Thu 03/06/27 | Wed 16/06/27 |
| 525 | 1892 | Reinstate MEP Sevices | 63 days | Mon 05/04/27 | Thu 17/06/27 |
| 526 | 2022 | Handover to Restoration Specialist | 6 days | Mon 08/03/27 | Mon 15/03/27 |
| 527 | 2015 | ID Fit-out Works by Restoration specialist | 120 days | Tue 16/03/27 | Wed 04/08/27 |
| 528 | **1893** | **US5-A / US5-B: LEVEL 1** | **218 days** | **Fri 11/12/26** | **Tue 31/08/27** |
| 529 | 1826 | Existing Services Termination/Removal/Protection | 12 days | Fri 11/12/26 | Thu 24/12/26 |
| 530 | 1827 | Soft striffing of fixtures and furnishing | 10 days | Sat 26/12/26 | Thu 07/01/27 |
| 531 | 1828 | Removal of existing doors/windows/Wall panelling and framing | 10 days | Fri 08/01/27 | Tue 19/01/27 |
| 532 | 1829 | Removal of fittings and its associated pipe works | 18 days | Sat 26/12/26 | Sat 16/01/27 |
| 533 | 1830 | Repair works of Concrete Structure | 20 days | Wed 20/01/27 | Sat 13/02/27 |
| 534 | 1843 | Demolition of existing Floor, Beams & Pile Cap | 20 days | Wed 20/01/27 | Sat 13/02/27 |
| 535 | 1844 | Underpinning works | 25 days | Tue 09/02/27 | Tue 09/03/27 |
| 536 | 1845 | Construct new Pile Cap | 20 days | Thu 04/03/27 | Mon 29/03/27 |
| 537 | 1846 | Construct New Beam, Stump & Slab | 20 days | Mon 22/03/27 | Wed 14/04/27 |
| 538 | 1831 | Repair works of walls & Ceiling | 25 days | Thu 15/04/27 | Fri 14/05/27 |
| 539 | 1847 | Construct new Wall | 20 days | Thu 15/04/27 | Sat 08/05/27 |
| 540 | 1832 | Repair works of Floor Finishing | 12 days | Sat 15/05/27 | Fri 28/05/27 |
| 541 | 1833 | Glazing repairs | 12 days | Sat 29/05/27 | Fri 11/06/27 |
| 542 | 1834 | Metal work repair | 10 days | Sat 29/05/27 | Wed 09/06/27 |
| 543 | 1835 | Install new floor and wall Finishes and wall Paneling including timbe | 20 days | Sat 29/05/27 | Mon 21/06/27 |
| 544 | 1836 | Install new reinstated Doors, Windows, louvers or vents. | 12 days | Tue 22/06/27 | Mon 05/07/27 |
| 545 | 1837 | Reinstate MEP Sevices | 70 days | Thu 15/04/27 | Tue 06/07/27 |
| 546 | 2023 | Handover to Restoration Specialist | 6 days | Wed 31/03/27 | Tue 06/04/27 |
| 547 | 2016 | ID Fit-out Works by Restoration specialist | 124 days | Wed 07/04/27 | Tue 31/08/27 |
| 548 | **1903** | **US5-C: LEVEL 1** | **244 days** | **Fri 11/12/26** | **Thu 30/09/27** |
| 549 | 1840 | Removal of temporary Site Office Partitions/Doors/Ceiling | 25 days | Fri 11/12/26 | Mon 11/01/27 |
| 550 | 1841 | Removal of fittings and its associated pipe works | 18 days | Tue 12/01/27 | Mon 01/02/27 |
| 551 | 1839 | Demolition of existing Floor Stairs, Beams & Slab | 15 days | Mon 05/04/27 | Wed 21/04/27 |
| 552 | 1838 | Construct New Beam & Slab | 25 days | Thu 15/04/27 | Fri 14/05/27 |
| 553 | 1895 | Repair works of walls & Ceiling | 20 days | Sat 15/05/27 | Mon 07/06/27 |
| 554 | 1896 | Construct new Wall | 20 days | Sat 15/05/27 | Mon 07/06/27 |
| 555 | 1897 | Repair works of Floor Finishing | 15 days | Tue 08/06/27 | Thu 24/06/27 |
| 556 | 1898 | Glazing repairs | 12 days | Fri 25/06/27 | Thu 08/07/27 |
| 557 | 1899 | Metal work repair | 10 days | Fri 25/06/27 | Tue 06/07/27 |
| 558 | 1900 | Install new floor and wall Finishes and wall Paneling including timbe | 30 days | Fri 25/06/27 | Thu 29/07/27 |
| 559 | 1901 | Install new reinstated Doors, Windows, louvers or vents. | 12 days | Fri 30/07/27 | Fri 13/08/27 |
| 560 | 1902 | Reinstate MEP Sevices | 78 days | Sat 15/05/27 | Sat 14/08/27 |
| 561 | 2024 | Handover to Restoration Specialist | 6 days | Fri 23/04/27 | Thu 29/04/27 |
| 562 | 2017 | ID Fit-out Works by Restoration specialist | 130 days | Fri 30/04/27 | Thu 30/09/27 |
| 563 | 908 | Removal of protection works and touch up | 120 days | Mon 08/03/27 | Wed 28/07/27 |
| 564 | 1904 | Reinstatement of the affected surrounding | 103 days | Sat 26/06/27 | Mon 25/10/27 |
| 565 | **1906** | **Coservation Building US7** | **453 days** | **Sat 31/01/26** | **Sat 31/07/27** |
| 566 | **1909** | **US7: ROOF** | **83 days** | **Sat 31/01/26** | **Wed 13/05/26** |
| 567 | 1910 | Existing Services Termination/Removal/Protection | 12 days | Sat 31/01/26 | Fri 13/02/26 |
| 568 | 1911 | Removal of extg. Roof Ceiling/Truss protection | 8 days | Sat 14/02/26 | Wed 25/02/26 |
| 569 | 1912 | Inspection and Strengthening of existing roof truss | 25 days | Thu 26/02/26 | Fri 27/03/26 |
| 570 | 1913 | Restoration works (Roofing, facia and gutters) | 25 days | Sat 28/03/26 | Mon 27/04/26 |
| 571 | 1915 | Reinstate MEP services at roof | 25 days | Tue 14/04/26 | Wed 13/05/26 |
| 572 | **1908** | **US7: LEVEL 3** | **132 days** | **Tue 28/04/26** | **Fri 02/10/26** |
| 573 | 1916 | Existing Services Termination/Removal/Protection | 10 days | Tue 28/04/26 | Sat 09/05/26 |
| 574 | 1917 | Soft striffing of fixtures and furnishing | 8 days | Mon 11/05/26 | Tue 19/05/26 |
| 575 | 1918 | Removal of existing doors/windows/Wall panelling and framing | 6 days | Wed 20/05/26 | Tue 26/05/26 |
| 576 | 1919 | Removal of fittings and its associated pipe works | 8 days | Mon 11/05/26 | Tue 19/05/26 |
| 577 | 1920 | Strengthening/Repair works of Concrete/Steel Structure | 12 days | Thu 28/05/26 | Thu 11/06/26 |
| 578 | 1921 | Repair works of walls & Ceiling | 8 days | Fri 12/06/26 | Sat 20/06/26 |
| 579 | 1922 | Repair works of Floor Finishing | 10 days | Mon 22/06/26 | Thu 02/07/26 |
| 580 | 1923 | Glazing repairs | 6 days | Fri 03/07/26 | Thu 09/07/26 |
| 581 | 1924 | Metal work repair | 6 days | Fri 03/07/26 | Thu 09/07/26 |
| 582 | 1925 | Install new floor and wall Finishes, wall Paneling including timber w | 10 days | Fri 03/07/26 | Tue 14/07/26 |
| 583 | 1926 | Install new reinstated Doors, Windows, louvers or vents. | 8 days | Wed 15/07/26 | Thu 23/07/26 |
| 584 | 1927 | Reinstate MEP Sevices | 55 days | Wed 20/05/26 | Fri 24/07/26 |
| 585 | 2025 | Handover to Restoration Specialist | 3 days | Fri 03/07/26 | Mon 06/07/26 |
| 586 | 2026 | ID Fit-out Works by Restoration specialist | 75 days | Tue 07/07/26 | Fri 02/10/26 |
| 587 | **1928** | **US7: LEVEL 2** | **227 days** | **Fri 12/06/26** | **Thu 11/03/27** |
| 588 | 1929 | Existing Services Termination/Removal/Protection | 12 days | Fri 12/06/26 | Thu 25/06/26 |
| 589 | 1930 | Soft striffing of fixtures and furnishing | 10 days | Fri 26/06/26 | Tue 07/07/26 |
| 590 | 1931 | Removal of existing doors/windows/Wall panelling and framing/Tir | 10 days | Wed 08/07/26 | Sat 18/07/26 |
| 591 | 1932 | Removal of Existing Timber flooring to be replaced with concrete sl | 8 days | Wed 08/07/26 | Thu 16/07/26 |
| 592 | 1933 | Removal of fittings and its associated pipe works | 18 days | Fri 26/06/26 | Thu 16/07/26 |

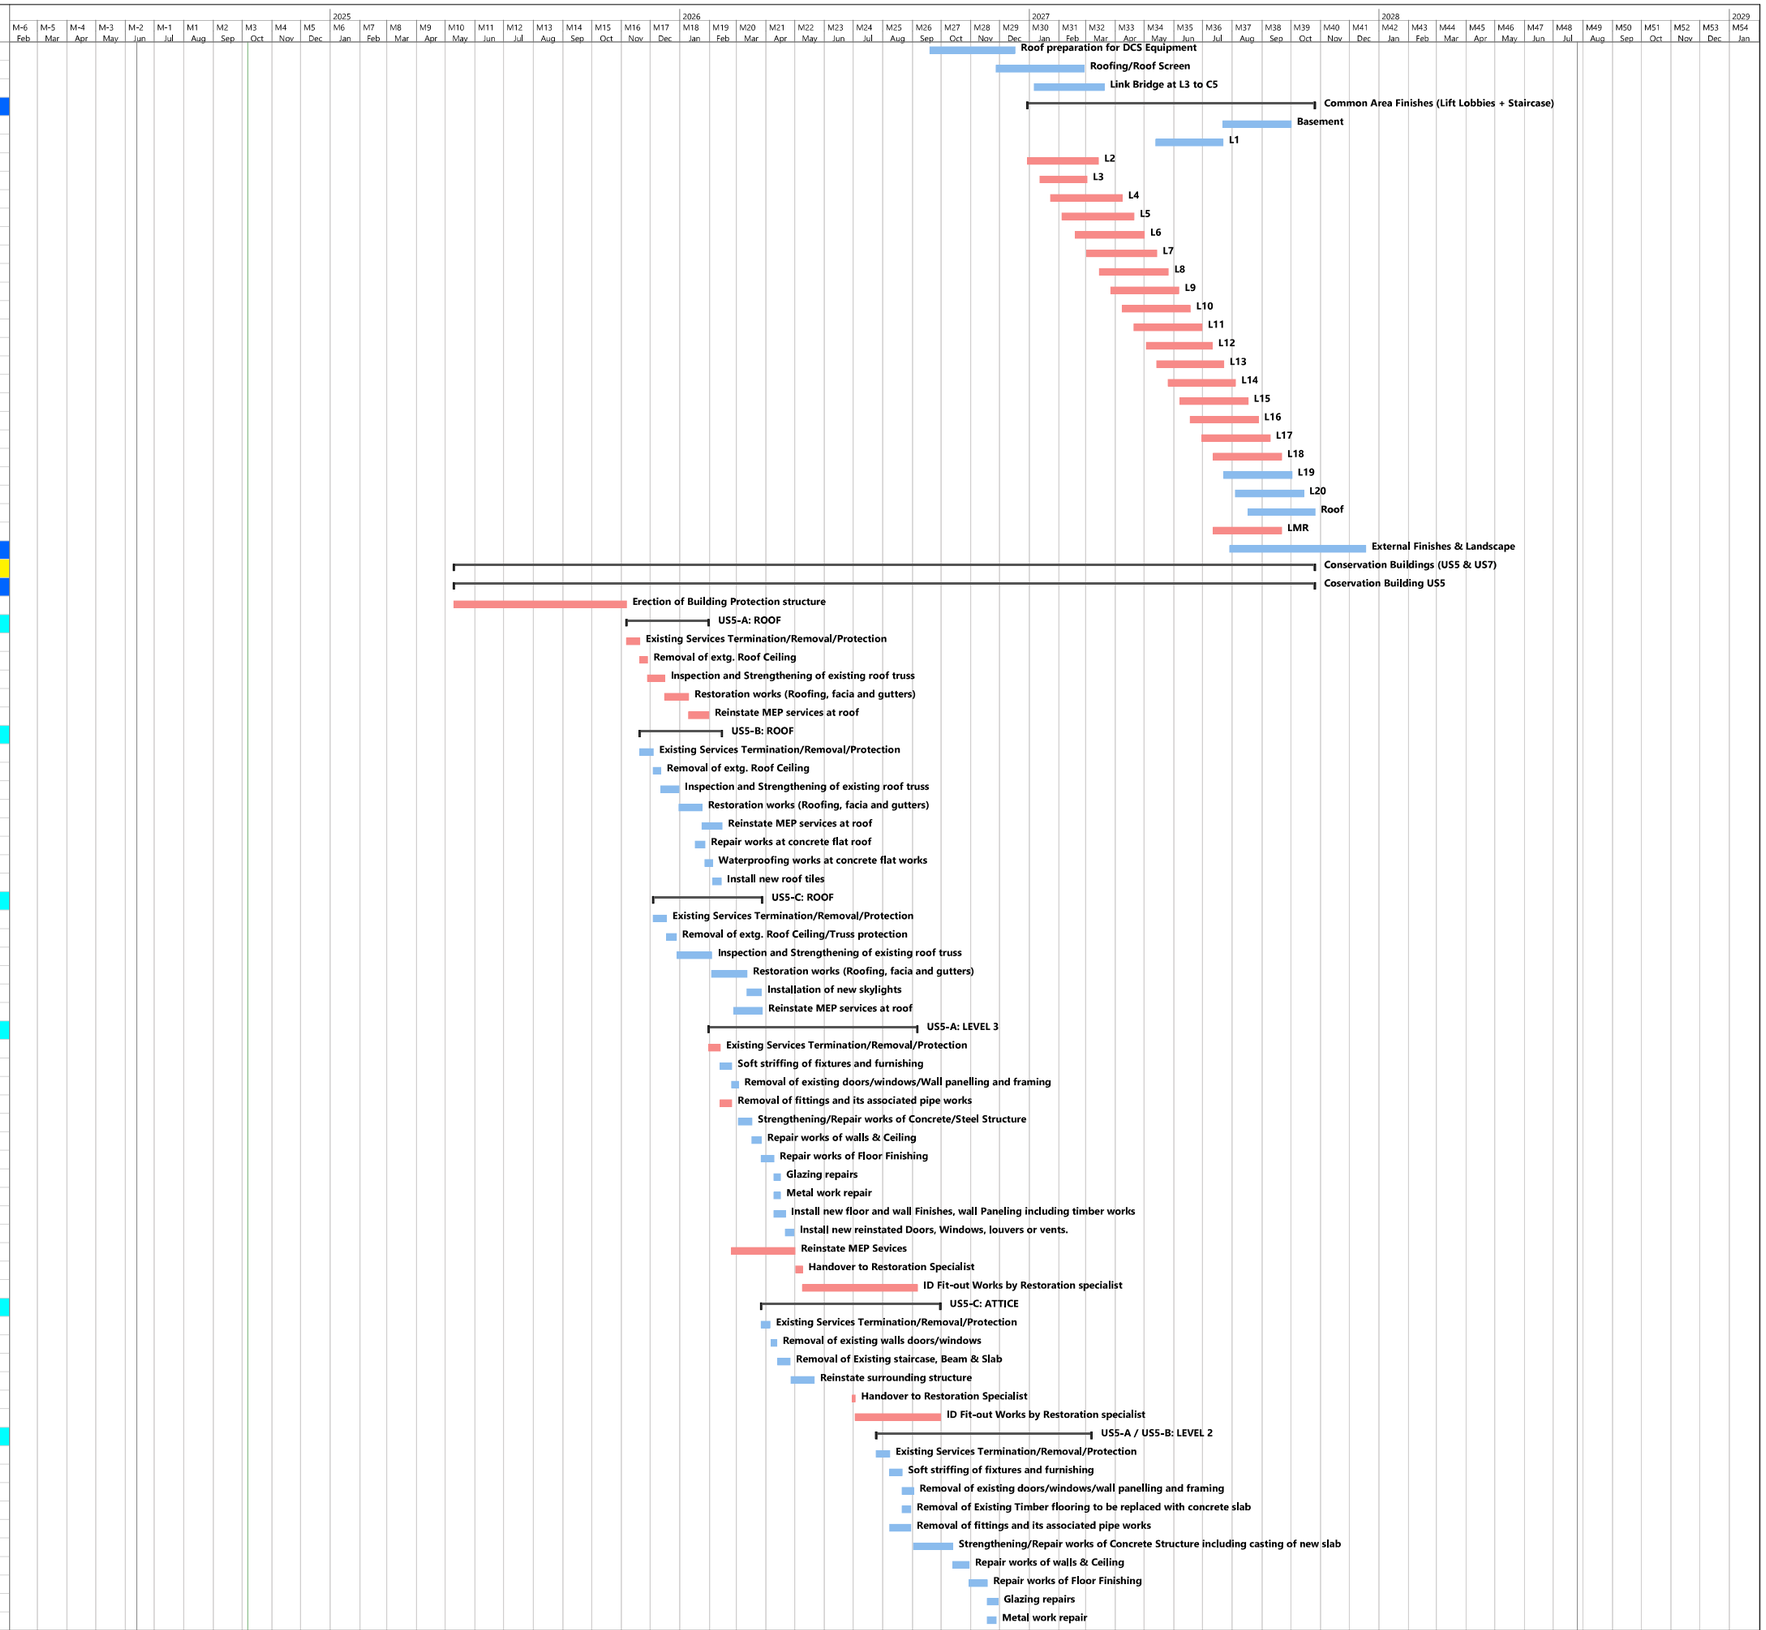


Project: Central Mall - Master P
Date: Mon 07/10/24

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress

| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 593 | 1934 | Strengthening/Repair works of Concrete Structure including casting | 25 days | Mon 20/07/26 | Tue 18/08/26 |
| 594 | 1935 | Repair works of walls & Ceiling | 15 days | Wed 19/08/26 | Fri 04/09/26 |
| 595 | 1936 | Repair works of Floor Finishing | 15 days | Sat 05/09/26 | Tue 22/09/26 |
| 596 | 1937 | Glazing repairs | 10 days | Wed 23/09/26 | Sat 03/10/26 |
| 597 | 1938 | Metal work repair | 8 days | Wed 23/09/26 | Thu 01/10/26 |
| 598 | 1939 | Install new floor and wall Finishes, wall Paneling including timber w | 20 days | Wed 23/09/26 | Thu 15/10/26 |
| 599 | 1940 | Install new reinstated Doors, Windows, louvers or vents. | 12 days | Fri 16/10/26 | Thu 29/10/26 |
| 600 | 1941 | Reinstate MEP Sevices | 63 days | Wed 19/08/26 | Fri 30/10/26 |
| 601 | 2027 | Handover to Restoration Specialist | 6 days | Sat 03/10/26 | Fri 09/10/26 |
| 602 | 2028 | ID Fit-out Works by Restoration specialist | 125 days | Sat 10/10/26 | Thu 11/03/27 |
| 603 | **1942** | **US7: LEVEL 1** | **221 days** | **Fri 16/10/26** | **Fri 09/07/27** |
| 604 | 1955 | Existing Services Termination/Removal/Protection | 12 days | Fri 16/10/26 | Thu 29/10/26 |
| 605 | 1956 | Soft striffing of fixtures and furnishing | 10 days | Fri 30/10/26 | Wed 11/11/26 |
| 606 | 1957 | Demolition of existing Floor Stairs, Beams & Slab | 15 days | Thu 12/11/26 | Sat 28/11/26 |
| 607 | 1958 | Construct New Beam & Slab | 25 days | Mon 23/11/26 | Mon 21/12/26 |
| 608 | 1959 | Repair works of walls & Ceiling | 15 days | Tue 22/12/26 | Sat 09/01/27 |
| 609 | 1960 | Construct new Wall | 15 days | Tue 22/12/26 | Sat 09/01/27 |
| 610 | 1961 | Repair works of Floor Finishing | 15 days | Mon 11/01/27 | Wed 27/01/27 |
| 611 | 1962 | Glazing repairs | 12 days | Thu 28/01/27 | Fri 12/02/27 |
| 612 | 1963 | Metal work repair | 10 days | Thu 28/01/27 | Wed 10/02/27 |
| 613 | 1964 | Install new floor and wall Finishes and wall Paneling including timbe | 25 days | Thu 28/01/27 | Sat 27/02/27 |
| 614 | 1965 | Install new reinstated Doors, Windows, louvers or vents. | 12 days | Mon 01/03/27 | Mon 15/03/27 |
| 615 | 1966 | Reinstate MEP Sevices | 70 days | Tue 22/12/26 | Thu 18/03/27 |
| 616 | 2029 | Handover to Restoration Specialist | 6 days | Tue 02/02/27 | Wed 10/02/27 |
| 617 | 2030 | ID Fit-out Works by Restoration specialist | 125 days | Thu 11/02/27 | Fri 09/07/27 |
| 618 | 1967 | Removal of protection works and touch up | 90 days | Tue 16/03/27 | Wed 30/06/27 |
| 619 | 1968 | Reinstatement of the affected surrounding | 75 days | Thu 06/05/27 | Sat 31/07/27 |
| 620 | **1773** | **Public Contribution (External works)** | **150 days** | **Wed 07/07/27** | **Fri 31/12/27** |
| 621 | 897 | Road Improvement - Road Expunction at Merchant Road | 150 days | Wed 07/07/27 | Fri 31/12/27 |
| 622 | 899 | Pedestrianization at Solomon and Merchant road | 77 days | Fri 01/10/27 | Fri 31/12/27 |
| 623 | **1984** | **Inspection** | **797 days** | **Sat 28/06/25** | **Sat 12/02/28** |
| 624 | 1978 | SSPG Services/Power Grid | 90 days | Wed 18/08/27 | Wed 01/12/27 |
| 625 | 1979 | NEA - TOP Clearance | 90 days | Fri 03/09/27 | Fri 17/12/27 |
| 626 | 1980 | PBU - Sanitary Department | 75 days | Fri 03/09/27 | Tue 30/11/27 |
| 627 | 1993 | LTA -Road | 40 days | Fri 10/12/27 | Sat 29/01/28 |
| 628 | **1981** | **GM Assessment** | **797 days** | **Sat 28/06/25** | **Sat 12/02/28** |
| 629 | 1982 | USR Green Mark Documents & Pre-Assessment | 685 days | Sat 28/06/25 | Wed 29/09/27 |
| 630 | 1983 | USR Green Mark Assessment & Verification | 112 days | Thu 30/09/27 | Sat 12/02/28 |
| 631 | **503** | **Temporary Occupation Permit (TOP)** | **1061 days** | **Mon 26/08/24** | **Fri 25/02/28** |
| 632 | 504 | M&E Final Testing & Commissioning | 42 days | Tue 31/08/27 | Mon 18/10/27 |
| 633 | 505 | Pre M&E RI Inspection | 14 days | Tue 19/10/27 | Thu 04/11/27 |
| 634 | 506 | M&E RI Inspection | 2 days | Fri 05/11/27 | Sat 06/11/27 |
| 635 | 507 | M&E Rectification works | 12 days | Mon 08/11/27 | Sat 20/11/27 |
| 636 | 508 | M&E RI Final Inspection | 2 days | Mon 22/11/27 | Tue 23/11/27 |
| 637 | 509 | Pre Architectural RI Inspection | 2 days | Wed 03/11/27 | Thu 04/11/27 |
| 638 | 510 | Architectural RI Inspection | 14 days | Fri 05/11/27 | Sat 20/11/27 |
| 639 | 511 | Architectural Rectification Works | 12 days | Mon 22/11/27 | Sat 04/12/27 |
| 640 | 512 | Architectural RI Final Inspection | 2 days | Mon 06/12/27 | Tue 07/12/27 |
| 641 | 513 | CPBU Clearance (Including form C ) | 0 days | Thu 25/11/27 | Thu 25/11/27 |
| 642 | 514 | RI Issue Form 2 | 3 days | Mon 26/08/24 | Wed 28/08/24 |
| 643 | 515 | Consultant Internal Pre-TOP Inspection | 14 days | Mon 22/11/27 | Tue 07/12/27 |
| 644 | 516 | BCA TOP 1st Inspection | 1 day | Wed 08/12/27 | Wed 08/12/27 |
| 645 | 517 | TOP Rectification Works | 33 days | Thu 09/12/27 | Tue 18/01/28 |
| 646 | 518 | BCA TOP 2nd Inspection | 1 day | Wed 19/01/28 | Wed 19/01/28 |
| 647 | 519 | TOP Rectification Works | 15 days | Thu 20/01/28 | Tue 08/02/28 |
| 648 | 520 | Green Mark Verification | 7 days | Mon 14/02/28 | Mon 21/02/28 |
| 649 | 521 | TOP Lodgement | 14 days | Wed 09/02/28 | Thu 24/02/28 |
| 650 | 522 | TOP Obtained / Completion Date | 1 day | Fri 25/02/28 | Fri 25/02/28 |
| 651 | **1790** | **Phase 2: Construction** | **1185 days** | **Mon 26/08/24** | **Tue 25/07/28** |
| 652 | **131** | **USR** | **1115 days** | **Mon 26/08/24** | **Tue 02/05/28** |
| 653 | 132 | Mob-in USR | 24 days | Mon 26/08/24 | Sat 21/09/24 |
| 654 | **523** | **Temporary Works/Hacking** | **315 days** | **Mon 23/09/24** | **Tue 07/10/25** |
| 655 | 133 | Rake Strut + L1 & B1 Demolition | 38 days | Mon 23/09/24 | Wed 06/11/24 |
| 656 | 203 | L1 Curing + Removal of raker strut - Building Footprint | 25 days | Tue 26/08/25 | Tue 23/09/25 |
| 657 | 192 | L1 Curing + Removal of raker strut - Outside Building Footprint | 37 days | Tue 26/08/25 | Tue 07/10/25 |
| 658 | **525** | **Piling** | **165 days** | **Thu 07/11/24** | **Tue 27/05/25** |
| 659 | 134 | ULT | 40 days | Thu 07/11/24 | Mon 23/12/24 |
| 660 | 135 | Piling/KP | 125 days | Tue 24/12/24 | Tue 27/05/25 |
| 661 | **528** | **Substructure** | **265 days** | **Wed 24/09/25** | **Tue 11/08/26** |
| 662 | **530** | **Building Footprints** | **265 days** | **Wed 24/09/25** | **Tue 11/08/26** |
| 663 | 202 | Pile Cap | 63 days | Wed 24/09/25 | Sat 06/12/25 |
| 664 | 201 | B2 | 65 days | Mon 08/12/25 | Wed 25/02/26 |
| 665 | 200 | Vertical Elements to B1 | 50 days | Mon 26/01/26 | Fri 27/03/26 |
| 666 | 199 | B1 | 75 days | Thu 12/03/26 | Fri 12/06/26 |
| 667 | 204 | Vertical Elements to L1 | 50 days | Sat 13/06/26 | Tue 11/08/26 |
| 668 | **531** | **Outside Building Footprints** | **227 days** | **Wed 08/10/25** | **Fri 10/07/26** |
| 669 | 205 | Pilecap | 53 days | Wed 08/10/25 | Tue 09/12/25 |
| 670 | 193 | B2 | 50 days | Wed 10/12/25 | Sat 07/02/26 |
| 671 | 206 | Vertical Elements to B1 | 52 days | Sat 10/01/26 | Fri 13/03/26 |
| 672 | 194 | B1 | 75 days | Fri 27/02/26 | Fri 29/05/26 |
| 673 | 207 | Vertical Elements to L1 | 50 days | Tue 12/05/26 | Fri 10/07/26 |
| 674 | **529** | **Superstructure** | **737 days** | **Wed 28/05/25** | **Sat 30/10/27** |
| 675 | **532** | **Residential Tower (PPVC, Cast-in-Situ Structure)** | **737 days** | **Wed 28/05/25** | **Sat 30/10/27** |
| 676 | 137 | L1 | 75 days | Wed 28/05/25 | Mon 25/08/25 |
| 677 | 138 | L2 | 35 days | Tue 26/08/25 | Sat 04/10/25 |
| 678 | 139 | L3 | 60 days | Mon 06/10/25 | Mon 15/12/25 |

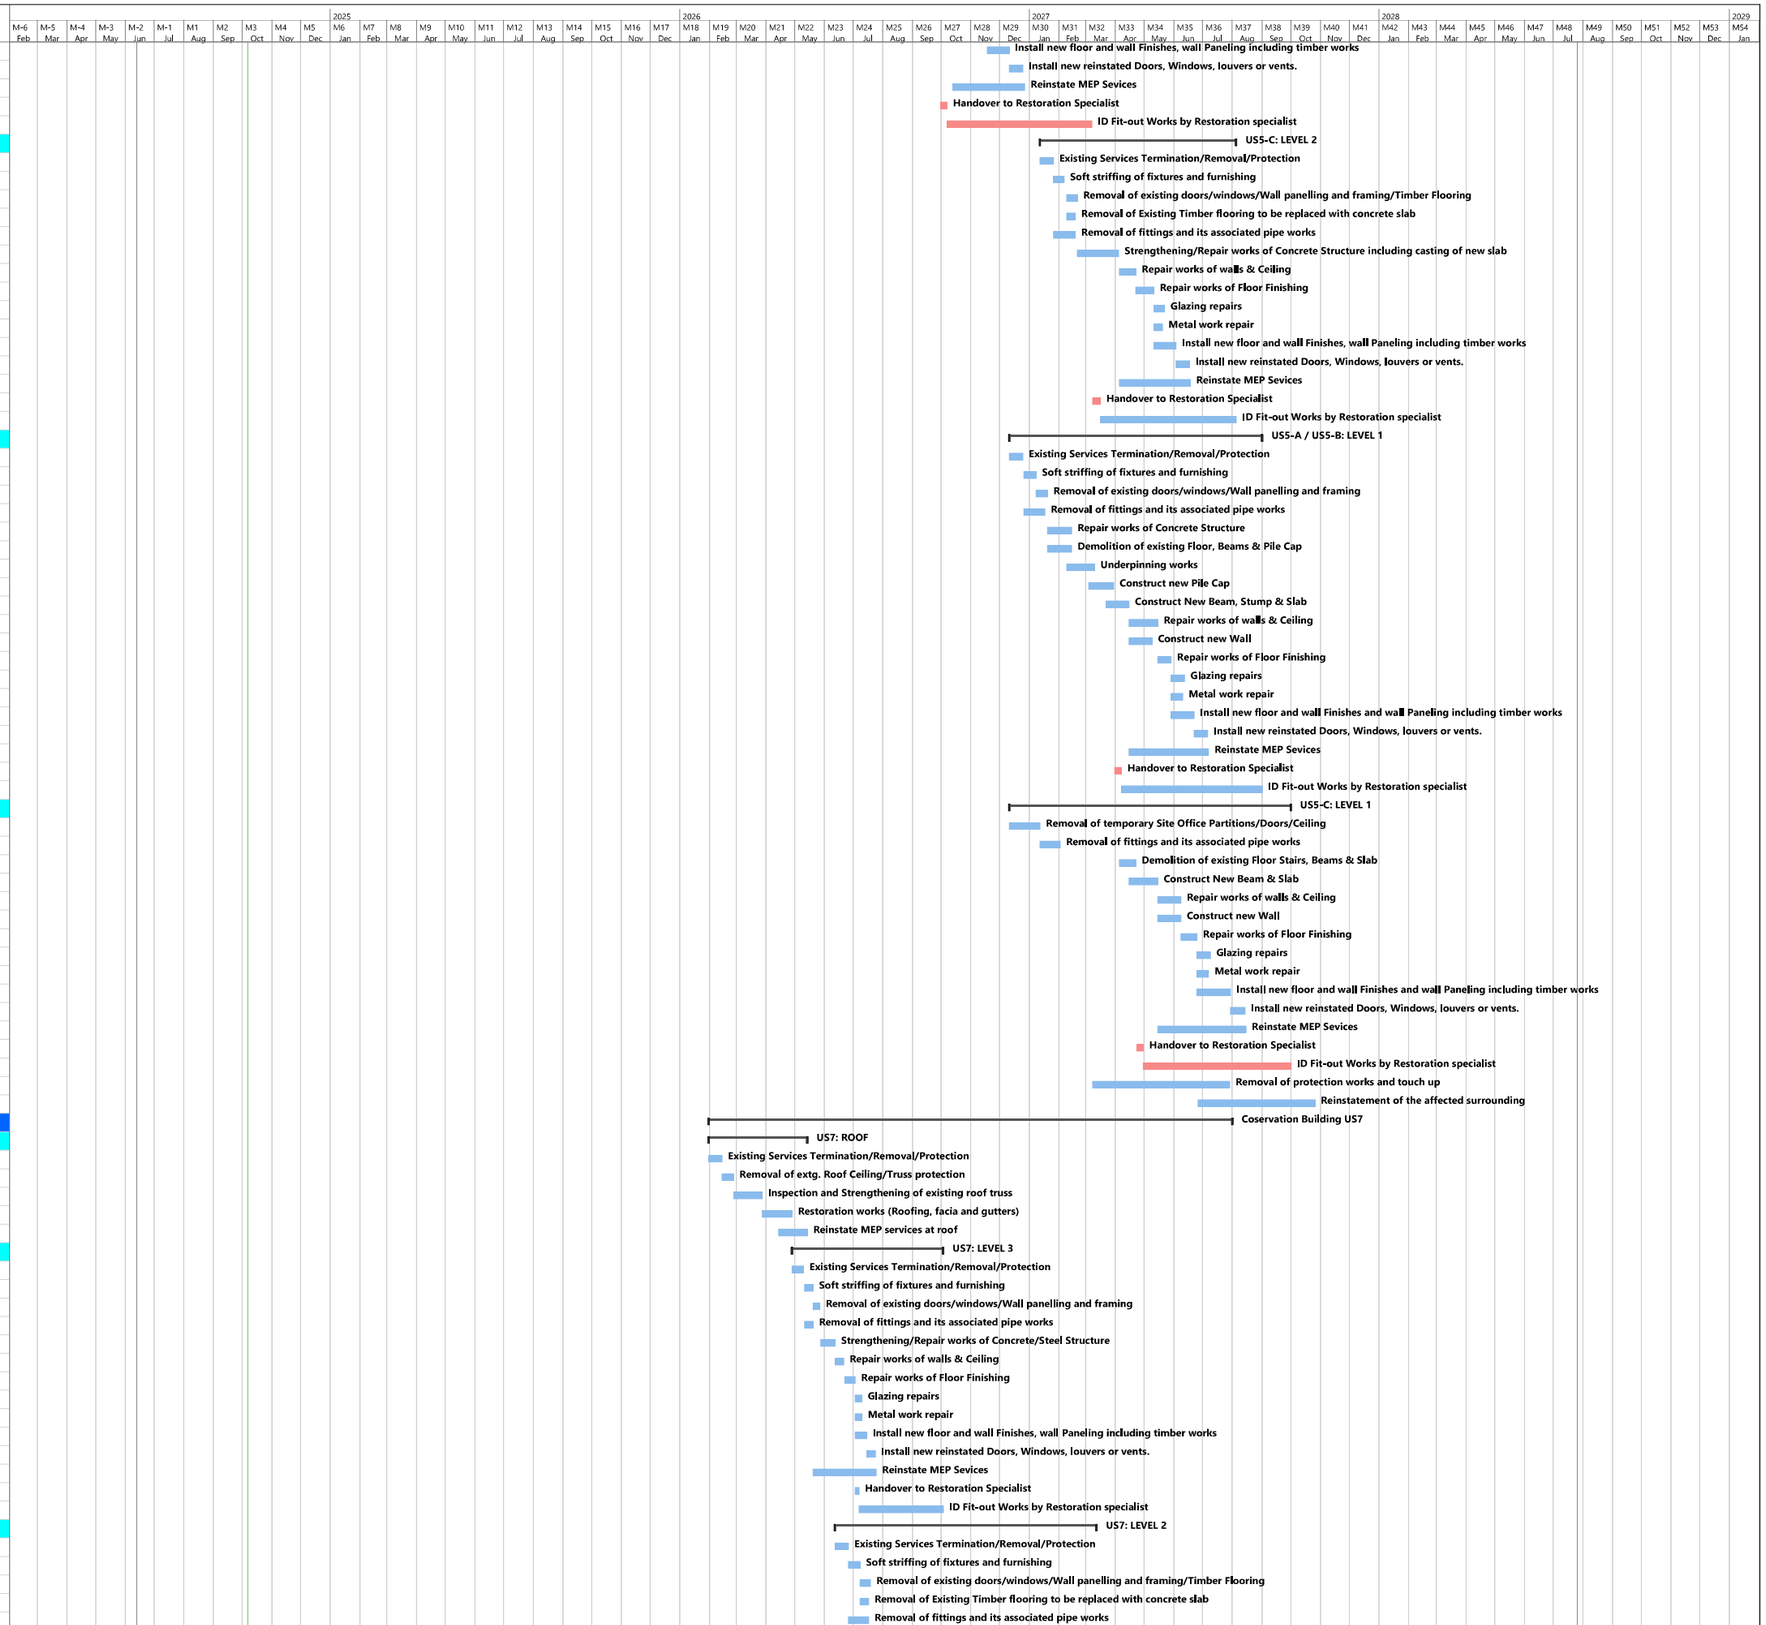


Project: Central Mall - Master P
Date: Mon 07/10/24

Task | Milestone | Project Summary | Inactive Milestone | Manual Task | Manual Summary Rollup | Start-only | External Tasks | Deadline | Critical Split | Manual Progress
Split | Summary | Inactive Task | Inactive Summary | Duration-only | Manual Summary | Finish-only | External Milestone | Critical | Progress

| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 679 | 140 | L4 | 25 days | Tue 16/12/25 | Thu 15/01/26 |
| 680 | 141 | L5 | 13 days | Fri 16/01/26 | Fri 30/01/26 |
| 681 | 142 | L6 | 13 days | Sat 31/01/26 | Sat 14/02/26 |
| 682 | 143 | L7 | 13 days | Mon 16/02/26 | Wed 04/03/26 |
| 683 | 144 | L8 | 13 days | Thu 05/03/26 | Thu 19/03/26 |
| 684 | 145 | L9 | 18 days | Sat 21/03/26 | Sat 11/04/26 |
| 685 | 146 | L10 | 13 days | Mon 13/04/26 | Mon 27/04/26 |
| 686 | 147 | L11 | 13 days | Tue 28/04/26 | Wed 13/05/26 |
| 687 | 148 | L12 | 13 days | Thu 14/05/26 | Fri 29/05/26 |
| 688 | 149 | L13 | 18 days | Sat 30/05/26 | Sat 20/06/26 |
| 689 | 150 | L14 | 13 days | Mon 22/06/26 | Mon 06/07/26 |
| 690 | 151 | L15 | 13 days | Tue 07/07/26 | Tue 21/07/26 |
| 691 | 152 | L16 | 13 days | Wed 22/07/26 | Wed 05/08/26 |
| 692 | 153 | L17 | 13 days | Thu 06/08/26 | Fri 21/08/26 |
| 693 | 154 | L18 | 18 days | Sat 22/08/26 | Fri 11/09/26 |
| 694 | 155 | L19 | 13 days | Sat 12/09/26 | Sat 26/09/26 |
| 695 | 156 | L20 | 13 days | Mon 28/09/26 | Mon 12/10/26 |
| 696 | 157 | L21 | 13 days | Tue 13/10/26 | Tue 27/10/26 |
| 697 | 158 | L22 | 13 days | Wed 28/10/26 | Thu 12/11/26 |
| 698 | 159 | L23 | 18 days | Fri 13/11/26 | Thu 03/12/26 |
| 699 | 160 | L24 | 13 days | Fri 04/12/26 | Fri 18/12/26 |
| 700 | 161 | L25 | 13 days | Sat 19/12/26 | Tue 05/01/27 |
| 701 | 162 | L26 | 13 days | Wed 06/01/27 | Wed 20/01/27 |
| 702 | 163 | L27 | 18 days | Thu 21/01/27 | Fri 12/02/27 |
| 703 | 164 | L28 | 13 days | Sat 13/02/27 | Sat 27/02/27 |
| 704 | 165 | L29 | 13 days | Mon 01/03/27 | Tue 16/03/27 |
| 705 | 166 | L30 | 13 days | Wed 17/03/27 | Thu 01/04/27 |
| 706 | 167 | L31 | 13 days | Fri 02/04/27 | Fri 16/04/27 |
| 707 | 168 | L32 | 13 days | Sat 17/04/27 | Mon 03/05/27 |
| 708 | 169 | L33 | 18 days | Tue 04/05/27 | Mon 24/05/27 |
| 709 | 170 | L34 | 25 days | Tue 25/05/27 | Tue 22/06/27 |
| 710 | 171 | L35 | 12 days | Mon 14/06/27 | Sat 26/06/27 |
| 711 | 172 | L36 | 12 days | Mon 28/06/27 | Sat 10/07/27 |
| 712 | 173 | L37 | 12 days | Mon 12/07/27 | Sat 24/07/27 |
| 713 | 174 | L38 | 12 days | Mon 26/07/27 | Sat 07/08/27 |
| 714 | 175 | L39 | 15 days | Tue 10/08/27 | Thu 26/08/27 |
| 715 | 176 | L40 | 15 days | Fri 27/08/27 | Mon 13/09/27 |
| 716 | 177 | LRF | 20 days | Tue 14/09/27 | Wed 06/10/27 |
| 717 | 208 | URF | 20 days | Thu 07/10/27 | Sat 30/10/27 |
| 718 | **533** | **Outside Residential Tower** | **453 days** | **Wed 28/05/25** | **Mon 23/11/26** |
| 719 | 191 | New L1 | 75 days | Wed 28/05/25 | Mon 25/08/25 |
| 720 | 195 | L1 | 50 days | Sat 11/07/26 | Tue 08/09/26 |
| 721 | 196 | L2 | 40 days | Tue 25/08/26 | Fri 09/10/26 |
| 722 | 197 | L3 | 50 days | Fri 25/09/26 | Mon 23/11/26 |
| 723 | **217** | **Finishing & MEP Works** | **606 days** | **Thu 05/03/26** | **Sat 04/03/28** |
| 724 | **577** | **Basement Finishing** | **315 days** | **Sat 11/07/26** | **Fri 23/07/27** |
| 725 | **580** | **Basement 2** | **255 days** | **Sat 11/07/26** | **Fri 14/05/27** |
| 726 | 578 | Cable Chamber Room/Transformer | 60 days | Sat 11/07/26 | Sat 19/09/26 |
| 727 | 581 | Consumer LV Switch Room (Retail) | 60 days | Tue 04/08/26 | Tue 13/10/26 |
| 728 | 582 | Tanks & Pump Rooms | 40 days | Wed 14/10/26 | Mon 30/11/26 |
| 729 | 583 | Bin Centre | 40 days | Tue 01/12/26 | Mon 18/01/27 |
| 730 | 579 | Carp Park Lots | 70 days | Tue 19/01/27 | Wed 14/04/27 |
| 731 | 590 | Ramp & Driveways | 25 days | Thu 15/04/27 | Fri 14/05/27 |
| 732 | **585** | **Basement 1** | **235 days** | **Wed 14/10/26** | **Fri 23/07/27** |
| 733 | 588 | MDF Rom | 50 days | Wed 14/10/26 | Fri 11/12/26 |
| 734 | 589 | Carp Park Lots | 60 days | Thu 15/04/27 | Thu 24/06/27 |
| 735 | 587 | Ramp & Driveways | 25 days | Fri 25/06/27 | Fri 23/07/27 |
| 736 | **925** | **Level 1 - Level 3 (Podium)** | **470 days** | **Tue 28/04/26** | **Fri 12/11/27** |
| 737 | **535** | **Level 1 Finishing** | **240 days** | **Tue 28/04/26** | **Thu 11/02/27** |
| 738 | 591 | SPK & Hydrant | 40 days | Tue 01/12/26 | Mon 18/01/27 |
| 739 | 592 | Shops | 90 days | Tue 28/04/26 | Fri 14/08/26 |
| 740 | 593 | Restaurant | 90 days | Sat 15/08/26 | Sat 28/11/26 |
| 741 | 594 | Toilets | 60 days | Mon 30/11/26 | Thu 11/02/27 |
| 742 | **536** | **Level 2 Finishing** | **220 days** | **Sat 15/08/26** | **Fri 07/05/27** |
| 743 | 598 | Genset | 40 days | Tue 01/12/26 | Mon 18/01/27 |
| 744 | 597 | Tanks | 40 days | Tue 19/01/27 | Mon 08/03/27 |
| 745 | 596 | Toilets | 70 days | Fri 12/02/27 | Fri 07/05/27 |
| 746 | 595 | Shops | 90 days | Sat 15/08/26 | Sat 28/11/26 |
| 747 | 599 | Restaurants | 90 days | Mon 30/11/26 | Fri 19/03/27 |
| 748 | 537 | Level 3 Finishes | 200 days | Sat 20/03/27 | Fri 12/11/27 |
| 749 | **600** | **Residential Floors** | **606 days** | **Thu 05/03/26** | **Sat 04/03/28** |
| 750 | **924** | **Level 3** | **75 days** | **Tue 10/08/27** | **Fri 05/11/27** |
| 751 | 926 | Structural clearance | 5 days | Tue 10/08/27 | Sat 14/08/27 |
| 752 | 927 | RC Kerb | 5 days | Mon 16/08/27 | Fri 20/08/27 |
| 753 | 928 | PC Panel/Drywall | 5 days | Sat 21/08/27 | Thu 26/08/27 |
| 754 | 929 | MEP 1st fix | 9 days | Tue 24/08/27 | Thu 02/09/27 |
| 755 | 930 | Waterproofing | 4 days | Mon 30/08/27 | Thu 02/09/27 |
| 756 | 931 | Window frame | 2 days | Fri 03/09/27 | Sat 04/09/27 |
| 757 | 932 | Door sub-frame installation | 2 days | Fri 03/09/27 | Sat 04/09/27 |
| 758 | 933 | Floor screeding | 5 days | Mon 06/09/27 | Fri 10/09/27 |
| 759 | 934 | Plaster and skim coat | 7 days | Thu 09/09/27 | Thu 16/09/27 |
| 760 | 935 | Railing installation | 3 days | Fri 17/09/27 | Mon 20/09/27 |
| 761 | 936 | Tiling | 7 days | Fri 17/09/27 | Fri 24/09/27 |
| 762 | 937 | Shower screen L angle | 1 day | Fri 17/09/27 | Fri 17/09/27 |
| 763 | 938 | Ceiling frame and board | 7 days | Sat 25/09/27 | Sat 02/10/27 |
| 764 | 939 | Wardrobe | 5 days | Mon 04/10/27 | Fri 08/10/27 |

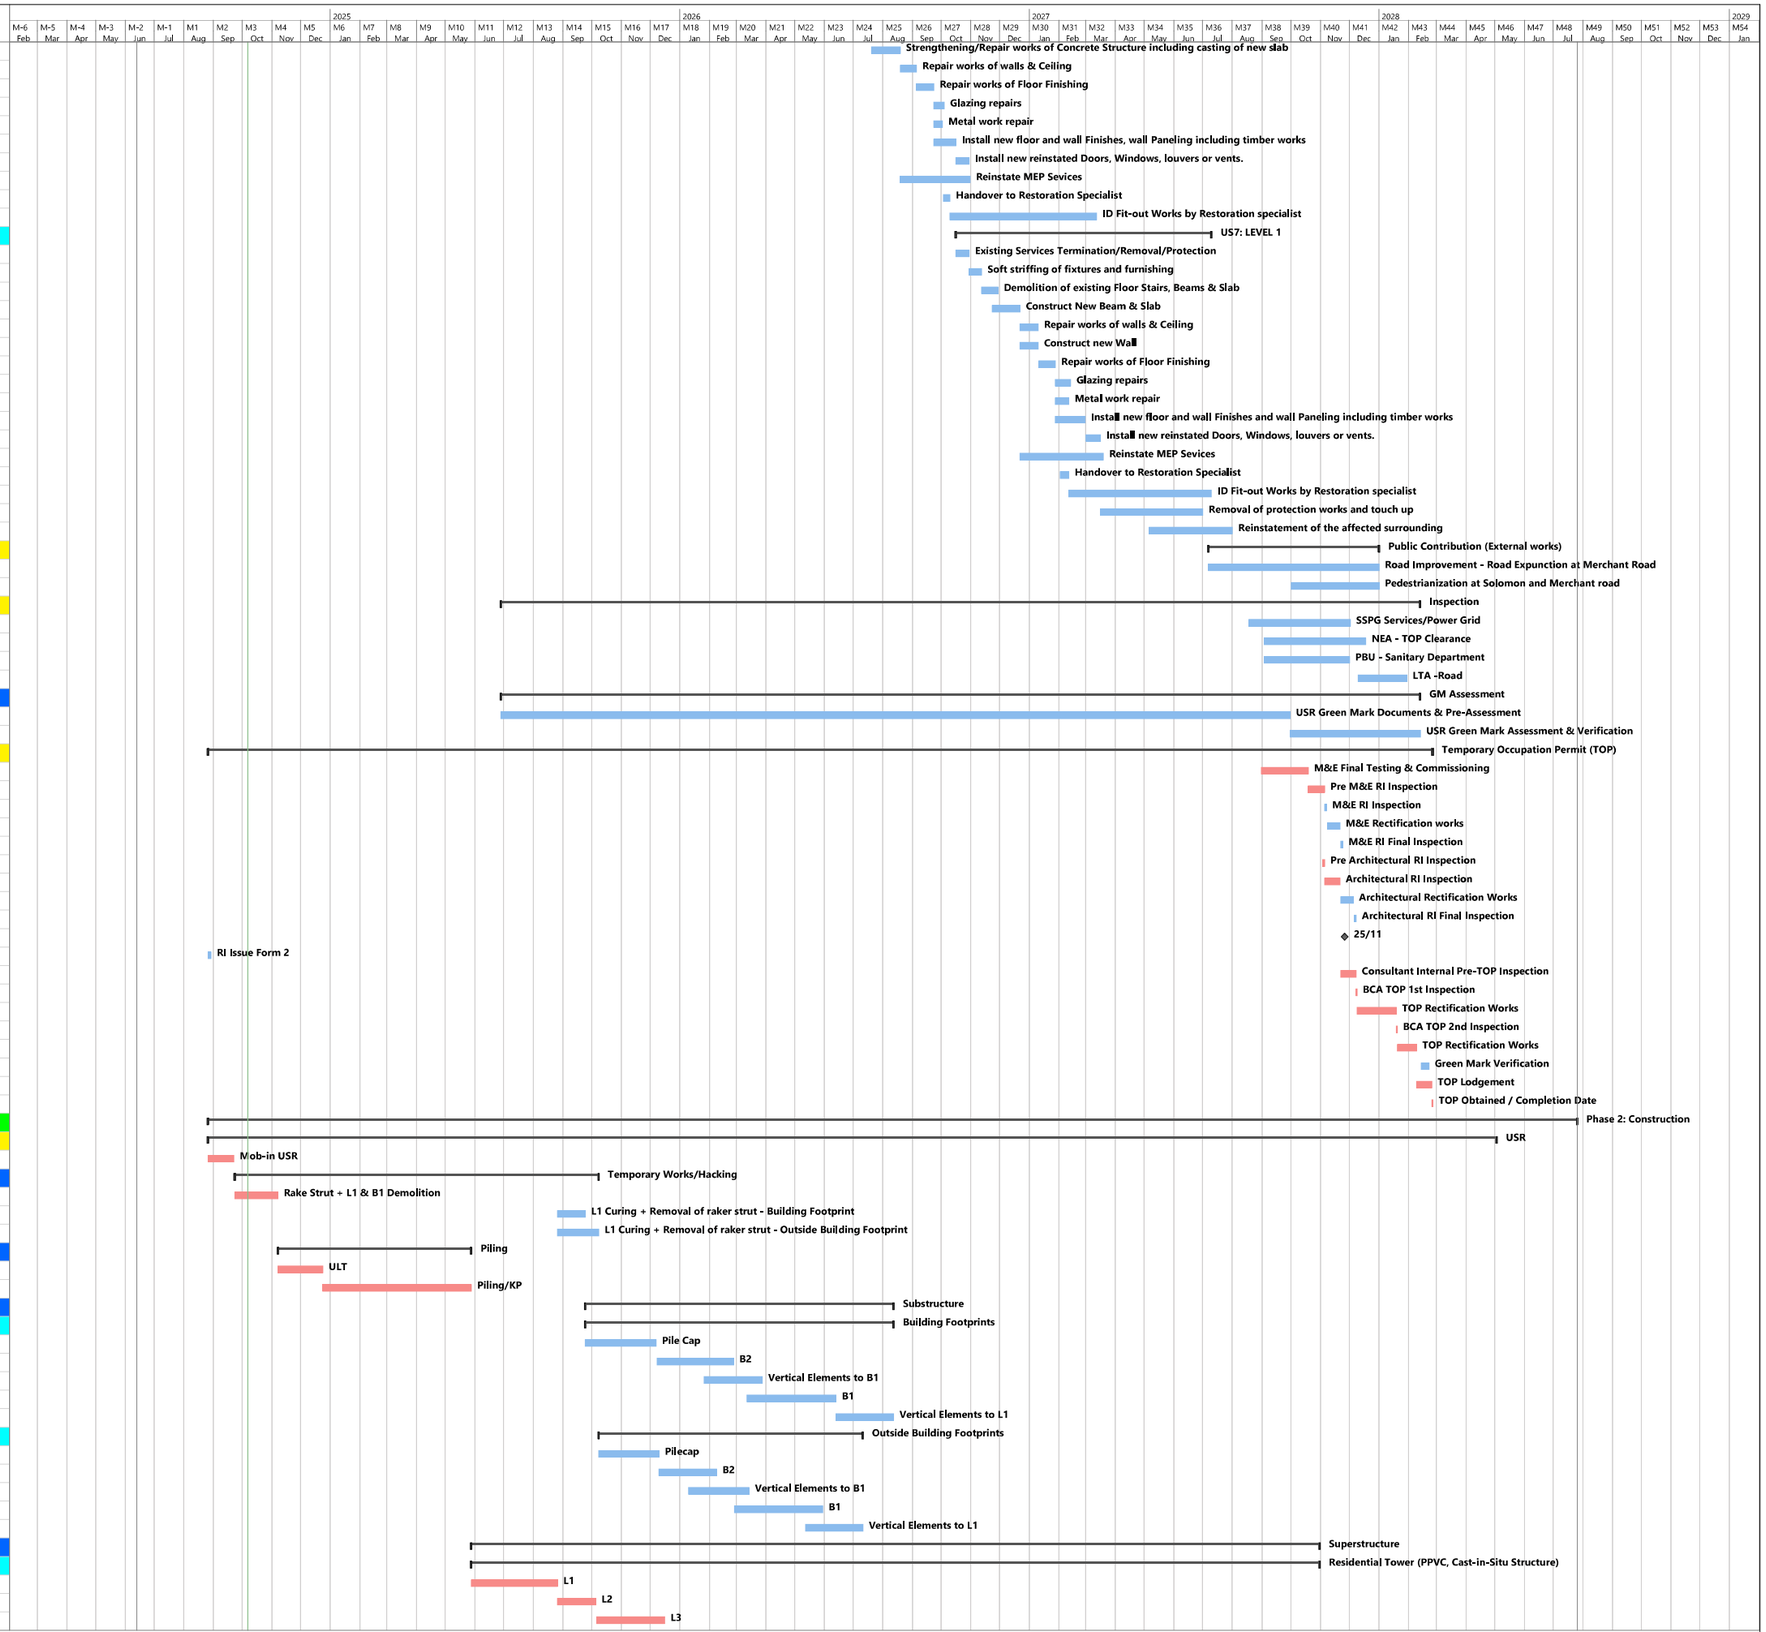


Project: Central Mall - Master P
Date: Mon 07/10/24

Task · Split · Milestone · Summary · Project Summary · Inactive Task · Inactive Milestone · Inactive Summary · Manual Task · Duration-only · Manual Summary Rollup · Manual Summary · Start-only · Finish-only · External Tasks · External Milestone · Deadline · Critical · Critical Split · Progress · Manual Progress

| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 765 | 940 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Mon 04/10/27 | Fri 08/10/27 |
| 766 | 941 | Engineered Timber Flooring | 5 days | Wed 06/10/27 | Mon 11/10/27 |
| 767 | 942 | Painting (sealer) | 6 days | Tue 12/10/27 | Mon 18/10/27 |
| 768 | 943 | Shower screen installation | 4 days | Tue 19/10/27 | Fri 22/10/27 |
| 769 | 944 | Door frame and leaf installation | 5 days | Tue 19/10/27 | Sat 23/10/27 |
| 770 | 945 | Kitchen appliance | 6 days | Mon 25/10/27 | Mon 01/11/27 |
| 771 | 946 | M&E final fix | 4 days | Tue 02/11/27 | Fri 05/11/27 |
| 772 | **538** | **Level 4** | **70 days** | **Thu 05/03/26** | **Fri 29/05/26** |
| 773 | 947 | Structural clearance | 5 days | Thu 05/03/26 | Tue 10/03/26 |
| 774 | 948 | RC Kerb | 5 days | Wed 11/03/26 | Mon 16/03/26 |
| 775 | 949 | PC Panel/Drywall | 5 days | Tue 17/03/26 | Mon 23/03/26 |
| 776 | 950 | MEP 1st fix | 9 days | Thu 19/03/26 | Mon 30/03/26 |
| 777 | 951 | Waterproofing | 4 days | Thu 26/03/26 | Mon 30/03/26 |
| 778 | 952 | Window frame | 2 days | Tue 31/03/26 | Wed 01/04/26 |
| 779 | 953 | Door sub-frame installation | 2 days | Tue 31/03/26 | Wed 01/04/26 |
| 780 | 954 | Floor screeding | 5 days | Thu 02/04/26 | Wed 08/04/26 |
| 781 | 955 | Plaster and skim coat | 7 days | Tue 07/04/26 | Tue 14/04/26 |
| 782 | 956 | Railing installation | 3 days | Wed 15/04/26 | Fri 17/04/26 |
| 783 | 957 | Tiling | 7 days | Wed 15/04/26 | Wed 22/04/26 |
| 784 | 958 | Shower screen L angle | 1 day | Wed 15/04/26 | Wed 15/04/26 |
| 785 | 959 | Ceiling frame and board | 7 days | Thu 23/04/26 | Thu 30/04/26 |
| 786 | 960 | Wardrobe | 5 days | Sat 02/05/26 | Thu 07/05/26 |
| 787 | 961 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Sat 02/05/26 | Thu 07/05/26 |
| 788 | 962 | Engineered Timber Flooring | 5 days | Mon 04/05/26 | Fri 08/05/26 |
| 789 | 963 | Painting (sealer) | 5 days | Sat 09/05/26 | Thu 14/05/26 |
| 790 | 964 | Shower screen installation | 4 days | Fri 15/05/26 | Tue 19/05/26 |
| 791 | 965 | Door frame and leaf installation | 4 days | Fri 15/05/26 | Tue 19/05/26 |
| 792 | 966 | Kitchen appliance | 4 days | Wed 20/05/26 | Sat 23/05/26 |
| 793 | 967 | M&E final fix | 4 days | Mon 25/05/26 | Fri 29/05/26 |
| 794 | **539** | **Level 5** | **70 days** | **Mon 23/03/26** | **Tue 16/06/26** |
| 795 | 968 | Structural clearance | 5 days | Mon 23/03/26 | Fri 27/03/26 |
| 796 | 969 | RC Kerb | 5 days | Sat 28/03/26 | Thu 02/04/26 |
| 797 | 970 | PC Panel/Drywall | 5 days | Sat 04/04/26 | Thu 09/04/26 |
| 798 | 971 | MEP 1st fix | 9 days | Tue 07/04/26 | Thu 16/04/26 |
| 799 | 972 | Waterproofing | 4 days | Mon 13/04/26 | Thu 16/04/26 |
| 800 | 973 | Window frame | 2 days | Fri 17/04/26 | Sat 18/04/26 |
| 801 | 974 | Door sub-frame installation | 2 days | Fri 17/04/26 | Sat 18/04/26 |
| 802 | 975 | Floor screeding | 5 days | Mon 20/04/26 | Fri 24/04/26 |
| 803 | 976 | Plaster and skim coat | 7 days | Thu 23/04/26 | Thu 30/04/26 |
| 804 | 977 | Railing installation | 3 days | Sat 02/05/26 | Tue 05/05/26 |
| 805 | 978 | Tiling | 7 days | Sat 02/05/26 | Sat 09/05/26 |
| 806 | 979 | Shower screen L angle | 1 day | Sat 02/05/26 | Sat 02/05/26 |
| 807 | 980 | Ceiling frame and board | 7 days | Mon 11/05/26 | Mon 18/05/26 |
| 808 | 981 | Wardrobe | 5 days | Tue 19/05/26 | Sat 23/05/26 |
| 809 | 982 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Tue 19/05/26 | Sat 23/05/26 |
| 810 | 983 | Engineered Timber Flooring | 5 days | Wed 20/05/26 | Mon 25/05/26 |
| 811 | 984 | Painting (sealer) | 5 days | Tue 26/05/26 | Tue 02/06/26 |
| 812 | 985 | Shower screen installation | 4 days | Wed 03/06/26 | Sat 06/06/26 |
| 813 | 986 | Door frame and leaf installation | 4 days | Wed 03/06/26 | Sat 06/06/26 |
| 814 | 987 | Kitchen appliance | 4 days | Mon 08/06/26 | Thu 11/06/26 |
| 815 | 988 | M&E final fix | 4 days | Fri 12/06/26 | Tue 16/06/26 |
| 816 | **540** | **Level 6** | **70 days** | **Thu 09/04/26** | **Thu 02/07/26** |
| 817 | 989 | Structural clearance | 5 days | Thu 09/04/26 | Tue 14/04/26 |
| 818 | 990 | RC Kerb | 5 days | Wed 15/04/26 | Mon 20/04/26 |
| 819 | 991 | PC Panel/Drywall | 5 days | Tue 21/04/26 | Sat 25/04/26 |
| 820 | 992 | MEP 1st fix | 9 days | Thu 23/04/26 | Mon 04/05/26 |
| 821 | 993 | Waterproofing | 4 days | Wed 29/04/26 | Mon 04/05/26 |
| 822 | 994 | Window frame | 2 days | Tue 05/05/26 | Wed 06/05/26 |
| 823 | 995 | Door sub-frame installation | 2 days | Tue 05/05/26 | Wed 06/05/26 |
| 824 | 996 | Floor screeding | 5 days | Thu 07/05/26 | Tue 12/05/26 |
| 825 | 997 | Plaster and skim coat | 7 days | Mon 11/05/26 | Mon 18/05/26 |
| 826 | 998 | Railing installation | 3 days | Tue 19/05/26 | Thu 21/05/26 |
| 827 | 999 | Tiling | 7 days | Tue 19/05/26 | Tue 26/05/26 |
| 828 | 1000 | Shower screen L angle | 1 day | Tue 19/05/26 | Tue 19/05/26 |
| 829 | 1001 | Ceiling frame and board | 7 days | Thu 28/05/26 | Fri 05/06/26 |
| 830 | 1002 | Wardrobe | 5 days | Sat 06/06/26 | Thu 11/06/26 |
| 831 | 1003 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Sat 06/06/26 | Thu 11/06/26 |
| 832 | 1004 | Engineered Timber Flooring | 5 days | Mon 08/06/26 | Fri 12/06/26 |
| 833 | 1005 | Painting (sealer) | 5 days | Sat 13/06/26 | Thu 18/06/26 |
| 834 | 1006 | Shower screen installation | 4 days | Fri 19/06/26 | Tue 23/06/26 |
| 835 | 1007 | Door frame and leaf installation | 4 days | Fri 19/06/26 | Tue 23/06/26 |
| 836 | 1008 | Kitchen appliance | 4 days | Wed 24/06/26 | Sat 27/06/26 |
| 837 | 1009 | M&E final fix | 4 days | Mon 29/06/26 | Thu 02/07/26 |
| 838 | **541** | **Level 7** | **70 days** | **Sat 25/04/26** | **Sat 18/07/26** |
| 839 | 1010 | Structural clearance | 5 days | Sat 25/04/26 | Thu 30/04/26 |
| 840 | 1011 | RC Kerb | 5 days | Sat 02/05/26 | Thu 07/05/26 |
| 841 | 1012 | PC Panel/Drywall | 5 days | Fri 08/05/26 | Wed 13/05/26 |
| 842 | 1013 | MEP 1st fix | 9 days | Mon 11/05/26 | Wed 20/05/26 |
| 843 | 1014 | Waterproofing | 4 days | Sat 16/05/26 | Wed 20/05/26 |
| 844 | 1015 | Window frame | 2 days | Thu 21/05/26 | Fri 22/05/26 |
| 845 | 1016 | Door sub-frame installation | 2 days | Thu 21/05/26 | Fri 22/05/26 |
| 846 | 1017 | Floor screeding | 5 days | Sat 23/05/26 | Fri 29/05/26 |
| 847 | 1018 | Plaster and skim coat | 7 days | Thu 28/05/26 | Fri 05/06/26 |
| 848 | 1019 | Railing installation | 3 days | Sat 06/06/26 | Tue 09/06/26 |
| 849 | 1020 | Tiling | 7 days | Sat 06/06/26 | Sat 13/06/26 |
| 850 | 1021 | Shower screen L angle | 1 day | Sat 06/06/26 | Sat 06/06/26 |

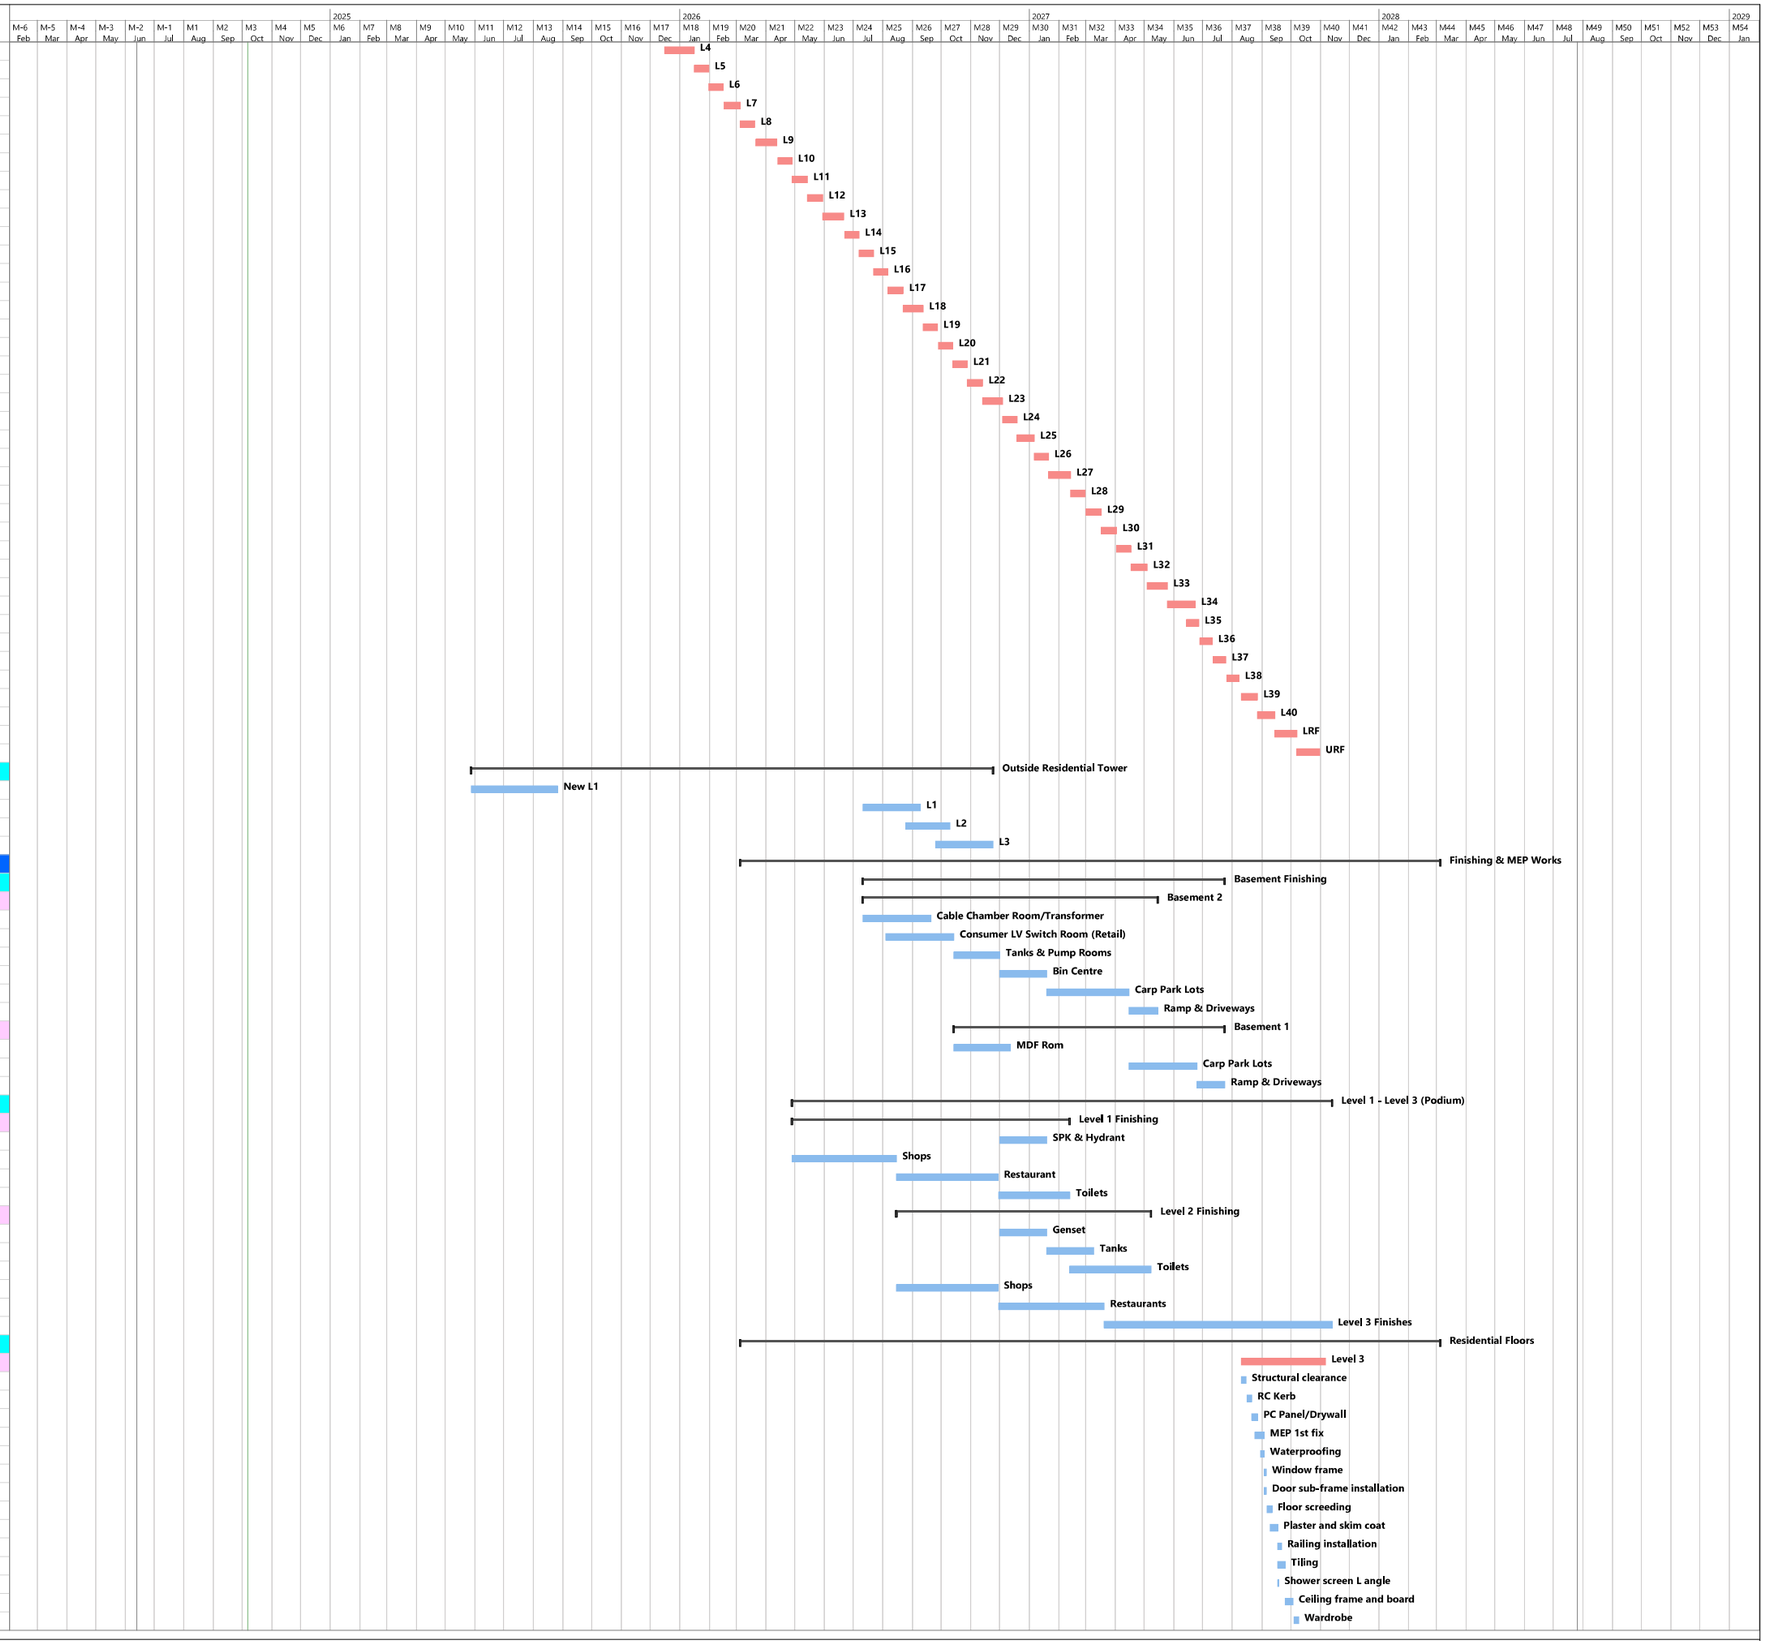


Project: Central Mall - Master P
Date: Mon 07/10/24

Task · Split · Milestone · Summary · Project Summary · Inactive Task · Inactive Milestone · Inactive Summary · Manual Task · Duration-only · Manual Summary Rollup · Manual Summary · Start-only · Finish-only · External Tasks · External Milestone · Deadline · Critical · Critical Split · Progress · Manual Progress

| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 851 | 1022 | Ceiling frame and board | 7 days | Mon 15/06/26 | Mon 22/06/26 |
| 852 | 1023 | Wardrobe | 5 days | Tue 23/06/26 | Sat 27/06/26 |
| 853 | 1024 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Tue 23/06/26 | Sat 27/06/26 |
| 854 | 1025 | Engineered Timber Flooring | 5 days | Wed 24/06/26 | Mon 29/06/26 |
| 855 | 1026 | Painting (sealer) | 5 days | Tue 30/06/26 | Sat 04/07/26 |
| 856 | 1027 | Shower screen installation | 4 days | Mon 06/07/26 | Thu 09/07/26 |
| 857 | 1028 | Door frame and leaf installation | 4 days | Mon 06/07/26 | Thu 09/07/26 |
| 858 | 1029 | Kitchen appliance | 4 days | Fri 10/07/26 | Tue 14/07/26 |
| 859 | 1030 | M&E final fix | 4 days | Wed 15/07/26 | Sat 18/07/26 |
| 860 | **542** | **Level 8** | **70 days** | **Wed 13/05/26** | **Tue 04/08/26** |
| 861 | 1031 | Structural clearance | 5 days | Wed 13/05/26 | Mon 18/05/26 |
| 862 | 1032 | RC Kerb | 5 days | Tue 19/05/26 | Sat 23/05/26 |
| 863 | 1033 | PC Panel/Drywall | 5 days | Mon 25/05/26 | Sat 30/05/26 |
| 864 | 1034 | MEP 1st fix | 9 days | Thu 28/05/26 | Mon 08/06/26 |
| 865 | 1035 | Waterproofing | 4 days | Thu 04/06/26 | Mon 08/06/26 |
| 866 | 1036 | Window frame | 2 days | Tue 09/06/26 | Wed 10/06/26 |
| 867 | 1037 | Door sub-frame installation | 2 days | Tue 09/06/26 | Wed 10/06/26 |
| 868 | 1038 | Floor screeding | 5 days | Thu 11/06/26 | Tue 16/06/26 |
| 869 | 1039 | Plaster and skim coat | 7 days | Mon 15/06/26 | Mon 22/06/26 |
| 870 | 1040 | Railing installation | 3 days | Tue 23/06/26 | Thu 25/06/26 |
| 871 | 1041 | Tiling | 7 days | Tue 23/06/26 | Tue 30/06/26 |
| 872 | 1042 | Shower screen L angle | 1 day | Tue 23/06/26 | Tue 23/06/26 |
| 873 | 1043 | Ceiling frame and board | 7 days | Wed 01/07/26 | Wed 08/07/26 |
| 874 | 1044 | Wardrobe | 5 days | Thu 09/07/26 | Tue 14/07/26 |
| 875 | 1045 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Thu 09/07/26 | Tue 14/07/26 |
| 876 | 1046 | Engineered Timber Flooring | 5 days | Fri 10/07/26 | Wed 15/07/26 |
| 877 | 1047 | Painting (sealer) | 5 days | Thu 16/07/26 | Tue 21/07/26 |
| 878 | 1048 | Shower screen installation | 4 days | Wed 22/07/26 | Sat 25/07/26 |
| 879 | 1049 | Door frame and leaf installation | 4 days | Wed 22/07/26 | Sat 25/07/26 |
| 880 | 1050 | Kitchen appliance | 4 days | Mon 27/07/26 | Thu 30/07/26 |
| 881 | 1051 | M&E final fix | 4 days | Fri 31/07/26 | Tue 04/08/26 |
| 882 | **543** | **Level 9** | **70 days** | **Sat 30/05/26** | **Fri 21/08/26** |
| 883 | 1052 | Structural clearance | 5 days | Sat 30/05/26 | Fri 05/06/26 |
| 884 | 1053 | RC Kerb | 5 days | Sat 06/06/26 | Thu 11/06/26 |
| 885 | 1054 | PC Panel/Drywall | 5 days | Fri 12/06/26 | Wed 17/06/26 |
| 886 | 1055 | MEP 1st fix | 9 days | Mon 15/06/26 | Wed 24/06/26 |
| 887 | 1056 | Waterproofing | 4 days | Sat 20/06/26 | Wed 24/06/26 |
| 888 | 1057 | Window frame | 2 days | Thu 25/06/26 | Fri 26/06/26 |
| 889 | 1058 | Door sub-frame installation | 2 days | Thu 25/06/26 | Fri 26/06/26 |
| 890 | 1059 | Floor screeding | 5 days | Sat 27/06/26 | Thu 02/07/26 |
| 891 | 1060 | Plaster and skim coat | 7 days | Wed 01/07/26 | Wed 08/07/26 |
| 892 | 1061 | Railing installation | 3 days | Thu 09/07/26 | Sat 11/07/26 |
| 893 | 1062 | Tiling | 7 days | Thu 09/07/26 | Thu 16/07/26 |
| 894 | 1063 | Shower screen L angle | 1 day | Thu 09/07/26 | Thu 09/07/26 |
| 895 | 1064 | Ceiling frame and board | 7 days | Fri 17/07/26 | Fri 24/07/26 |
| 896 | 1065 | Wardrobe | 5 days | Sat 25/07/26 | Thu 30/07/26 |
| 897 | 1066 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Sat 25/07/26 | Thu 30/07/26 |
| 898 | 1067 | Engineered Timber Flooring | 5 days | Mon 27/07/26 | Fri 31/07/26 |
| 899 | 1068 | Painting (sealer) | 5 days | Sat 01/08/26 | Thu 06/08/26 |
| 900 | 1069 | Shower screen installation | 4 days | Fri 07/08/26 | Wed 12/08/26 |
| 901 | 1070 | Door frame and leaf installation | 4 days | Fri 07/08/26 | Wed 12/08/26 |
| 902 | 1071 | Kitchen appliance | 4 days | Thu 13/08/26 | Mon 17/08/26 |
| 903 | 1072 | M&E final fix | 4 days | Tue 18/08/26 | Fri 21/08/26 |
| 904 | **544** | **Level 10** | **70 days** | **Wed 17/06/26** | **Mon 07/09/26** |
| 905 | 1073 | Structural clearance | 5 days | Wed 17/06/26 | Mon 22/06/26 |
| 906 | 1074 | RC Kerb | 5 days | Tue 23/06/26 | Sat 27/06/26 |
| 907 | 1075 | PC Panel/Drywall | 5 days | Mon 29/06/26 | Fri 03/07/26 |
| 908 | 1076 | MEP 1st fix | 9 days | Wed 01/07/26 | Fri 10/07/26 |
| 909 | 1077 | Waterproofing | 4 days | Tue 07/07/26 | Fri 10/07/26 |
| 910 | 1078 | Window frame | 2 days | Sat 11/07/26 | Mon 13/07/26 |
| 911 | 1079 | Door sub-frame installation | 2 days | Sat 11/07/26 | Mon 13/07/26 |
| 912 | 1080 | Floor screeding | 5 days | Tue 14/07/26 | Sat 18/07/26 |
| 913 | 1081 | Plaster and skim coat | 7 days | Fri 17/07/26 | Fri 24/07/26 |
| 914 | 1082 | Railing installation | 3 days | Sat 25/07/26 | Tue 28/07/26 |
| 915 | 1083 | Tiling | 7 days | Sat 25/07/26 | Sat 01/08/26 |
| 916 | 1084 | Shower screen L angle | 1 day | Sat 25/07/26 | Sat 25/07/26 |
| 917 | 1085 | Ceiling frame and board | 7 days | Mon 03/08/26 | Tue 11/08/26 |
| 918 | 1086 | Wardrobe | 5 days | Wed 12/08/26 | Mon 17/08/26 |
| 919 | 1087 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Wed 12/08/26 | Mon 17/08/26 |
| 920 | 1088 | Engineered Timber Flooring | 5 days | Thu 13/08/26 | Tue 18/08/26 |
| 921 | 1089 | Painting (sealer) | 5 days | Wed 19/08/26 | Mon 24/08/26 |
| 922 | 1090 | Shower screen installation | 4 days | Tue 25/08/26 | Fri 28/08/26 |
| 923 | 1091 | Door frame and leaf installation | 4 days | Tue 25/08/26 | Fri 28/08/26 |
| 924 | 1092 | Kitchen appliance | 4 days | Sat 29/08/26 | Wed 02/09/26 |
| 925 | 1093 | M&E final fix | 4 days | Thu 03/09/26 | Mon 07/09/26 |
| 926 | **545** | **Level 11** | **70 days** | **Fri 03/07/26** | **Wed 23/09/26** |
| 927 | 1094 | Structural clearance | 5 days | Fri 03/07/26 | Wed 08/07/26 |
| 928 | 1095 | RC Kerb | 5 days | Thu 09/07/26 | Tue 14/07/26 |
| 929 | 1096 | PC Panel/Drywall | 5 days | Wed 15/07/26 | Mon 20/07/26 |
| 930 | 1097 | MEP 1st fix | 9 days | Fri 17/07/26 | Mon 27/07/26 |
| 931 | 1098 | Waterproofing | 4 days | Thu 23/07/26 | Mon 27/07/26 |
| 932 | 1099 | Window frame | 2 days | Tue 28/07/26 | Wed 29/07/26 |
| 933 | 1100 | Door sub-frame installation | 2 days | Tue 28/07/26 | Wed 29/07/26 |
| 934 | 1101 | Floor screeding | 5 days | Thu 30/07/26 | Tue 04/08/26 |
| 935 | 1102 | Plaster and skim coat | 7 days | Mon 03/08/26 | Tue 11/08/26 |
| 936 | 1103 | Railing installation | 3 days | Wed 12/08/26 | Fri 14/08/26 |

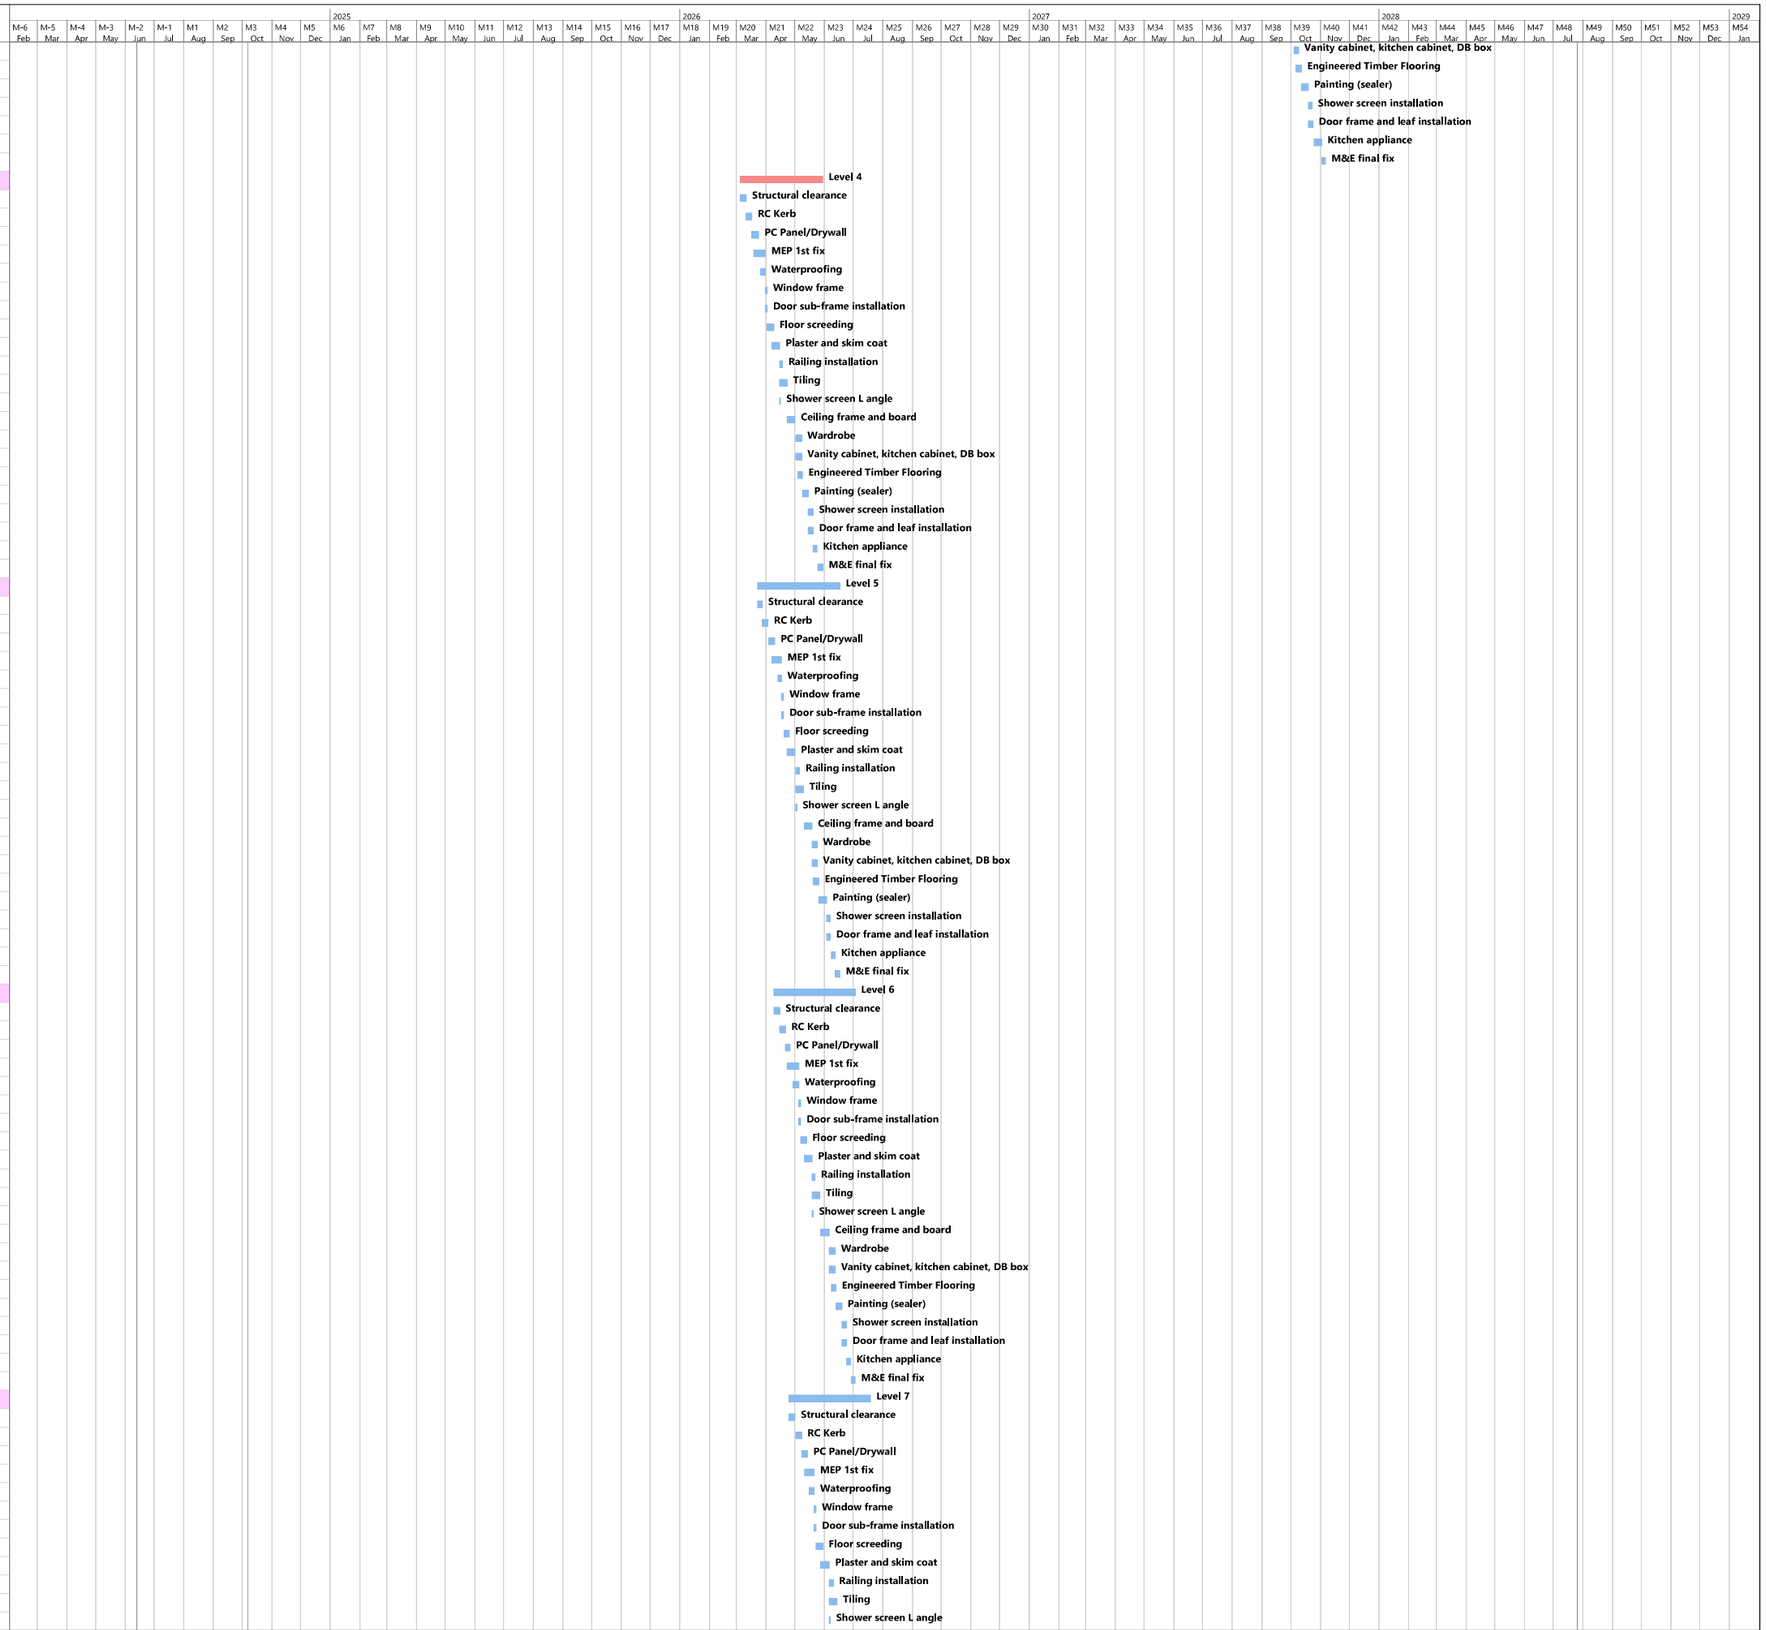


Project: Central Mall - Master P
Date: Mon 07/10/24

Task · Split · Milestone · Summary · Project Summary · Inactive Task · Inactive Milestone · Inactive Summary · Manual Task · Duration-only · Manual Summary Rollup · Manual Summary · Start-only · Finish-only · External Tasks · External Milestone · Deadline · Critical · Critical Split · Progress · Manual Progress

| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 937 | 1104 | Tiling | 7 days | Wed 12/08/26 | Wed 19/08/26 |
| 938 | 1105 | Shower screen L angle | 1 day | Wed 12/08/26 | Wed 12/08/26 |
| 939 | 1106 | Ceiling frame and board | 7 days | Thu 20/08/26 | Thu 27/08/26 |
| 940 | 1107 | Wardrobe | 5 days | Fri 28/08/26 | Wed 02/09/26 |
| 941 | 1108 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Fri 28/08/26 | Wed 02/09/26 |
| 942 | 1109 | Engineered Timber Flooring | 5 days | Fri 28/08/26 | Wed 02/09/26 |
| 943 | 1110 | Painting (sealer) | 5 days | Thu 03/09/26 | Tue 08/09/26 |
| 944 | 1111 | Shower screen installation | 4 days | Wed 09/09/26 | Sat 12/09/26 |
| 945 | 1112 | Door frame and leaf installation | 4 days | Wed 09/09/26 | Sat 12/09/26 |
| 946 | 1113 | Kitchen appliance | 4 days | Mon 14/09/26 | Thu 17/09/26 |
| 947 | 1114 | M&E final fix | 4 days | Sat 19/09/26 | Wed 23/09/26 |
| 948 | **546** | **Level 12** | **70 days** | **Mon 20/07/26** | **Fri 09/10/26** |
| 949 | 1115 | Structural clearance | 5 days | Mon 20/07/26 | Fri 24/07/26 |
| 950 | 1116 | RC Kerb | 5 days | Sat 25/07/26 | Thu 30/07/26 |
| 951 | 1117 | PC Panel/Drywall | 5 days | Fri 31/07/26 | Wed 05/08/26 |
| 952 | 1118 | MEP 1st fix | 9 days | Mon 03/08/26 | Thu 13/08/26 |
| 953 | 1119 | Waterproofing | 4 days | Sat 08/08/26 | Thu 13/08/26 |
| 954 | 1120 | Window frame | 2 days | Fri 14/08/26 | Sat 15/08/26 |
| 955 | 1121 | Door sub-frame installation | 2 days | Fri 14/08/26 | Sat 15/08/26 |
| 956 | 1122 | Floor screeding | 5 days | Mon 17/08/26 | Fri 21/08/26 |
| 957 | 1123 | Plaster and skim coat | 7 days | Thu 20/08/26 | Thu 27/08/26 |
| 958 | 1124 | Railing installation | 3 days | Fri 28/08/26 | Mon 31/08/26 |
| 959 | 1125 | Tiling | 7 days | Fri 28/08/26 | Fri 04/09/26 |
| 960 | 1126 | Shower screen L angle | 1 day | Fri 28/08/26 | Fri 28/08/26 |
| 961 | 1127 | Ceiling frame and board | 7 days | Sat 05/09/26 | Sat 12/09/26 |
| 962 | 1128 | Wardrobe | 5 days | Mon 14/09/26 | Fri 18/09/26 |
| 963 | 1129 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Mon 14/09/26 | Fri 18/09/26 |
| 964 | 1130 | Engineered Timber Flooring | 5 days | Tue 15/09/26 | Sat 19/09/26 |
| 965 | 1131 | Painting (sealer) | 5 days | Mon 21/09/26 | Fri 25/09/26 |
| 966 | 1132 | Shower screen installation | 4 days | Sat 26/09/26 | Wed 30/09/26 |
| 967 | 1133 | Door frame and leaf installation | 4 days | Sat 26/09/26 | Wed 30/09/26 |
| 968 | 1134 | Kitchen appliance | 4 days | Thu 01/10/26 | Mon 05/10/26 |
| 969 | 1135 | M&E final fix | 4 days | Tue 06/10/26 | Fri 09/10/26 |
| 970 | **547** | **Level 13** | **70 days** | **Wed 05/08/26** | **Mon 26/10/26** |
| 971 | 1136 | Structural clearance | 5 days | Wed 05/08/26 | Tue 11/08/26 |
| 972 | 1137 | RC Kerb | 5 days | Wed 12/08/26 | Mon 17/08/26 |
| 973 | 1138 | PC Panel/Drywall | 5 days | Tue 18/08/26 | Sat 22/08/26 |
| 974 | 1139 | MEP 1st fix | 9 days | Thu 20/08/26 | Sat 29/08/26 |
| 975 | 1140 | Waterproofing | 4 days | Wed 26/08/26 | Sat 29/08/26 |
| 976 | 1141 | Window frame | 2 days | Mon 31/08/26 | Tue 01/09/26 |
| 977 | 1142 | Door sub-frame installation | 2 days | Mon 31/08/26 | Tue 01/09/26 |
| 978 | 1143 | Floor screeding | 5 days | Wed 02/09/26 | Mon 07/09/26 |
| 979 | 1144 | Plaster and skim coat | 7 days | Sat 05/09/26 | Sat 12/09/26 |
| 980 | 1145 | Railing installation | 3 days | Mon 14/09/26 | Wed 16/09/26 |
| 981 | 1146 | Tiling | 7 days | Mon 14/09/26 | Mon 21/09/26 |
| 982 | 1147 | Shower screen L angle | 1 day | Mon 14/09/26 | Mon 14/09/26 |
| 983 | 1148 | Ceiling frame and board | 7 days | Tue 22/09/26 | Tue 29/09/26 |
| 984 | 1149 | Wardrobe | 5 days | Wed 30/09/26 | Mon 05/10/26 |
| 985 | 1150 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Wed 30/09/26 | Mon 05/10/26 |
| 986 | 1151 | Engineered Timber Flooring | 5 days | Thu 01/10/26 | Tue 06/10/26 |
| 987 | 1152 | Painting (sealer) | 5 days | Wed 07/10/26 | Mon 12/10/26 |
| 988 | 1153 | Shower screen installation | 4 days | Tue 13/10/26 | Fri 16/10/26 |
| 989 | 1154 | Door frame and leaf installation | 4 days | Tue 13/10/26 | Fri 16/10/26 |
| 990 | 1155 | Kitchen appliance | 4 days | Sat 17/10/26 | Wed 21/10/26 |
| 991 | 1156 | M&E final fix | 4 days | Thu 22/10/26 | Mon 26/10/26 |
| 992 | **548** | **Level 14** | **70 days** | **Sat 22/08/26** | **Thu 12/11/26** |
| 993 | 1157 | Structural clearance | 5 days | Sat 22/08/26 | Thu 27/08/26 |
| 994 | 1158 | RC Kerb | 5 days | Fri 28/08/26 | Wed 02/09/26 |
| 995 | 1159 | PC Panel/Drywall | 5 days | Thu 03/09/26 | Tue 08/09/26 |
| 996 | 1160 | MEP 1st fix | 9 days | Sat 05/09/26 | Tue 15/09/26 |
| 997 | 1161 | Waterproofing | 4 days | Fri 11/09/26 | Tue 15/09/26 |
| 998 | 1162 | Window frame | 2 days | Wed 16/09/26 | Thu 17/09/26 |
| 999 | 1163 | Door sub-frame installation | 2 days | Wed 16/09/26 | Thu 17/09/26 |
| 1000 | 1164 | Floor screeding | 5 days | Fri 18/09/26 | Wed 23/09/26 |
| 1001 | 1165 | Plaster and skim coat | 7 days | Tue 22/09/26 | Tue 29/09/26 |
| 1002 | 1166 | Railing installation | 3 days | Wed 30/09/26 | Fri 02/10/26 |
| 1003 | 1167 | Tiling | 7 days | Wed 30/09/26 | Wed 07/10/26 |
| 1004 | 1168 | Shower screen L angle | 1 day | Wed 30/09/26 | Wed 30/09/26 |
| 1005 | 1169 | Ceiling frame and board | 7 days | Thu 08/10/26 | Thu 15/10/26 |
| 1006 | 1170 | Wardrobe | 5 days | Fri 16/10/26 | Wed 21/10/26 |
| 1007 | 1171 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Fri 16/10/26 | Wed 21/10/26 |
| 1008 | 1172 | Engineered Timber Flooring | 5 days | Sat 17/10/26 | Thu 22/10/26 |
| 1009 | 1173 | Painting (sealer) | 5 days | Fri 23/10/26 | Wed 28/10/26 |
| 1010 | 1174 | Shower screen installation | 4 days | Thu 29/10/26 | Mon 02/11/26 |
| 1011 | 1175 | Door frame and leaf installation | 4 days | Thu 29/10/26 | Mon 02/11/26 |
| 1012 | 1176 | Kitchen appliance | 4 days | Tue 03/11/26 | Fri 06/11/26 |
| 1013 | 1177 | M&E final fix | 4 days | Sat 07/11/26 | Thu 12/11/26 |
| 1014 | **549** | **Level 15** | **70 days** | **Tue 08/09/26** | **Sat 28/11/26** |
| 1015 | 1178 | Structural clearance | 5 days | Tue 08/09/26 | Sat 12/09/26 |
| 1016 | 1179 | RC Kerb | 5 days | Mon 14/09/26 | Fri 18/09/26 |
| 1017 | 1180 | PC Panel/Drywall | 5 days | Sat 19/09/26 | Thu 24/09/26 |
| 1018 | 1181 | MEP 1st fix | 9 days | Tue 22/09/26 | Thu 01/10/26 |
| 1019 | 1182 | Waterproofing | 4 days | Mon 28/09/26 | Thu 01/10/26 |
| 1020 | 1183 | Window frame | 2 days | Fri 02/10/26 | Sat 03/10/26 |
| 1021 | 1184 | Door sub-frame installation | 2 days | Fri 02/10/26 | Sat 03/10/26 |
| 1022 | 1185 | Floor screeding | 5 days | Mon 05/10/26 | Fri 09/10/26 |



| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 1023 | 1186 | Plaster and skim coat | 7 days | Thu 08/10/26 | Thu 15/10/26 |
| 1024 | 1187 | Railing installation | 3 days | Fri 16/10/26 | Mon 19/10/26 |
| 1025 | 1188 | Tiling | 7 days | Fri 16/10/26 | Fri 23/10/26 |
| 1026 | 1189 | Shower screen L angle | 1 day | Fri 16/10/26 | Fri 16/10/26 |
| 1027 | 1190 | Ceiling frame and board | 7 days | Sat 24/10/26 | Sat 31/10/26 |
| 1028 | 1191 | Wardrobe | 5 days | Mon 02/11/26 | Fri 06/11/26 |
| 1029 | 1192 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Mon 02/11/26 | Fri 06/11/26 |
| 1030 | 1193 | Engineered Timber Flooring | 5 days | Tue 03/11/26 | Sat 07/11/26 |
| 1031 | 1194 | Painting (sealer) | 5 days | Tue 10/11/26 | Sat 14/11/26 |
| 1032 | 1195 | Shower screen installation | 4 days | Mon 16/11/26 | Thu 19/11/26 |
| 1033 | 1196 | Door frame and leaf installation | 4 days | Mon 16/11/26 | Thu 19/11/26 |
| 1034 | 1197 | Kitchen appliance | 4 days | Fri 20/11/26 | Tue 24/11/26 |
| 1035 | 1198 | M&E final fix | 4 days | Wed 25/11/26 | Sat 28/11/26 |
| 1036 | **550** | **Level 16** | **70 days** | **Thu 24/09/26** | **Tue 15/12/26** |
| 1037 | 1199 | Structural clearance | 5 days | Thu 24/09/26 | Tue 29/09/26 |
| 1038 | 1200 | RC Kerb | 5 days | Wed 30/09/26 | Mon 05/10/26 |
| 1039 | 1201 | PC Panel/Drywall | 5 days | Tue 06/10/26 | Sat 10/10/26 |
| 1040 | 1202 | MEP 1st fix | 9 days | Thu 08/10/26 | Sat 17/10/26 |
| 1041 | 1203 | Waterproofing | 4 days | Wed 14/10/26 | Sat 17/10/26 |
| 1042 | 1204 | Window frame | 2 days | Mon 19/10/26 | Tue 20/10/26 |
| 1043 | 1205 | Door sub-frame installation | 2 days | Mon 19/10/26 | Tue 20/10/26 |
| 1044 | 1206 | Floor screeding | 5 days | Wed 21/10/26 | Mon 26/10/26 |
| 1045 | 1207 | Plaster and skim coat | 7 days | Sat 24/10/26 | Sat 31/10/26 |
| 1046 | 1208 | Railing installation | 3 days | Mon 02/11/26 | Wed 04/11/26 |
| 1047 | 1209 | Tiling | 7 days | Mon 02/11/26 | Tue 10/11/26 |
| 1048 | 1210 | Shower screen L angle | 1 day | Mon 02/11/26 | Mon 02/11/26 |
| 1049 | 1211 | Ceiling frame and board | 7 days | Wed 11/11/26 | Wed 18/11/26 |
| 1050 | 1212 | Wardrobe | 5 days | Thu 19/11/26 | Tue 24/11/26 |
| 1051 | 1213 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Thu 19/11/26 | Tue 24/11/26 |
| 1052 | 1214 | Engineered Timber Flooring | 5 days | Fri 20/11/26 | Wed 25/11/26 |
| 1053 | 1215 | Painting (sealer) | 5 days | Thu 26/11/26 | Tue 01/12/26 |
| 1054 | 1216 | Shower screen installation | 4 days | Wed 02/12/26 | Sat 05/12/26 |
| 1055 | 1217 | Door frame and leaf installation | 4 days | Wed 02/12/26 | Sat 05/12/26 |
| 1056 | 1218 | Kitchen appliance | 4 days | Mon 07/12/26 | Thu 10/12/26 |
| 1057 | 1219 | M&E final fix | 4 days | Fri 11/12/26 | Tue 15/12/26 |
| 1058 | **551** | **Level 17** | **70 days** | **Sat 10/10/26** | **Sat 02/01/27** |
| 1059 | 1220 | Structural clearance | 5 days | Sat 10/10/26 | Thu 15/10/26 |
| 1060 | 1221 | RC Kerb | 5 days | Fri 16/10/26 | Wed 21/10/26 |
| 1061 | 1222 | PC Panel/Drywall | 5 days | Thu 22/10/26 | Tue 27/10/26 |
| 1062 | 1223 | MEP 1st fix | 9 days | Sat 24/10/26 | Tue 03/11/26 |
| 1063 | 1224 | Waterproofing | 4 days | Fri 30/10/26 | Tue 03/11/26 |
| 1064 | 1225 | Window frame | 2 days | Wed 04/11/26 | Thu 05/11/26 |
| 1065 | 1226 | Door sub-frame installation | 2 days | Wed 04/11/26 | Thu 05/11/26 |
| 1066 | 1227 | Floor screeding | 5 days | Fri 06/11/26 | Thu 12/11/26 |
| 1067 | 1228 | Plaster and skim coat | 7 days | Wed 11/11/26 | Wed 18/11/26 |
| 1068 | 1229 | Railing installation | 3 days | Thu 19/11/26 | Sat 21/11/26 |
| 1069 | 1230 | Tiling | 7 days | Thu 19/11/26 | Thu 26/11/26 |
| 1070 | 1231 | Shower screen L angle | 1 day | Thu 19/11/26 | Thu 19/11/26 |
| 1071 | 1232 | Ceiling frame and board | 7 days | Fri 27/11/26 | Fri 04/12/26 |
| 1072 | 1233 | Wardrobe | 5 days | Sat 05/12/26 | Thu 10/12/26 |
| 1073 | 1234 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Sat 05/12/26 | Thu 10/12/26 |
| 1074 | 1235 | Engineered Timber Flooring | 5 days | Mon 07/12/26 | Fri 11/12/26 |
| 1075 | 1236 | Painting (sealer) | 5 days | Sat 12/12/26 | Thu 17/12/26 |
| 1076 | 1237 | Shower screen installation | 4 days | Fri 18/12/26 | Tue 22/12/26 |
| 1077 | 1238 | Door frame and leaf installation | 4 days | Fri 18/12/26 | Tue 22/12/26 |
| 1078 | 1239 | Kitchen appliance | 4 days | Wed 23/12/26 | Mon 28/12/26 |
| 1079 | 1240 | M&E final fix | 4 days | Tue 29/12/26 | Sat 02/01/27 |
| 1080 | **552** | **Level 18** | **70 days** | **Tue 27/10/26** | **Tue 19/01/27** |
| 1081 | 1241 | Structural clearance | 5 days | Tue 27/10/26 | Sat 31/10/26 |
| 1082 | 1242 | RC Kerb | 5 days | Mon 02/11/26 | Fri 06/11/26 |
| 1083 | 1243 | PC Panel/Drywall | 5 days | Sat 07/11/26 | Fri 13/11/26 |
| 1084 | 1244 | MEP 1st fix | 9 days | Wed 11/11/26 | Fri 20/11/26 |
| 1085 | 1245 | Waterproofing | 4 days | Tue 17/11/26 | Fri 20/11/26 |
| 1086 | 1246 | Window frame | 2 days | Sat 21/11/26 | Mon 23/11/26 |
| 1087 | 1247 | Door sub-frame installation | 2 days | Sat 21/11/26 | Mon 23/11/26 |
| 1088 | 1248 | Floor screeding | 5 days | Tue 24/11/26 | Sat 28/11/26 |
| 1089 | 1249 | Plaster and skim coat | 7 days | Fri 27/11/26 | Fri 04/12/26 |
| 1090 | 1250 | Railing installation | 3 days | Sat 05/12/26 | Tue 08/12/26 |
| 1091 | 1251 | Tiling | 7 days | Sat 05/12/26 | Sat 12/12/26 |
| 1092 | 1252 | Shower screen L angle | 1 day | Sat 05/12/26 | Sat 05/12/26 |
| 1093 | 1253 | Ceiling frame and board | 7 days | Mon 14/12/26 | Mon 21/12/26 |
| 1094 | 1254 | Wardrobe | 5 days | Tue 22/12/26 | Mon 28/12/26 |
| 1095 | 1255 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Tue 22/12/26 | Mon 28/12/26 |
| 1096 | 1256 | Engineered Timber Flooring | 5 days | Wed 23/12/26 | Tue 29/12/26 |
| 1097 | 1257 | Painting (sealer) | 5 days | Wed 30/12/26 | Tue 05/01/27 |
| 1098 | 1258 | Shower screen installation | 4 days | Wed 06/01/27 | Sat 09/01/27 |
| 1099 | 1259 | Door frame and leaf installation | 4 days | Wed 06/01/27 | Sat 09/01/27 |
| 1100 | 1260 | Kitchen appliance | 4 days | Mon 11/01/27 | Thu 14/01/27 |
| 1101 | 1261 | M&E final fix | 4 days | Fri 15/01/27 | Tue 19/01/27 |
| 1102 | **553** | **Level 19** | **70 days** | **Fri 13/11/26** | **Thu 04/02/27** |
| 1103 | 1262 | Structural clearance | 5 days | Fri 13/11/26 | Wed 18/11/26 |
| 1104 | 1263 | RC Kerb | 5 days | Thu 19/11/26 | Tue 24/11/26 |
| 1105 | 1264 | PC Panel/Drywall | 5 days | Wed 25/11/26 | Mon 30/11/26 |
| 1106 | 1265 | MEP 1st fix | 9 days | Fri 27/11/26 | Mon 07/12/26 |
| 1107 | 1266 | Waterproofing | 4 days | Thu 03/12/26 | Mon 07/12/26 |
| 1108 | 1267 | Window frame | 2 days | Tue 08/12/26 | Wed 09/12/26 |

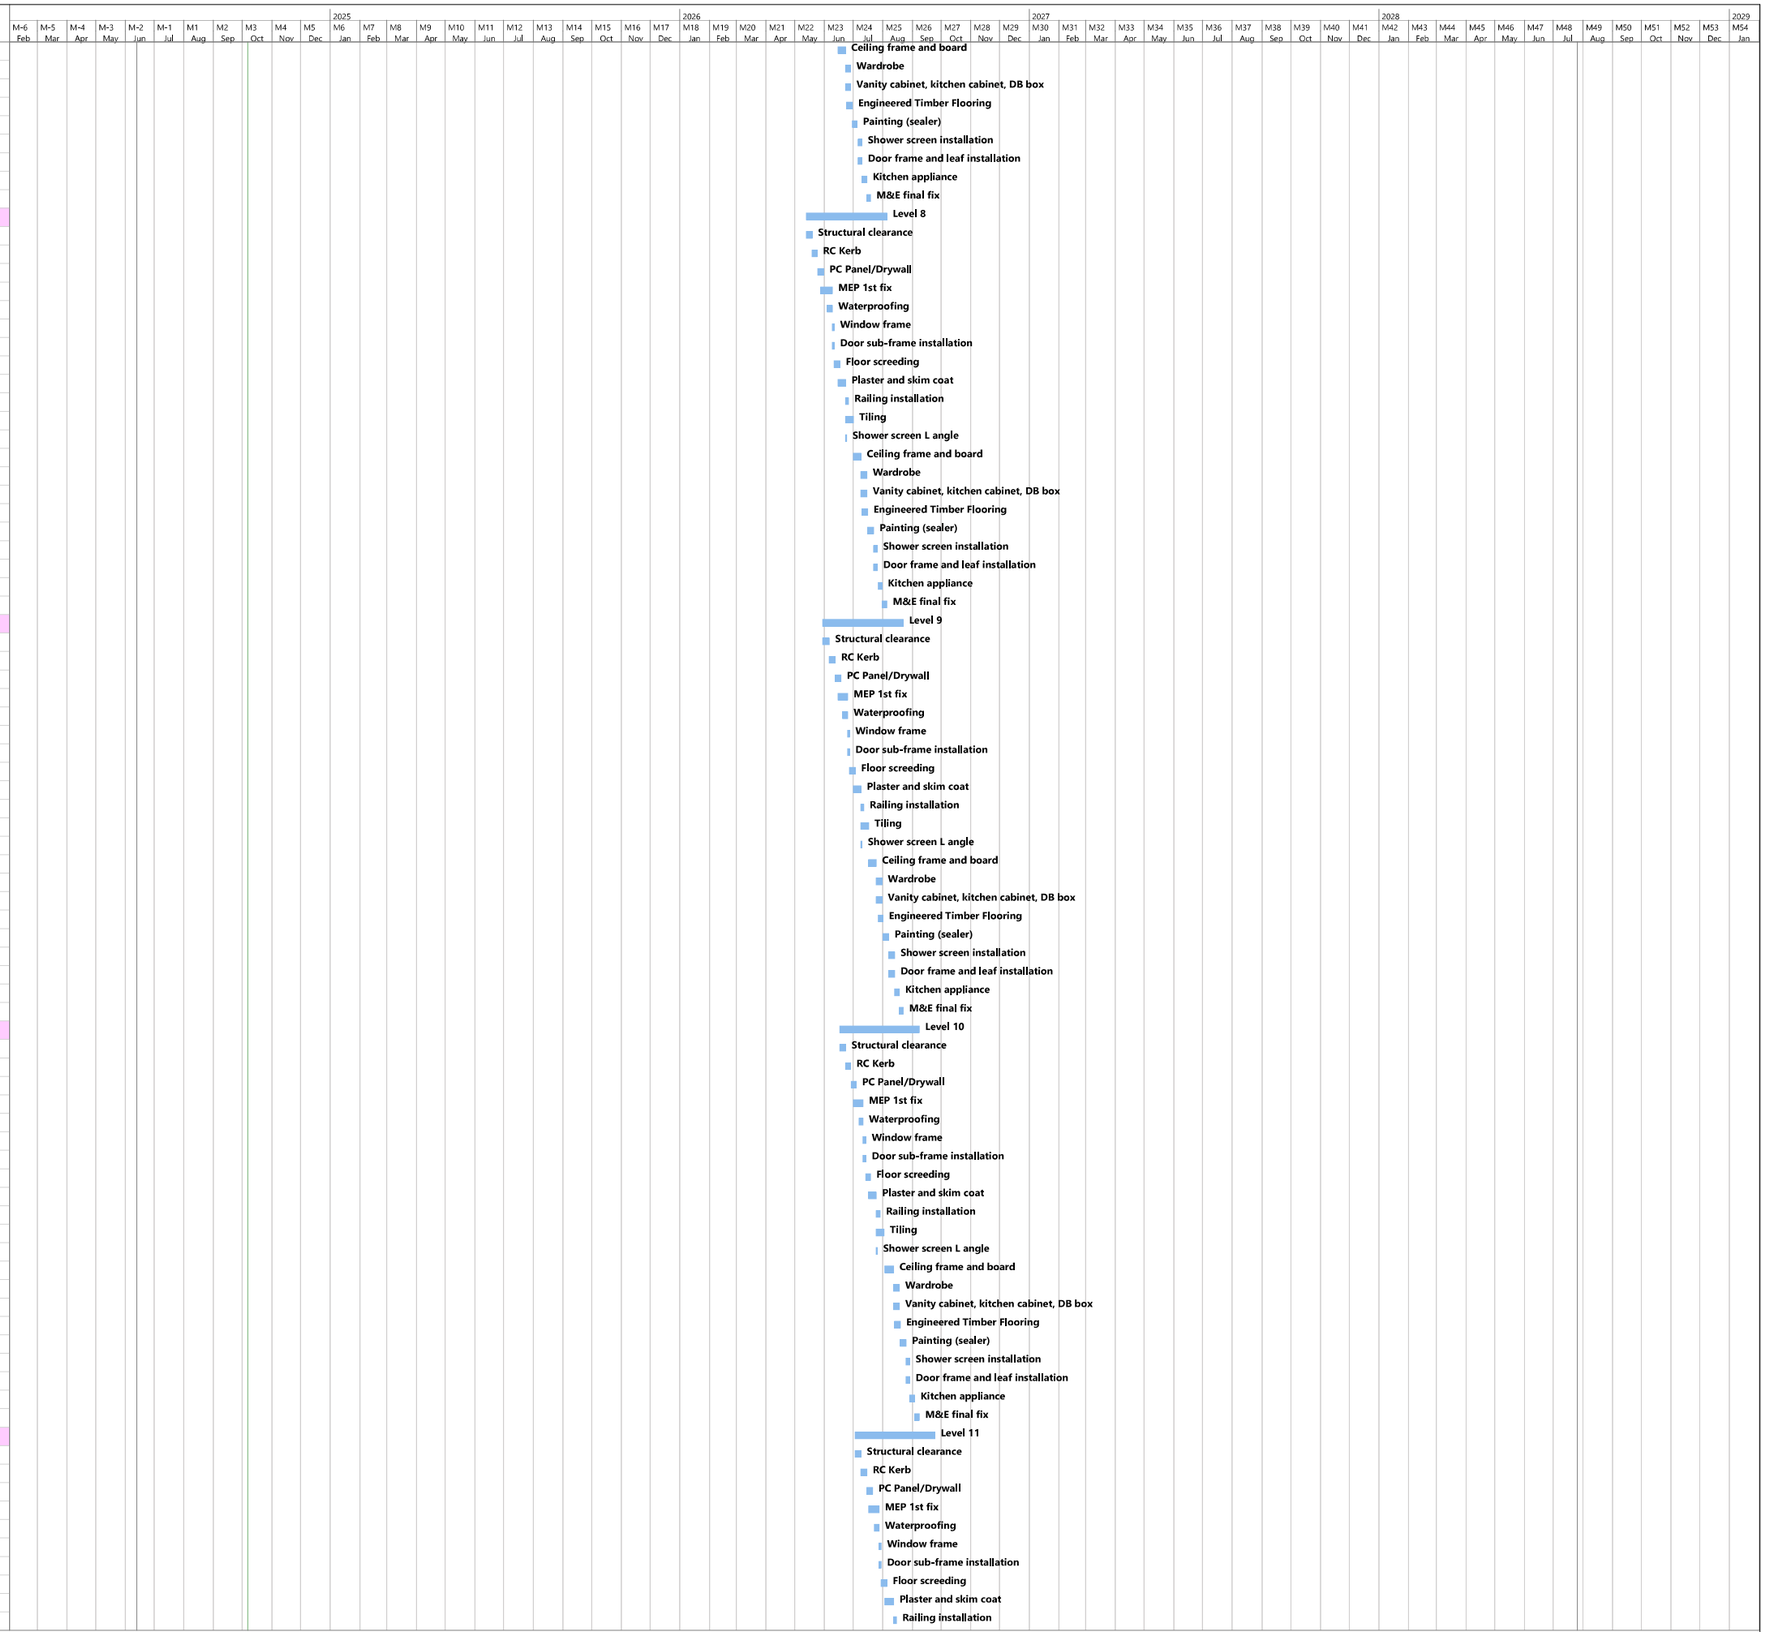


Project: Central Mall - Master P
Date: Mon 07/10/24

Task · Split · Milestone · Summary · Project Summary · Inactive Task · Inactive Milestone · Inactive Summary · Manual Task · Duration-only · Manual Summary Rollup · Manual Summary · Start-only · Finish-only · External Tasks · External Milestone · Deadline · Critical · Critical Split · Progress · Manual Progress

| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 1109 | 1268 | Door sub-frame installation | 2 days | Tue 08/12/26 | Wed 09/12/26 |
| 1110 | 1269 | Floor screeding | 5 days | Thu 10/12/26 | Tue 15/12/26 |
| 1111 | 1270 | Plaster and skim coat | 7 days | Mon 14/12/26 | Mon 21/12/26 |
| 1112 | 1271 | Railing installation | 3 days | Tue 22/12/26 | Thu 24/12/26 |
| 1113 | 1272 | Tiling | 7 days | Tue 22/12/26 | Wed 30/12/26 |
| 1114 | 1273 | Shower screen L angle | 1 day | Tue 22/12/26 | Tue 22/12/26 |
| 1115 | 1274 | Ceiling frame and board | 7 days | Thu 31/12/26 | Fri 08/01/27 |
| 1116 | 1275 | Wardrobe | 5 days | Sat 09/01/27 | Thu 14/01/27 |
| 1117 | 1276 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Sat 09/01/27 | Thu 14/01/27 |
| 1118 | 1277 | Engineered Timber Flooring | 5 days | Mon 11/01/27 | Fri 15/01/27 |
| 1119 | 1278 | Painting (sealer) | 5 days | Sat 16/01/27 | Thu 21/01/27 |
| 1120 | 1279 | Shower screen installation | 4 days | Fri 22/01/27 | Tue 26/01/27 |
| 1121 | 1280 | Door frame and leaf installation | 4 days | Fri 22/01/27 | Tue 26/01/27 |
| 1122 | 1281 | Kitchen appliance | 4 days | Wed 27/01/27 | Sat 30/01/27 |
| 1123 | 1282 | M&E final fix | 4 days | Mon 01/02/27 | Thu 04/02/27 |
| 1124 | **554** | **Level 20** | **70 days** | **Mon 30/11/26** | **Tue 23/02/27** |
| 1125 | 1283 | Structural clearance | 5 days | Mon 30/11/26 | Fri 04/12/26 |
| 1126 | 1284 | RC Kerb | 5 days | Sat 05/12/26 | Thu 10/12/26 |
| 1127 | 1285 | PC Panel/Drywall | 5 days | Fri 11/12/26 | Wed 16/12/26 |
| 1128 | 1286 | MEP 1st fix | 9 days | Mon 14/12/26 | Wed 23/12/26 |
| 1129 | 1287 | Waterproofing | 4 days | Sat 19/12/26 | Wed 23/12/26 |
| 1130 | 1288 | Window frame | 2 days | Thu 24/12/26 | Sat 26/12/26 |
| 1131 | 1289 | Door sub-frame installation | 2 days | Thu 24/12/26 | Sat 26/12/26 |
| 1132 | 1290 | Floor screeding | 5 days | Mon 28/12/26 | Sat 02/01/27 |
| 1133 | 1291 | Plaster and skim coat | 7 days | Thu 31/12/26 | Fri 08/01/27 |
| 1134 | 1292 | Railing installation | 3 days | Sat 09/01/27 | Tue 12/01/27 |
| 1135 | 1293 | Tiling | 7 days | Sat 09/01/27 | Sat 16/01/27 |
| 1136 | 1294 | Shower screen L angle | 1 day | Sat 09/01/27 | Sat 09/01/27 |
| 1137 | 1295 | Ceiling frame and board | 7 days | Mon 18/01/27 | Mon 25/01/27 |
| 1138 | 1296 | Wardrobe | 5 days | Tue 26/01/27 | Sat 30/01/27 |
| 1139 | 1297 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Tue 26/01/27 | Sat 30/01/27 |
| 1140 | 1298 | Engineered Timber Flooring | 5 days | Wed 27/01/27 | Mon 01/02/27 |
| 1141 | 1299 | Painting (sealer) | 5 days | Tue 02/02/27 | Tue 09/02/27 |
| 1142 | 1300 | Shower screen installation | 4 days | Wed 10/02/27 | Sat 13/02/27 |
| 1143 | 1301 | Door frame and leaf installation | 4 days | Wed 10/02/27 | Sat 13/02/27 |
| 1144 | 1302 | Kitchen appliance | 4 days | Mon 15/02/27 | Thu 18/02/27 |
| 1145 | 1303 | M&E final fix | 4 days | Fri 19/02/27 | Tue 23/02/27 |
| 1146 | **555** | **Level 21** | **70 days** | **Wed 16/12/26** | **Fri 12/03/27** |
| 1147 | 1304 | Structural clearance | 5 days | Wed 16/12/26 | Mon 21/12/26 |
| 1148 | 1305 | RC Kerb | 5 days | Tue 22/12/26 | Mon 28/12/26 |
| 1149 | 1306 | PC Panel/Drywall | 5 days | Tue 29/12/26 | Mon 04/01/27 |
| 1150 | 1307 | MEP 1st fix | 9 days | Thu 31/12/26 | Mon 11/01/27 |
| 1151 | 1308 | Waterproofing | 4 days | Thu 07/01/27 | Mon 11/01/27 |
| 1152 | 1309 | Window frame | 2 days | Tue 12/01/27 | Wed 13/01/27 |
| 1153 | 1310 | Door sub-frame installation | 2 days | Tue 12/01/27 | Wed 13/01/27 |
| 1154 | 1311 | Floor screeding | 5 days | Thu 14/01/27 | Tue 19/01/27 |
| 1155 | 1312 | Plaster and skim coat | 7 days | Mon 18/01/27 | Mon 25/01/27 |
| 1156 | 1313 | Railing installation | 3 days | Tue 26/01/27 | Thu 28/01/27 |
| 1157 | 1314 | Tiling | 7 days | Tue 26/01/27 | Tue 02/02/27 |
| 1158 | 1315 | Shower screen L angle | 1 day | Tue 26/01/27 | Tue 26/01/27 |
| 1159 | 1316 | Ceiling frame and board | 7 days | Wed 03/02/27 | Fri 12/02/27 |
| 1160 | 1317 | Wardrobe | 5 days | Sat 13/02/27 | Thu 18/02/27 |
| 1161 | 1318 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Sat 13/02/27 | Thu 18/02/27 |
| 1162 | 1319 | Engineered Timber Flooring | 5 days | Mon 15/02/27 | Fri 19/02/27 |
| 1163 | 1320 | Painting (sealer) | 5 days | Sat 20/02/27 | Thu 25/02/27 |
| 1164 | 1321 | Shower screen installation | 4 days | Fri 26/02/27 | Tue 02/03/27 |
| 1165 | 1322 | Door frame and leaf installation | 4 days | Fri 26/02/27 | Tue 02/03/27 |
| 1166 | 1323 | Kitchen appliance | 4 days | Wed 03/03/27 | Sat 06/03/27 |
| 1167 | 1324 | M&E final fix | 4 days | Mon 08/03/27 | Fri 12/03/27 |
| 1168 | **556** | **Level 22** | **70 days** | **Mon 04/01/27** | **Tue 30/03/27** |
| 1169 | 1325 | Structural clearance | 5 days | Mon 04/01/27 | Fri 08/01/27 |
| 1170 | 1326 | RC Kerb | 5 days | Sat 09/01/27 | Thu 14/01/27 |
| 1171 | 1327 | PC Panel/Drywall | 5 days | Fri 15/01/27 | Wed 20/01/27 |
| 1172 | 1328 | MEP 1st fix | 9 days | Mon 18/01/27 | Wed 27/01/27 |
| 1173 | 1329 | Waterproofing | 4 days | Sat 23/01/27 | Wed 27/01/27 |
| 1174 | 1330 | Window frame | 2 days | Thu 28/01/27 | Fri 29/01/27 |
| 1175 | 1331 | Door sub-frame installation | 2 days | Thu 28/01/27 | Fri 29/01/27 |
| 1176 | 1332 | Floor screeding | 5 days | Sat 30/01/27 | Thu 04/02/27 |
| 1177 | 1333 | Plaster and skim coat | 7 days | Wed 03/02/27 | Fri 12/02/27 |
| 1178 | 1334 | Railing installation | 3 days | Sat 13/02/27 | Tue 16/02/27 |
| 1179 | 1335 | Tiling | 7 days | Sat 13/02/27 | Sat 20/02/27 |
| 1180 | 1336 | Shower screen L angle | 1 day | Sat 13/02/27 | Sat 13/02/27 |
| 1181 | 1337 | Ceiling frame and board | 7 days | Mon 22/02/27 | Mon 01/03/27 |
| 1182 | 1338 | Wardrobe | 5 days | Tue 02/03/27 | Sat 06/03/27 |
| 1183 | 1339 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Tue 02/03/27 | Sat 06/03/27 |
| 1184 | 1340 | Engineered Timber Flooring | 5 days | Wed 03/03/27 | Mon 08/03/27 |
| 1185 | 1341 | Painting (sealer) | 5 days | Tue 09/03/27 | Mon 15/03/27 |
| 1186 | 1342 | Shower screen installation | 4 days | Tue 16/03/27 | Fri 19/03/27 |
| 1187 | 1343 | Door frame and leaf installation | 4 days | Tue 16/03/27 | Fri 19/03/27 |
| 1188 | 1344 | Kitchen appliance | 4 days | Sat 20/03/27 | Wed 24/03/27 |
| 1189 | 1345 | M&E final fix | 4 days | Thu 25/03/27 | Tue 30/03/27 |
| 1190 | **557** | **Level 23** | **70 days** | **Wed 20/01/27** | **Thu 15/04/27** |
| 1191 | 1346 | Structural clearance | 5 days | Wed 20/01/27 | Mon 25/01/27 |
| 1192 | 1347 | RC Kerb | 5 days | Tue 26/01/27 | Sat 30/01/27 |
| 1193 | 1348 | PC Panel/Drywall | 5 days | Mon 01/02/27 | Fri 05/02/27 |
| 1194 | 1349 | MEP 1st fix | 9 days | Wed 03/02/27 | Mon 15/02/27 |

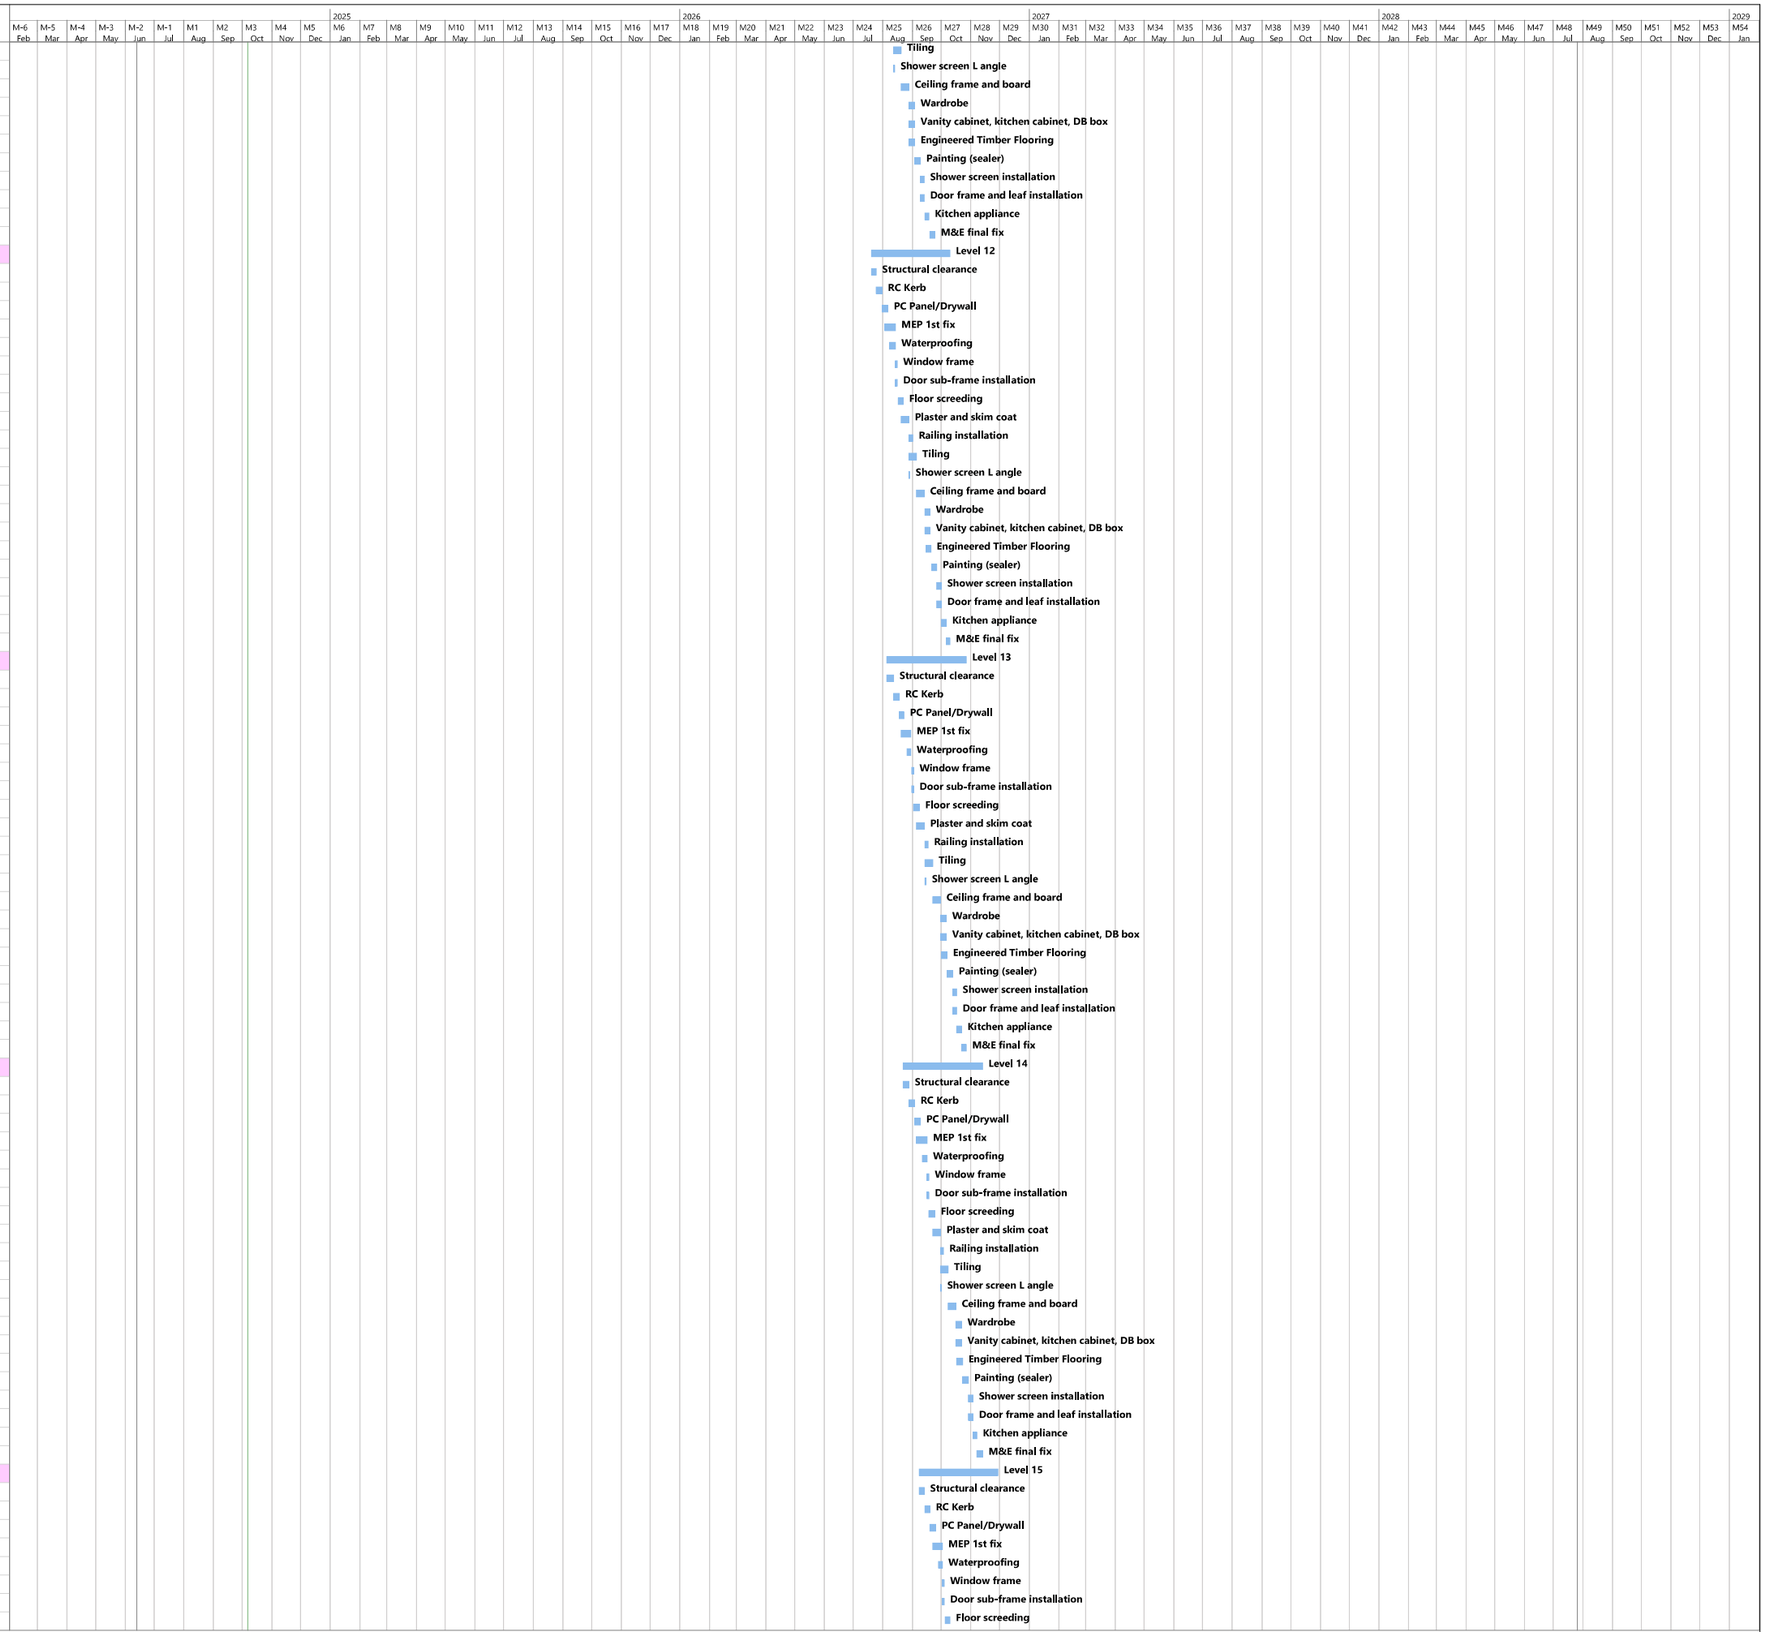

| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 1195 | 1350 | Waterproofing | 4 days | Thu 11/02/27 | Mon 15/02/27 |
| 1196 | 1351 | Window frame | 2 days | Tue 16/02/27 | Wed 17/02/27 |
| 1197 | 1352 | Door sub-frame installation | 2 days | Tue 16/02/27 | Wed 17/02/27 |
| 1198 | 1353 | Floor screeding | 5 days | Thu 18/02/27 | Tue 23/02/27 |
| 1199 | 1354 | Plaster and skim coat | 7 days | Mon 22/02/27 | Mon 01/03/27 |
| 1200 | 1355 | Railing installation | 3 days | Tue 02/03/27 | Thu 04/03/27 |
| 1201 | 1356 | Tiling | 7 days | Tue 02/03/27 | Tue 09/03/27 |
| 1202 | 1357 | Shower screen L angle | 1 day | Tue 02/03/27 | Tue 02/03/27 |
| 1203 | 1358 | Ceiling frame and board | 7 days | Thu 11/03/27 | Thu 18/03/27 |
| 1204 | 1359 | Wardrobe | 5 days | Fri 19/03/27 | Wed 24/03/27 |
| 1205 | 1360 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Fri 19/03/27 | Wed 24/03/27 |
| 1206 | 1361 | Engineered Timber Flooring | 5 days | Sat 20/03/27 | Thu 25/03/27 |
| 1207 | 1362 | Painting (sealer) | 5 days | Sat 27/03/27 | Thu 01/04/27 |
| 1208 | 1363 | Shower screen installation | 4 days | Fri 02/04/27 | Tue 06/04/27 |
| 1209 | 1364 | Door frame and leaf installation | 4 days | Fri 02/04/27 | Tue 06/04/27 |
| 1210 | 1365 | Kitchen appliance | 4 days | Wed 07/04/27 | Sat 10/04/27 |
| 1211 | 1366 | M&E final fix | 4 days | Mon 12/04/27 | Thu 15/04/27 |
| 1212 | **558** | **Level 24** | **70 days** | **Fri 05/02/27** | **Mon 03/05/27** |
| 1213 | 1367 | Structural clearance | 5 days | Fri 05/02/27 | Fri 12/02/27 |
| 1214 | 1368 | RC Kerb | 5 days | Sat 13/02/27 | Thu 18/02/27 |
| 1215 | 1369 | PC Panel/Drywall | 5 days | Fri 19/02/27 | Wed 24/02/27 |
| 1216 | 1370 | MEP 1st fix | 9 days | Mon 22/02/27 | Wed 03/03/27 |
| 1217 | 1371 | Waterproofing | 4 days | Sat 27/02/27 | Wed 03/03/27 |
| 1218 | 1372 | Window frame | 2 days | Thu 04/03/27 | Fri 05/03/27 |
| 1219 | 1373 | Door sub-frame installation | 2 days | Thu 04/03/27 | Fri 05/03/27 |
| 1220 | 1374 | Floor screeding | 5 days | Sat 06/03/27 | Fri 12/03/27 |
| 1221 | 1375 | Plaster and skim coat | 7 days | Thu 11/03/27 | Thu 18/03/27 |
| 1222 | 1376 | Railing installation | 3 days | Fri 19/03/27 | Mon 22/03/27 |
| 1223 | 1377 | Tiling | 7 days | Fri 19/03/27 | Sat 27/03/27 |
| 1224 | 1378 | Shower screen L angle | 1 day | Fri 19/03/27 | Fri 19/03/27 |
| 1225 | 1379 | Ceiling frame and board | 7 days | Mon 29/03/27 | Mon 05/04/27 |
| 1226 | 1380 | Wardrobe | 5 days | Tue 06/04/27 | Sat 10/04/27 |
| 1227 | 1381 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Tue 06/04/27 | Sat 10/04/27 |
| 1228 | 1382 | Engineered Timber Flooring | 5 days | Wed 07/04/27 | Mon 12/04/27 |
| 1229 | 1383 | Painting (sealer) | 5 days | Tue 13/04/27 | Sat 17/04/27 |
| 1230 | 1384 | Shower screen installation | 4 days | Mon 19/04/27 | Thu 22/04/27 |
| 1231 | 1385 | Door frame and leaf installation | 4 days | Mon 19/04/27 | Thu 22/04/27 |
| 1232 | 1386 | Kitchen appliance | 4 days | Fri 23/04/27 | Tue 27/04/27 |
| 1233 | 1387 | M&E final fix | 4 days | Wed 28/04/27 | Mon 03/05/27 |
| 1234 | **559** | **Level 25** | **70 days** | **Wed 24/02/27** | **Wed 19/05/27** |
| 1235 | 1388 | Structural clearance | 5 days | Wed 24/02/27 | Mon 01/03/27 |
| 1236 | 1389 | RC Kerb | 5 days | Tue 02/03/27 | Sat 06/03/27 |
| 1237 | 1390 | PC Panel/Drywall | 5 days | Mon 08/03/27 | Sat 13/03/27 |
| 1238 | 1391 | MEP 1st fix | 9 days | Thu 11/03/27 | Sat 20/03/27 |
| 1239 | 1392 | Waterproofing | 4 days | Wed 17/03/27 | Sat 20/03/27 |
| 1240 | 1393 | Window frame | 2 days | Mon 22/03/27 | Tue 23/03/27 |
| 1241 | 1394 | Door sub-frame installation | 2 days | Mon 22/03/27 | Tue 23/03/27 |
| 1242 | 1395 | Floor screeding | 5 days | Wed 24/03/27 | Tue 30/03/27 |
| 1243 | 1396 | Plaster and skim coat | 7 days | Mon 29/03/27 | Mon 05/04/27 |
| 1244 | 1397 | Railing installation | 3 days | Tue 06/04/27 | Thu 08/04/27 |
| 1245 | 1398 | Tiling | 7 days | Tue 06/04/27 | Tue 13/04/27 |
| 1246 | 1399 | Shower screen L angle | 1 day | Tue 06/04/27 | Tue 06/04/27 |
| 1247 | 1400 | Ceiling frame and board | 7 days | Wed 14/04/27 | Wed 21/04/27 |
| 1248 | 1401 | Wardrobe | 5 days | Thu 22/04/27 | Tue 27/04/27 |
| 1249 | 1402 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Thu 22/04/27 | Tue 27/04/27 |
| 1250 | 1403 | Engineered Timber Flooring | 5 days | Fri 23/04/27 | Wed 28/04/27 |
| 1251 | 1404 | Painting (sealer) | 5 days | Thu 29/04/27 | Wed 05/05/27 |
| 1252 | 1405 | Shower screen installation | 4 days | Thu 06/05/27 | Mon 10/05/27 |
| 1253 | 1406 | Door frame and leaf installation | 4 days | Thu 06/05/27 | Mon 10/05/27 |
| 1254 | 1407 | Kitchen appliance | 4 days | Tue 11/05/27 | Fri 14/05/27 |
| 1255 | 1408 | M&E final fix | 4 days | Sat 15/05/27 | Wed 19/05/27 |
| 1256 | **560** | **Level 26** | **70 days** | **Sat 13/03/27** | **Fri 04/06/27** |
| 1257 | 1409 | Structural clearance | 5 days | Sat 13/03/27 | Thu 18/03/27 |
| 1258 | 1410 | RC Kerb | 5 days | Fri 19/03/27 | Wed 24/03/27 |
| 1259 | 1411 | PC Panel/Drywall | 5 days | Thu 25/03/27 | Wed 31/03/27 |
| 1260 | 1412 | MEP 1st fix | 9 days | Mon 29/03/27 | Wed 07/04/27 |
| 1261 | 1413 | Waterproofing | 4 days | Sat 03/04/27 | Wed 07/04/27 |
| 1262 | 1414 | Window frame | 2 days | Thu 08/04/27 | Fri 09/04/27 |
| 1263 | 1415 | Door sub-frame installation | 2 days | Thu 08/04/27 | Fri 09/04/27 |
| 1264 | 1416 | Floor screeding | 5 days | Sat 10/04/27 | Thu 15/04/27 |
| 1265 | 1417 | Plaster and skim coat | 7 days | Wed 14/04/27 | Wed 21/04/27 |
| 1266 | 1418 | Railing installation | 3 days | Thu 22/04/27 | Sat 24/04/27 |
| 1267 | 1419 | Tiling | 7 days | Thu 22/04/27 | Thu 29/04/27 |
| 1268 | 1420 | Shower screen L angle | 1 day | Thu 22/04/27 | Thu 22/04/27 |
| 1269 | 1421 | Ceiling frame and board | 7 days | Fri 30/04/27 | Sat 08/05/27 |
| 1270 | 1422 | Wardrobe | 5 days | Mon 10/05/27 | Fri 14/05/27 |
| 1271 | 1423 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Mon 10/05/27 | Fri 14/05/27 |
| 1272 | 1424 | Engineered Timber Flooring | 5 days | Tue 11/05/27 | Sat 15/05/27 |
| 1273 | 1425 | Painting (sealer) | 5 days | Mon 17/05/27 | Fri 21/05/27 |
| 1274 | 1426 | Shower screen installation | 4 days | Sat 22/05/27 | Wed 26/05/27 |
| 1275 | 1427 | Door frame and leaf installation | 4 days | Sat 22/05/27 | Wed 26/05/27 |
| 1276 | 1428 | Kitchen appliance | 4 days | Thu 27/05/27 | Mon 31/05/27 |
| 1277 | 1429 | M&E final fix | 4 days | Tue 01/06/27 | Fri 04/06/27 |
| 1278 | **561** | **Level 27** | **70 days** | **Wed 31/03/27** | **Mon 21/06/27** |
| 1279 | 1430 | Structural clearance | 5 days | Wed 31/03/27 | Mon 05/04/27 |
| 1280 | 1431 | RC Kerb | 5 days | Tue 06/04/27 | Sat 10/04/27 |

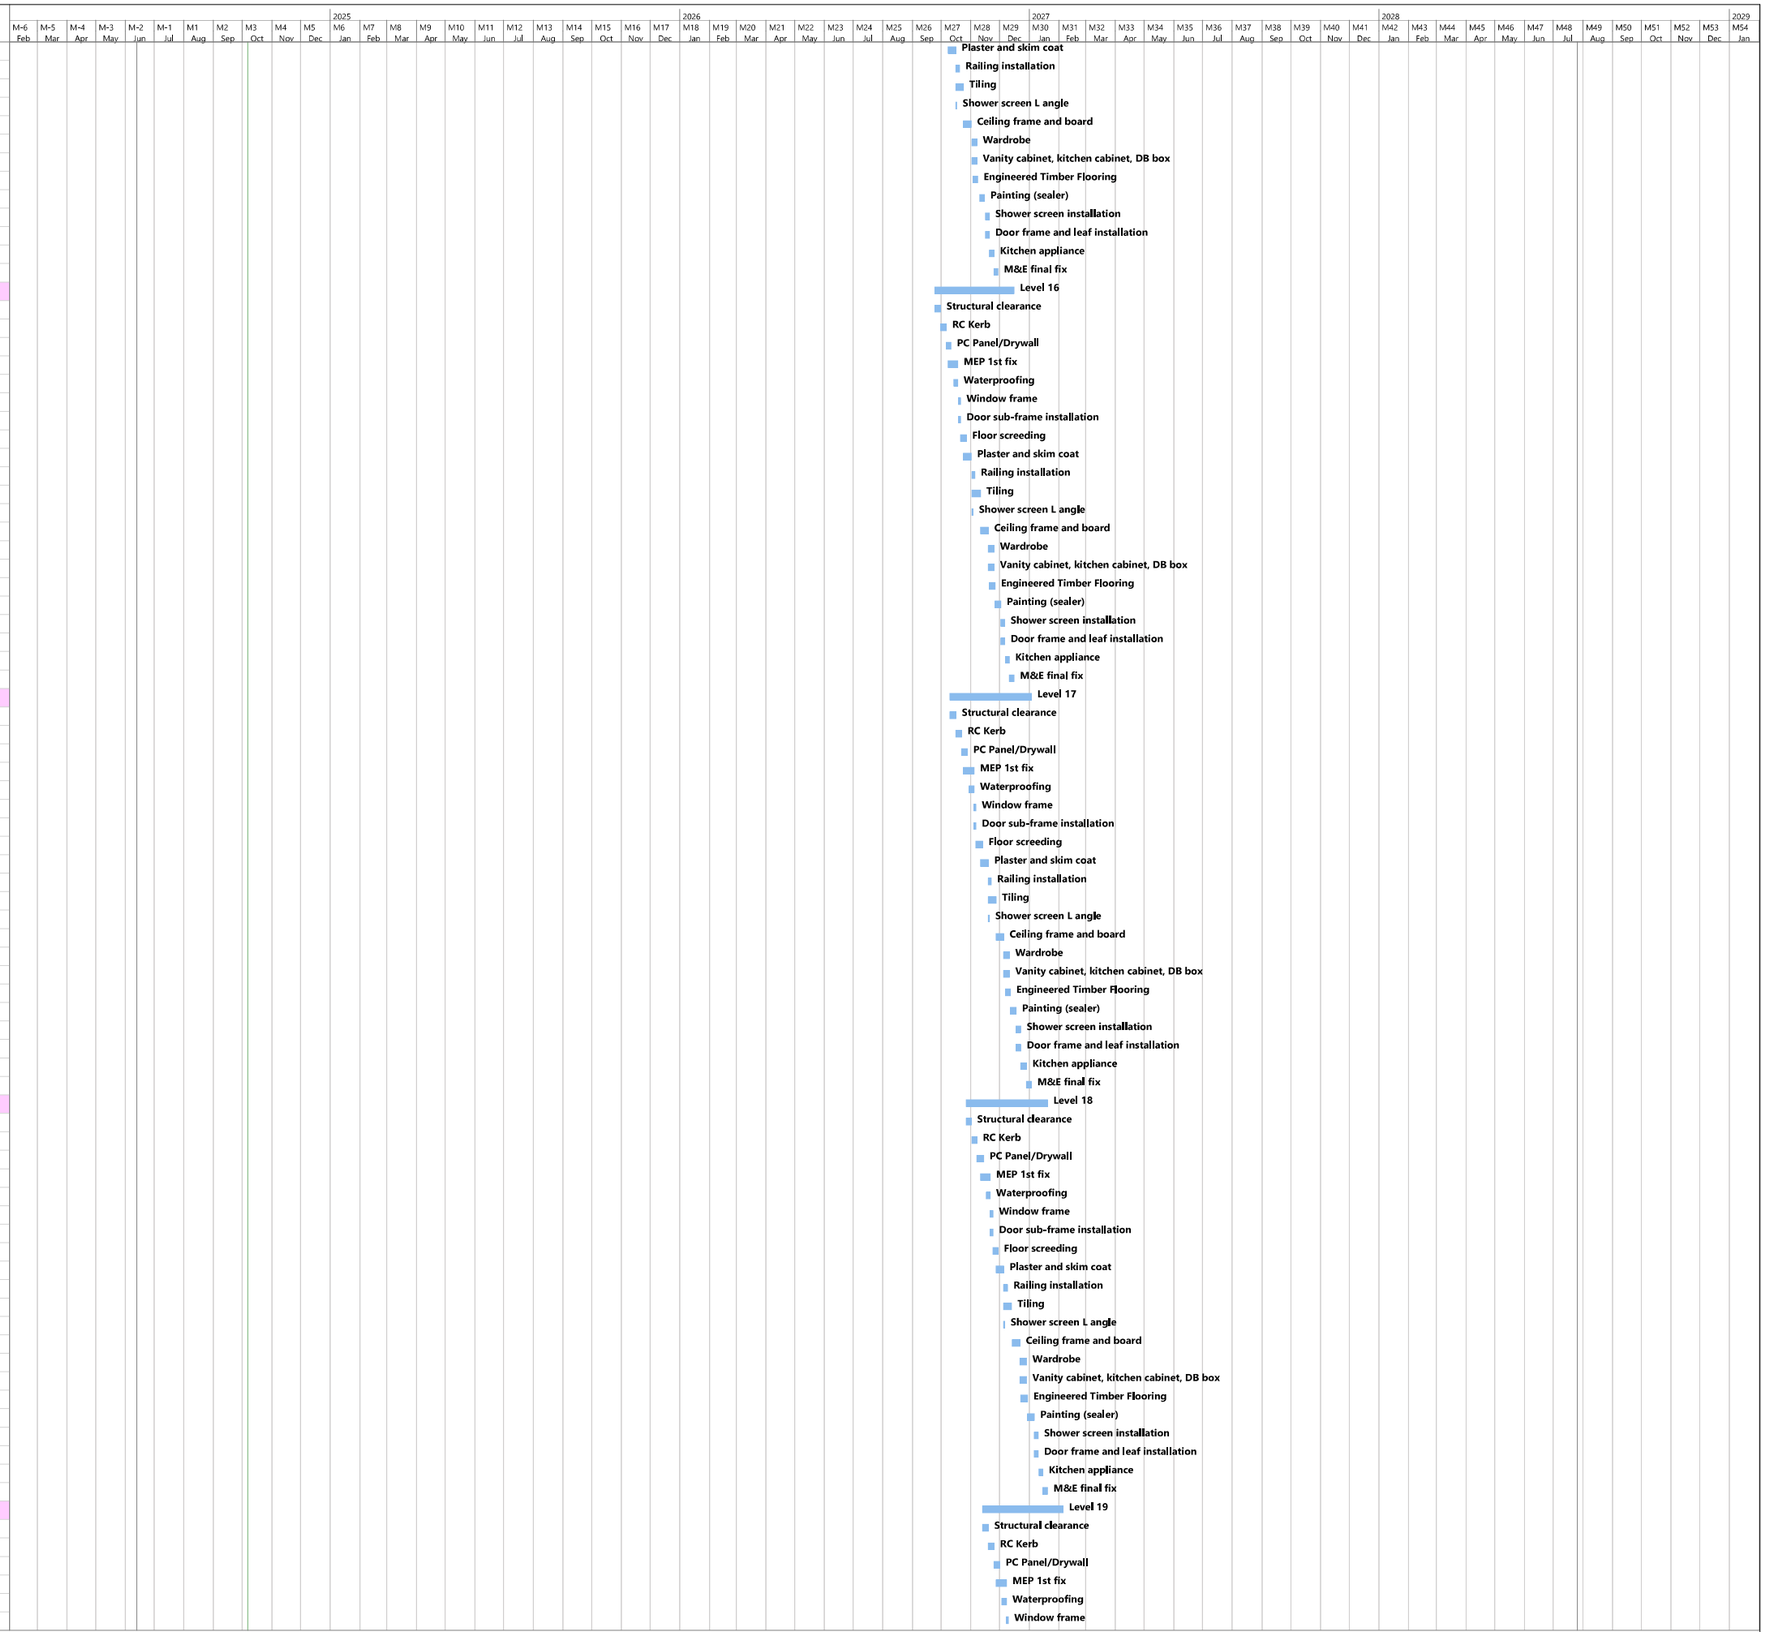

| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 1281 | 1432 | PC Panel/Drywall | 5 days | Mon 12/04/27 | Fri 16/04/27 |
| 1282 | 1433 | MEP 1st fix | 9 days | Wed 14/04/27 | Fri 23/04/27 |
| 1283 | 1434 | Waterproofing | 4 days | Tue 20/04/27 | Fri 23/04/27 |
| 1284 | 1435 | Window frame | 2 days | Sat 24/04/27 | Mon 26/04/27 |
| 1285 | 1436 | Door sub-frame installation | 2 days | Sat 24/04/27 | Mon 26/04/27 |
| 1286 | 1437 | Floor screeding | 5 days | Tue 27/04/27 | Mon 03/05/27 |
| 1287 | 1438 | Plaster and skim coat | 7 days | Fri 30/04/27 | Sat 08/05/27 |
| 1288 | 1439 | Railing installation | 3 days | Mon 10/05/27 | Wed 12/05/27 |
| 1289 | 1440 | Tiling | 7 days | Mon 10/05/27 | Mon 17/05/27 |
| 1290 | 1441 | Shower screen L angle | 1 day | Mon 10/05/27 | Mon 10/05/27 |
| 1291 | 1442 | Ceiling frame and board | 7 days | Tue 18/05/27 | Tue 25/05/27 |
| 1292 | 1443 | Wardrobe | 5 days | Wed 26/05/27 | Mon 31/05/27 |
| 1293 | 1444 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Wed 26/05/27 | Mon 31/05/27 |
| 1294 | 1445 | Engineered Timber Flooring | 5 days | Thu 27/05/27 | Tue 01/06/27 |
| 1295 | 1446 | Painting (sealer) | 5 days | Wed 02/06/27 | Mon 07/06/27 |
| 1296 | 1447 | Shower screen installation | 4 days | Tue 08/06/27 | Fri 11/06/27 |
| 1297 | 1448 | Door frame and leaf installation | 4 days | Tue 08/06/27 | Fri 11/06/27 |
| 1298 | 1449 | Kitchen appliance | 4 days | Sat 12/06/27 | Wed 16/06/27 |
| 1299 | 1450 | M&E final fix | 4 days | Thu 17/06/27 | Mon 21/06/27 |
| 1300 | **562** | **Level 28** | **70 days** | **Fri 16/04/27** | **Wed 07/07/27** |
| 1301 | 1451 | Structural clearance | 5 days | Fri 16/04/27 | Wed 21/04/27 |
| 1302 | 1452 | RC Kerb | 5 days | Thu 22/04/27 | Tue 27/04/27 |
| 1303 | 1453 | PC Panel/Drywall | 5 days | Wed 28/04/27 | Tue 04/05/27 |
| 1304 | 1454 | MEP 1st fix | 9 days | Fri 30/04/27 | Tue 11/05/27 |
| 1305 | 1455 | Waterproofing | 4 days | Fri 07/05/27 | Tue 11/05/27 |
| 1306 | 1456 | Window frame | 2 days | Wed 12/05/27 | Thu 13/05/27 |
| 1307 | 1457 | Door sub-frame installation | 2 days | Wed 12/05/27 | Thu 13/05/27 |
| 1308 | 1458 | Floor screeding | 5 days | Fri 14/05/27 | Wed 19/05/27 |
| 1309 | 1459 | Plaster and skim coat | 7 days | Tue 18/05/27 | Tue 25/05/27 |
| 1310 | 1460 | Railing installation | 3 days | Wed 26/05/27 | Fri 28/05/27 |
| 1311 | 1461 | Tiling | 7 days | Wed 26/05/27 | Wed 02/06/27 |
| 1312 | 1462 | Shower screen L angle | 1 day | Wed 26/05/27 | Wed 26/05/27 |
| 1313 | 1463 | Ceiling frame and board | 7 days | Thu 03/06/27 | Thu 10/06/27 |
| 1314 | 1464 | Wardrobe | 5 days | Fri 11/06/27 | Wed 16/06/27 |
| 1315 | 1465 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Fri 11/06/27 | Wed 16/06/27 |
| 1316 | 1466 | Engineered Timber Flooring | 5 days | Sat 12/06/27 | Thu 17/06/27 |
| 1317 | 1467 | Painting (sealer) | 5 days | Fri 18/06/27 | Wed 23/06/27 |
| 1318 | 1468 | Shower screen installation | 4 days | Thu 24/06/27 | Mon 28/06/27 |
| 1319 | 1469 | Door frame and leaf installation | 4 days | Thu 24/06/27 | Mon 28/06/27 |
| 1320 | 1470 | Kitchen appliance | 4 days | Tue 29/06/27 | Fri 02/07/27 |
| 1321 | 1471 | M&E final fix | 4 days | Sat 03/07/27 | Wed 07/07/27 |
| 1322 | **563** | **Level 29** | **70 days** | **Tue 04/05/27** | **Fri 23/07/27** |
| 1323 | 1472 | Structural clearance | 5 days | Tue 04/05/27 | Sat 08/05/27 |
| 1324 | 1473 | RC Kerb | 5 days | Mon 10/05/27 | Fri 14/05/27 |
| 1325 | 1474 | PC Panel/Drywall | 5 days | Sat 15/05/27 | Thu 20/05/27 |
| 1326 | 1475 | MEP 1st fix | 9 days | Tue 18/05/27 | Thu 27/05/27 |
| 1327 | 1476 | Waterproofing | 4 days | Mon 24/05/27 | Thu 27/05/27 |
| 1328 | 1477 | Window frame | 2 days | Fri 28/05/27 | Sat 29/05/27 |
| 1329 | 1478 | Door sub-frame installation | 2 days | Fri 28/05/27 | Sat 29/05/27 |
| 1330 | 1479 | Floor screeding | 5 days | Mon 31/05/27 | Fri 04/06/27 |
| 1331 | 1480 | Plaster and skim coat | 7 days | Thu 03/06/27 | Thu 10/06/27 |
| 1332 | 1481 | Railing installation | 3 days | Fri 11/06/27 | Mon 14/06/27 |
| 1333 | 1482 | Tiling | 7 days | Fri 11/06/27 | Fri 18/06/27 |
| 1334 | 1483 | Shower screen L angle | 1 day | Fri 11/06/27 | Fri 11/06/27 |
| 1335 | 1484 | Ceiling frame and board | 7 days | Sat 19/06/27 | Sat 26/06/27 |
| 1336 | 1485 | Wardrobe | 5 days | Mon 28/06/27 | Fri 02/07/27 |
| 1337 | 1486 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Mon 28/06/27 | Fri 02/07/27 |
| 1338 | 1487 | Engineered Timber Flooring | 5 days | Tue 29/06/27 | Sat 03/07/27 |
| 1339 | 1488 | Painting (sealer) | 5 days | Mon 05/07/27 | Fri 09/07/27 |
| 1340 | 1489 | Shower screen installation | 4 days | Sat 10/07/27 | Wed 14/07/27 |
| 1341 | 1490 | Door frame and leaf installation | 4 days | Sat 10/07/27 | Wed 14/07/27 |
| 1342 | 1491 | Kitchen appliance | 4 days | Thu 15/07/27 | Mon 19/07/27 |
| 1343 | 1492 | M&E final fix | 4 days | Tue 20/07/27 | Fri 23/07/27 |
| 1344 | **564** | **Level 30** | **70 days** | **Thu 20/05/27** | **Tue 10/08/27** |
| 1345 | 1493 | Structural clearance | 5 days | Thu 20/05/27 | Tue 25/05/27 |
| 1346 | 1494 | RC Kerb | 5 days | Wed 26/05/27 | Mon 31/05/27 |
| 1347 | 1495 | PC Panel/Drywall | 5 days | Tue 01/06/27 | Sat 05/06/27 |
| 1348 | 1496 | MEP 1st fix | 9 days | Thu 03/06/27 | Sat 12/06/27 |
| 1349 | 1497 | Waterproofing | 4 days | Wed 09/06/27 | Sat 12/06/27 |
| 1350 | 1498 | Window frame | 2 days | Mon 14/06/27 | Tue 15/06/27 |
| 1351 | 1499 | Door sub-frame installation | 2 days | Mon 14/06/27 | Tue 15/06/27 |
| 1352 | 1500 | Floor screeding | 5 days | Wed 16/06/27 | Mon 21/06/27 |
| 1353 | 1501 | Plaster and skim coat | 7 days | Sat 19/06/27 | Sat 26/06/27 |
| 1354 | 1502 | Railing installation | 3 days | Mon 28/06/27 | Wed 30/06/27 |
| 1355 | 1503 | Tiling | 7 days | Mon 28/06/27 | Mon 05/07/27 |
| 1356 | 1504 | Shower screen L angle | 1 day | Mon 28/06/27 | Mon 28/06/27 |
| 1357 | 1505 | Ceiling frame and board | 7 days | Tue 06/07/27 | Tue 13/07/27 |
| 1358 | 1506 | Wardrobe | 5 days | Wed 14/07/27 | Mon 19/07/27 |
| 1359 | 1507 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Wed 14/07/27 | Mon 19/07/27 |
| 1360 | 1508 | Engineered Timber Flooring | 5 days | Thu 15/07/27 | Tue 20/07/27 |
| 1361 | 1509 | Painting (sealer) | 5 days | Wed 21/07/27 | Mon 26/07/27 |
| 1362 | 1510 | Shower screen installation | 4 days | Tue 27/07/27 | Fri 30/07/27 |
| 1363 | 1511 | Door frame and leaf installation | 4 days | Tue 27/07/27 | Fri 30/07/27 |
| 1364 | 1512 | Kitchen appliance | 4 days | Sat 31/07/27 | Wed 04/08/27 |
| 1365 | 1513 | M&E final fix | 4 days | Thu 05/08/27 | Tue 10/08/27 |
| 1366 | **565** | **Level 31** | **70 days** | **Sat 05/06/27** | **Thu 26/08/27** |



| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 1367 | 1514 | Structural clearance | 5 days | Sat 05/06/27 | Thu 10/06/27 |
| 1368 | 1515 | RC Kerb | 5 days | Fri 11/06/27 | Wed 16/06/27 |
| 1369 | 1516 | PC Panel/Drywall | 5 days | Thu 17/06/27 | Tue 22/06/27 |
| 1370 | 1517 | MEP 1st fix | 9 days | Sat 19/06/27 | Tue 29/06/27 |
| 1371 | 1518 | Waterproofing | 4 days | Fri 25/06/27 | Tue 29/06/27 |
| 1372 | 1519 | Window frame | 2 days | Wed 30/06/27 | Thu 01/07/27 |
| 1373 | 1520 | Door sub-frame installation | 2 days | Wed 30/06/27 | Thu 01/07/27 |
| 1374 | 1521 | Floor screeding | 5 days | Fri 02/07/27 | Wed 07/07/27 |
| 1375 | 1522 | Plaster and skim coat | 7 days | Tue 06/07/27 | Tue 13/07/27 |
| 1376 | 1523 | Railing installation | 3 days | Wed 14/07/27 | Fri 16/07/27 |
| 1377 | 1524 | Tiling | 7 days | Wed 14/07/27 | Wed 21/07/27 |
| 1378 | 1525 | Shower screen L angle | 1 day | Wed 14/07/27 | Wed 14/07/27 |
| 1379 | 1526 | Ceiling frame and board | 7 days | Thu 22/07/27 | Thu 29/07/27 |
| 1380 | 1527 | Wardrobe | 5 days | Fri 30/07/27 | Wed 04/08/27 |
| 1381 | 1528 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Fri 30/07/27 | Wed 04/08/27 |
| 1382 | 1529 | Engineered Timber Flooring | 5 days | Sat 31/07/27 | Thu 05/08/27 |
| 1383 | 1530 | Painting (sealer) | 5 days | Fri 06/08/27 | Thu 12/08/27 |
| 1384 | 1531 | Shower screen installation | 4 days | Fri 13/08/27 | Tue 17/08/27 |
| 1385 | 1532 | Door frame and leaf installation | 4 days | Fri 13/08/27 | Tue 17/08/27 |
| 1386 | 1533 | Kitchen appliance | 4 days | Wed 18/08/27 | Sat 21/08/27 |
| 1387 | 1534 | M&E final fix | 4 days | Mon 23/08/27 | Thu 26/08/27 |
| 1388 | **566** | **Level 32** | **70 days** | **Tue 22/06/27** | **Sat 11/09/27** |
| 1389 | 1535 | Structural clearance | 5 days | Tue 22/06/27 | Sat 26/06/27 |
| 1390 | 1536 | RC Kerb | 5 days | Mon 28/06/27 | Fri 02/07/27 |
| 1391 | 1537 | PC Panel/Drywall | 5 days | Sat 03/07/27 | Thu 08/07/27 |
| 1392 | 1538 | MEP 1st fix | 9 days | Tue 06/07/27 | Thu 15/07/27 |
| 1393 | 1539 | Waterproofing | 4 days | Mon 12/07/27 | Thu 15/07/27 |
| 1394 | 1540 | Window frame | 2 days | Fri 16/07/27 | Sat 17/07/27 |
| 1395 | 1541 | Door sub-frame installation | 2 days | Fri 16/07/27 | Sat 17/07/27 |
| 1396 | 1542 | Floor screeding | 5 days | Mon 19/07/27 | Fri 23/07/27 |
| 1397 | 1543 | Plaster and skim coat | 7 days | Thu 22/07/27 | Thu 29/07/27 |
| 1398 | 1544 | Railing installation | 3 days | Fri 30/07/27 | Mon 02/08/27 |
| 1399 | 1545 | Tiling | 7 days | Fri 30/07/27 | Fri 06/08/27 |
| 1400 | 1546 | Shower screen L angle | 1 day | Fri 30/07/27 | Fri 30/07/27 |
| 1401 | 1547 | Ceiling frame and board | 7 days | Sat 07/08/27 | Mon 16/08/27 |
| 1402 | 1548 | Wardrobe | 5 days | Tue 17/08/27 | Sat 21/08/27 |
| 1403 | 1549 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Tue 17/08/27 | Sat 21/08/27 |
| 1404 | 1550 | Engineered Timber Flooring | 5 days | Wed 18/08/27 | Mon 23/08/27 |
| 1405 | 1551 | Painting (sealer) | 5 days | Tue 24/08/27 | Sat 28/08/27 |
| 1406 | 1552 | Shower screen installation | 4 days | Mon 30/08/27 | Thu 02/09/27 |
| 1407 | 1553 | Door frame and leaf installation | 4 days | Mon 30/08/27 | Thu 02/09/27 |
| 1408 | 1554 | Kitchen appliance | 4 days | Fri 03/09/27 | Tue 07/09/27 |
| 1409 | 1555 | M&E final fix | 4 days | Wed 08/09/27 | Sat 11/09/27 |
| 1410 | **567** | **Level 33** | **70 days** | **Thu 08/07/27** | **Tue 28/09/27** |
| 1411 | 1556 | Structural clearance | 5 days | Thu 08/07/27 | Tue 13/07/27 |
| 1412 | 1557 | RC Kerb | 5 days | Wed 14/07/27 | Mon 19/07/27 |
| 1413 | 1558 | PC Panel/Drywall | 5 days | Tue 20/07/27 | Sat 24/07/27 |
| 1414 | 1559 | MEP 1st fix | 9 days | Thu 22/07/27 | Sat 31/07/27 |
| 1415 | 1560 | Waterproofing | 4 days | Wed 28/07/27 | Sat 31/07/27 |
| 1416 | 1561 | Window frame | 2 days | Mon 02/08/27 | Tue 03/08/27 |
| 1417 | 1562 | Door sub-frame installation | 2 days | Mon 02/08/27 | Tue 03/08/27 |
| 1418 | 1563 | Floor screeding | 5 days | Wed 04/08/27 | Tue 10/08/27 |
| 1419 | 1564 | Plaster and skim coat | 7 days | Sat 07/08/27 | Mon 16/08/27 |
| 1420 | 1565 | Railing installation | 3 days | Tue 17/08/27 | Thu 19/08/27 |
| 1421 | 1566 | Tiling | 7 days | Tue 17/08/27 | Tue 24/08/27 |
| 1422 | 1567 | Shower screen L angle | 1 day | Tue 17/08/27 | Tue 17/08/27 |
| 1423 | 1568 | Ceiling frame and board | 7 days | Wed 25/08/27 | Wed 01/09/27 |
| 1424 | 1569 | Wardrobe | 5 days | Thu 02/09/27 | Tue 07/09/27 |
| 1425 | 1570 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Thu 02/09/27 | Tue 07/09/27 |
| 1426 | 1571 | Engineered Timber Flooring | 5 days | Fri 03/09/27 | Wed 08/09/27 |
| 1427 | 1572 | Painting (sealer) | 5 days | Thu 09/09/27 | Tue 14/09/27 |
| 1428 | 1573 | Shower screen installation | 4 days | Wed 15/09/27 | Sat 18/09/27 |
| 1429 | 1574 | Door frame and leaf installation | 4 days | Wed 15/09/27 | Sat 18/09/27 |
| 1430 | 1575 | Kitchen appliance | 4 days | Mon 20/09/27 | Thu 23/09/27 |
| 1431 | 1576 | M&E final fix | 4 days | Fri 24/09/27 | Tue 28/09/27 |
| 1432 | **568** | **Level 34** | **70 days** | **Sat 24/07/27** | **Thu 14/10/27** |
| 1433 | 1577 | Structural clearance | 5 days | Sat 24/07/27 | Thu 29/07/27 |
| 1434 | 1578 | RC Kerb | 5 days | Fri 30/07/27 | Wed 04/08/27 |
| 1435 | 1579 | PC Panel/Drywall | 5 days | Thu 05/08/27 | Wed 11/08/27 |
| 1436 | 1580 | MEP 1st fix | 9 days | Sat 07/08/27 | Wed 18/08/27 |
| 1437 | 1581 | Waterproofing | 4 days | Sat 14/08/27 | Wed 18/08/27 |
| 1438 | 1582 | Window frame | 2 days | Thu 19/08/27 | Fri 20/08/27 |
| 1439 | 1583 | Door sub-frame installation | 2 days | Thu 19/08/27 | Fri 20/08/27 |
| 1440 | 1584 | Floor screeding | 5 days | Sat 21/08/27 | Thu 26/08/27 |
| 1441 | 1585 | Plaster and skim coat | 7 days | Wed 25/08/27 | Wed 01/09/27 |
| 1442 | 1586 | Railing installation | 3 days | Thu 02/09/27 | Sat 04/09/27 |
| 1443 | 1587 | Tiling | 7 days | Thu 02/09/27 | Thu 09/09/27 |
| 1444 | 1588 | Shower screen L angle | 1 day | Thu 02/09/27 | Thu 02/09/27 |
| 1445 | 1589 | Ceiling frame and board | 7 days | Fri 10/09/27 | Fri 17/09/27 |
| 1446 | 1590 | Wardrobe | 5 days | Sat 18/09/27 | Thu 23/09/27 |
| 1447 | 1591 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Sat 18/09/27 | Thu 23/09/27 |
| 1448 | 1592 | Engineered Timber Flooring | 5 days | Mon 20/09/27 | Fri 24/09/27 |
| 1449 | 1593 | Painting (sealer) | 5 days | Sat 25/09/27 | Thu 30/09/27 |
| 1450 | 1594 | Shower screen installation | 4 days | Fri 01/10/27 | Tue 05/10/27 |
| 1451 | 1595 | Door frame and leaf installation | 4 days | Fri 01/10/27 | Tue 05/10/27 |
| 1452 | 1596 | Kitchen appliance | 4 days | Wed 06/10/27 | Sat 09/10/27 |



| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 1453 | 1597 | M&E final fix | 4 days | Mon 11/10/27 | Thu 14/10/27 |
| 1454 | **569** | **Level 35** | **70 days** | **Wed 11/08/27** | **Mon 01/11/27** |
| 1455 | 1598 | Structural clearance | 5 days | Wed 11/08/27 | Mon 16/08/27 |
| 1456 | 1599 | RC Kerb | 5 days | Tue 17/08/27 | Sat 21/08/27 |
| 1457 | 1600 | PC Panel/Drywall | 5 days | Mon 23/08/27 | Fri 27/08/27 |
| 1458 | 1601 | MEP 1st fix | 9 days | Wed 25/08/27 | Fri 03/09/27 |
| 1459 | 1602 | Waterproofing | 4 days | Tue 31/08/27 | Fri 03/09/27 |
| 1460 | 1603 | Window frame | 2 days | Sat 04/09/27 | Mon 06/09/27 |
| 1461 | 1604 | Door sub-frame installation | 2 days | Sat 04/09/27 | Mon 06/09/27 |
| 1462 | 1605 | Floor screeding | 5 days | Tue 07/09/27 | Sat 11/09/27 |
| 1463 | 1606 | Plaster and skim coat | 7 days | Fri 10/09/27 | Fri 17/09/27 |
| 1464 | 1607 | Railing installation | 3 days | Sat 18/09/27 | Tue 21/09/27 |
| 1465 | 1608 | Tiling | 7 days | Sat 18/09/27 | Sat 25/09/27 |
| 1466 | 1609 | Shower screen L angle | 1 day | Sat 18/09/27 | Sat 18/09/27 |
| 1467 | 1610 | Ceiling frame and board | 7 days | Mon 27/09/27 | Mon 04/10/27 |
| 1468 | 1611 | Wardrobe | 5 days | Tue 05/10/27 | Sat 09/10/27 |
| 1469 | 1612 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Tue 05/10/27 | Sat 09/10/27 |
| 1470 | 1613 | Engineered Timber Flooring | 5 days | Wed 06/10/27 | Mon 11/10/27 |
| 1471 | 1614 | Painting (sealer) | 5 days | Tue 12/10/27 | Sat 16/10/27 |
| 1472 | 1615 | Shower screen installation | 4 days | Mon 18/10/27 | Thu 21/10/27 |
| 1473 | 1616 | Door frame and leaf installation | 4 days | Mon 18/10/27 | Thu 21/10/27 |
| 1474 | 1617 | Kitchen appliance | 4 days | Fri 22/10/27 | Tue 26/10/27 |
| 1475 | 1618 | M&E final fix | 4 days | Wed 27/10/27 | Mon 01/11/27 |
| 1476 | **570** | **Level 36** | **70 days** | **Fri 27/08/27** | **Wed 17/11/27** |
| 1477 | 1619 | Structural clearance | 5 days | Fri 27/08/27 | Wed 01/09/27 |
| 1478 | 1620 | RC Kerb | 5 days | Thu 02/09/27 | Tue 07/09/27 |
| 1479 | 1621 | PC Panel/Drywall | 5 days | Wed 08/09/27 | Mon 13/09/27 |
| 1480 | 1622 | MEP 1st fix | 9 days | Fri 10/09/27 | Mon 20/09/27 |
| 1481 | 1623 | Waterproofing | 4 days | Thu 16/09/27 | Mon 20/09/27 |
| 1482 | 1624 | Window frame | 2 days | Tue 21/09/27 | Wed 22/09/27 |
| 1483 | 1625 | Door sub-frame installation | 2 days | Tue 21/09/27 | Wed 22/09/27 |
| 1484 | 1626 | Floor screeding | 5 days | Thu 23/09/27 | Tue 28/09/27 |
| 1485 | 1627 | Plaster and skim coat | 7 days | Mon 27/09/27 | Mon 04/10/27 |
| 1486 | 1628 | Railing installation | 3 days | Tue 05/10/27 | Thu 07/10/27 |
| 1487 | 1629 | Tiling | 7 days | Tue 05/10/27 | Tue 12/10/27 |
| 1488 | 1630 | Shower screen L angle | 1 day | Tue 05/10/27 | Tue 05/10/27 |
| 1489 | 1631 | Ceiling frame and board | 7 days | Wed 13/10/27 | Wed 20/10/27 |
| 1490 | 1632 | Wardrobe | 5 days | Thu 21/10/27 | Tue 26/10/27 |
| 1491 | 1633 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Thu 21/10/27 | Tue 26/10/27 |
| 1492 | 1634 | Engineered Timber Flooring | 5 days | Fri 22/10/27 | Wed 27/10/27 |
| 1493 | 1635 | Painting (sealer) | 5 days | Thu 28/10/27 | Wed 03/11/27 |
| 1494 | 1636 | Shower screen installation | 4 days | Thu 04/11/27 | Mon 08/11/27 |
| 1495 | 1637 | Door frame and leaf installation | 4 days | Thu 04/11/27 | Mon 08/11/27 |
| 1496 | 1638 | Kitchen appliance | 4 days | Tue 09/11/27 | Fri 12/11/27 |
| 1497 | 1639 | M&E final fix | 4 days | Sat 13/11/27 | Wed 17/11/27 |
| 1498 | **571** | **Level 37** | **70 days** | **Thu 07/10/27** | **Wed 29/12/27** |
| 1499 | 1640 | Structural clearance | 5 days | Thu 07/10/27 | Tue 12/10/27 |
| 1500 | 1641 | RC Kerb | 5 days | Wed 13/10/27 | Mon 18/10/27 |
| 1501 | 1642 | PC Panel/Drywall | 5 days | Tue 19/10/27 | Sat 23/10/27 |
| 1502 | 1643 | MEP 1st fix | 9 days | Thu 21/10/27 | Mon 01/11/27 |
| 1503 | 1644 | Waterproofing | 4 days | Wed 27/10/27 | Mon 01/11/27 |
| 1504 | 1645 | Window frame | 2 days | Tue 02/11/27 | Wed 03/11/27 |
| 1505 | 1646 | Door sub-frame installation | 2 days | Tue 02/11/27 | Wed 03/11/27 |
| 1506 | 1647 | Floor screeding | 5 days | Thu 04/11/27 | Tue 09/11/27 |
| 1507 | 1648 | Plaster and skim coat | 7 days | Mon 08/11/27 | Mon 15/11/27 |
| 1508 | 1649 | Railing installation | 3 days | Tue 16/11/27 | Thu 18/11/27 |
| 1509 | 1650 | Tiling | 7 days | Tue 16/11/27 | Tue 23/11/27 |
| 1510 | 1651 | Shower screen L angle | 1 day | Tue 16/11/27 | Tue 16/11/27 |
| 1511 | 1652 | Ceiling frame and board | 7 days | Wed 24/11/27 | Wed 01/12/27 |
| 1512 | 1653 | Wardrobe | 5 days | Thu 02/12/27 | Tue 07/12/27 |
| 1513 | 1654 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Thu 02/12/27 | Tue 07/12/27 |
| 1514 | 1655 | Engineered Timber Flooring | 5 days | Fri 03/12/27 | Wed 08/12/27 |
| 1515 | 1656 | Painting (sealer) | 5 days | Thu 09/12/27 | Tue 14/12/27 |
| 1516 | 1657 | Shower screen installation | 4 days | Wed 15/12/27 | Sat 18/12/27 |
| 1517 | 1658 | Door frame and leaf installation | 4 days | Wed 15/12/27 | Sat 18/12/27 |
| 1518 | 1659 | Kitchen appliance | 4 days | Mon 20/12/27 | Thu 23/12/27 |
| 1519 | 1660 | M&E final fix | 4 days | Fri 24/12/27 | Wed 29/12/27 |
| 1520 | **572** | **Level 38** | **70 days** | **Sat 23/10/27** | **Sat 15/01/28** |
| 1521 | 1661 | Structural clearance | 5 days | Sat 23/10/27 | Thu 28/10/27 |
| 1522 | 1662 | RC Kerb | 5 days | Sat 30/10/27 | Thu 04/11/27 |
| 1523 | 1663 | PC Panel/Drywall | 5 days | Fri 05/11/27 | Wed 10/11/27 |
| 1524 | 1664 | MEP 1st fix | 9 days | Mon 08/11/27 | Wed 17/11/27 |
| 1525 | 1665 | Waterproofing | 4 days | Sat 13/11/27 | Wed 17/11/27 |
| 1526 | 1666 | Window frame | 2 days | Thu 18/11/27 | Fri 19/11/27 |
| 1527 | 1667 | Door sub-frame installation | 2 days | Thu 18/11/27 | Fri 19/11/27 |
| 1528 | 1668 | Floor screeding | 5 days | Sat 20/11/27 | Thu 25/11/27 |
| 1529 | 1669 | Plaster and skim coat | 7 days | Wed 24/11/27 | Wed 01/12/27 |
| 1530 | 1670 | Railing installation | 3 days | Thu 02/12/27 | Sat 04/12/27 |
| 1531 | 1671 | Tiling | 7 days | Thu 02/12/27 | Thu 09/12/27 |
| 1532 | 1672 | Shower screen L angle | 1 day | Thu 02/12/27 | Thu 02/12/27 |
| 1533 | 1673 | Ceiling frame and board | 7 days | Fri 10/12/27 | Fri 17/12/27 |
| 1534 | 1674 | Wardrobe | 5 days | Sat 18/12/27 | Thu 23/12/27 |
| 1535 | 1675 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Sat 18/12/27 | Thu 23/12/27 |
| 1536 | 1676 | Engineered Timber Flooring | 5 days | Mon 20/12/27 | Fri 24/12/27 |
| 1537 | 1677 | Painting (sealer) | 5 days | Mon 27/12/27 | Fri 31/12/27 |
| 1538 | 1678 | Shower screen installation | 4 days | Mon 03/01/28 | Thu 06/01/28 |

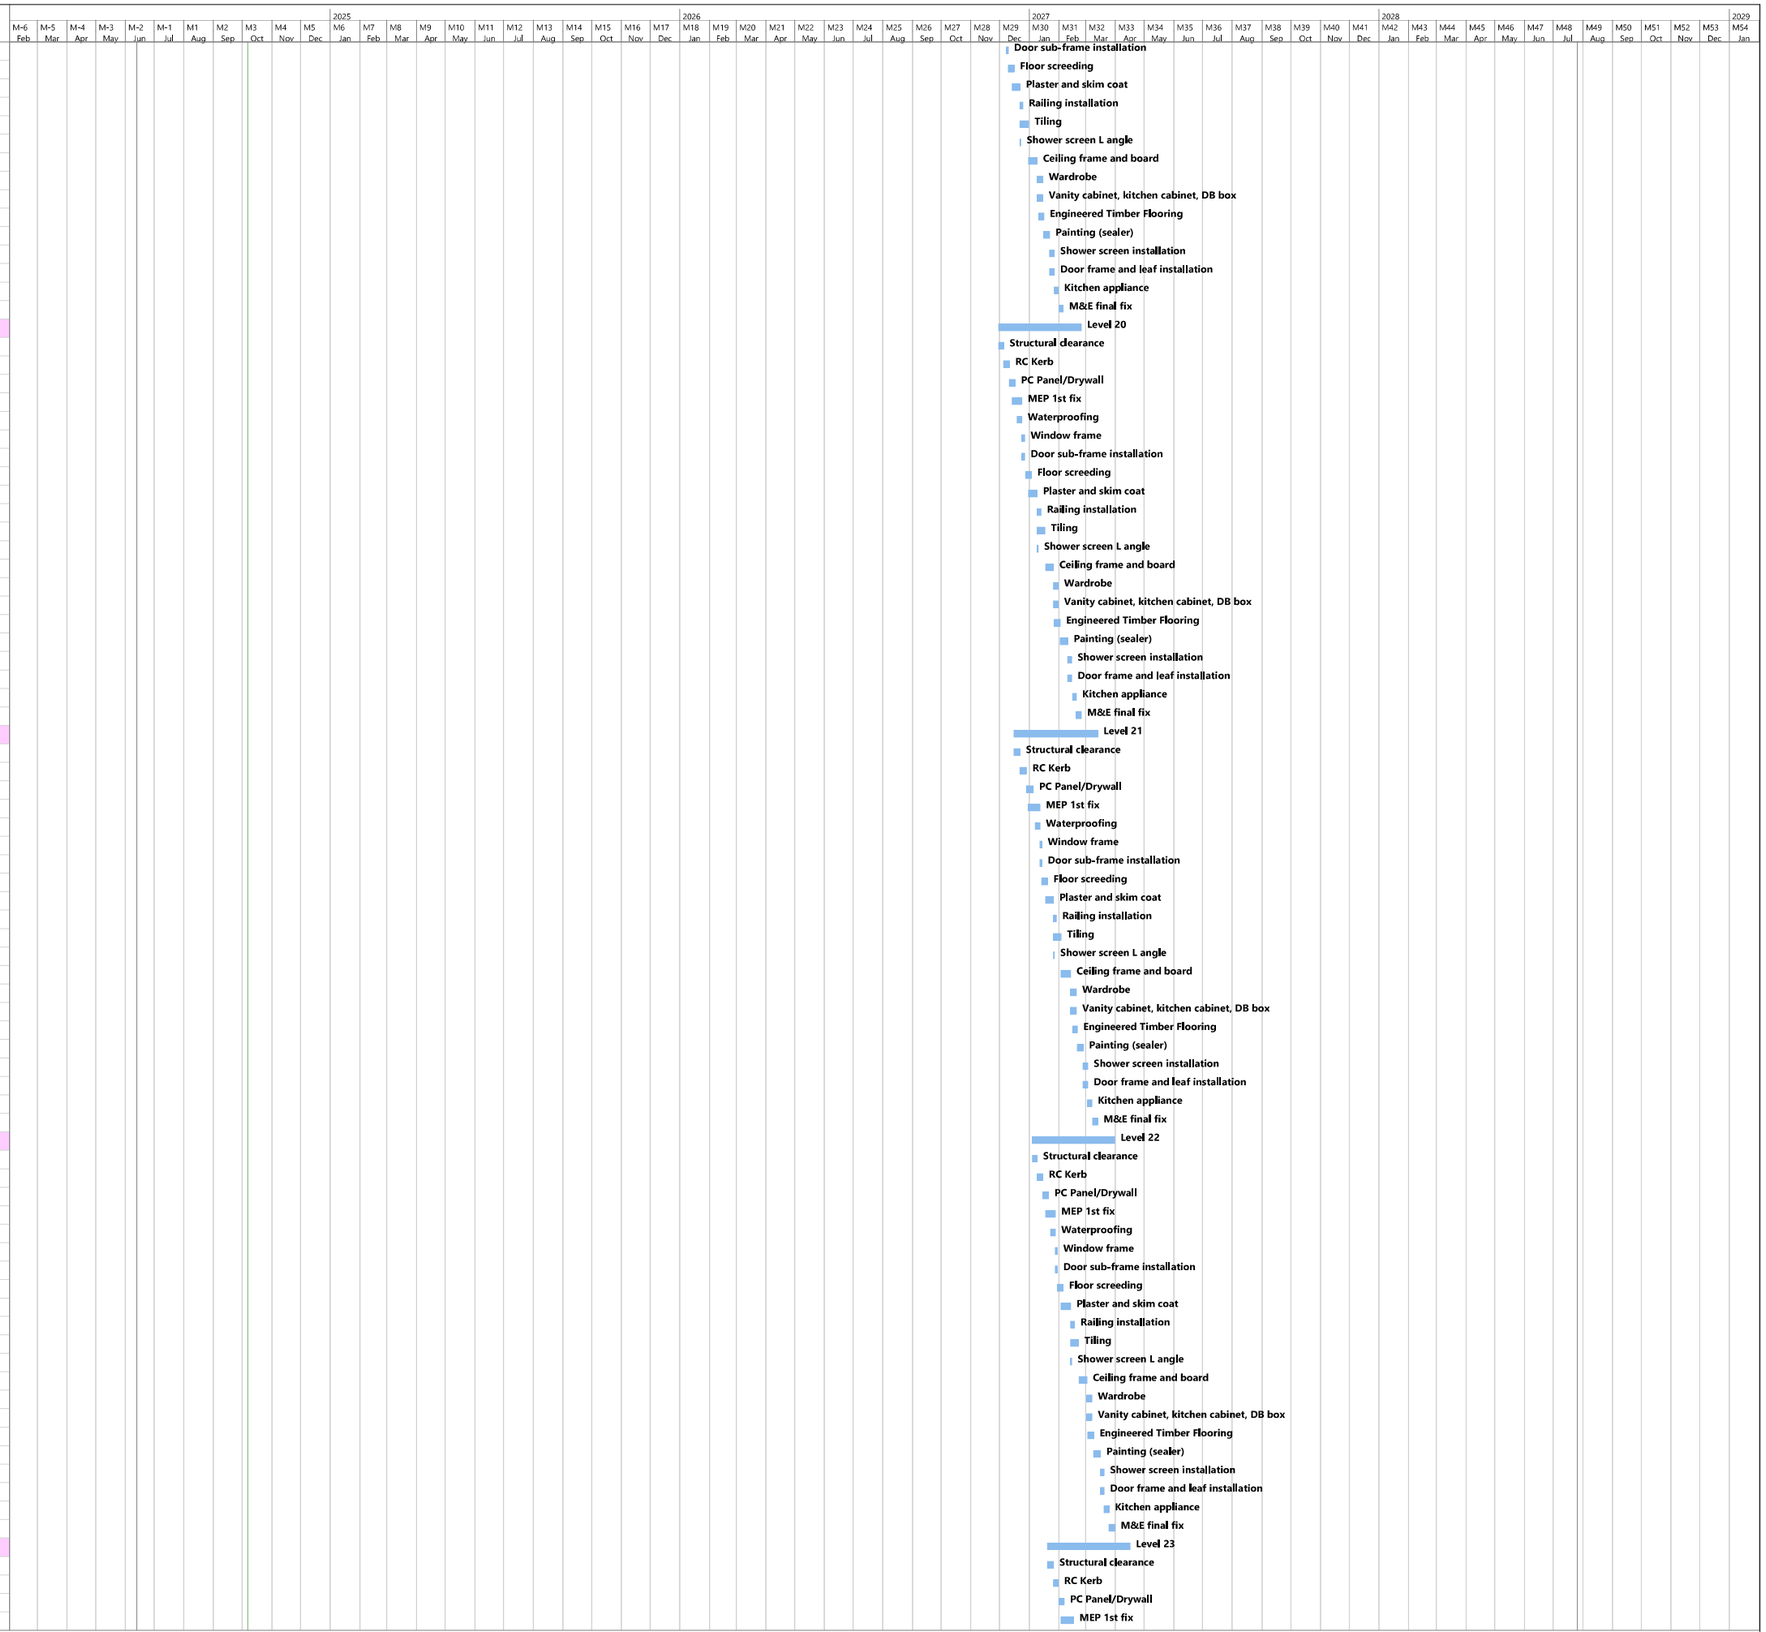


Project: Central Mall - Master P
Date: Mon 07/10/24

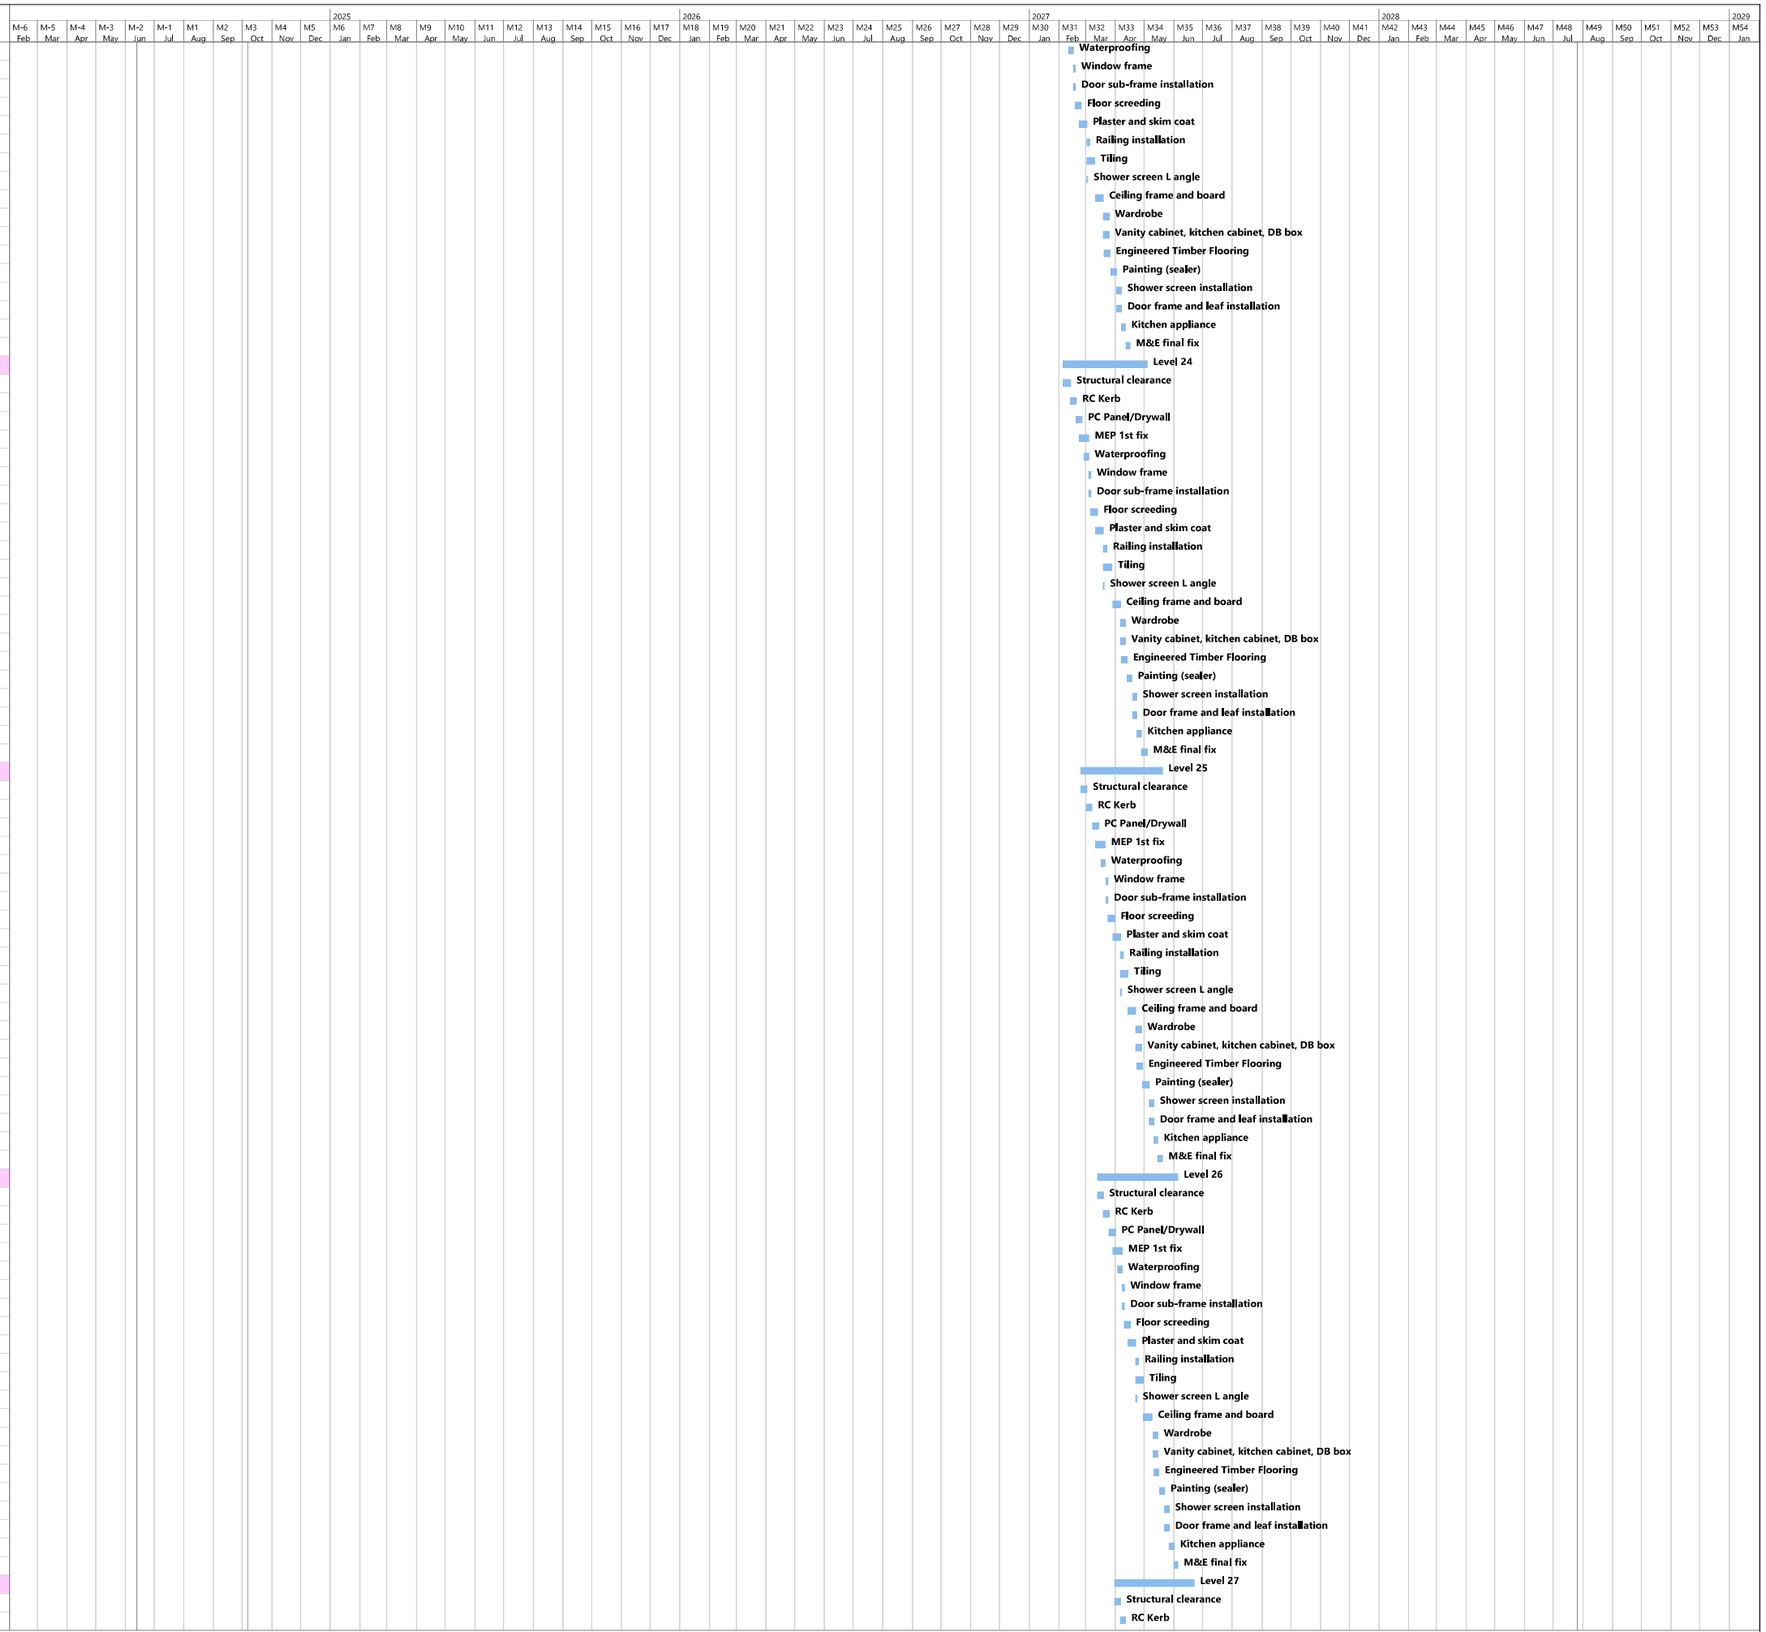Task · Split · Milestone · Summary · Project Summary · Inactive Task · Inactive Milestone · Inactive Summary · Manual Task · Duration-only · Manual Summary Rollup · Manual Summary · Start-only · Finish-only · External Tasks · External Milestone · Deadline · Critical · Critical Split · Progress · Manual Progress
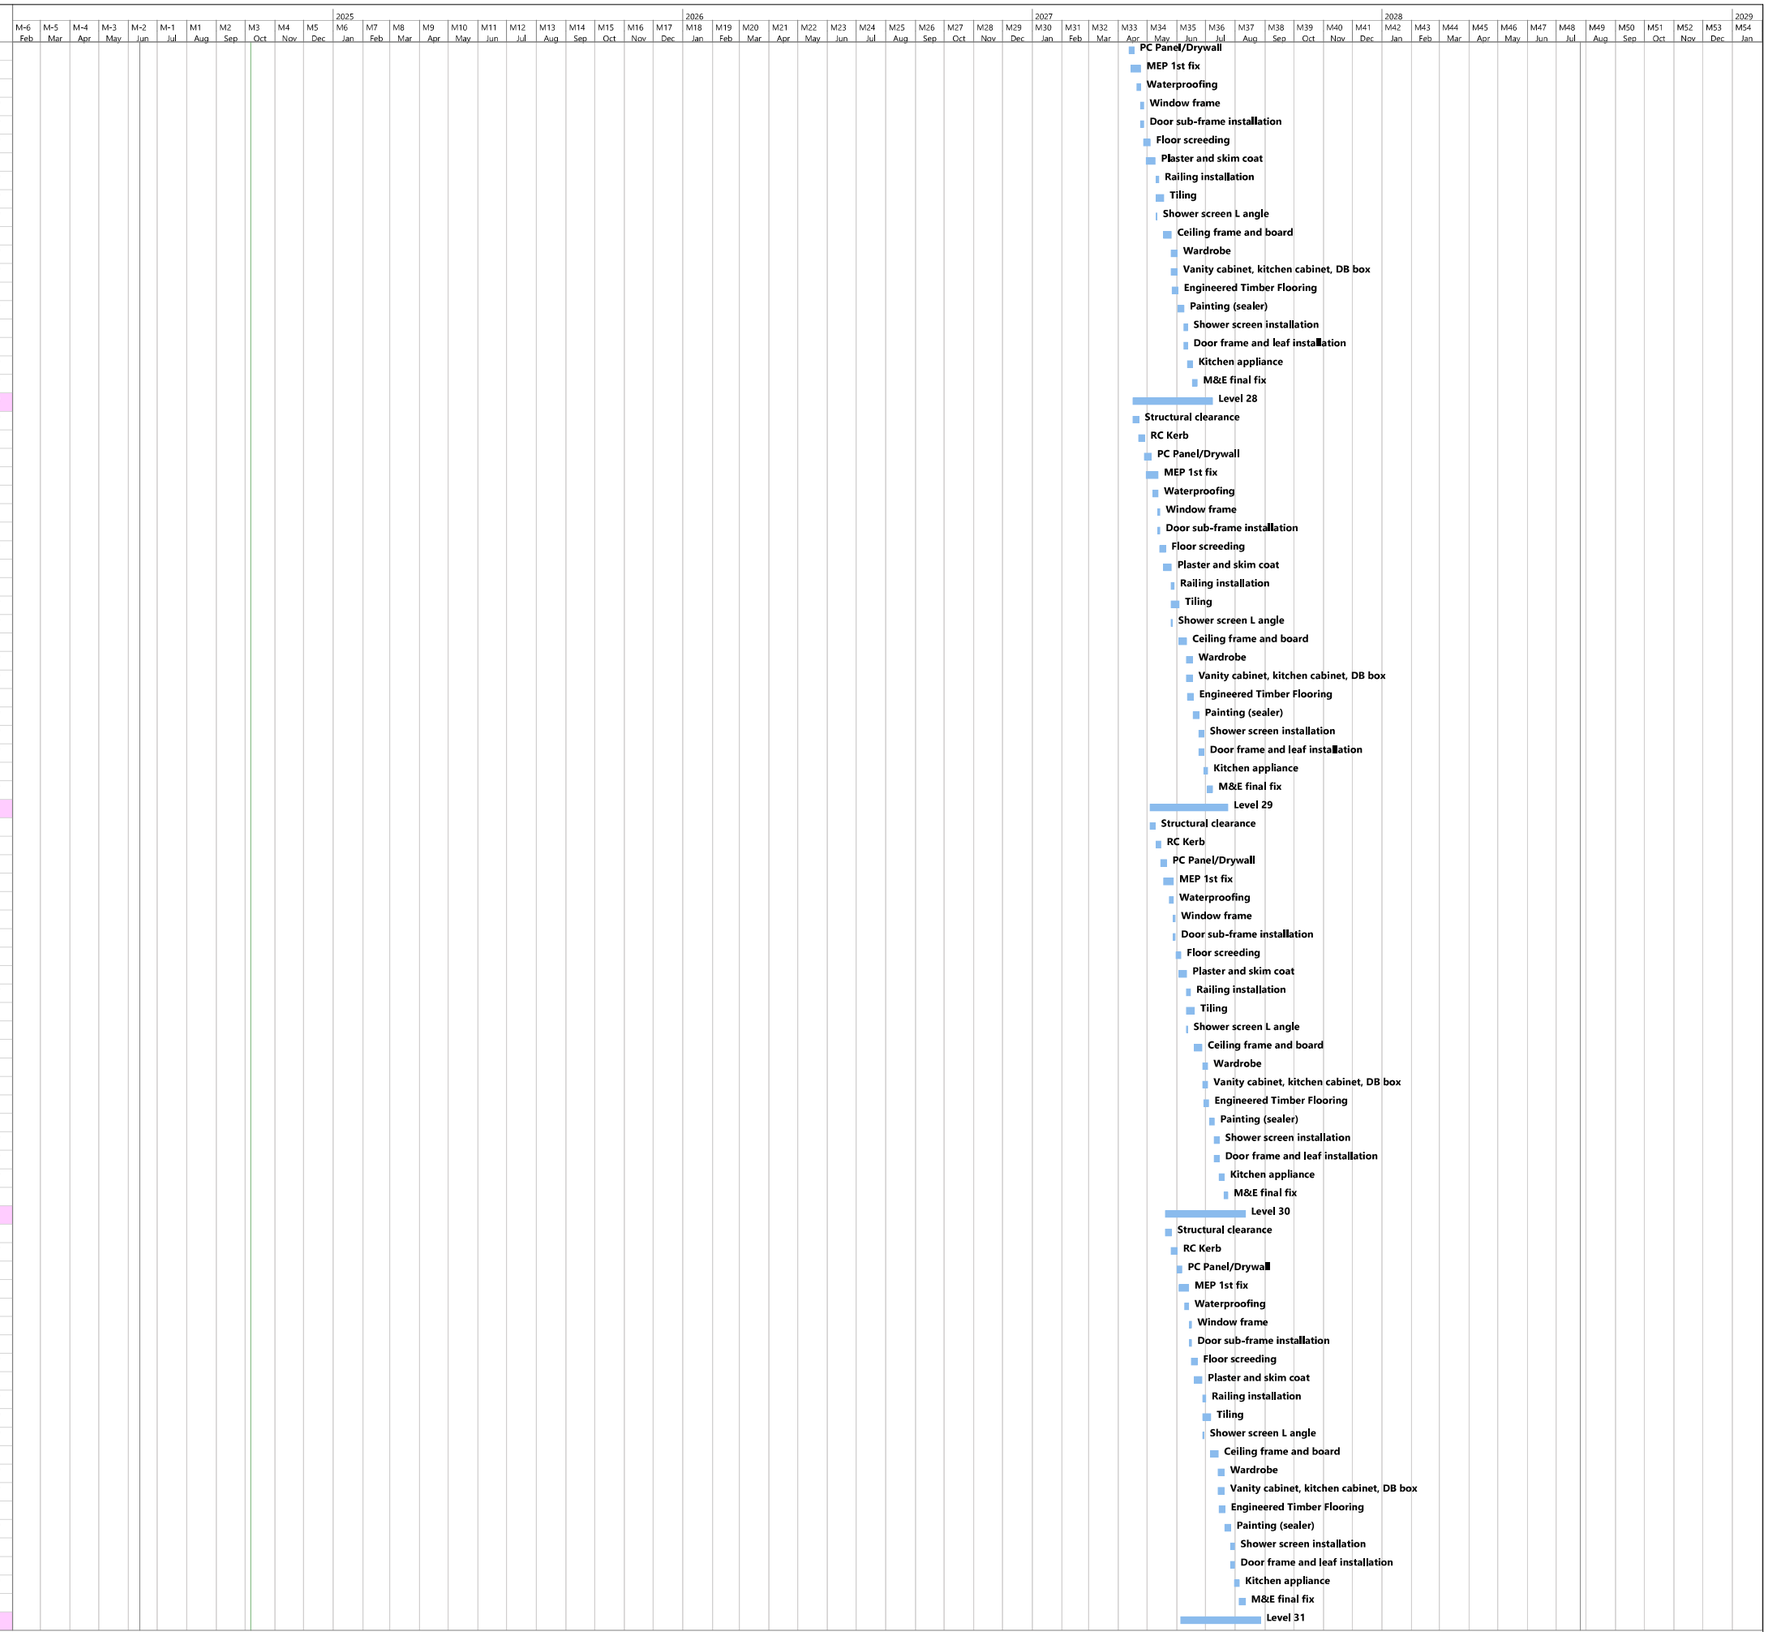
| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 1539 | 1679 | Door frame and leaf installation | 4 days | Mon 03/01/28 | Thu 06/01/28 |
| 1540 | 1680 | Kitchen appliance | 4 days | Fri 07/01/28 | Tue 11/01/28 |
| 1541 | 1681 | M&E final fix | 4 days | Wed 12/01/28 | Sat 15/01/28 |
| 1542 | **573** | **Level 39** | **70 days** | **Wed 10/11/27** | **Thu 03/02/28** |
| 1543 | 1682 | Structural clearance | 5 days | Wed 10/11/27 | Mon 15/11/27 |
| 1544 | 1683 | RC Kerb | 5 days | Tue 16/11/27 | Sat 20/11/27 |
| 1545 | 1684 | PC Panel/Drywall | 5 days | Mon 22/11/27 | Fri 26/11/27 |
| 1546 | 1685 | MEP 1st fix | 9 days | Wed 24/11/27 | Fri 03/12/27 |
| 1547 | 1686 | Waterproofing | 4 days | Tue 30/11/27 | Fri 03/12/27 |
| 1548 | 1687 | Window frame | 2 days | Sat 04/12/27 | Mon 06/12/27 |
| 1549 | 1688 | Door sub-frame installation | 2 days | Sat 04/12/27 | Mon 06/12/27 |
| 1550 | 1689 | Floor screeding | 5 days | Tue 07/12/27 | Sat 11/12/27 |
| 1551 | 1690 | Plaster and skim coat | 7 days | Fri 10/12/27 | Fri 17/12/27 |
| 1552 | 1691 | Railing installation | 3 days | Sat 18/12/27 | Tue 21/12/27 |
| 1553 | 1692 | Tiling | 7 days | Sat 18/12/27 | Mon 27/12/27 |
| 1554 | 1693 | Shower screen L angle | 1 day | Sat 18/12/27 | Sat 18/12/27 |
| 1555 | 1694 | Ceiling frame and board | 7 days | Tue 28/12/27 | Wed 05/01/28 |
| 1556 | 1695 | Wardrobe | 5 days | Thu 06/01/28 | Tue 11/01/28 |
| 1557 | 1696 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Thu 06/01/28 | Tue 11/01/28 |
| 1558 | 1697 | Engineered Timber Flooring | 5 days | Fri 07/01/28 | Wed 12/01/28 |
| 1559 | 1698 | Painting (sealer) | 5 days | Thu 13/01/28 | Tue 18/01/28 |
| 1560 | 1699 | Shower screen installation | 4 days | Wed 19/01/28 | Sat 22/01/28 |
| 1561 | 1700 | Door frame and leaf installation | 4 days | Wed 19/01/28 | Sat 22/01/28 |
| 1562 | 1701 | Kitchen appliance | 4 days | Mon 24/01/28 | Sat 29/01/28 |
| 1563 | 1702 | M&E final fix | 4 days | Mon 31/01/28 | Thu 03/02/28 |
| 1564 | **574** | **Level 40** | **70 days** | **Wed 10/11/27** | **Thu 03/02/28** |
| 1565 | 1703 | Structural clearance | 5 days | Wed 10/11/27 | Mon 15/11/27 |
| 1566 | 1704 | RC Kerb | 5 days | Tue 16/11/27 | Sat 20/11/27 |
| 1567 | 1705 | PC Panel/Drywall | 5 days | Mon 22/11/27 | Fri 26/11/27 |
| 1568 | 1706 | MEP 1st fix | 9 days | Wed 24/11/27 | Fri 03/12/27 |
| 1569 | 1707 | Waterproofing | 4 days | Tue 30/11/27 | Fri 03/12/27 |
| 1570 | 1708 | Window frame | 2 days | Sat 04/12/27 | Mon 06/12/27 |
| 1571 | 1709 | Door sub-frame installation | 2 days | Sat 04/12/27 | Mon 06/12/27 |
| 1572 | 1710 | Floor screeding | 5 days | Tue 07/12/27 | Sat 11/12/27 |
| 1573 | 1711 | Plaster and skim coat | 7 days | Fri 10/12/27 | Fri 17/12/27 |
| 1574 | 1712 | Railing installation | 3 days | Sat 18/12/27 | Tue 21/12/27 |
| 1575 | 1713 | Tiling | 7 days | Sat 18/12/27 | Mon 27/12/27 |
| 1576 | 1714 | Shower screen L angle | 1 day | Sat 18/12/27 | Sat 18/12/27 |
| 1577 | 1715 | Ceiling frame and board | 7 days | Tue 28/12/27 | Wed 05/01/28 |
| 1578 | 1716 | Wardrobe | 5 days | Thu 06/01/28 | Tue 11/01/28 |
| 1579 | 1717 | Vanity cabinet, kitchen cabinet, DB box | 5 days | Thu 06/01/28 | Tue 11/01/28 |
| 1580 | 1718 | Engineered Timber Flooring | 5 days | Fri 07/01/28 | Wed 12/01/28 |
| 1581 | 1719 | Painting (sealer) | 5 days | Thu 13/01/28 | Tue 18/01/28 |
| 1582 | 1720 | Shower screen installation | 4 days | Wed 19/01/28 | Sat 22/01/28 |
| 1583 | 1721 | Door frame and leaf installation | 4 days | Wed 19/01/28 | Sat 22/01/28 |
| 1584 | 1722 | Kitchen appliance | 4 days | Mon 24/01/28 | Sat 29/01/28 |
| 1585 | 1723 | M&E final fix | 4 days | Mon 31/01/28 | Thu 03/02/28 |
| 1586 | **575** | **LRF** | **50 days** | **Wed 10/11/27** | **Sat 08/01/28** |
| 1587 | **576** | **URF** | **45 days** | **Mon 10/01/28** | **Sat 04/03/28** |
| 1588 | **218** | **Common Area Finishes (Lift Lobbies + Staircase)** | **564 days** | **Mon 06/04/26** | **Sat 12/02/28** |
| 1589 | **684** | **Retail** | **110 days** | **Sat 15/05/27** | **Tue 21/09/27** |
| 1590 | 683 | Basement 1 | 50 days | Sat 15/05/27 | Mon 12/07/27 |
| 1591 | 691 | Basement 2 | 50 days | Wed 02/06/27 | Thu 29/07/27 |
| 1592 | 690 | L1 | 50 days | Sat 19/06/27 | Tue 17/08/27 |
| 1593 | 692 | L2 | 50 days | Wed 07/07/27 | Fri 03/09/27 |
| 1594 | 682 | L3 | 50 days | Sat 24/07/27 | Tue 21/09/27 |
| 1595 | **680** | **Residential** | **564 days** | **Mon 06/04/26** | **Sat 12/02/28** |
| 1596 | 689 | Basement 1 | 60 days | Tue 13/07/27 | Tue 21/09/27 |
| 1597 | 688 | Basement 2 | 60 days | Fri 30/07/27 | Fri 08/10/27 |
| 1598 | 687 | L1 | 60 days | Wed 18/08/27 | Tue 26/10/27 |
| 1599 | 686 | L2 | 60 days | Sat 04/09/27 | Sat 13/11/27 |
| 1600 | 685 | L3 | 60 days | Wed 22/09/27 | Wed 01/12/27 |
| 1601 | 643 | L4 | 60 days | Mon 06/04/26 | Wed 17/06/26 |
| 1602 | 644 | L5 | 60 days | Wed 22/04/26 | Fri 03/07/26 |
| 1603 | 645 | L6 | 60 days | Sat 09/05/26 | Mon 20/07/26 |
| 1604 | 646 | L7 | 60 days | Tue 26/05/26 | Wed 05/08/26 |
| 1605 | 647 | L8 | 60 days | Sat 13/06/26 | Sat 22/08/26 |
| 1606 | 648 | L9 | 60 days | Tue 30/06/26 | Tue 08/09/26 |
| 1607 | 649 | L10 | 60 days | Thu 16/07/26 | Thu 24/09/26 |
| 1608 | 650 | L11 | 60 days | Sat 01/08/26 | Sat 10/10/26 |
| 1609 | 651 | L12 | 60 days | Wed 19/08/26 | Tue 27/10/26 |
| 1610 | 652 | L13 | 60 days | Fri 04/09/26 | Fri 13/11/26 |
| 1611 | 653 | L14 | 60 days | Mon 21/09/26 | Mon 30/11/26 |
| 1612 | 654 | L15 | 60 days | Wed 07/10/26 | Wed 16/12/26 |
| 1613 | 655 | L16 | 60 days | Fri 23/10/26 | Mon 04/01/27 |
| 1614 | 656 | L17 | 60 days | Tue 10/11/26 | Wed 20/01/27 |
| 1615 | 657 | L18 | 60 days | Thu 26/11/26 | Fri 05/02/27 |
| 1616 | 658 | L19 | 60 days | Sat 12/12/26 | Wed 24/02/27 |
| 1617 | 659 | L20 | 60 days | Wed 30/12/26 | Sat 13/03/27 |
| 1618 | 660 | L21 | 60 days | Sat 16/01/27 | Wed 31/03/27 |
| 1619 | 661 | L22 | 60 days | Tue 02/02/27 | Fri 16/04/27 |
| 1620 | 662 | L23 | 60 days | Sat 20/02/27 | Tue 04/05/27 |
| 1621 | 663 | L24 | 60 days | Tue 09/03/27 | Thu 20/05/27 |
| 1622 | 664 | L25 | 60 days | Sat 27/03/27 | Sat 05/06/27 |
| 1623 | 665 | L26 | 60 days | Tue 13/04/27 | Tue 22/06/27 |
| 1624 | 666 | L27 | 60 days | Thu 29/04/27 | Thu 08/07/27 |

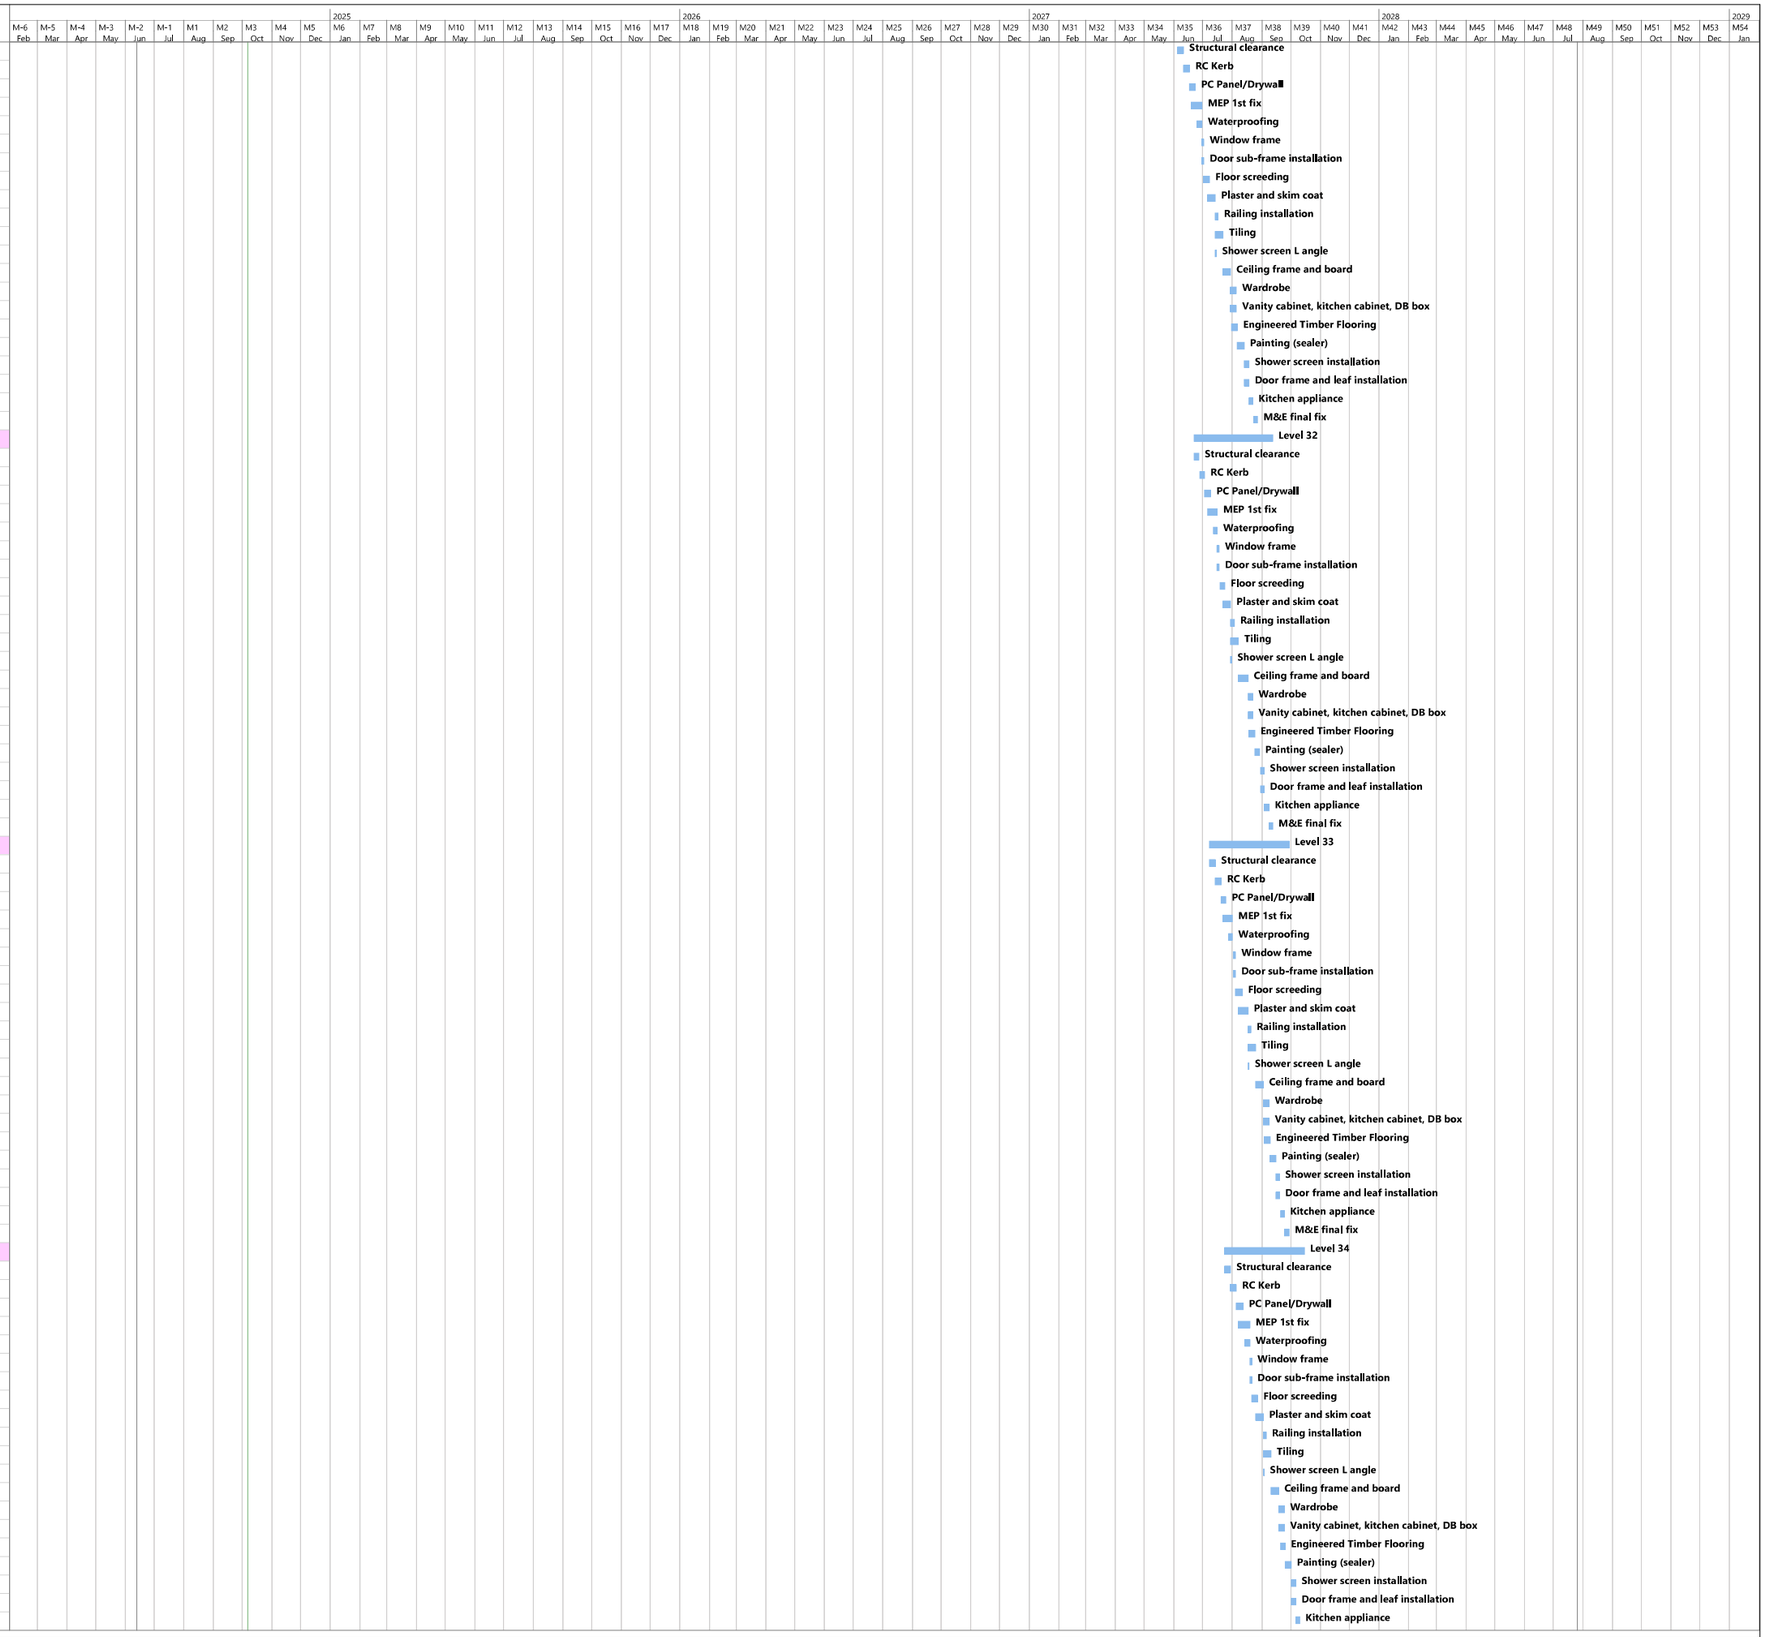

| ID | Unique ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 1625 | 667 | L28 | 60 days | Mon 17/05/27 | Sat 24/07/27 |
| 1626 | 668 | L29 | 60 days | Wed 02/06/27 | Wed 11/08/27 |
| 1627 | 669 | L30 | 60 days | Fri 18/06/27 | Fri 27/08/27 |
| 1628 | 670 | L31 | 60 days | Mon 05/07/27 | Mon 13/09/27 |
| 1629 | 671 | L32 | 60 days | Wed 21/07/27 | Wed 29/09/27 |
| 1630 | 672 | L33 | 60 days | Fri 06/08/27 | Fri 15/10/27 |
| 1631 | 673 | L34 | 60 days | Tue 24/08/27 | Tue 02/11/27 |
| 1632 | 674 | L35 | 60 days | Thu 09/09/27 | Thu 18/11/27 |
| 1633 | 675 | L36 | 60 days | Sat 25/09/27 | Sat 04/12/27 |
| 1634 | 676 | L37 | 60 days | Tue 12/10/27 | Tue 21/12/27 |
| 1635 | 677 | L38 | 60 days | Thu 28/10/27 | Sat 08/01/28 |
| 1636 | 678 | L39 | 60 days | Mon 15/11/27 | Tue 25/01/28 |
| 1637 | 679 | L40 | 60 days | Wed 01/12/27 | Sat 12/02/28 |
| 1638 | **219** | **External Finishes and Landscape** | **140 days** | **Sat 13/11/27** | **Tue 02/05/28** |
| 1639 | 694 | Level 1 | 75 days | Sat 13/11/27 | Sat 12/02/28 |
| 1640 | 693 | Level 2 | 75 days | Fri 31/12/27 | Fri 31/03/28 |
| 1641 | 695 | Level 3 | 75 days | Wed 02/02/28 | Tue 02/05/28 |
| 1642 | **220** | **Public Contribution (External works)** | **318 days** | **Tue 15/12/26** | **Fri 31/12/27** |
| 1643 | 697 | Road Improvement - Road Juction 1 (upper cross st./Chin Swee Rd), Junction 2 (Havelock Rd./New Bridge Rd.) & Junction 3 (Merchant | 168 days | Tue 15/12/26 | Tue 06/07/27 |
| 1644 | 696 | Refurbishment of existing POB | 241 days | Tue 15/12/26 | Thu 30/09/27 |
| 1645 | 898 | New Bus Stop at Havelock road + New Shared track | 150 days | Wed 07/07/27 | Fri 31/12/27 |
| 1646 | **724** | **Inspection** | **918 days** | **Sat 28/06/25** | **Sat 08/07/28** |
| 1647 | **725** | **Storey Shelter Inspection** | **62 days** | **Fri 04/02/28** | **Tue 18/04/28** |
| 1648 | 726 | Pre-commissioning Inspection | 60 days | Fri 04/02/28 | Sat 15/04/28 |
| 1649 | 727 | USR Commissioning Inspection | 2 days | Mon 17/04/28 | Tue 18/04/28 |
| 1650 | **737** | **CONQUAS Inspection Works** | **335 days** | **Wed 24/02/27** | **Fri 31/03/28** |
| 1651 | 738 | Waterponding & Waterproofing Test (incl planter boxes) | 305 days | Wed 24/02/27 | Thu 24/02/28 |
| 1652 | 739 | Tiles Pull-out Test | 70 days | Sat 08/05/27 | Wed 28/07/27 |
| 1653 | 740 | Window Watertightness Test | 160 days | Tue 25/05/27 | Mon 29/11/27 |
| 1654 | 741 | Lift Lobbies Assessment | 90 days | Fri 19/11/27 | Wed 08/03/28 |
| 1655 | 742 | Internal Finishes Assessment | 220 days | Wed 26/05/27 | Sat 12/02/28 |
| 1656 | 743 | External Wall | 60 days | Mon 13/12/27 | Thu 24/02/28 |
| 1657 | 744 | External Works | 60 days | Fri 31/12/27 | Tue 14/03/28 |
| 1658 | 745 | M&E Assessment | 60 days | Wed 19/01/28 | Fri 31/03/28 |
| 1659 | **746** | **QM Inspection Works** | **150 days** | **Sat 16/10/27** | **Sat 15/04/28** |
| 1660 | 747 | USR | 150 days | Sat 16/10/27 | Sat 15/04/28 |
| 1661 | **757** | **CSO Inspection Works** | **150 days** | **Tue 16/11/27** | **Thu 18/05/28** |
| 1662 | 758 | USR | 150 days | Tue 16/11/27 | Thu 18/05/28 |
| 1663 | 1971 | SSPG Services/Power Grid | 100 days | Wed 19/01/28 | Mon 22/05/28 |
| 1664 | 1970 | NEA - MV, PWCS and TNIA | 100 days | Wed 01/12/27 | Fri 31/03/28 |
| 1665 | 1972 | PBU - Sanitary Department | 75 days | Sat 26/02/28 | Mon 29/05/28 |
| 1666 | 1994 | LTA - Road | 70 days | Thu 02/12/27 | Fri 25/02/28 |
| 1667 | **1969** | **GM Assessment** | **918 days** | **Sat 28/06/25** | **Sat 08/07/28** |
| 1668 | 1974 | USR Green Mark Documents & Pre-Assessment | 780 days | Sat 28/06/25 | Fri 21/01/28 |
| 1669 | 1973 | USR Green Mark Assessment & Verification | 138 days | Sat 22/01/28 | Sat 08/07/28 |
| 1670 | **718** | **Temporary Occupation Permit (TOP)** | **152 days** | **Sat 22/01/28** | **Tue 25/07/28** |
| 1671 | 698 | M&E Final Testing & Commissioning | 45 days | Sat 22/01/28 | Fri 17/03/28 |
| 1672 | 699 | Pre M&E RI Inspection | 14 days | Sat 18/03/28 | Mon 03/04/28 |
| 1673 | 700 | M&E RI Inspection | 2 days | Tue 04/04/28 | Wed 05/04/28 |
| 1674 | 701 | M&E Rectification works | 12 days | Thu 06/04/28 | Thu 20/04/28 |
| 1675 | 702 | M&E RI Final Inspection | 2 days | Fri 21/04/28 | Sat 22/04/28 |
| 1676 | 703 | Pre Architectural RI Inspection | 2 days | Sat 01/04/28 | Mon 03/04/28 |
| 1677 | 704 | Architectural RI Inspection | 14 days | Tue 04/04/28 | Thu 20/04/28 |
| 1678 | 705 | Architectural Rectification Works | 12 days | Fri 21/04/28 | Sat 06/05/28 |
| 1679 | 706 | Architectural RI Final Inspection | 2 days | Mon 08/05/28 | Wed 10/05/28 |
| 1680 | 707 | CPBU Clearance (Including form C ) | 0 days | Tue 25/04/28 | Tue 25/04/28 |
| 1681 | 708 | RI Issue Form 2 | 3 days | Thu 11/05/28 | Sat 13/05/28 |
| 1682 | 709 | Consultant Internal Pre-TOP Inspection | 14 days | Fri 21/04/28 | Wed 10/05/28 |
| 1683 | 710 | BCA TOP 1st Inspection | 1 day | Thu 11/05/28 | Thu 11/05/28 |
| 1684 | 711 | TOP Rectification Works | 33 days | Fri 12/05/28 | Mon 19/06/28 |
| 1685 | 712 | BCA TOP 2nd Inspection | 1 day | Tue 20/06/28 | Tue 20/06/28 |
| 1686 | 713 | TOP Rectification Works | 15 days | Wed 21/06/28 | Fri 07/07/28 |
| 1687 | 714 | Green Mark Verification | 7 days | Fri 07/07/28 | Fri 14/07/28 |
| 1688 | 715 | TOP Lodgement | 14 days | Sat 08/07/28 | Mon 24/07/28 |
| 1689 | 716 | TOP Obtained / Completion Date | 1 day | Tue 25/07/28 | Tue 25/07/28 |

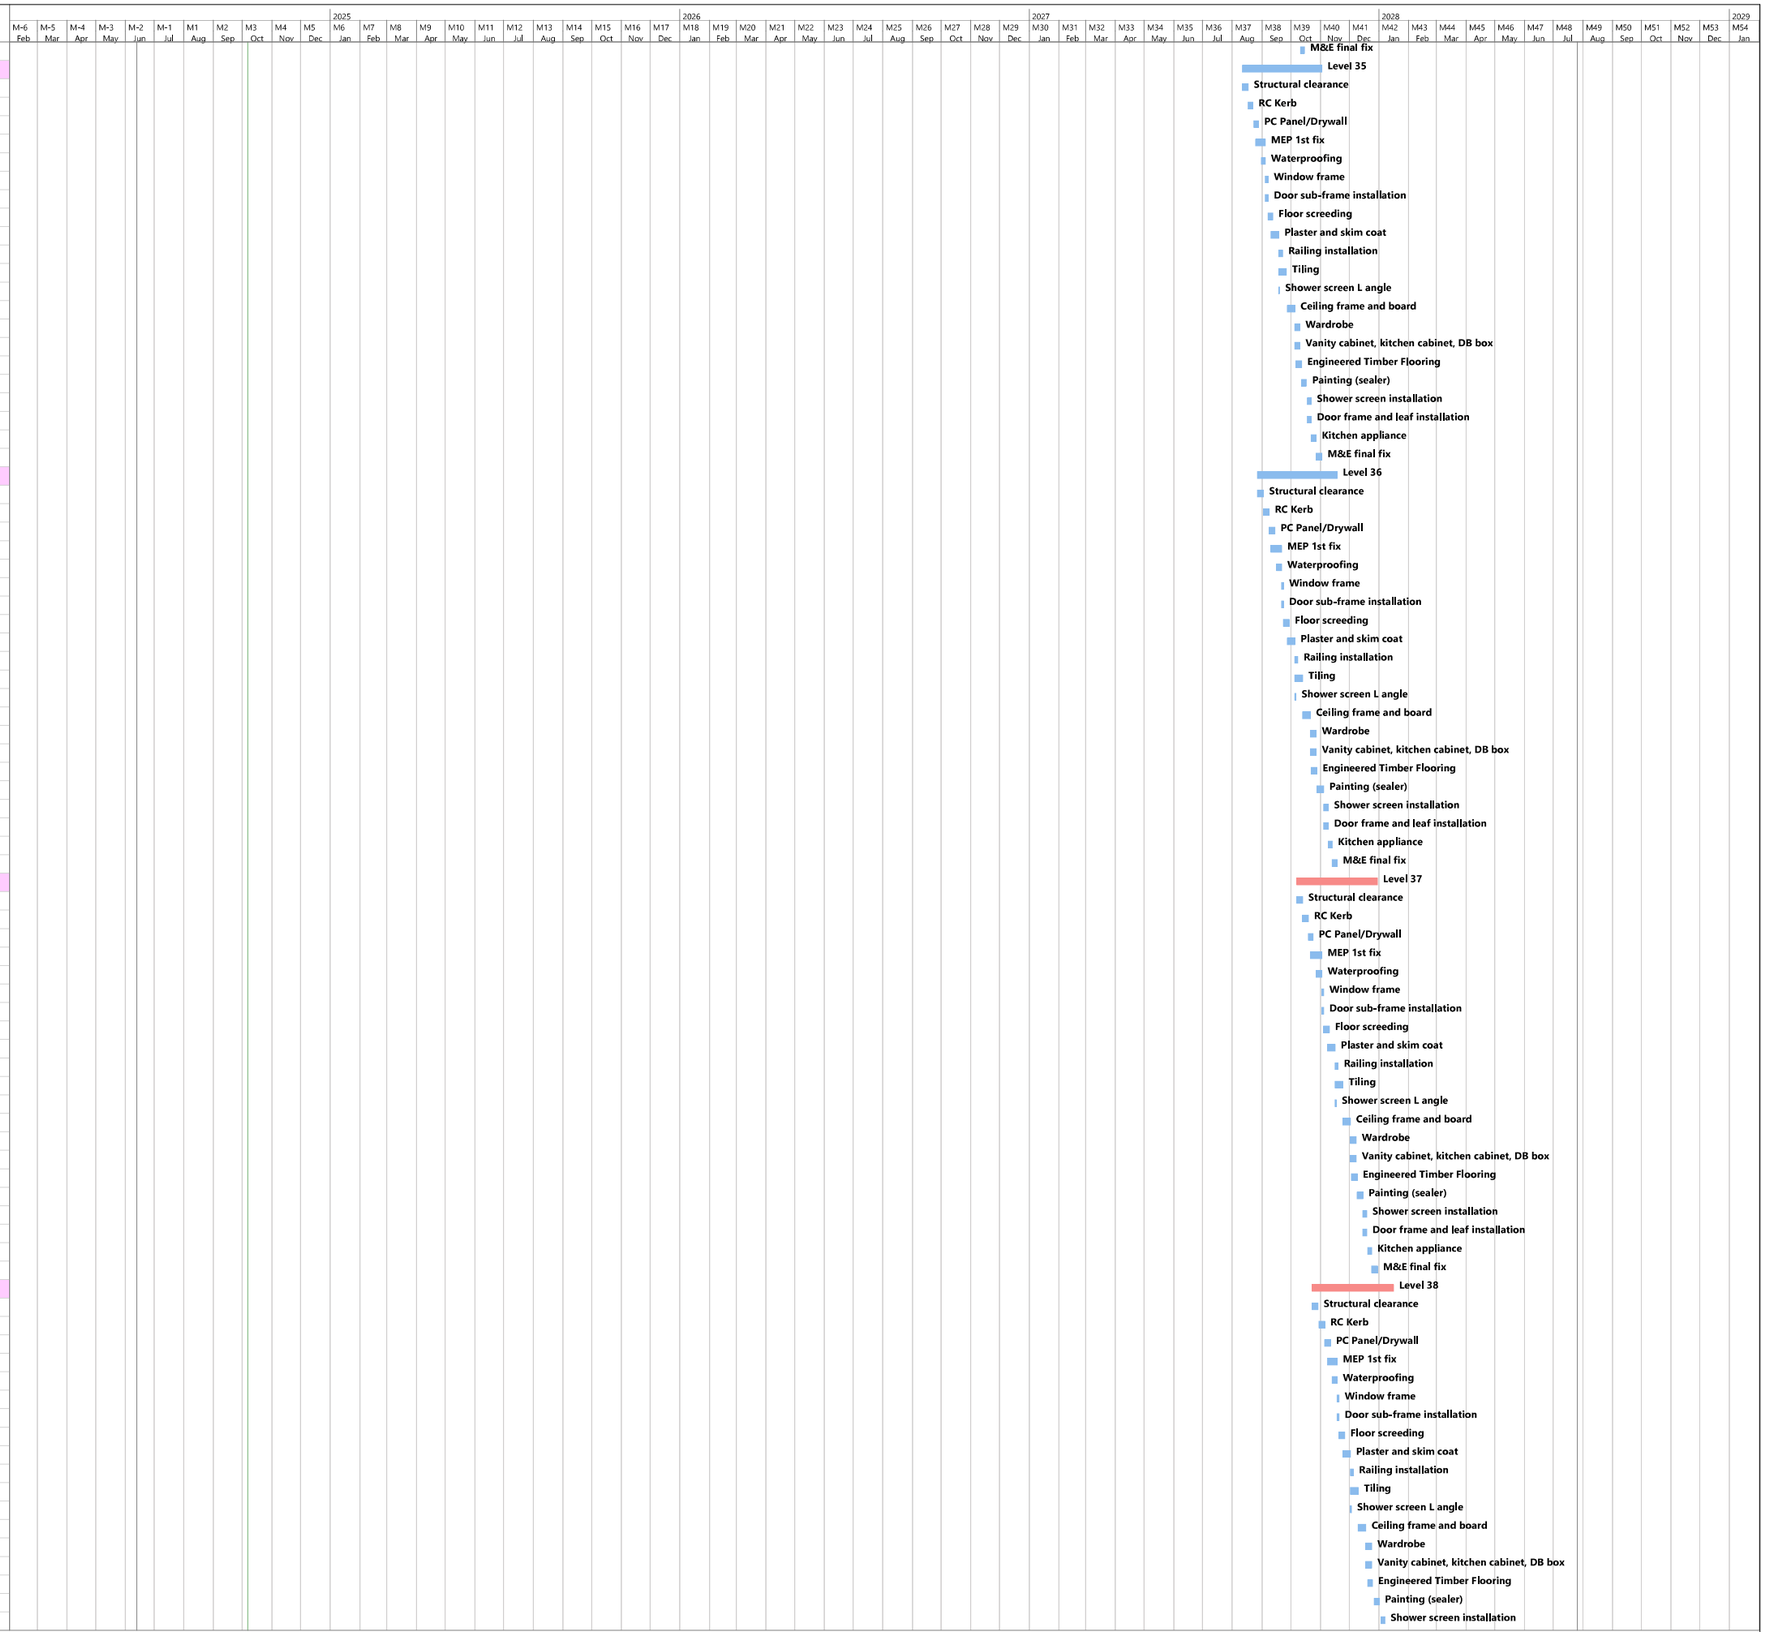

**SECTION 4**

**PROGRAMME**

## 4.2 Authority Submission Status for M&E Services – 1st Submission

| Service | Authority | Original Submission | | | Comments/Resubmission | | | Approval/ | | |
|---|---|---|---|---|---|---|---|---|---|---|
| | | Scheduled | Actual | Comment | Resubmit | Comment | Resubmit | Comment | Resubmit | Clearance |
| Application for Electricity Supply (USR & US1) | SP Services Ltd | Sep 2024 | 16 Sep 2024 | 17 Sep 2024 | 17 Sep 2024 | | | | | 23 Sep 2024 |
| Application for Electricity Supply (USC, US3, US5 & US7) | SP Services Ltd | Sep 2024 | 16 Sep 2024 | 18 Sep 2024 | 19 Sep 2024 | | | | | 25 Sep 2024 |
| Power Supply Substation (USR & US1) | SP PowerGrid Ltd | Dec 2024 | 26 Dec 2024 | | | | | | | |
| Power Supply Substation (USC, US3, US5 & US7) | SP PowerGrid Ltd | Dec 2024 | 6 Dec 2024 | 17 Dec 2024 | | | | | | |
| LT Reticulation | SP Services Ltd | | | | | | | | | |
| Sanitary Installation | PUB Water Reclamation (Network) Dept | 30 Sep 2025 (USR & US1) (USC, US3, US5 & US7) | 25 Nov 2025 (USR & US1) 4 Sep 2025 (USC, US3, US5 & US7) | 8 Dec 2025 (USR & US1) 18 Sep 2025 (USC, US3, US5 & US7) | 27 Jan 2026 (USR & US1) 3 Mar 2026 (USC, US3, US5 & US7) | | | | | 30 Jan 2026 (USR & US1) 23 Mar 2026 (USC, US3, US5 & US7) |
| Domestic Water Supply | PUB (Water Supply) Network Dept | 30 Sep 2025 | 9 Jul 2025 (USR & US1) 12 Jun 2025 (USC, US3, US5 & US7) | 9 Jul 2025 (USR & US1) 25 Jul 2025 (USC, US3, US5 & US7) | 26 Aug 2025 (USR & US1) 3 Sep 2025 (USC, US3, US5 & US7) | 2 Oct 2026 (USR & US1) | 2 Jan 2026 (USR & US1) | 8 Jan 2026 (USR & US1) | | 7 Feb 2026 (USR & US1) 31 Mar 2026 (USC, US3, US5 & US7) |
| Gas Supply Installation | City Energy Pte Ltd | 30 Sep 2025 (USR & US1) (USC, US3, US5 & US7) | 4 Feb 2026 (USR & US1) 2 Feb 2026 (USC, US3, US5 & US7) | 20 Feb 2026 (USR & US1) 23 Mar 2026 (USC, US3, US5 & US7) | 2 Apr 2026 (USR & US1) 10 Jun 2026 (USC, US3, US5 & US7) | 8 April 2026 (USR & US1) 12 Jun 2026 (USC, US3, US5 & US7) | 22 Apr 2026 (USR & US1) 9 Jul 2026 (USC, US3, US5 & US7) | | | 5 May 2026 (USR & US1) 16 Jul 2026 (USC, US3, US5 & US7) |
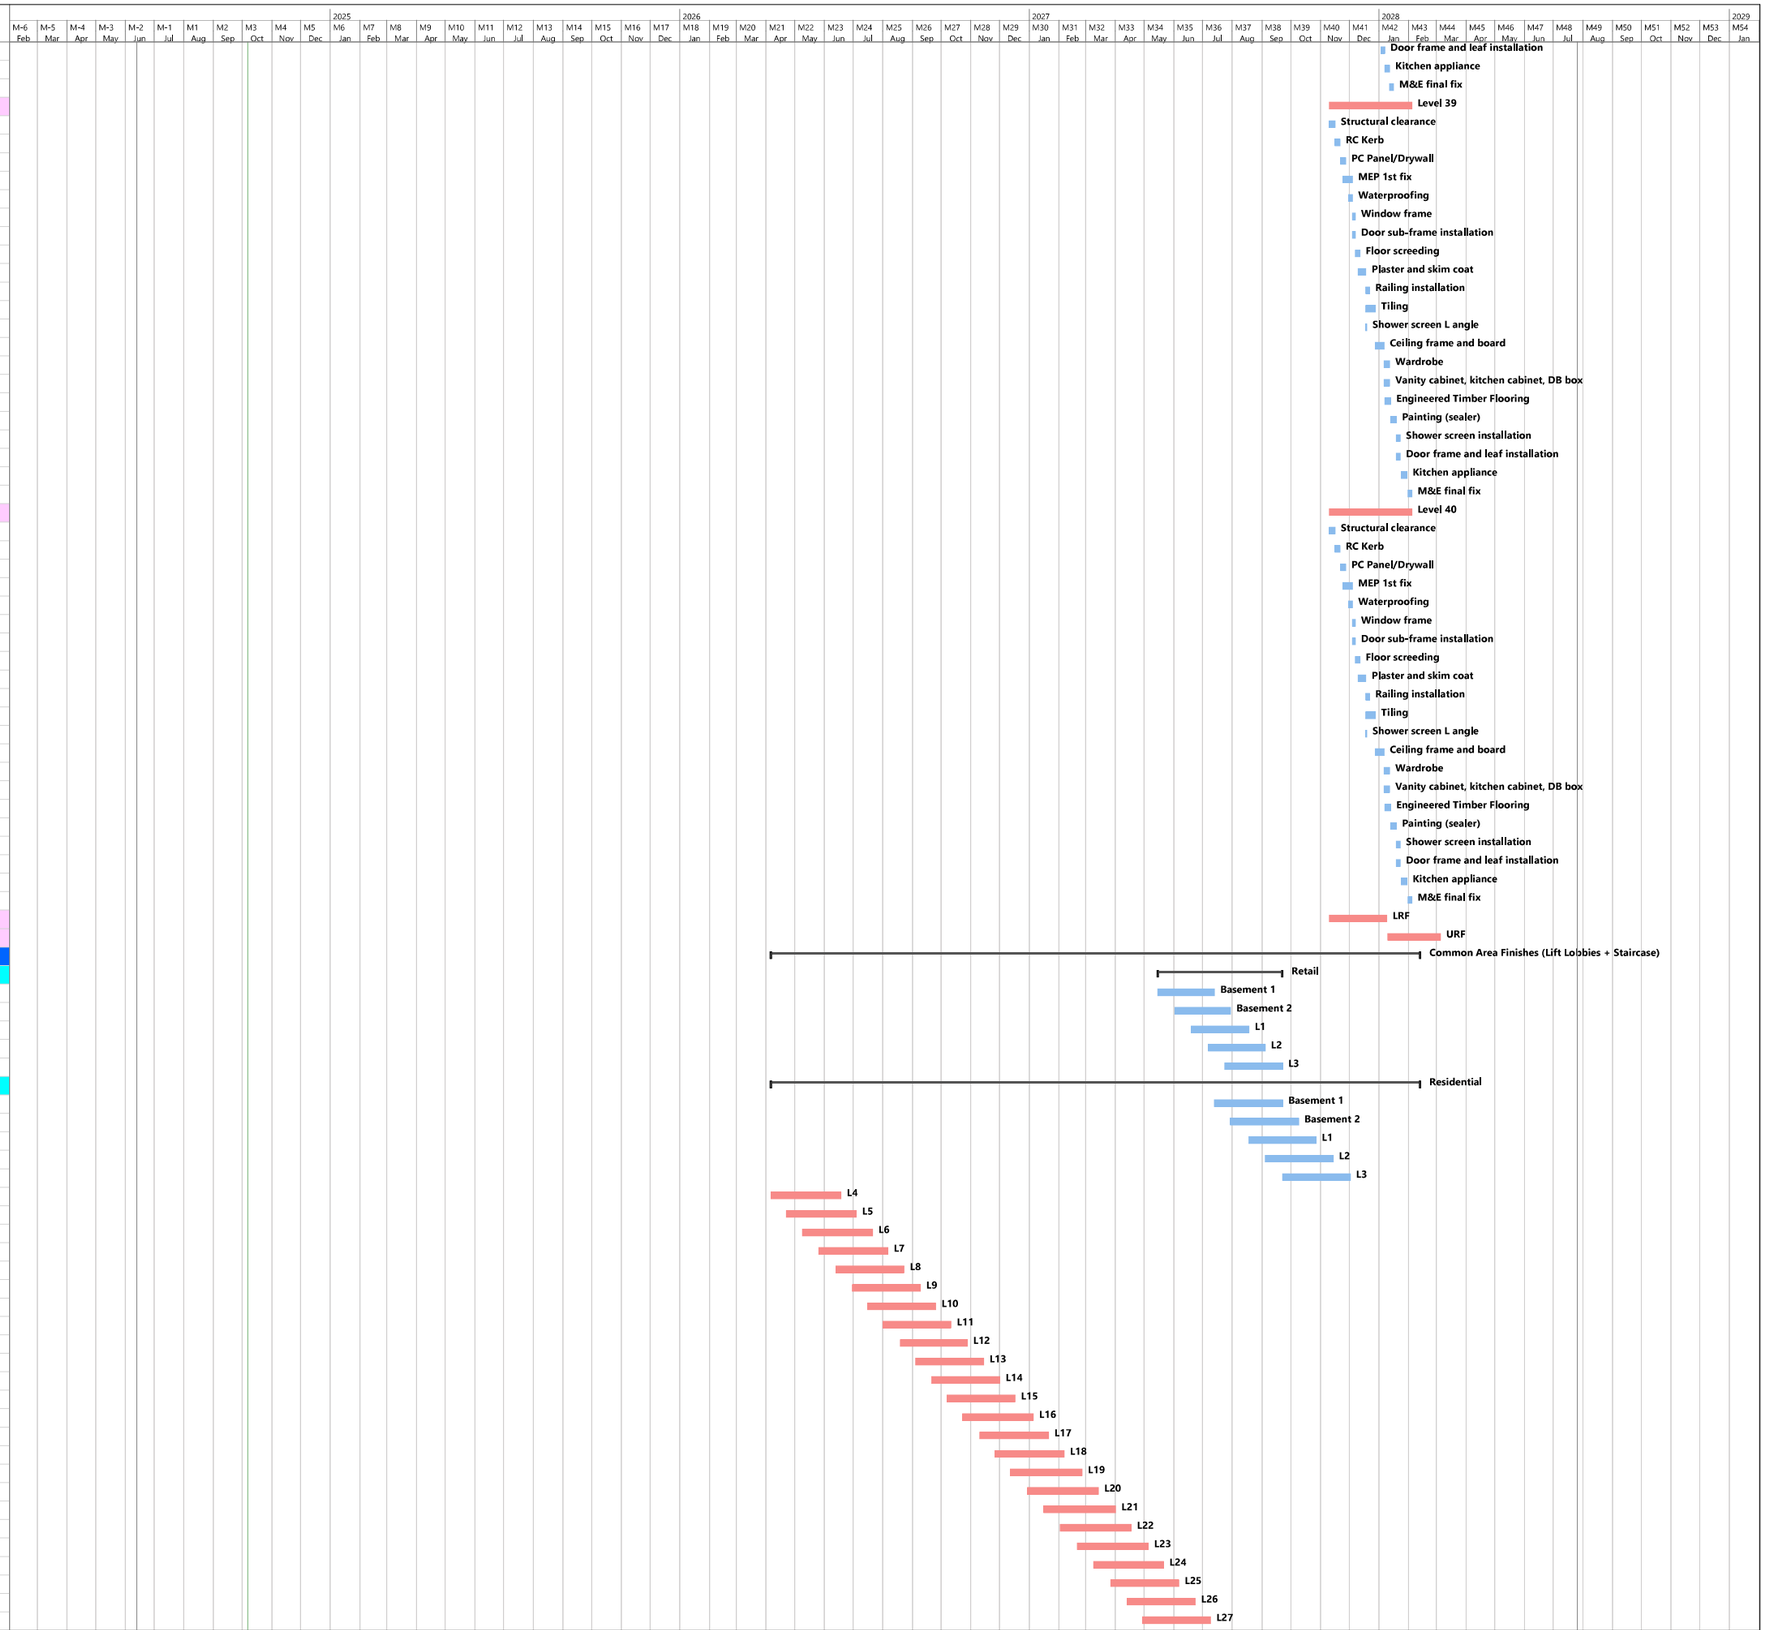
| Service | Authority | Original Submission | | | Comments/Resubmission | | | Approval/ | | |
|---|---|---|---|---|---|---|---|---|---|---|
| | | Scheduled | Actual | Comment | Resubmit | Comment | Resubmit | Comment | Resubmit | Clearance |
| External Water Reticulation System | PUB (Water Supply) Network Dept | | | | | | | | | |
| Telephone/Fiber Optic Installation (USR & US1) | TFCC | Aug 2024 | 29 Aug 2024 | 23 Sep 2024 | 10 Jun 2026 | | | | | 22 Jul 2026 |
| Telephone/Fiber Optic Installation (USC, US3, US5 & US7) | TFCC | Jan 2024 | 16 Jan 2025 | 10 Mar 2025 | 11 Jul 2025 | 2 Sep 2025 | 15 Oct 2025 | | | 23 Feb 2026 |
| Street Lighting Submission | LTA | | | | | | | | | |
| Air-conditioning & Mechanical Ventilation Installation | FSSD | 30 Dec 2025 (USR & US1) (USC, US3, US5 & US7) | 7 Sep 2026 (USR & US1) (USC, US3, US5 & US7) | | | | | | | 15 Sep 2026 (USR & US1) 15 Sep 2026 (USC, US3, US5 & US7) |
| Fire Fighting & Alarm Installation | FSSD | 30 Jun 2025 (USR & US1) (USC, US3, US5 & US7) | 17 Sep 2026 (USR & US1) 2 Jun 2026 (USC, US3, US5 & US7) | 17 Sep 2026 (USR & US1) 5 Jun 2026 (USC, US3, US5 & US7) | 19 Sep 2026 (USR & US1) 9 Jun 2026 (USC, US3, US5 & US7) | | | | | (USR & US1) 25 Jun 2026 (USC, US3, US5 & US7) |
| Emergency Voice Communication System | FSSD | 17 Jul 2026 (USR & US1) 30 Jun 2026 (USC, US3, US5 & US7) | 17 Jul 2026 (USR & US1) 30 Jun 2026 (USC, US3, US5 & US7) | 3 Jul 2026 (USC, US3, US5 & US7) | 13 Jul 2026 (USC, US3, US5 & US7) | | | | | 26 Jul 2026 (USR & US1) 30 Jul 2026 (USC, US3, US5 & US7) |

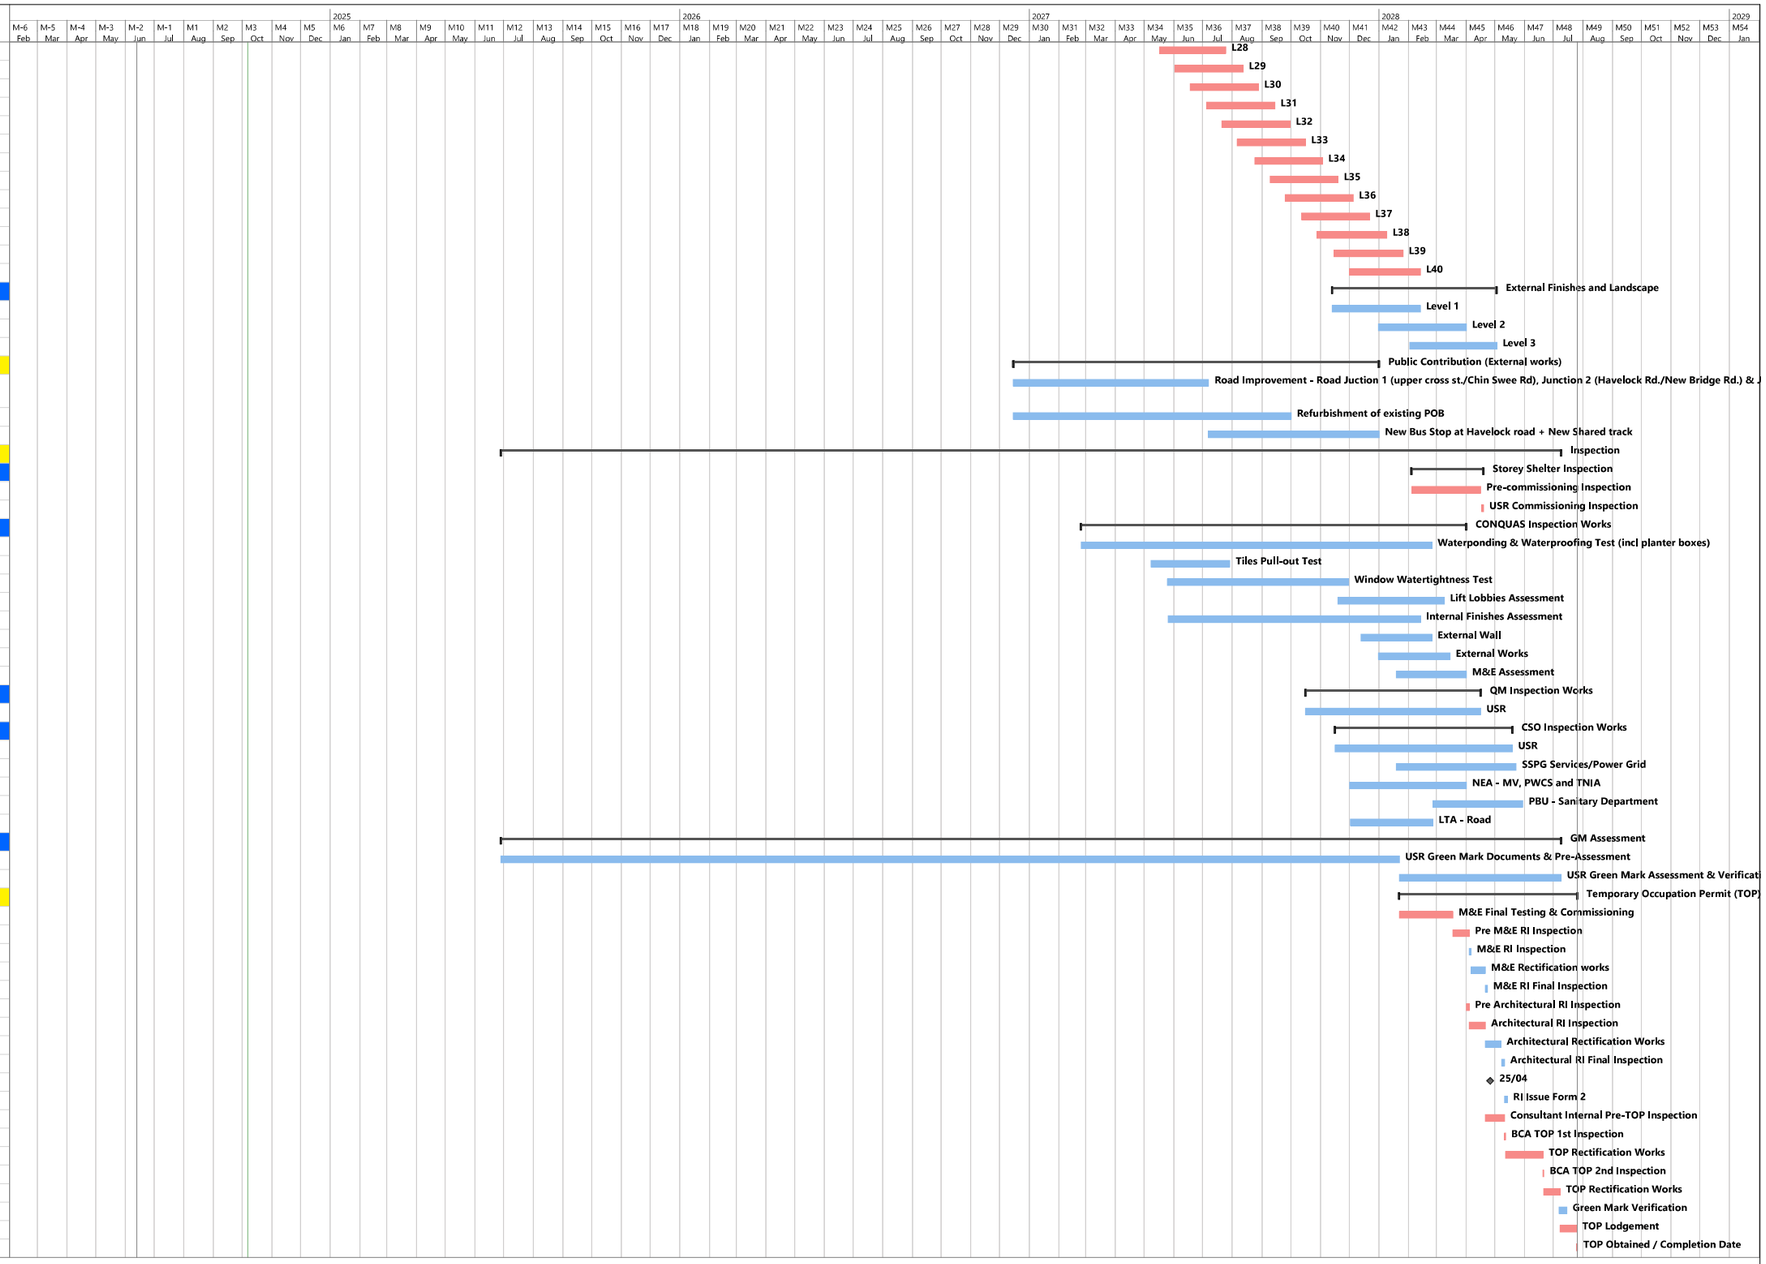**SECTION 4**

**PROGRAMME**

### 4.3 Authority Submission Status for M&E Services (Amendments) – 2nd Submission – NOT APPLICABLE

| Service | Authority | Original Submission | | Comments/Resubmission | | | | | | Approval/ |
|---|---|---|---|---|---|---|---|---|---|---|
| | | Scheduled | Actual | Comment | Resubmit | Comment | Resubmit | Comment | Resubmit | Clearance |
| Application for Electricity Supply | SP Services Ltd | | | | | | | | | |
| Power Supply Substation | SP PowerGrid Ltd | | | | | | | | | |
| Metering Layout | SP Services Ltd | | | | | | | | | |
| Sanitary Installation | PUB Water Reclamation (Network) Dept | | | | | | | | | |
| Domestic Water Supply (External Water Reticulation System) | PUB (Water Supply) Network Dept | | | | | | | | | |
| Gas Supply Installation | City Gas Pte Ltd | | | | | | | | | |
| Air Conditioning & Ventilation Inst. | FSSD | | | | | | | | | |
| Fire Fighting & Alarm Installation | FSSD | | | | | | | | | |
| Telephone Installation | TFCC | | | | | | | | | |
| Broadband Co-axial Cable System (BCS) | Starhub Cable Vision | | | | | | | | | |
| Fuel Storage | FSSD | | | | | | | | | |
| | NEA (Pollution Control) | | | | | | | | | |
| | | | | | | | | | | |

**SECTION 5**

**PROJECT RECORDS**

## 5.1 List of Internal Files

**Standard Files**

| File Ref: | | File Ref: | |
|---|---|---|---|
| - Owner | | - Architect | |
| - Authorities | | - Other Consultants | |
| - Contractors | | - CC | |
| - CF | | - PQP/QSP | ✓ |

**Project Files to be initiated by PM as and when required**

| File Ref: | | File Ref: | | File Ref: | |
|---|---|---|---|---|---|
| MC/EC | ✓ | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |

(✓*where applicable*)

**SECTION 5**

**PROJECT RECORDS**

## 5.2 Filing of Drawings

The following team members shall take charge of filing of drawings, stamping "SUPERSEDED" drawings, etc.

| Description | Team Member |
|---|---|
| Incoming Architectural Floor Plans | Softcopy saved in the server |
| Incoming Architectural Sketches/Details | |
| Incoming Structural Drawings | |
| M&E Drawings<br>- Electrical Installation<br>- Lift Installation<br>- Air Conditioning & Ventilation Installation<br>- Plumbing & Sanitary Installation<br>- Swimming Pool & Filtration Installation | |

**SECTION 6**

**INTERFACING**

## 6.1 Method of Interface

| Description | Method of Interface | |
|---|---|---|
| Client's Review & Approval | M&E Design Report | ✓ |
| | Pre-planned meeting at fixed intervals | ✓ |
| | Letter and telephone | ✓ |
| | Email | ✓ |
| | | |
| Interface With External Design Teams | M&E Design Report | ✓ |
| | Pre-planned meeting at fixed intervals | ✓ |
| | Letter and telephone | ✓ |
| | Email | ✓ |
| | | |
| Interface Between Internal Design Teams | Telephone | ✓ |
| | Email | ✓ |
| | Internal Project Team Meeting | ✓ |
| | Circulation of Information | ✓ |
| | | |

(*ü where applicable*)

**SECTION 6**

**INTERFACING**

## 6.2 Internal Design Interface – NOT APPLICABLE

| Item No. | Description* | Required From | Required By | Date Required | Remarks |
|---|---|---|---|---|---|
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |

** Information required by INTERNAL DESIGN TEAM MEMBERS*

**SECTION 6**

**INTERFACING**

### 6.3 Circulation of Documents to External Parties

| | Code:<br>A - Approval Required<br>C - For Comments<br>I - For Information Only | Client/ Client Rep. | * Client's Project Manager | Architect | Structural Engineer | Quantity Surveyor | |
|---|---|---|---|---|---|---|---|
| **1.** | **Letters/Fax:** | | | | | | |
| a. | Project Design | A | – | I | – | – | |
| b. | Project Administration | – | – | – | – | – | |
| c. | Project Cost Estimate/ Contract Cost | A | – | I | – | I | |
| **2.** | **Drawings** | | | | | | |
| a. | Outline Design Drgs. | A | – | C | I | I | |
| b. | Sketch Design Drgs. | A | – | C | I | I | |
| c. | Final Design Drgs. | A | – | C | I | I | |
| d. | Shop Drawings | I | – | A | – | – | |
| e. | As Built Drgs. | I | – | I | – | – | |
| **3.** | **Other Document** | | | | | | |
| a. | Specification | A | – | I | I | I | |
| b. | Tender Document | A | – | I | I | I | |
| c. | Tender Evaluation Report | A | – | I | – | I | |
| d. | Design Report | A | – | I | – | – | |
| e. | Progress Report | – | – | – | – | – | |
| f. | Financial Report | – | – | – | – | – | |
| g. | Minutes of Meeting | – | – | – | – | – | |
| h. | Inspection Report | I | – | I | – | – | |
| i. | Testing & Comm. Report | I | – | I | – | – | |
| j. | O & M Manual | I | – | I | – | – | |

*Note: Applicable only, if the client engaged a Project Manager.

**SECTION 7**

**WORK AUTHORISATION**

| Activity \ Authorised Signatories | PD | QP | PM | AE | SS |
|---|---|---|---|---|---|
| General Correspondences with Client | | | ✓ | ✓ | |
| General Correspondences with Other Consultants | | | ✓ | ✓ | |
| M&E Cost Estimate Report | – | – | – | | |
| M&E Design Report | – | – | – | | |
| Check Prints | | ✓ | | | |
| Tender Drawing Approval | – | – | – | | |
| Tender Specification Approval | – | – | – | | |
| List of Tenderers | – | – | – | | |
| Tender Questionnaires | – | – | – | | |
| Tender Reports | – | – | – | | |
| Draft Letter of Award | – | – | – | | |
| Review of Contractor's Shop Drawing | | | ✓ | ✓ | |
| Review of Contractor's Technical Submittal | | | ✓ | ✓ | |
| Review of Contractor's Sample Submittal | | | ✓ | ✓ | |
| Contractor's Request for Deviation | ✓ | ✓ | ✓ | | |
| Progress Payment Valuation Form | – | | – | | |
| Final Account Valuation | – | | – | | |
| Draft Variation Order | – | | – | | |
| Engineer/Architect's Instruction/Direction | – | | – | | |
| Site Instruction/Direction | | | – | | |
| Correspondence/Submission to Authorities | ✓ | ✓ | ✓ | | |

(✓*where authorised*)

Key to abbreviations:-

PD : Project Director
QP : Qualified Person
PM : Project Manager/Assistant Project Manager
AE : Assistant Engineer
SS : ACEPL Site Staff

**SECTION 8**

**DESIGN INPUT & METHODOLOGY**

## 8.1 List of Client's Standards, Reference Documents or Brief – NOT APPLICABLE

| ITEM | KEPT BY |
|---|---|
| | |
| | |
| | |
| | |
| | |

## 8.2 List of Applicable Code of Practice and Regulations

| Services | Title of Code of Practice/Standard |
|---|---|
| Electrical Wiring | SS 638 (formerly CP 5) |
| Lightning Protection System | SS 555 : 2018 |
| Telephone Installation | COPIF 2018 |
| Emergency Voice Communication System | SS 546: 2022 |
| Air Conditioning & Ventilation Installation | SS 553 : 2016 |
| Automatic Fire Alarm System | SS 645 : 2019 |
| Sprinkler System | SS CP 52 : 2004 |
| Dry/Wet Riser System | SS 575 : 2012 |
| Lift & Escalator Installation | SS 550 : 2020 |
| Sanitary System | Code of Practice on Sewerage & Sanitary Works |
| Plumbing System | SS 636 : 2018 |
| Town Gas/LPG Supply System | SS 608 : 2015 |
| Boiler and Steam Supply System | – |
| Mechanical Smoke Control System | – |

**SECTION 8**

**DESIGN INPUT & METHODOLOGY**

## 8.3 List of Design Guide or Handbook Used

Carrier's Handbook of Air Conditioning System Design

ASHRAE Handbooks

Institute of Plumbing's Plumbing Services Design Guide

## 8.4 List of Pre-Consultation and Waiver – NOT APPLICABLE

| S/N | Description | Date of Application | Date of Approval | Remarks |
|---|---|---|---|---|
| 1 | | | | |
| 2 | | | | |
| 3 | | | | |
| 4 | | | | |
| 5 | | | | |

*To fill in actual information

## 8.5 List of Applicable Quality System Procedures

Alpha Consulting Engineers Pte Ltd's Quality Management System Procedures

| Section | Title | ✓where applicable |
|---|---|---|
| M1 | Preparation of Consultancy Offer | ✓ |
| M2 | Project Commissioning and Service Agreement | ✓ |
| M3 | Design Control | ✓ |
| M4 | Design Change Control | ✓ |
| M5 | Tender Process and Evaluation | – |
| M6 | Authority Submission | ✓ |
| M7 | Construction Process Control | ✓ |
| M8 | Testing and Commissioning | ✓ |
| S1 | Document Control | ✓ |
| S2 | Documentation of Quality & Environmental Management System Procedure | ✓ |
| S3 | Documentation of Project Quality Plan | ✓ |
| S4 | Specification Control | ✓ |
| S5 | Library Control | – |
| S6 | Archive Control | ✓ |
| S7 | Filing Control | ✓ |
| S8 | Drawing Control | ✓ |
| S9 | Administration Control | ✓ |
| S10 | Purchasing Control | – |
| S11 | Training Control | – |
| S12 | Computer Control | – |
| S13 | Non-Conformity and Corrective Action Procedures | ✓ |
| S14 | Quality & Environmental System Audit | ✓ |
| S15 | Feedback Reporting | ✓ |
| S16 | Clients Feedback | ✓ |
| S17 | Management Review | ✓ |
| S18 | Risk Identification, Assessment & Control | ✓ |

**8.6 List of Software Used For Design/Analysis**

| DESCRIPTION/ PACKAGE NAME | VERSION | SUPPLIER/ SOURCE | PURPOSE | |
|---|---|---|---|---|
| Cophos | 3.31 | Zumtobel | Lighting design | |
| Carrier E20-II | 3.21 | Carrier | Programme for determination of heat load, duct size and its losses, etc. | ✓ |
| Gensize 2 | 2.1 | Onan | Generator sizing | |
| Hyena | 4.00.1 | ACADS-BSG | Fire Sprinkler & Hydrant Analysis | |
| Dialux | 4.11 | Changi Light | Lighting design | |
| Lift Traffic | 7.18 | Elevate | Lift traffic calculation | ✓ |
| Fault Level Calculation | 11.11 | ETAP | Calculation of fault level and voltage drop | |
| | | | | |

(✓*where applicable*)

**SECTION 9**

**ENVIRONMENTAL CONSIDERATIONS**

## 9.1 Sustainable Design Features/Criteria – NOT APPLICABLE

| Item | Remarks |
|---|---|
| Green Mark criteria | |
| Green Design Features | |

## 9.2 Site PPE Requirement

The necessary Personal Protective Equipment (detailed below) shall be provided by the main contractor/Company in accordance to the site EHS requirements prior to the site monitoring.

| PPE | ✓where applicable |
|---|---|
| Safety Helmet | ✓ |
| Safety Shoes | ✓ |
| Eye Protection | |
| Ear Protection | |
| Safety Harness / Belt | |
| Others: | |

## 9.3 Site Emergency Preparedness

Site staff shall comply with the site emergency preparedness and response procedure, established by the main contractor/owner, which shall include the following details.

| Items | ✓where applicable |
|---|---|
| Evacuation Route | ✓ |
| Emergency Exit | ✓ |
| Assembly Point | ✓ |
| Emergency Contact List / Person | ✓ |
| Alarm system / methods | ✓ |

**SECTION 9**

**ENVIRONMENTAL CONSIDERATIONS**

## 9.4 Reporting of Environmental Non-conformances

When encountering environmental non-conformances, Site Staff shall be responsible to feedback to the main contractor.

## 9.5 List of Applicable Environmental Management System Procedures

Alpha Consulting Engineers Pte Ltd's Environmental Management System Procedures

| Section | Title | ✓where applicable |
|---|---|---|
| E1 | Aspect / Impact Identification, Risk Assessment & Risk Control | ✓ |
| E2 | Identifying Legal & Other Requirements | ✓ |
| E3 | Objectives, Targets & Programmes | ✓ |
| E4 | Communication | ✓ |
| E5 | Emergency Preparedness & Response | ✓ |
| E6 | Monitoring & Measurement | ✓ |
| E7 | Control of Air & Noise Pollution | ✓ |
| E8 | Management of Wastes | ✓ |

**SECTION 10**

**CLIENT'S REQUIREMENTS**

**10.1 List of Output Required by Client:**

| Item | * Remarks |
|---|---|
| M&E Design Report | A |
| M&E Cost Estimate Report | A |
| Pre-Qualification of Tenderers | A |
| Tender Documents | A |
| Tender Report | A |
| Payment Valuation for QS | A |
| Certificates of Supervision for TOP/CSC | I |

* *Remarks*

*A: for approval* *C: for comment* *I: for Information* *Re: for record*

*Other purposes and for action: please specify.*

**10.2 Specific Procedures Required By Client** *(If applicable)*

**NOT APPLICABLE**

**SECTION 11**

**LIST OF SUB-JOB**

**11.1 List of Sub-Job Numbers – NOT APPLICABLE**

| Sub Job No | Description | Allocation Details |
|---|---|---|
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
